Medor Adminstration Building

Consultant : Prof. Dr. Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish
Medor Adminstration Building		275	10-Jul-10	10-Apr-11
general		275	10-Jul-10	10-Apr-11
A1000	Receiving IFC drawings	0	10-Jul-10	
A1010	Receiving advance payement	0	10-Jul-10	
A1020	start construction phase	0	19-Jul-10	
A1030	finish construction	0		10-Apr-11
engineering		37	10-Jul-10	15-Aug-10
A1990	submit ground floor's shop drawings for approval	1	10-Jul-10	10-Jul-10
A2000	ground floor's shop drawings approval	0		18-Jul-10
A2010	submit 1st floor shop drawings for approval	1	14-Jul-10	14-Jul-10
A2020	1st floor shop drawings approval	0		22-Jul-10
A2030	submit 2nd floor shop drawings for approval	1	19-Jul-10	19-Jul-10
A2040	2nd floor shop drawings approval	0		27-Jul-10
A2050	submit 3rd floor shop drawings for approval	1	24-Jul-10	24-Jul-10
A2060	3rd floor shop drawings approval	0		01-Aug-10
A2070	submit 4th floor shop drawings for approval	1	28-Jul-10	28-Jul-10
A2080	4th floor shop drawings approval	0		05-Aug-10
A2090	submit 5th floor shop drawings for approval	1	02-Aug-10	02-Aug-10
A2100	5th floor shop drawings approval	0		10-Aug-10
A2110	submit 6th floor shop drawings for approval	1	07-Aug-10	07-Aug-10
A2120	6th floor shop drawings approval	0		15-Aug-10
skeleton		266	19-Jul-10	10-Apr-11

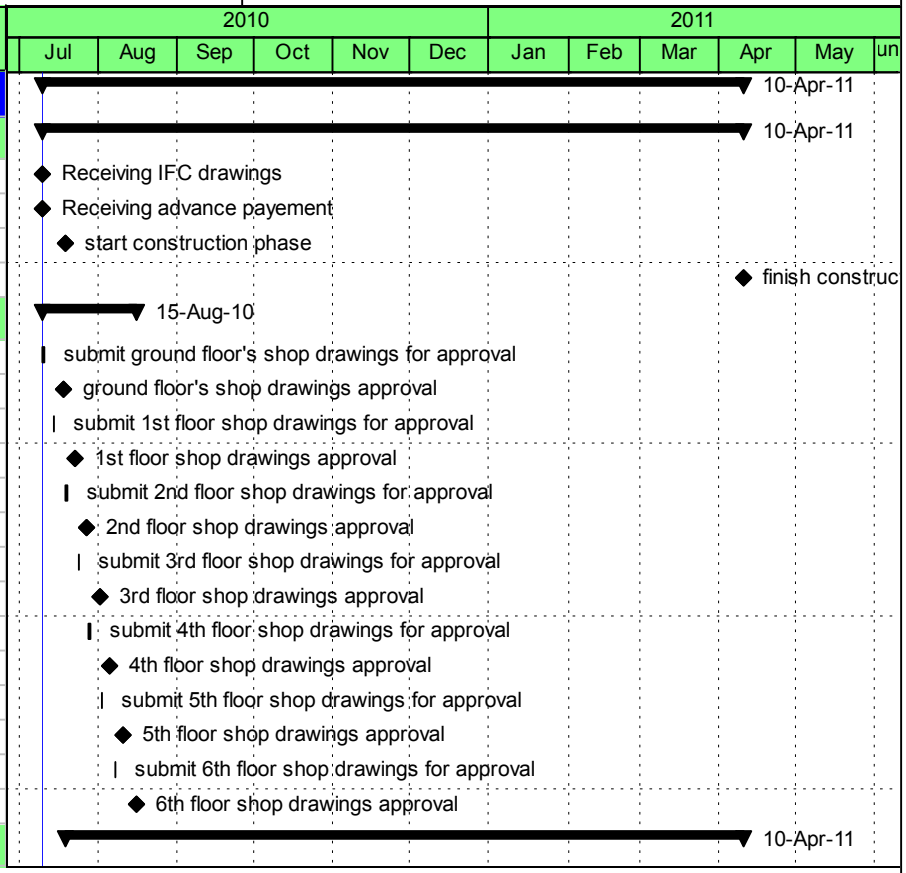

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Classic WBS Layout Basic

TASK filter: All Activities

Date	Revision	Checked	Approved
06-Jul-10	Rev. 01		

Gama For Trading & Contracting

Medor Adminstration Building

Consultant : Prof. Dr. Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish
ground floor		29	19-Jul-10	16-Aug-10
A1330	columns Formwork & Rft. Part 2	10	19-Jul-10	29-Jul-10
A1340	Columns Pouring Part2	1	31-Jul-10	31-Jul-10
A1350	Slab Formwork & Rft. Part1	10	19-Jul-10	29-Jul-10
A1360	Slab Pouring Part1	1	31-Jul-10	31-Jul-10
A1370	Slab Formwork & Rft. Part2	11	03-Aug-10	15-Aug-10
A1380	Slab Pouring Part2	1	16-Aug-10	16-Aug-10
1st floor		51	03-Aug-10	22-Sep-10
A1390	columns Formwork & Rft. Part1	10	03-Aug-10	14-Aug-10
A1400	Columns Pouring Part1	1	15-Aug-10	15-Aug-10
A1410	columns Formwork & Rft. Part 2	10	19-Aug-10	30-Aug-10
A1420	Slab Formwork & Rft. Part1	14	18-Aug-10	02-Sep-10
A1440	Columns Pouring Part2	1	31-Aug-10	31-Aug-10
A1450	Slab Pouring Part1	1	04-Sep-10	04-Sep-10
A1460	Slab Formwork & Rft. Part2	14	04-Sep-10	21-Sep-10
A1480	Slab Pouring Part2	1	22-Sep-10	22-Sep-10
2nd floor		51	07-Sep-10	27-Oct-10
A1490	columns Formwork & Rft. Part1	10	07-Sep-10	20-Sep-10
A1500	Columns Pouring Part1	1	21-Sep-10	21-Sep-10
A1510	columns Formwork & Rft. Part 2	10	26-Sep-10	06-Oct-10
A1520	Slab Formwork & Rft. Part1	14	25-Sep-10	10-Oct-10
A1540	Columns Pouring Part2	1	07-Oct-10	07-Oct-10
A1550	Slab Pouring Part1	1	11-Oct-10	11-Oct-10

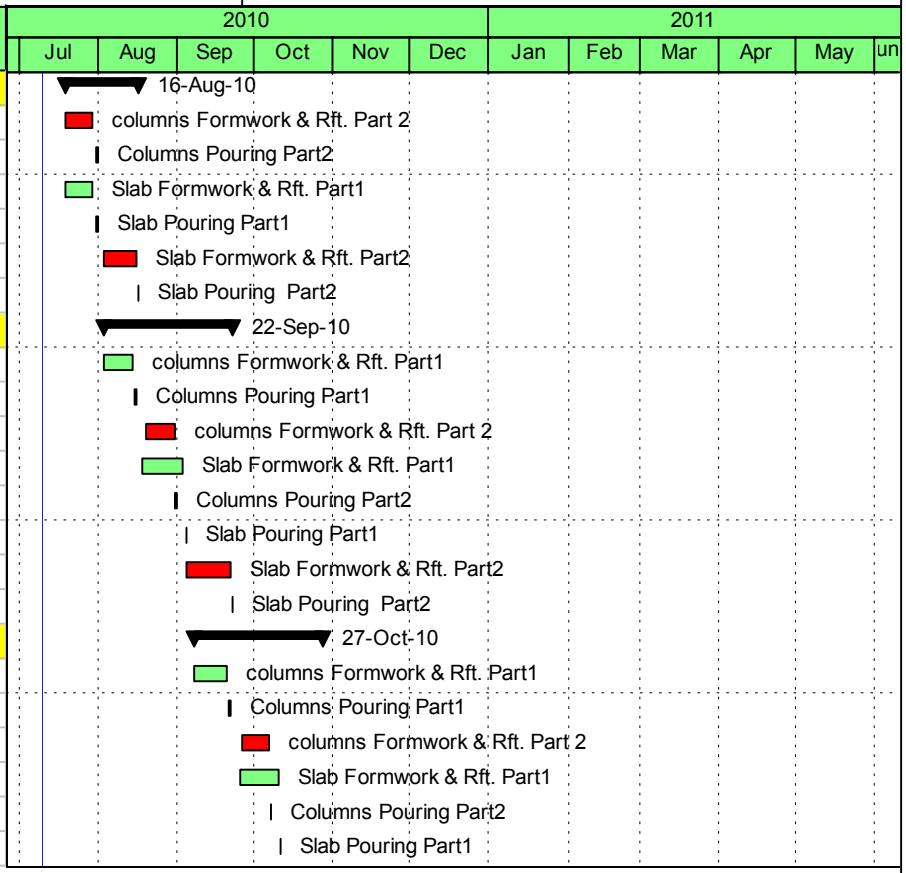

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Classic WBS Layout Basic

TASK filter: All Activities

Date	Revision	Checked	Approved
06-Jul-10	Rev. 01		

Medor Adminstration Building

Consultant : Prof. Dr. Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish
A1560	Slab Formwork & Rft. Part2	14	11-Oct-10	26-Oct-10
A1580	Slab Pouring Part2	1	27-Oct-10	27-Oct-10
3rd floor		54	14-Oct-10	06-Dec-10
A1590	columns Formwork & Rft. Part1	10	14-Oct-10	25-Oct-10
A1600	Columns Pouring Part1	1	26-Oct-10	26-Oct-10
A1610	columns Formwork & Rft. Part 2	10	31-Oct-10	10-Nov-10
A1620	Slab Formwork & Rft. Part1	14	30-Oct-10	14-Nov-10
A1640	Columns Pouring Part2	1	11-Nov-10	11-Nov-10
A1650	Slab Pouring Part1	1	20-Nov-10	20-Nov-10
A1660	Slab Formwork & Rft. Part2	14	20-Nov-10	05-Dec-10
A1680	Slab Pouring Part2	1	06-Dec-10	06-Dec-10
4th floor		49	23-Nov-10	10-Jan-11
A1690	columns Formwork & Rft. Part1	10	23-Nov-10	04-Dec-10
A1700	Columns Pouring Part1	1	05-Dec-10	05-Dec-10
A1710	columns Formwork & Rft. Part 2	10	09-Dec-10	20-Dec-10
A1720	Slab Formwork & Rft. Part1	14	08-Dec-10	23-Dec-10
A1740	Columns Pouring Part2	1	21-Dec-10	21-Dec-10
A1750	Slab Pouring Part1	1	25-Dec-10	25-Dec-10
A1760	Slab Formwork & Rft. Part2	14	25-Dec-10	09-Jan-11
A1780	Slab Pouring Part2	1	10-Jan-11	10-Jan-11
5th floor		49	28-Dec-10	14-Feb-11
A1790	columns Formwork & Rft. Part1	10	28-Dec-10	08-Jan-11
A1800	Columns Pouring Part1	1	09-Jan-11	09-Jan-11

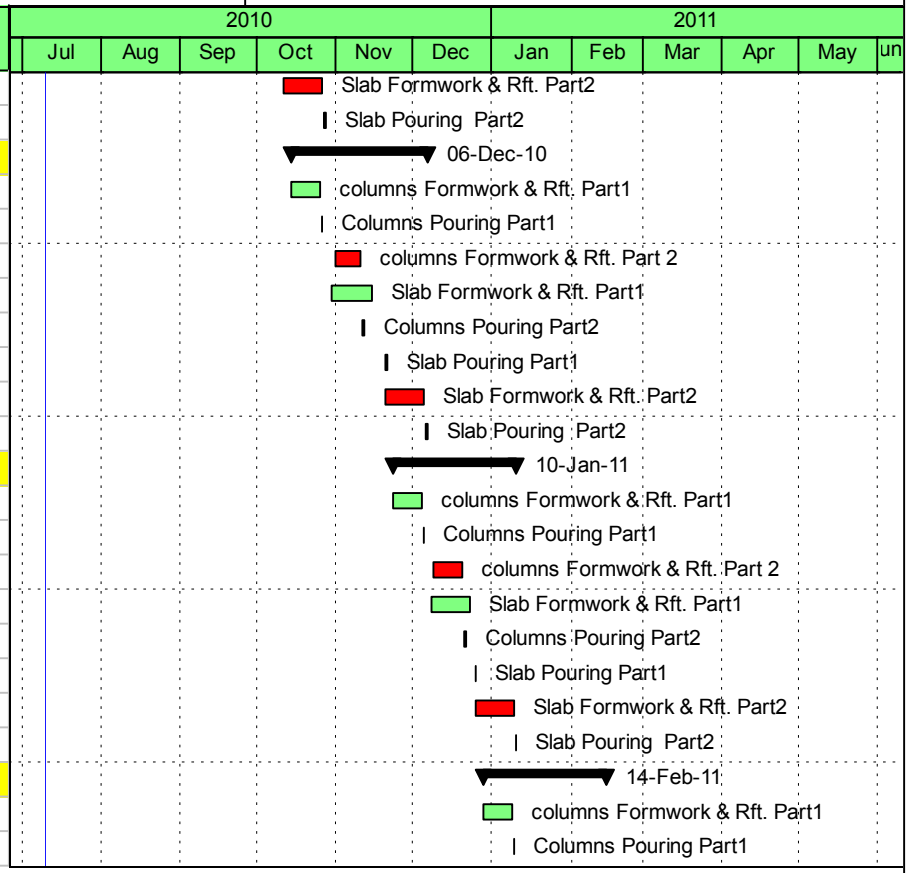

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Classic WBS Layout Basic

TASK filter: All Activities

Date	Revision	Checked	Approved
06-Jul-10	Rev. 01		

Medor Adminstration Building

Consultant : Prof. Dr. Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish
A1810	columns Formwork & Rft. Part 2	10	13-Jan-11	24-Jan-11
A1820	Slab Formwork & Rft. Part1	14	12-Jan-11	27-Jan-11
A1840	Columns Pouring Part2	1	25-Jan-11	25-Jan-11
A1850	Slab Pouring Part1	1	29-Jan-11	29-Jan-11
A1860	Slab Formwork & Rft. Part2	14	29-Jan-11	13-Feb-11
A1880	Slab Pouring Part2	1	14-Feb-11	14-Feb-11
6th floor		49	01-Feb-11	21-Mar-11
A1890	columns Formwork & Rft. Part1	10	01-Feb-11	12-Feb-11
A1900	Columns Pouring Part1	1	13-Feb-11	13-Feb-11
A1910	columns Formwork & Rft. Part 2	10	17-Feb-11	28-Feb-11
A1920	Slab Formwork & Rft. Part1	10	16-Feb-11	27-Feb-11
A1940	Columns Pouring Part2	1	01-Mar-11	01-Mar-11
A1950	Slab Pouring Part1	1	28-Feb-11	28-Feb-11
A1960	Slab Formwork & Rft. Part2	14	05-Mar-11	20-Mar-11
A1980	Slab Pouring Part2	1	21-Mar-11	21-Mar-11
Roof floor		18	24-Mar-11	10-Apr-11
A2130	columns Formwork & Rft.	5	24-Mar-11	29-Mar-11
A2140	Columns Pouring	1	30-Mar-11	30-Mar-11
A2150	Slab Formwork & Rft.	8	31-Mar-11	09-Apr-11
A2160	Slab Pouring	1	10-Apr-11	10-Apr-11

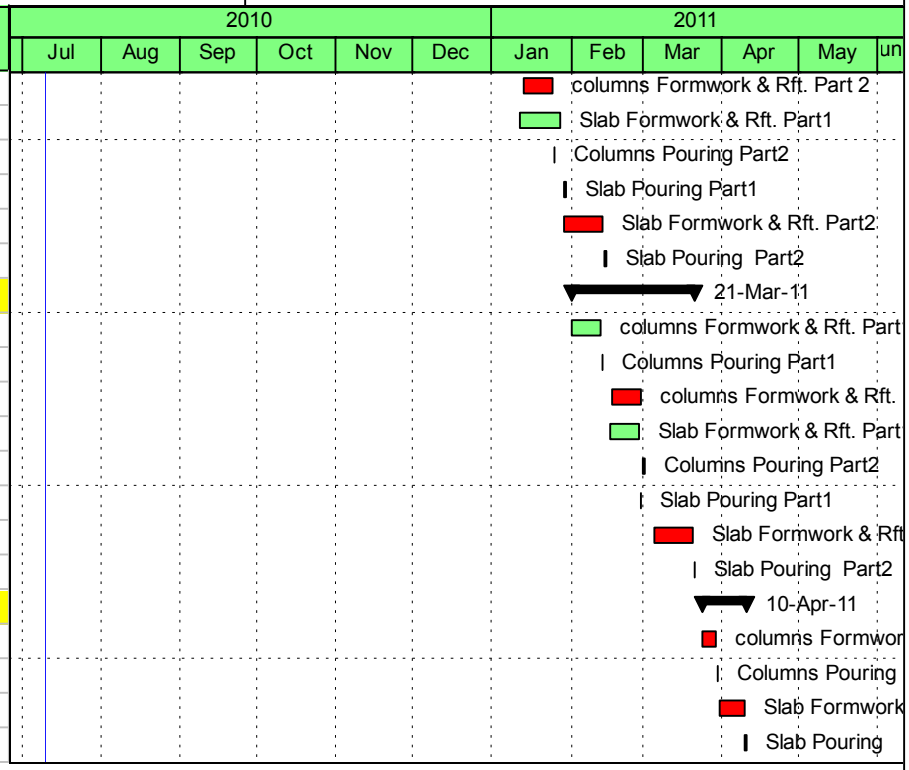

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

Classic WBS Layout Basic

TASK filter: All Activities

Date	Revision	Checked	Approved
06-Jul-10	Rev. 01		
