Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
Office Building 14B01 Substructure Package		85	01-Jul-10	07-Oct-10
General		85	01-Jul-10	07-Oct-10
A1000	Start project	0	01-Jul-10	
A1020	Mobilization	8	01-Jul-10	10-Jul-10
A1320	Receive issue for construction drawings	0	01-Jul-10	
A1010	Finish project	0		07-Oct-10
Engineering		42	01-Jul-10	18-Aug-10
Tank		3	08-Jul-10	11-Jul-10
A1260	submittals of all tank's shop drawings	0	08-Jul-10	
A2170	Approval of all tank's shop drawings	0		11-Jul-10
Tower 1		33	01-Jul-10	08-Aug-10
Submittals		30	01-Jul-10	05-Aug-10
A1140	Submittal of All R.C raft dimension	0	01-Jul-10	
A1150	Submittal of All column layout	0	01-Jul-10	
A1160	Submittal of All R.C raft RFT&starters	0	12-Jul-10	
A1170	Submittal of All basement columns & walls...	0	22-Jul-10	
A1180	Submittal of All basement slab concrete di...	0	29-Jul-10	
A1190	Submittal of All basement slab RFT	0	05-Aug-10	
Approvals		30	04-Jul-10	08-Aug-10
A1141	Approval of All R.C raft dimension	0		04-Jul-10
A1151	Approval of All column layout	0		04-Jul-10
A1161	Approval of All R.C raft RFT&starters	0		14-Jul-10
A1171	Approval of All basement columns & walls ...	0		25-Jul-10
A1181	Approval of All basement slab concrete di...	0		01-Aug-10
A1191	Approval of All basement slab RFT	0		08-Aug-10
Tower 2		33	12-Jul-10	18-Aug-10
Submittals		30	12-Jul-10	16-Aug-10

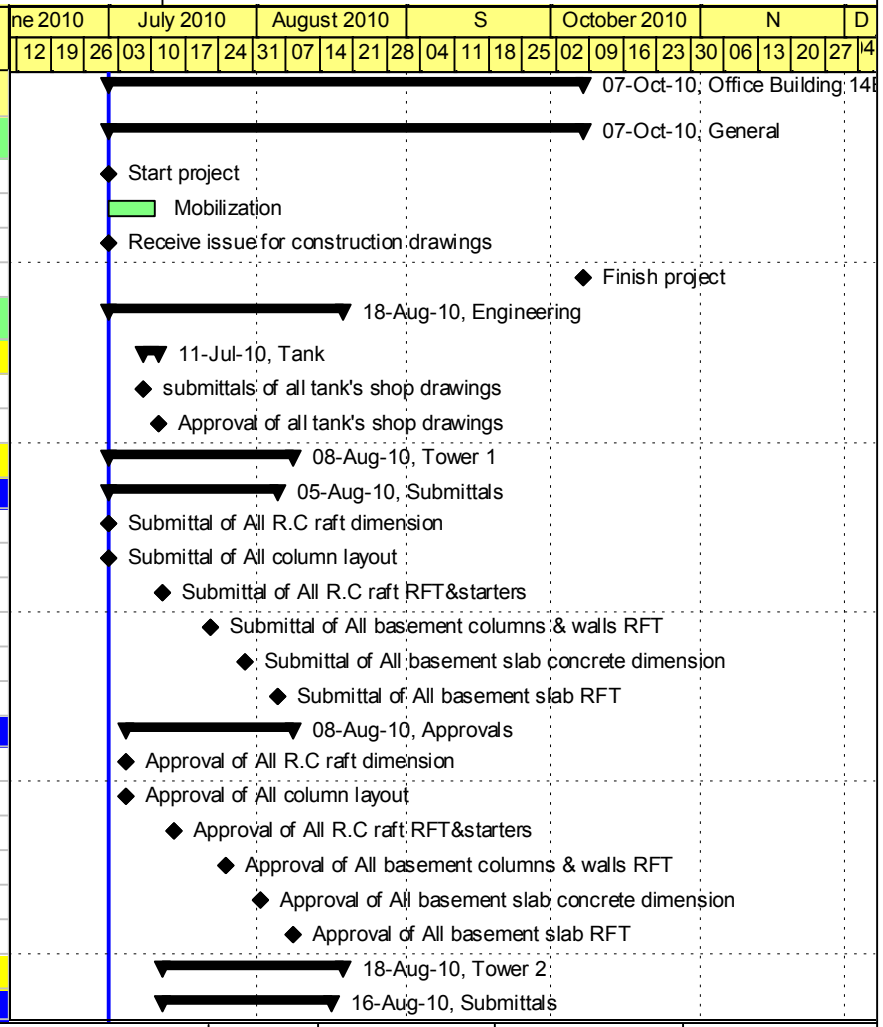

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved

Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
A1200	Submittal of R.C raft dimension	0	12-Jul-10	
A1210	Submittal of column layout	0	12-Jul-10	
A1220	Submittal of R.C raft RFT&starters	0	22-Jul-10	
A1230	Submittal of basement columns & walls RFT	0	29-Jul-10	
A1240	Submittal of basement slab concrete dime...	0	05-Aug-10	
A1250	Submittal of basement slab RFT	0	16-Aug-10	
Approvals		30	14-Jul-10	18-Aug-10
A1201	Approval of R.C raft dimension	0		14-Jul-10
A1211	Approval of column layout	0		14-Jul-10
A1221	Approval of R.C raft RFT&starters	0		25-Jul-10
A1231	Approval of basement columns & walls RFT	0		01-Aug-10
A1241	Approval of basement slab concrete dimen...	0		08-Aug-10
A1251	Approval of basement slab RFT	0		18-Aug-10
construction		81	06-Jul-10	07-Oct-10
A1580	Start construction	0	06-Jul-10	
A1590	Finish construction	0		04-Oct-10
Office building		80	07-Jul-10	07-Oct-10
Tower 1		80	07-Jul-10	07-Oct-10
Area 1 (550 m2)		53	31-Jul-10	29-Sep-10
R.C Raft		8	31-Jul-10	08-Aug-10
A1270	Formwork For R.C raft	6	31-Jul-10	05-Aug-10
A1280	Rebar For R.C raft	5	02-Aug-10	07-Aug-10
A1290	M&E conduits For R.C raft (by others)	0		04-Aug-10
A1300	Pouring For R.C raft	1	08-Aug-10	08-Aug-10
Basement Walls & Columns		9	15-Aug-10	24-Aug-10
A1360	Formwork For basement walls & col.	8	15-Aug-10	23-Aug-10
A1370	Rebar For basement walls & col.	4	17-Aug-10	21-Aug-10

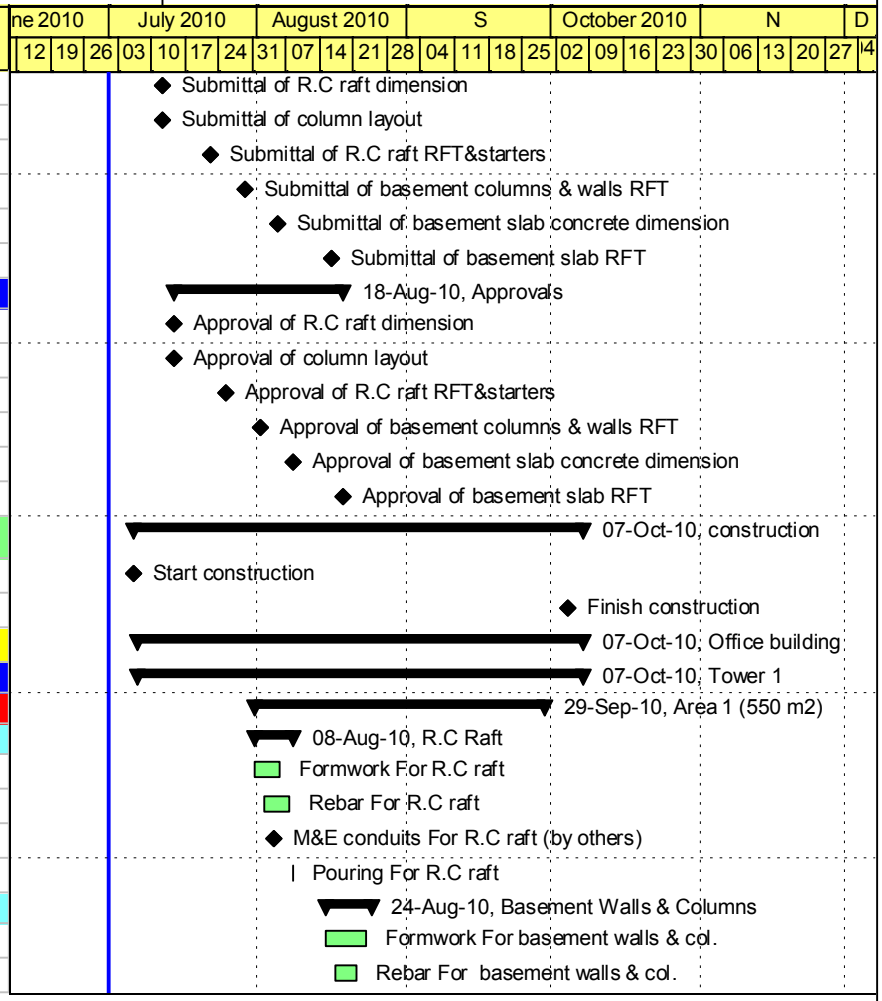

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved

Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
A1380	Pouring For basement walls & col.	1	24-Aug-10	24-Aug-10
Basement Slab		8	21-Sep-10	29-Sep-10
A1390	Formwork For basement Slab & stairs	6	21-Sep-10	27-Sep-10
A1400	Rebar For basement Slab & stairs	3	26-Sep-10	28-Sep-10
A1410	M&E conduits For basement Slab & stairs ...	0		27-Sep-10
A1420	Pouring For basement Slab & stairs	1	29-Sep-10	29-Sep-10
Insulation & Water Proofing		8	26-Aug-10	04-Sep-10
A1340	Water proofing bituminous membrane	4	26-Aug-10	30-Aug-10
A1310	Isolation For Foundation bituminous emulsi...	4	28-Aug-10	31-Aug-10
A1350	Water proofing protection layer cartonal	4	31-Aug-10	04-Sep-10
Area 2 (1450 m2)		42	07-Jul-10	24-Aug-10
R.C Raft		16	07-Jul-10	25-Jul-10
A1030	Formwork For R.C raft	8	07-Jul-10	15-Jul-10
A1040	Rebar For R.C raft	7	15-Jul-10	22-Jul-10
A1050	M&E conduits For R.C raft (by others)	0		21-Jul-10
A1060	Pouring For R.C raft	2	24-Jul-10	25-Jul-10
Basement Walls & Columns		9	27-Jul-10	05-Aug-10
A1070	Formwork For basement walls & col.	7	27-Jul-10	03-Aug-10
A1080	Rebar For basement walls & col.	3	02-Aug-10	04-Aug-10
A1090	Pouring For basement walls & col.	1	05-Aug-10	05-Aug-10
Basement Slab		15	08-Aug-10	24-Aug-10
A1100	Formwork For basement Slab & stairs	10	08-Aug-10	18-Aug-10
A1110	Rebar For basement Slab & stairs	6	17-Aug-10	23-Aug-10
A1120	M&E conduits For basement Slab & stairs(...	0		22-Aug-10
A1130	Pouring For basement Slab &stairs	1	24-Aug-10	24-Aug-10
Insulation & Water Proofing		12	08-Aug-10	21-Aug-10
A1064	Water proofing bituminous membrane	6	08-Aug-10	14-Aug-10
A1061	Isolation For Foundation bituminous emulsi...	6	09-Aug-10	15-Aug-10

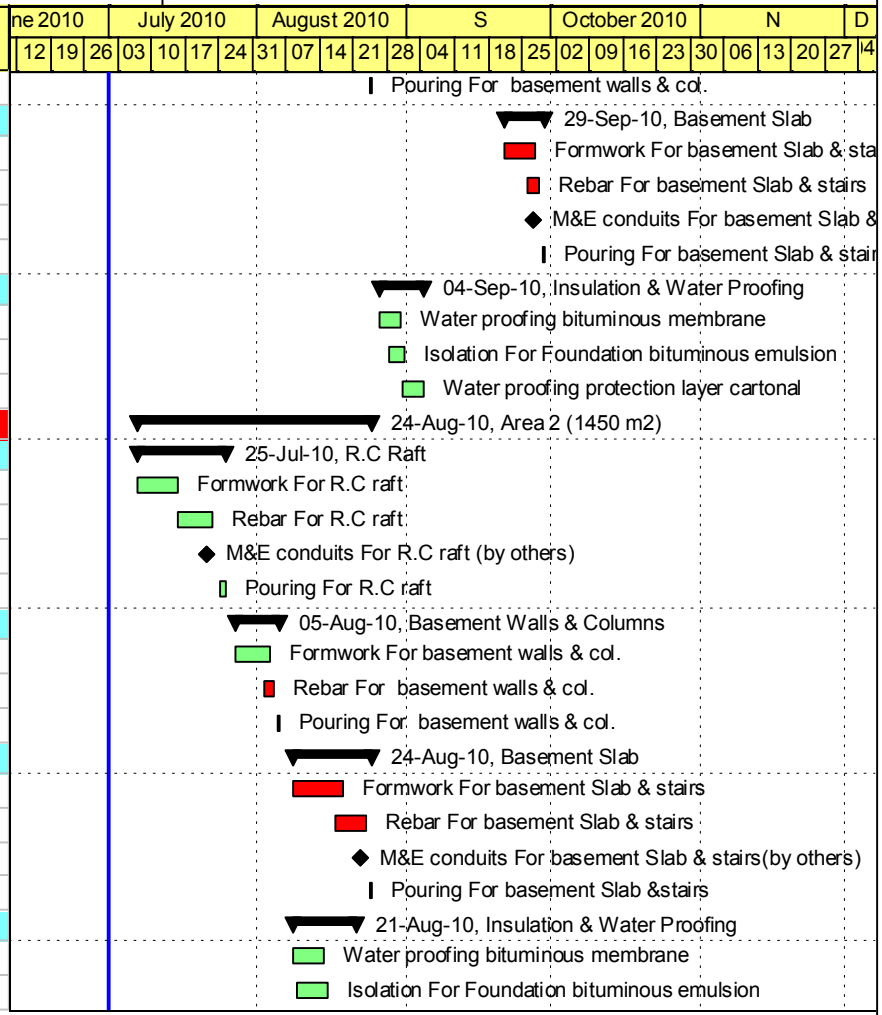

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved

Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
A1065	Water proofing protection layer cartonal	6	15-Aug-10	21-Aug-10
Area 3 (660 m2)		42	07-Jul-10	24-Aug-10
R.C Raft		13	07-Jul-10	21-Jul-10
A1430	Formwork For R.C raft	6	07-Jul-10	13-Jul-10
A1440	Rebar For R.C raft	5	15-Jul-10	20-Jul-10
A1450	M&E conduits For R.C raft (by others)	0		19-Jul-10
A1460	Pouring For R.C raft	1	21-Jul-10	21-Jul-10
Basement Walls & Columns		12	25-Jul-10	07-Aug-10
A1510	Formwork For basement walls & col.	9	25-Jul-10	03-Aug-10
A1520	Rebar For basement walls & col.	4	02-Aug-10	05-Aug-10
A1530	Pouring For basement walls & col.	1	07-Aug-10	07-Aug-10
Basement Slab		12	09-Aug-10	22-Aug-10
A1540	Formwork For basement Slab & stairs	8	09-Aug-10	17-Aug-10
A1550	Rebar For basement Slab & stairs	5	16-Aug-10	21-Aug-10
A1560	M&E conduits For Ground Floor Slab & st...	0		19-Aug-10
A1570	Pouring For basement Slab & stairs	1	22-Aug-10	22-Aug-10
Insulation & Water Proofing		14	09-Aug-10	24-Aug-10
A1490	Water proofing bituminous membrane	6	09-Aug-10	15-Aug-10
A1470	Isolation For Foundation bituminous emulsi...	8	11-Aug-10	19-Aug-10
A1500	Water proofing protection layer cartonal	8	16-Aug-10	24-Aug-10
Earth Work For Tower 1		11	05-Sep-10	16-Sep-10
A2370	Backfilling Around Foundation	11	05-Sep-10	16-Sep-10
Testing & Handingover For Tower 1		2	06-Oct-10	07-Oct-10
A2390	Testing & Handingover	2	06-Oct-10	07-Oct-10
Tower 2		70	18-Jul-10	06-Oct-10
Area 1 (550 m2)		46	18-Jul-10	08-Sep-10
R.C Raft		13	18-Jul-10	01-Aug-10
A1760	Formwork For R.C raft	6	18-Jul-10	24-Jul-10

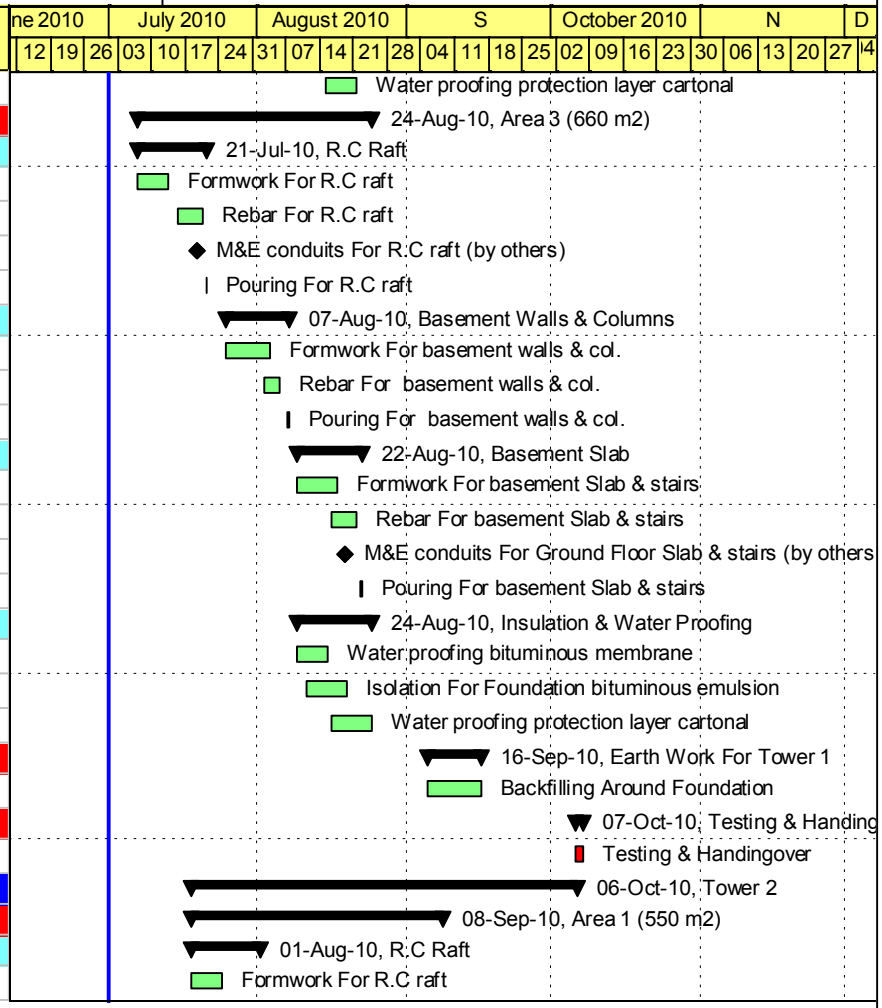

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved

Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
A1770	Rebar For R.C raft	5	26-Jul-10	31-Jul-10
A1780	M&E conduits For R.C raft (by others)	0		29-Jul-10
A1790	Pouring For R.C raft	1	01-Aug-10	01-Aug-10
Basement Walls & Columns		9	11-Aug-10	21-Aug-10
A1800	Formwork For basement walls & col.	8	11-Aug-10	19-Aug-10
A1810	Rebar For basement walls & col.	4	14-Aug-10	17-Aug-10
A1820	Pouring For basement walls & col.	1	21-Aug-10	21-Aug-10
Basement Slab		11	28-Aug-10	08-Sep-10
A1840	Formwork For basement Slab & stairs	8	28-Aug-10	05-Sep-10
A1850	Rebar For basement Slab & stairs	4	04-Sep-10	07-Sep-10
A1860	M&E conduits For Ground Floor Slab & st...	0		06-Sep-10
A1870	Pouring For basement Slab & stairs	1	08-Sep-10	08-Sep-10
Insulation & Water Proofing		8	23-Aug-10	31-Aug-10
A1890	Water proofing bituminous membrane	4	23-Aug-10	26-Aug-10
A1830	Isolation For Foundation bituminous emulsi...	6	25-Aug-10	31-Aug-10
A1900	Water proofing protection layer cartonal	3	28-Aug-10	30-Aug-10
Area 2 (1450 m2)		50	20-Jul-10	15-Sep-10
R.C Raft		14	20-Jul-10	04-Aug-10
A1600	Formwork For R.C raft	8	20-Jul-10	28-Jul-10
A1610	Rebar For R.C raft	7	26-Jul-10	02-Aug-10
A1620	M&E conduits For R.C raft (by others)	0		01-Aug-10
A1630	Pouring For R.C raft	2	03-Aug-10	04-Aug-10
Basement Walls & Columns		11	07-Aug-10	18-Aug-10
A1640	Formwork For basement walls & col.	10	07-Aug-10	17-Aug-10
A1650	Rebar For basement walls & col.	6	09-Aug-10	15-Aug-10
A1660	Pouring For basement walls & col.	1	18-Aug-10	18-Aug-10
Basement Slab		15	30-Aug-10	15-Sep-10
A1690	Formwork For basement Slab & stairs	10	30-Aug-10	09-Sep-10

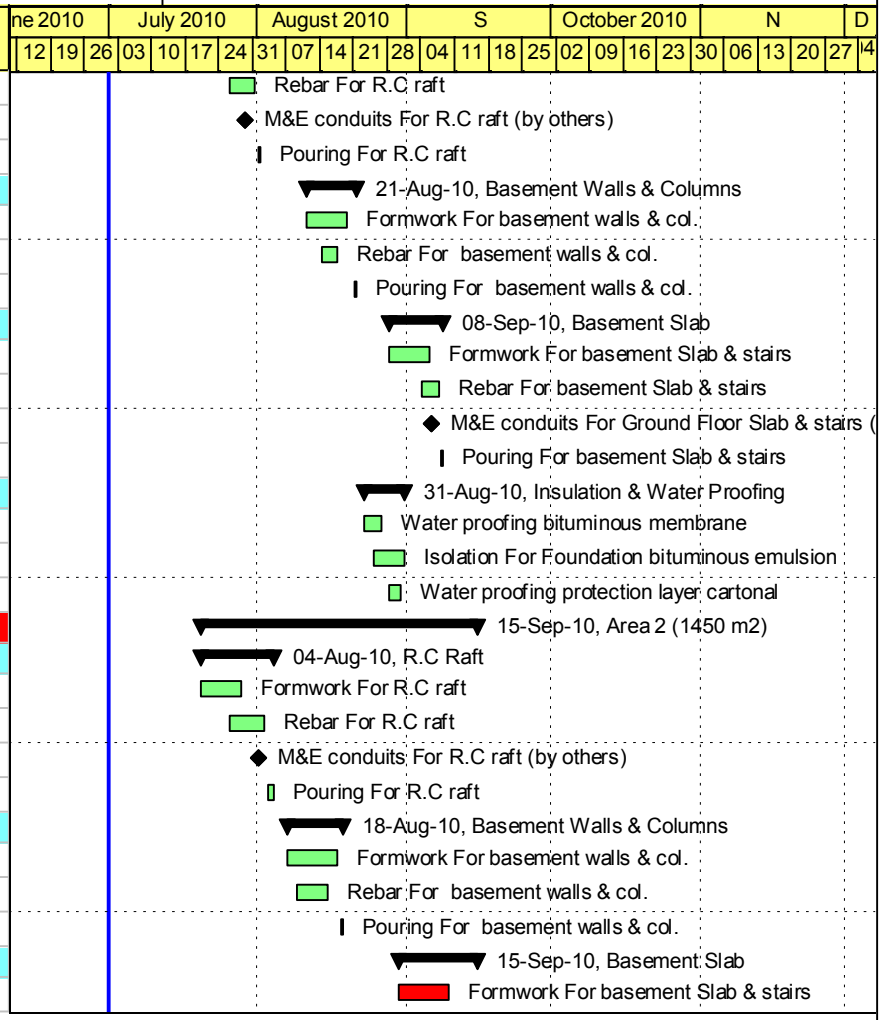

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved

Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
A1700	Rebar For basement Slab & stairs	6	08-Sep-10	14-Sep-10
A1710	M&E conduits For basement Slab & stairs ...	0		13-Sep-10
A1720	Pouring For basement Slab & stairs	1	15-Sep-10	15-Sep-10
Insulation & Water Proofing		14	19-Aug-10	04-Sep-10
A1670	Isolation For Foundation bituminous emulsi...	8	19-Aug-10	28-Aug-10
A1740	Water proofing bituminous membrane	7	21-Aug-10	28-Aug-10
A1750	Water proofing protection layer cartonal	6	29-Aug-10	04-Sep-10
Area 3 (660 m2)		54	31-Jul-10	30-Sep-10
R.C Raft		11	31-Jul-10	11-Aug-10
A1910	Formwork For R.C raft	9	31-Jul-10	09-Aug-10
A1920	Rebar For R.C raft	8	02-Aug-10	10-Aug-10
A1930	M&E conduits For R.C raft (by others)	0		09-Aug-10
A1940	Pouring For R.C raft	1	11-Aug-10	11-Aug-10
Basement Walls & Columns		11	14-Aug-10	25-Aug-10
A1950	Formwork For basement walls & col.	10	14-Aug-10	24-Aug-10
A1960	Rebar For basement walls & col.	6	16-Aug-10	22-Aug-10
A1970	Pouring For basement walls & col.	1	25-Aug-10	25-Aug-10
Basement Slab		15	14-Sep-10	30-Sep-10
A1990	Formwork For basement Slab & stairs	8	14-Sep-10	22-Sep-10
A2000	Rebar For basement Slab & stairs	5	23-Sep-10	28-Sep-10
A2010	M&E conduits For basement Slab & stairs(...	0		27-Sep-10
A2020	Pouring For basement Slab & stairs	1	30-Sep-10	30-Sep-10
Insulation & Water Proofing		12	07-Sep-10	20-Sep-10
A2040	Water proofing bituminous membrane	6	07-Sep-10	13-Sep-10
A1980	Isolation For Foundation bituminous emulsi...	6	09-Sep-10	15-Sep-10
A2050	Water proofing protection layer cartonal	6	14-Sep-10	20-Sep-10
Earth Work For Tower 2		12	21-Sep-10	04-Oct-10
A2380	Backfilling Around Foundation	12	21-Sep-10	04-Oct-10

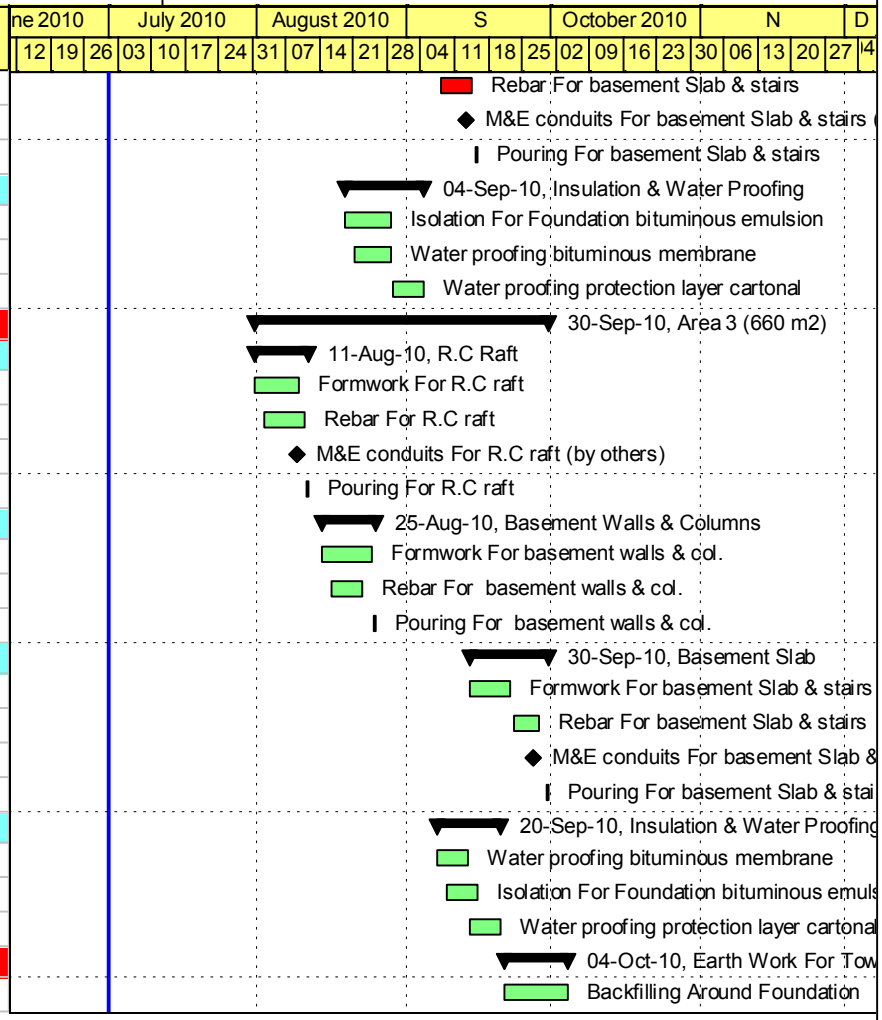

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved

Office Building 14B01 Substructure Package

Cntractor : Mivan .Ltd

Activity ID	Activity Name	Original Duration	Start	Finish
Testing & Handingover For Tower 2		2	05-Oct-10	06-Oct-10
A2400	Testing & Handingover	2	05-Oct-10	06-Oct-10
Tank		63	20-Jul-10	30-Sep-10
A2060	Formworks for R.C raft	2	20-Jul-10	21-Jul-10
A2070	Rebar for R.C raft	3	22-Jul-10	25-Jul-10
A2079	M&E conduits For R.C raft (by others)	0		24-Jul-10
A2080	Pouring For R.C raft	1	26-Jul-10	26-Jul-10
A2090	Formwork For Tank walls	8	27-Jul-10	04-Aug-10
A2100	Rebar For Tank walls	6	05-Aug-10	11-Aug-10
A2109	M&E conduits For R.C walls (by others)	0		10-Aug-10
A2110	Pouring For Tank walls	1	12-Aug-10	12-Aug-10
A2120	Formwork For Tank Slab	10	14-Aug-10	24-Aug-10
A2130	Rebar For Tank Slab	6	25-Aug-10	31-Aug-10
A2119	M&E conduits For tank's slab (by others)	0		30-Aug-10
A2140	Pouring For Tank slab	1	01-Sep-10	01-Sep-10
A2150	Internal insulation	15	02-Sep-10	19-Sep-10
A2160	External insulation	10	20-Sep-10	30-Sep-10

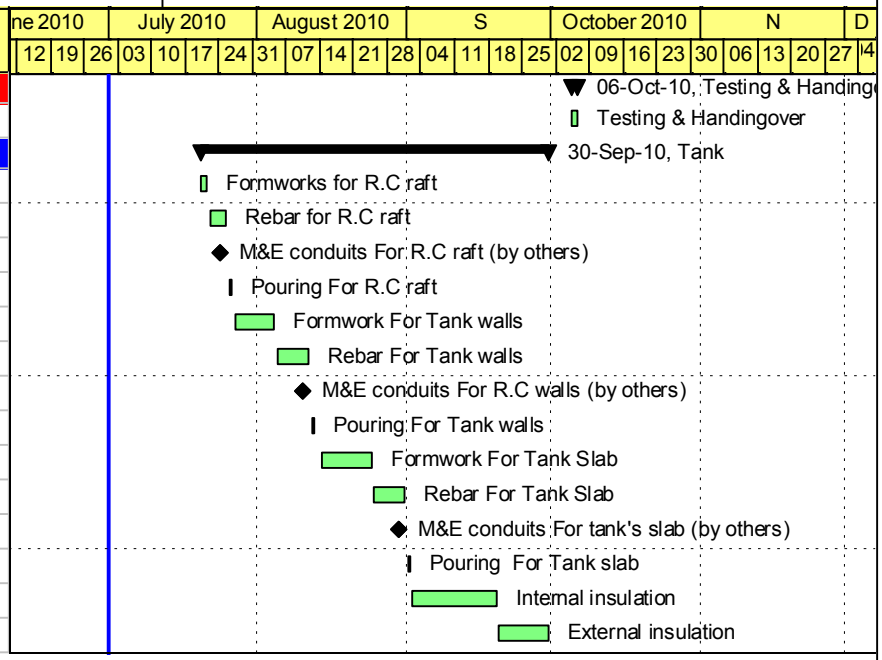

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
