Cairo Festival City

Office Building 14B01 Substructure Package

Date	Revision	Checked	Approved
18-Sep-10	Revsion 1		

Activity ID	Activity Name	Original Duration	Start	Finish
Office Building 14B01 Substructure Package		108	12-Jul-10	15-Nov-10
General		108	12-Jul-10	15-Nov-10
A1000	Start project	0	12-Jul-10	
A1020	Mobilization	8	12-Jul-10	20-Jul-10
A1320	Receive issue for construction drawings	0	12-Jul-10	
A1010	Finish project	0		15-Nov-10
Engineering		41	12-Jul-10	29-Aug-10
Tank		3	19-Jul-10	22-Jul-10
A1260	submittals of all tank's shop drawings	0		19-Jul-10
A2170	Approval of all tank's shop drawings	0		22-Jul-10
Tower 1		32	12-Jul-10	18-Aug-10
Submittals		29	12-Jul-10	15-Aug-10
A1140	Submittal of All R.C raft dimension	0		12-Jul-10
A1150	Submittal of All column layout	0		12-Jul-10
A1160	Submittal of All R.C raft RFT&starters	0		21-Jul-10
A1170	Submittal of All basement columns & wall...	0		01-Aug-10
A1180	Submittal of All basement slab concrete d...	0		08-Aug-10
A1190	Submittal of All basement slab RFT	0		15-Aug-10
Approvals		29	15-Jul-10	18-Aug-10
A1141	Approval of All R.C raft dimension	0		15-Jul-10
A1151	Approval of All column layout	0		15-Jul-10
A1161	Approval of All R.C raft RFT&starters	0		25-Jul-10
A1171	Approval of All basement columns & wall...	0		04-Aug-10
A1181	Approval of All basement slab concrete di...	0		11-Aug-10
A1191	Approval of All basement slab RFT	0		18-Aug-10
Tower 2		33	21-Jul-10	29-Aug-10

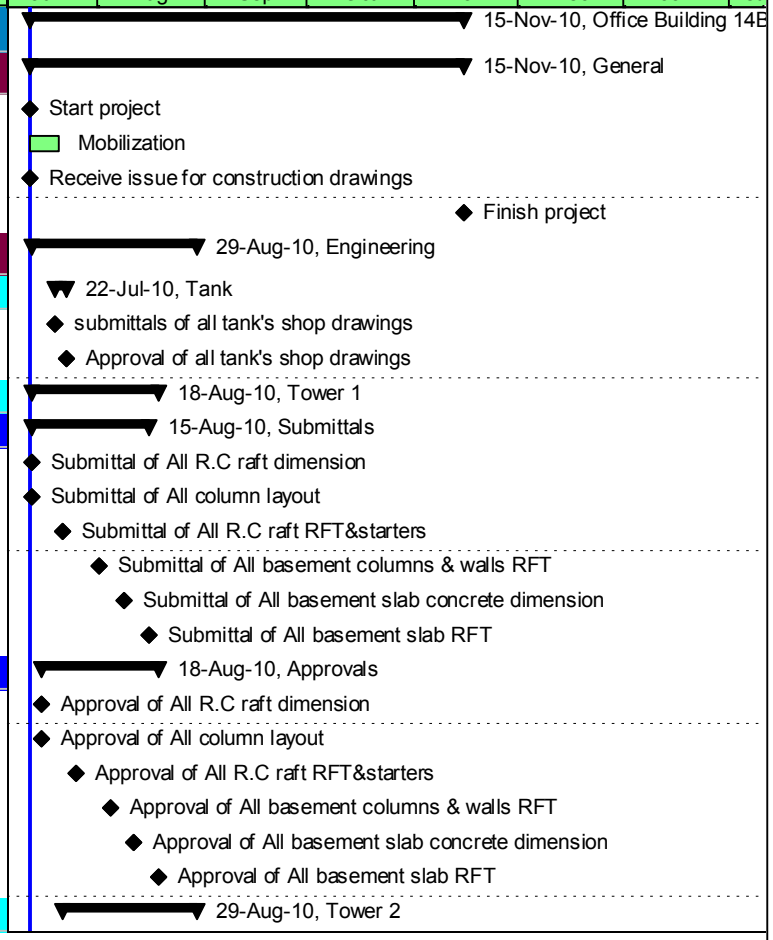

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Cairo Festival City

Office Building 14B01 Substructure Package

Date	Revision	Checked	Approved
18-Sep-10	Revsion 1		

Activity ID	Activity Name	Original Duration	Start	Finish
Submittals		30	21-Jul-10	25-Aug-10
A1200	Submittal of All R.C raft dimension	0		21-Jul-10
A1210	Submittal of All column layout	0		21-Jul-10
A1220	Submittal of All R.C raft RFT&starters	0		01-Aug-10
A1230	Submittal of All basement columns & wall...	0		08-Aug-10
A1240	Submittal of All basement slab concrete d...	0		15-Aug-10
A1250	Submittal of All basement slab RFT	0		25-Aug-10
Approvals		30	25-Jul-10	29-Aug-10
A1201	Approval of All R.C raft dimension	0		25-Jul-10
A1211	Approval of All column layout	0		25-Jul-10
A1221	Approval of All R.C raft RFT&starters	0		04-Aug-10
A1231	Approval of All basement columns & wall...	0		10-Aug-10
A1241	Approval of All basement slab concrete di...	0		18-Aug-10
A1251	Approval of All basement slab RFT	0		29-Aug-10
construction		103	18-Jul-10	15-Nov-10
Office building		103	18-Jul-10	15-Nov-10
Tower 1		85	18-Jul-10	25-Oct-10
R.C Raft		62	18-Jul-10	28-Sep-10
A2410	Formwork For R.C raft	58	18-Jul-10	23-Sep-10
A2420	Rebar For R.C raft	60	19-Jul-10	27-Sep-10
A2780	Pouring For R.C raft (area 1)	1	05-Sep-...	05-Sep-10
A2790	Pouring For R.C raft (area 2)	1	08-Sep-...	08-Sep-10
A2700	M&E conduits For R.C raft (by others)	7	18-Sep-10	25-Sep-10
A2440	Pouring For R.C raft (area 3)	1	25-Sep-10	25-Sep-10
A2860	Pouring For R.C raft (area 4)	1	28-Sep-10	28-Sep-10
Basement Walls & Columns		26	08-Sep-10	09-Oct-10

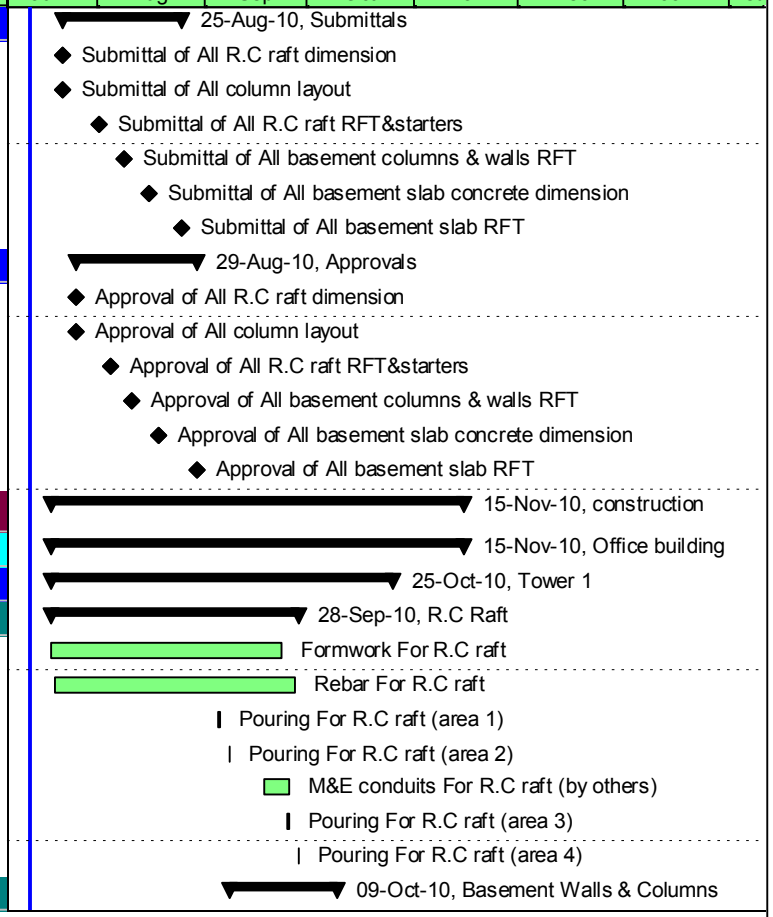

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Cairo Festival City

Office Building 14B01 Substructure Package

Date	Revision	Checked	Approved
18-Sep-10	Revsion 1		

Activity ID	Activity Name	Original Duration	Start	Finish
A2460	Rebar For basement walls & col.	23	08-Sep-10	05-Oct-10
A2450	Formwork For basement walls & col.	20	15-Sep-10	07-Oct-10
A2470	Pouring For basement walls & col.(area 1)	1	22-Sep-10	22-Sep-10
A2870	Pouring For basement walls & col.(area 2)	1	28-Sep-10	28-Sep-10
A2880	Pouring For basement walls & col.(area 3)	1	03-Oct-10	03-Oct-10
A2890	Pouring For basement walls & col.(area 4)	1	09-Oct-10	09-Oct-10
Basement Slab		**21**	**25-Sep-10**	**18-Oct-10**
A2480	Formwork&Rebar For basement Slab & s...	7	25-Sep-10	02-Oct-10
A2900	Formwork&Rebar For basement Slab & s...	7	30-Sep-10	07-Oct-10
A2800	Pouring For basement Slab & stairs (Area...	1	03-Oct-10	03-Oct-10
A2910	Formwork&Rebar For basement Slab & s...	7	05-Oct-10	12-Oct-10
A2810	Pouring For basement Slab & stairs (Area...	1	09-Oct-10	09-Oct-10
A2920	Formwork&Rebar For basement Slab & s...	7	10-Oct-10	17-Oct-10
A2510	Pouring For basement Slab & stairs (Are...	1	13-Oct-10	13-Oct-10
A2930	Pouring For basement Slab & stairs (Are...	1	18-Oct-10	18-Oct-10
Insulation & Water Proofing		**20**	**23-Sep-10**	**16-Oct-10**
A2530	Isolation For Foundation bituminous emul...	9	23-Sep-10	03-Oct-10
A2520	Water proofing bituminous membrane	15	27-Sep-10	13-Oct-10
A2540	Water proofing protection layer cartonal	15	29-Sep-10	16-Oct-10
Earth Work For Tower 1		**19**	**02-Oct-10**	**23-Oct-10**
A2370	Backfilling Around Foundation	19	02-Oct-10	23-Oct-10
Handingover For Tower 1		**2**	**24-Oct-10**	**25-Oct-10**
A2390	Handingover	2	24-Oct-10	25-Oct-10
Tower 2		**86**	**05-Aug-...**	**14-Nov-10**
R.C Raft		**58**	**05-Aug-...**	**12-Oct-10**
A2550	Formwork For R.C raft	56	05-Aug-...	10-Oct-10
A2560	Rebar For R.C raft	48	15-Aug-...	10-Oct-10

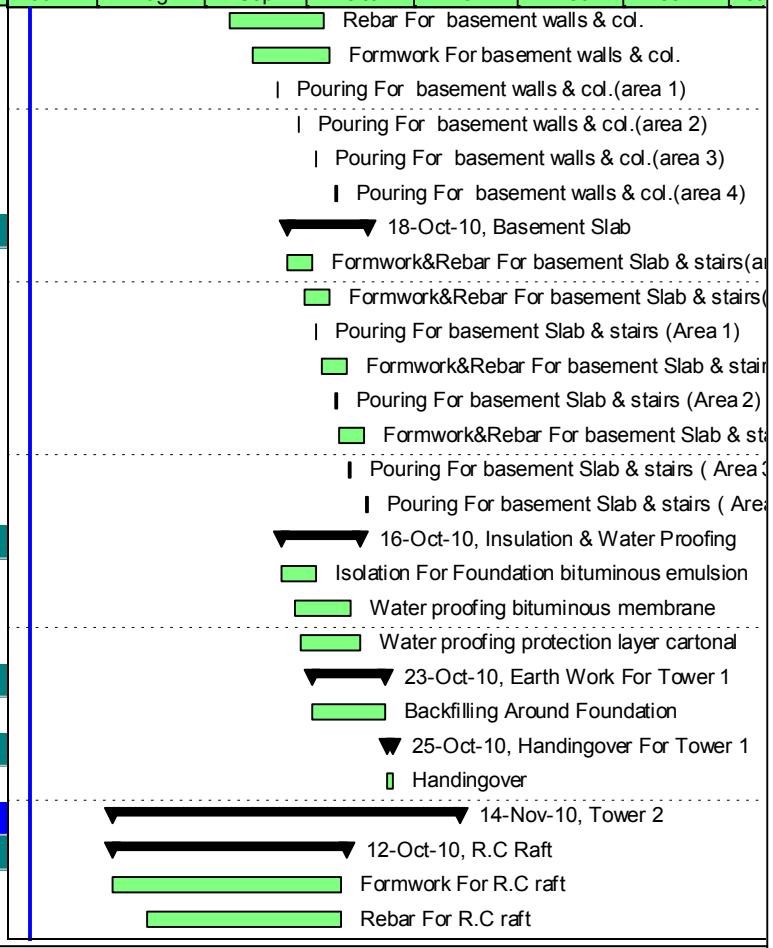

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Cairo Festival City

Office Building 14B01 Substructure Package

Date	Revision	Checked	Approved
18-Sep-10	Revsion 1		

Activity ID	Activity Name	Original Duration	Start	Finish
A2570	M&E conduits For R.C raft (by others)	7	26-Sep-10	03-Oct-10
A2580	Pouring For R.C raft (Area 1)	1	05-Oct-10	05-Oct-10
A2820	Pouring For R.C raft (Area 2)	1	07-Oct-10	07-Oct-10
A2830	Pouring For R.C raft (Area 3)	1	10-Oct-10	10-Oct-10
A2940	Pouring For R.C raft (Area 4)	1	12-Oct-10	12-Oct-10
Basement Walls & Columns		**43**	**08-Sep-10**	**28-Oct-10**
A2600	Rebar For basement walls & col.	34	08-Sep-10	19-Oct-10
A2590	Formwork For basement walls & col.	32	15-Sep-10	21-Oct-10
A2610	Pouring For basement walls & col.(Area 1)	1	13-Oct-10	13-Oct-10
A2950	Pouring For basement walls & col.(Area 2)	1	18-Oct-10	18-Oct-10
A2960	Pouring For basement walls & col.(Area 3)	1	23-Oct-10	23-Oct-10
A2970	Pouring For basement walls & col.(Area 4)	1	28-Oct-10	28-Oct-10
Basement Slab		**23**	**16-Oct-10**	**10-Nov-10**
A2620	Formwork&Rebar For basement Slab & s...	7	16-Oct-10	23-Oct-10
A2990	Formwork&Rebar For basement Slab & s...	7	20-Oct-10	27-Oct-10
A2650	Pouring For basement Slab & stairs (Area...	1	24-Oct-10	24-Oct-10
A3000	Formwork&Rebar For basement Slab & s...	7	25-Oct-10	01-Nov-10
A2840	Pouring For basement Slab & stairs (Area...	1	28-Oct-10	28-Oct-10
A2850	Pouring For basement Slab & stairs (Area...	1	02-Nov-10	02-Nov-10
A3010	Formwork&Rebar For basement Slab & s...	7	02-Nov-10	09-Nov-10
A2980	Pouring For basement Slab & stairs (Area...	1	10-Nov-10	10-Nov-10
Insulation & Water Proofing		**23**	**10-Oct-10**	**04-Nov-10**
A2660	Isolation For Foundation bituminous emul...	6	10-Oct-10	16-Oct-10
A2670	Water proofing bituminous membrane	14	18-Oct-10	02-Nov-10
A2680	Water proofing protection layer cartonal	14	20-Oct-10	04-Nov-10
Earth Work For Tower 2		**18**	**23-Oct-10**	**11-Nov-10**
A2380	Backfilling Around Foundation	18	23-Oct-10	11-Nov-10

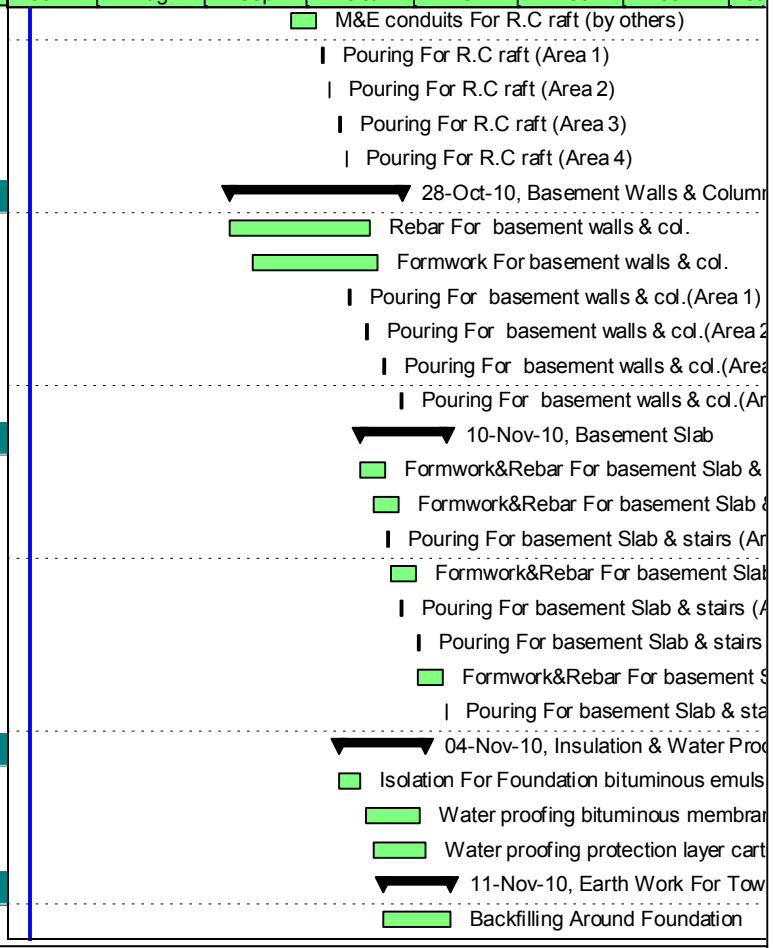

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Cairo Festival City

Office Building 14B01 Substructure Package

Date	Revision	Checked	Approved
18-Sep-10	Revsion 1		

Activity ID	Activity Name	Original Duration	Start	Finish
Handingover For Tower 2		2	13-Nov-10	14-Nov-10
A2400	Handingover	2	13-Nov-10	14-Nov-10
Tank		61	05-Sep-10	15-Nov-10
A2060	Formworks for R.C raft	2	05-Sep-10	06-Sep-10
A2070	Rebar for R.C raft	3	05-Sep-10	07-Sep-10
A2079	M&E conduits For R.C raft (by others)	0		16-Sep-10
A2080	Pouring For R.C raft	1	18-Sep-10	18-Sep-10
A2090	Formwork For Tank walls	8	20-Sep-10	28-Sep-10
A2100	Rebar For Tank walls	6	22-Sep-10	28-Sep-10
A2109	M&E conduits For R.C walls (by others)	0		27-Sep-10
A2110	Pouring For Tank walls	1	30-Sep-10	30-Sep-10
A2120	Formwork For Tank Slab	12	02-Oct-10	14-Oct-10
A2130	Rebar For Tank Slab	6	14-Oct-10	20-Oct-10
A2119	M&E conduits For tank's slab (by others)	0		20-Oct-10
A2140	Pouring For Tank slab	1	23-Oct-10	23-Oct-10
A2150	Internal insulation	5	31-Oct-10	04-Nov-10
A2160	External insulation	5	06-Nov-10	10-Nov-10
A2180	Testing & Handingover	4	11-Nov-10	15-Nov-10

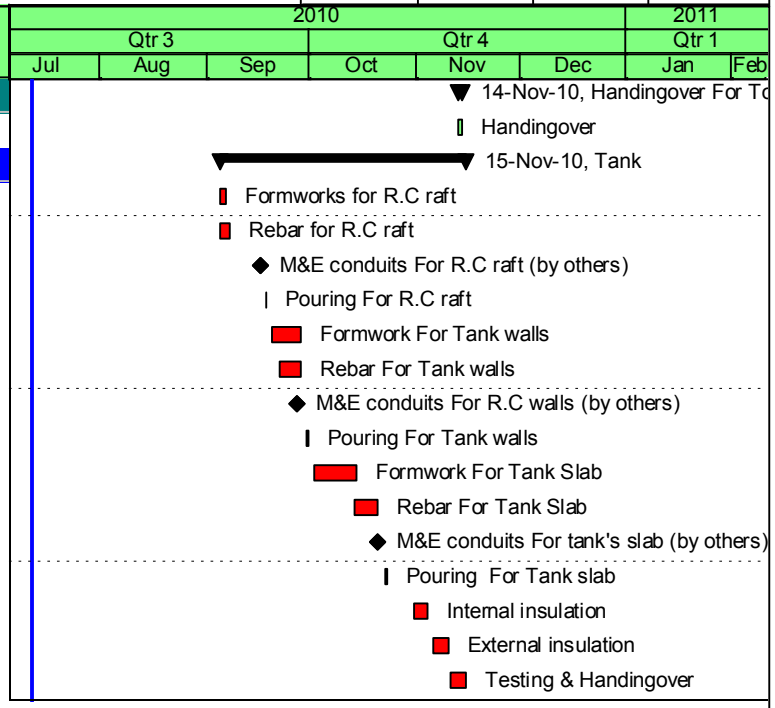

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities
