Date	Revision	Checked	Approved
28-Aug-10	Revision 1		

Cairo Festival City

Office Building 14B01 substructure Package

Activity ID	Activity Name	Original Duration	Start	Finish
Office Building 14B01 Substructure Package		84	01-Jul-10	07-Oct-10
General		84	01-Jul-10	07-Oct-10
A1000	Start project	0	01-Jul-10	
A1020	Mobilization	8	01-Jul-10	10-Jul-10
A1320	Receive issue for construction drawings	0	01-Jul-10	
A1010	Finish project	0		07-Oct-10
Engineering		41	01-Jul-10	18-Aug-10
Tank		3	08-Jul-10	12-Jul-10
A1260	submittals of all tank's shop drawings	0		08-Jul-10
A2170	Approval of all tank's shop drawings	0		12-Jul-10
Tower 1		32	01-Jul-10	08-Aug-10
Submittals		29	01-Jul-10	04-Aug-10
A1140	Submittal of All R.C raft dimension	0		01-Jul-10
A1150	Submittal of All column layout	0		01-Jul-10
A1160	Submittal of All R.C raft RFT&starters	0		11-Jul-10
A1170	Submittal of All basement columns & walls RFT	0		21-Jul-10
A1180	Submittal of All basement slab concrete dimension	0		28-Jul-10
A1190	Submittal of All basement slab RFT	0		04-Aug-10
Approvals		29	05-Jul-10	08-Aug-10
A1141	Approval of All R.C raft dimension	0		05-Jul-10
A1151	Approval of All column layout	0		05-Jul-10
A1161	Approval of All R.C raft RFT&starters	0		14-Jul-10
A1171	Approval of All basement columns & walls RFT	0		25-Jul-10
A1181	Approval of All basement slab concrete dimension	0		01-Aug-10

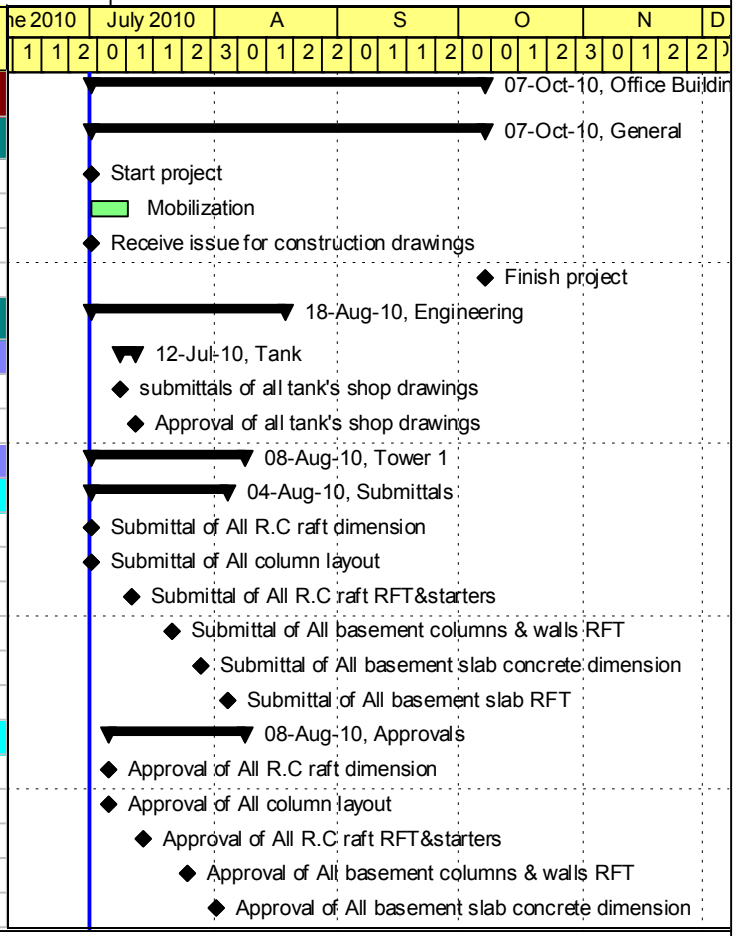

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
28-Aug-10	Revision 1		

Cairo Festival City

Office Building 14B01 substructure Package

Activity ID	Activity Name	Original Duration	Start	Finish
A1191	Approval of All basement slab RFT	0		08-Aug-10
Tower 2		33	11-Jul-10	18-Aug-10
Submittals		30	11-Jul-10	15-Aug-10
A1200	Submittal of All R.C raft dimension	0		11-Jul-10
A1210	Submittal of All column layout	0		11-Jul-10
A1220	Submittal of All R.C raft RFT&starters	0		21-Jul-10
A1230	Submittal of All basement columns & walls RFT	0		28-Jul-10
A1240	Submittal of All basement slab concrete dimension	0		04-Aug-10
A1250	Submittal of All basement slab RFT	0		15-Aug-10
Approvals		30	14-Jul-10	18-Aug-10
A1201	Approval of All R.C raft dimension	0		14-Jul-10
A1211	Approval of All column layout	0		14-Jul-10
A1221	Approval of All R.C raft RFT&starters	0		25-Jul-10
A1231	Approval of All basement columns & walls RFT	0		31-Jul-10
A1241	Approval of All basement slab concrete dimension	0		08-Aug-10
A1251	Approval of All basement slab RFT	0		18-Aug-10
construction		80	06-Jul-10	07-Oct-10
Office building		80	06-Jul-10	07-Oct-10
Tower 1		80	06-Jul-10	07-Oct-10
R.C Raft		27	06-Jul-10	05-Aug-10
A2410	Formwork For R.C raft	26	06-Jul-10	04-Aug-10
A2420	Rebar For R.C raft	24	08-Jul-10	04-Aug-10
A2700	M&E conduits For R.C raft (by others) area 1	0		19-Jul-10
A2780	Pouring For R.C raft (area 1)	1	20-Jul-10	20-Jul-10

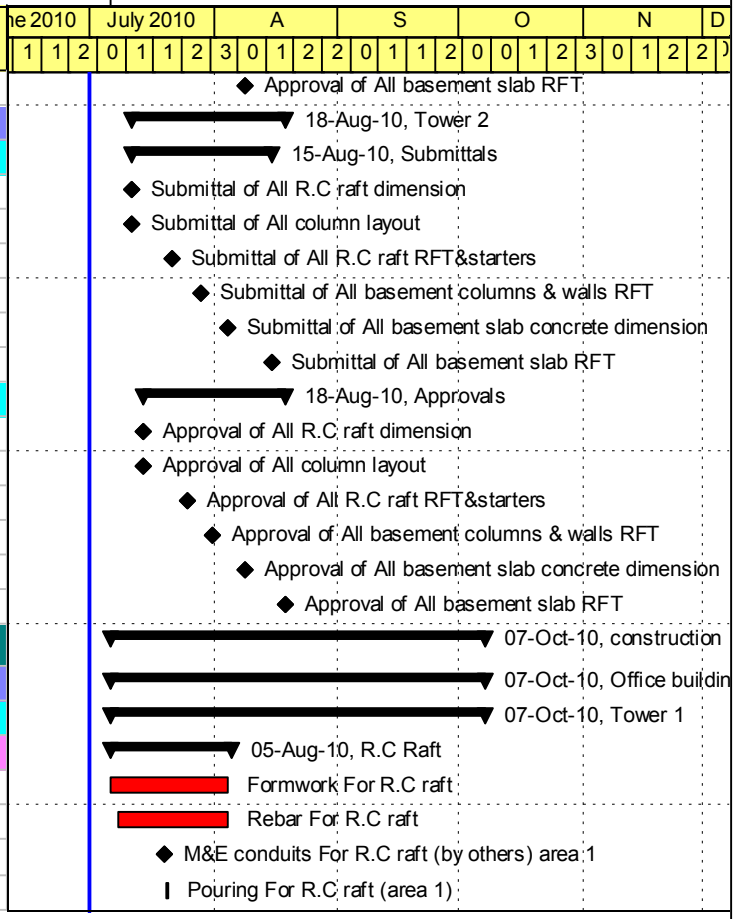

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
28-Aug-10	Revision 1		

Cairo Festival City

Office Building 14B01 substructure Package

Activity ID	Activity Name	Original Duration	Start	Finish
A2690	M&E conduits For R.C raft (by others) area 2	0		22-Jul-10
A2790	Pouring For R.C raft (area 2)	1	24-Jul-10	24-Jul-10
A2710	M&E conduits For R.C raft (by others) area 3	0		04-Aug-10
A2440	Pouring For R.C raft (area 3)	1	05-Aug-10	05-Aug-10
Basement Walls & Columns		24	25-Jul-10	21-Aug-10
A2450	Formwork For basement walls & col.	23	25-Jul-10	19-Aug-10
A2460	Rebar For basement walls & col.	20	27-Jul-10	18-Aug-10
A2470	Pouring For basement walls & col.	18	01-Aug-10	21-Aug-10
Basement Slab		47	07-Aug-10	30-Sep-10
A2480	Formwork For basement Slab & stairs	44	07-Aug-10	27-Sep-10
A2490	Rebar For basement Slab & stairs	40	14-Aug-10	29-Sep-10
A2770	M&E conduits For basement Slab & stairs (by others) Area 3	0		17-Aug-10
A2800	Pouring For basement Slab & stairs (Area 3)	1	19-Aug-10	19-Aug-10
A2760	M&E conduits For basement Slab & stairs (by others) Area 2	0		21-Aug-10
A2810	Pouring For basement Slab & stairs (Area 2)	1	24-Aug-10	24-Aug-10
A2500	M&E conduits For basement Slab & stairs (by others) Area 1	0		27-Sep-10
A2510	Pouring For basement Slab & stairs (Area 1)	1	30-Sep-10	30-Sep-10
Insulation & Water Proofing		24	04-Aug-10	31-Aug-10
A2530	Isolation For Foundation bituminous emulsion	20	04-Aug-10	26-Aug-10
A2520	Water proofing bituminous membrane	20	05-Aug-10	28-Aug-10
A2540	Water proofing protection layer cartonal	16	14-Aug-10	31-Aug-10
Earth Work For Tower 1		11	01-Sep-10	14-Sep-10
A2370	Backfilling Around Foundation	11	01-Sep-10	14-Sep-10
Handingover For Tower 1		2	06-Oct-10	07-Oct-10

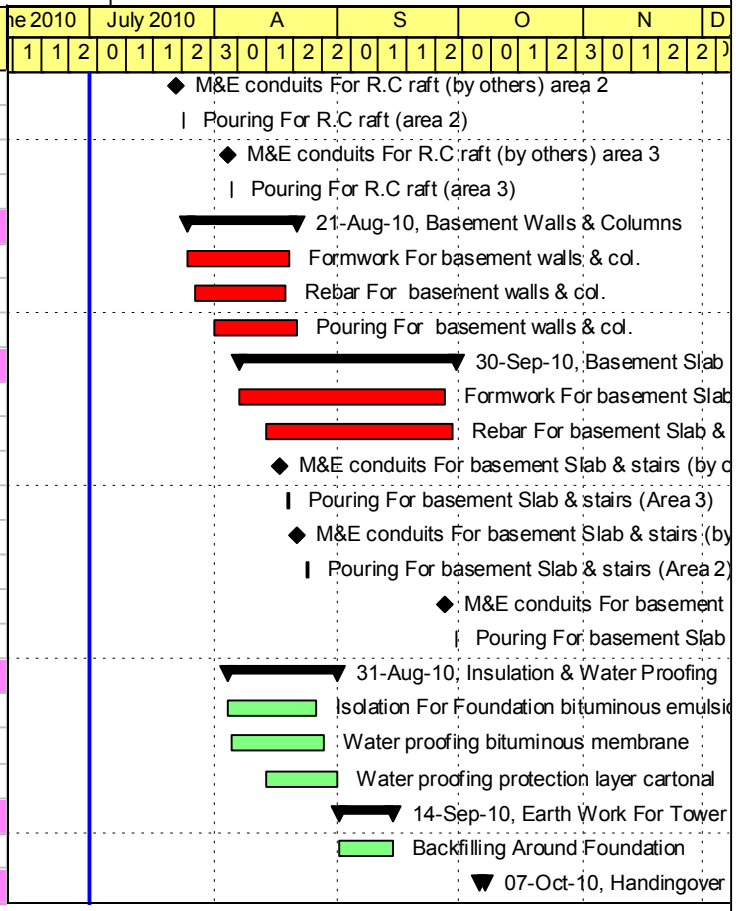

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
28-Aug-10	Revision 1		

Cairo Festival City

Office Building 14B01 substructure Package

Activity ID	Activity Name	Original Duration	Start	Finish
A2390	Handingover	2	06-Oct-10	07-Oct-10
Tower 2		71	17-Jul-10	07-Oct-10
R.C Raft		23	17-Jul-10	11-Aug-10
A2550	Formwork For R.C raft	20	17-Jul-10	08-Aug-10
A2560	Rebar For R.C raft	20	19-Jul-10	10-Aug-10
A2570	M&E conduits For R.C raft (by others) Area 1	0		24-Jul-10
A2580	Pouring For R.C raft (Area 1)	1	27-Jul-10	27-Jul-10
A2720	M&E conduits For R.C raft (by others) Area 2	0		01-Aug-10
A2820	Pouring For R.C raft (Area 2)	1	04-Aug-10	04-Aug-10
A2730	M&E conduits For R.C raft (by others) Area 3	0		09-Aug-10
A2830	Pouring For R.C raft (Area 3)	1	11-Aug-10	11-Aug-10
Basement Walls & Columns		16	31-Jul-10	17-Aug-10
A2590	Formwork For basement walls & col.	15	31-Jul-10	16-Aug-10
A2600	Rebar For basement walls & col.	12	02-Aug-10	15-Aug-10
A2610	Pouring For basement walls & col.	6	11-Aug-10	17-Aug-10
Basement Slab		29	19-Aug-10	22-Sep-10
A2620	Formwork For basement Slab & stairs	23	19-Aug-10	15-Sep-10
A2630	Rebar For basement Slab & stairs	22	26-Aug-10	21-Sep-10
A2640	M&E conduits For basement Slab & stairs (by others) Area 1	0		28-Aug-10
A2650	Pouring For basement Slab & stairs (Area 1)	1	30-Aug-10	30-Aug-10
A2740	M&E conduits For basement Slab & stairs (by others) Area 2	0		08-Sep-10
A2840	Pouring For basement Slab & stairs (Area 2)	1	12-Sep-10	12-Sep-10
A2750	M&E conduits For basement Slab & stairs (by others) Area 3	0		20-Sep-10
A2850	Pouring For basement Slab & stairs (Area3)	1	22-Sep-10	22-Sep-10

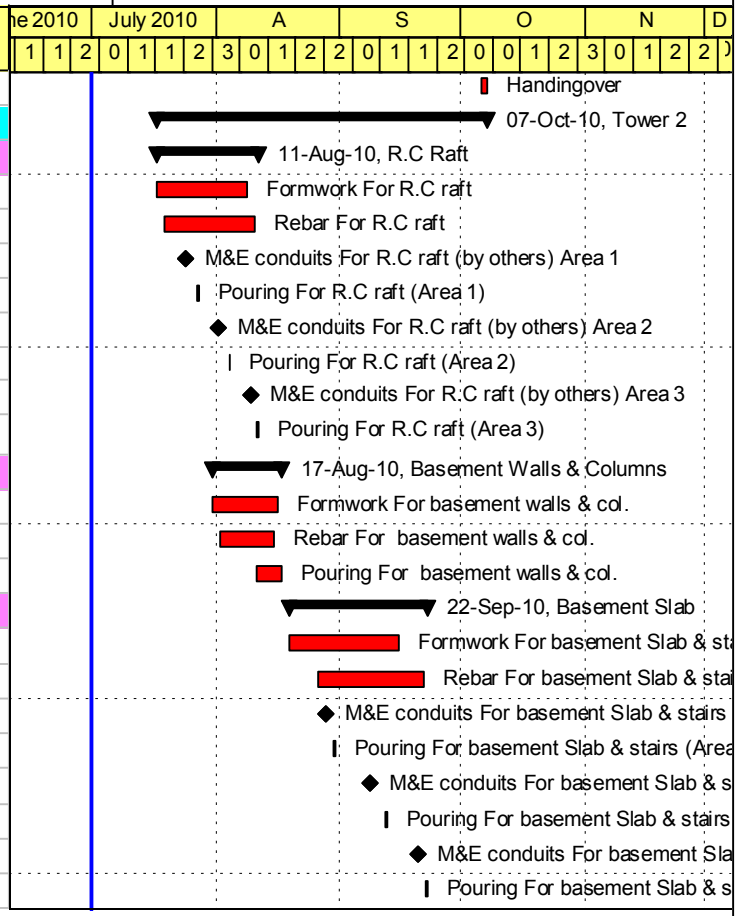

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
28-Aug-10	Revision 1		

Cairo Festival City

Office Building 14B01 substructure Package

Activity ID	Activity Name	Original Duration	Start	Finish
Insulation & Water Proofing		11	12-Aug-10	24-Aug-10
A2660	Isolation For Foundation bituminous emulsion	6	12-Aug-10	18-Aug-10
A2670	Water proofing bituminous membrane	6	14-Aug-10	19-Aug-10
A2680	Water proofing protection layer cartonal	6	18-Aug-10	24-Aug-10
Earth Work For Tower 2		12	25-Aug-10	07-Sep-10
A2380	Backfilling Around Foundation	12	25-Aug-10	07-Sep-10
Handingover For Tower 2		6	02-Oct-10	07-Oct-10
A2400	Handingover	6	02-Oct-10	07-Oct-10
Tank		67	21-Jul-10	07-Oct-10
A2060	Formworks for R.C raft	2	21-Jul-10	22-Jul-10
A2070	Rebar for R.C raft	3	24-Jul-10	26-Jul-10
A2079	M&E conduits For R.C raft (by others)	0		25-Jul-10
A2080	Pouring For R.C raft	1	27-Jul-10	27-Jul-10
A2090	Formwork For Tank walls	8	28-Jul-10	05-Aug-10
A2100	Rebar For Tank walls	6	07-Aug-10	12-Aug-10
A2109	M&E conduits For R.C walls (by others)	0		11-Aug-10
A2110	Pouring For Tank walls	1	14-Aug-10	14-Aug-10
A2120	Formwork For Tank Slab	10	15-Aug-10	25-Aug-10
A2130	Rebar For Tank Slab	6	26-Aug-10	01-Sep-10
A2119	M&E conduits For tank's slab (by others)	0		31-Aug-10
A2140	Pouring For Tank slab	1	02-Sep-10	02-Sep-10
A2150	Internal insulation	15	04-Sep-10	21-Sep-10
A2160	External insulation	10	22-Sep-10	03-Oct-10
A2180	Testing & Handingover	4	04-Oct-10	07-Oct-10

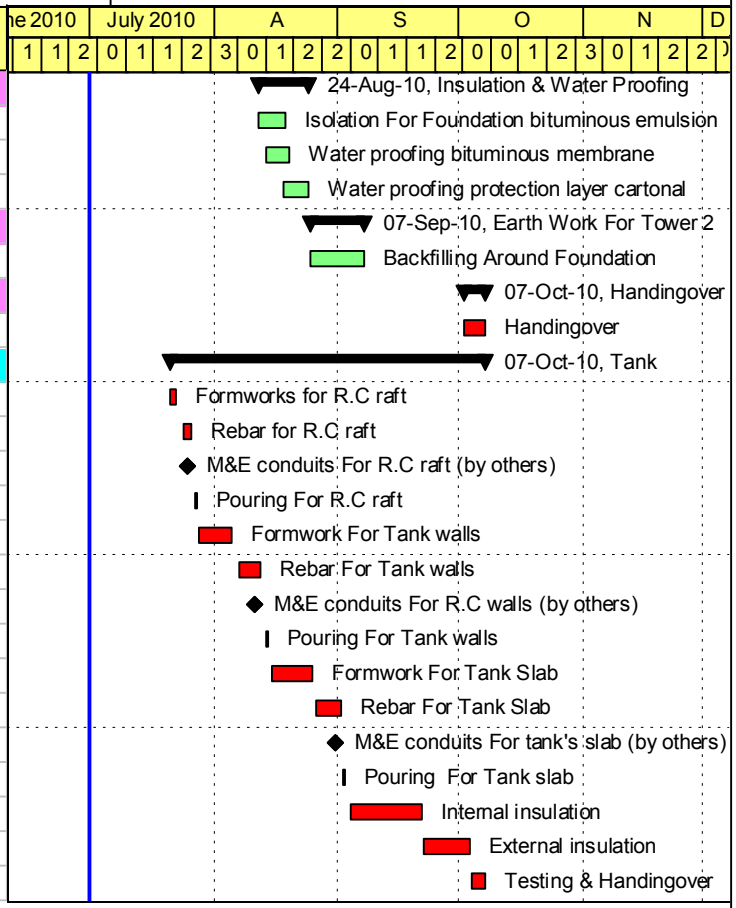

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities
