# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Danone Dairy Farm** | | | | |
| **General** | | | | |
| **Dates** | | | | |
| **General** | | | | |
| DGN-D001 | Start Date Of The Project | 0 | 01AUG10* | |
| DGN-D002 | End Date Of The Project | 0 | | 27FEB11* |
| **Engineering** | | | | |
| **Checking Building & Kantien** | | | | |
| **Building** | | | | |
| **Electrical** | | | | |
| DESD-CH013 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-CH023 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESD-CH001 | Work Shop Drawings Submittal | 10 | 05AUG10 | 16AUG10 |
| DESD-CH002 | Approval the work shop drawing | 7 | 17AUG10 | 24AUG10 |
| DESD-CH006 | Reinforcement Details Submittal | 8 | 14SEP10 | 22SEP10 |
| DESD-CH003 | Reinforcment WSD & BBL Approval | 7 | 23SEP10 | 30SEP10 |
| **Cow Sheds** | | | | |
| **Cow Shed** | | | | |
| **Electrical** | | | | |
| DESD-CW150 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-CW160 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESD-CW101 | Work Shop Drawings Submittal | 7 | 01AUG10 | 08AUG10 |
| DESD-CW102 | Approval the work shop drawing | 7 | 09AUG10 | 16AUG10 |
| DESD-CW106 | Reinforcement Details Submittal | 7 | 23AUG10 | 30AUG10 |
| DESD-CW103 | Reinforcment WSD & BBL Approval | 7 | 31AUG10 | 07SEP10 |
| **Steel Works** | | | | |
| DESD-CW104 | Work Shop Drawings | 0 | 01SEP10* | |
| DESD-CW105 | Approval the work shop drawing | 7 | 02SEP10 | 09SEP10 |

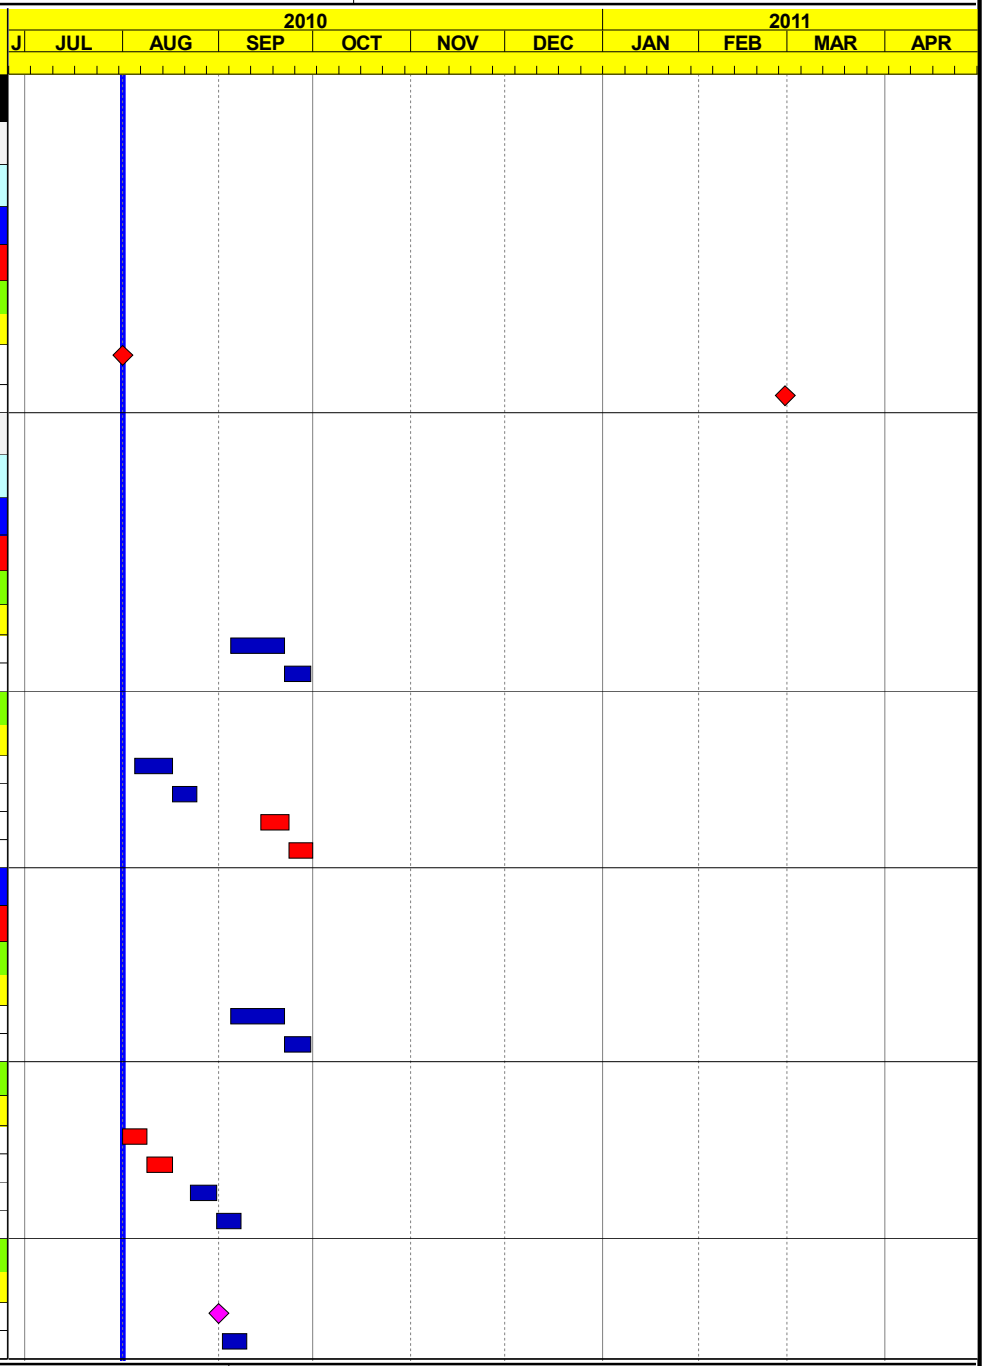


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 1 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Feeding Sheds** | | | | |
| **Feeding Shed** | | | | |
| **Electrical** | | | | |
| DESD-FD110 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-FD111 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESD-FD101 | Work Shop Drawings Submittal | 8 | 01AUG10 | 09AUG10 |
| DESD-FD102 | Approval the work shop drawing | 7 | 10AUG10 | 17AUG10 |
| DESD-FD106 | Reinforcement Details Submittal | 8 | 25AUG10 | 02SEP10 |
| DESD-FD103 | Reinforcment WSD & BBL Approval | 7 | 04SEP10 | 11SEP10 |
| **Food Bunk** | | | | |
| **Building** | | | | |
| **Electrical** | | | | |
| DESD-FB10 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-FB11 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESD-FB001 | Work Shop Drawings Submittal | 7 | 01AUG10 | 08AUG10 |
| DESD-FB002 | Approval the work shop drawing | 7 | 09AUG10 | 16AUG10 |
| DESD-FB006 | Reinforcement Details Submittal | 7 | 21AUG10 | 28AUG10 |
| DESD-FB003 | Reinforcment WSD & BBL Approval | 7 | 29AUG10 | 05SEP10 |
| **Steel Works** | | | | |
| DESD-FB004 | Work Shop Drawings | 0 | 06SEP10* | |
| DESD-FB005 | Approval the work shop drawing | 7 | 07SEP10 | 14SEP10 |
| **Food Storage Tank** | | | | |
| **Building** | | | | |
| **Civil Works** | | | | |
| DESD-MT001 | Work Shop Drawings Submittal | 10 | 09AUG10 | 19AUG10 |
| DESD-MT002 | Approval the work shop drawing | 7 | 21AUG10 | 28AUG10 |
| DESD-MT006 | Reinforcement Details Submittal | 8 | 20SEP10 | 28SEP10 |
| DESD-MT003 | Reinforcment WSD & BBL Approval | 7 | 29SEP10 | 06OCT10 |
| **Hospital** | | | | |
| **Building** | | | | |
| **Electrical** | | | | |
| DESC-HS010 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |

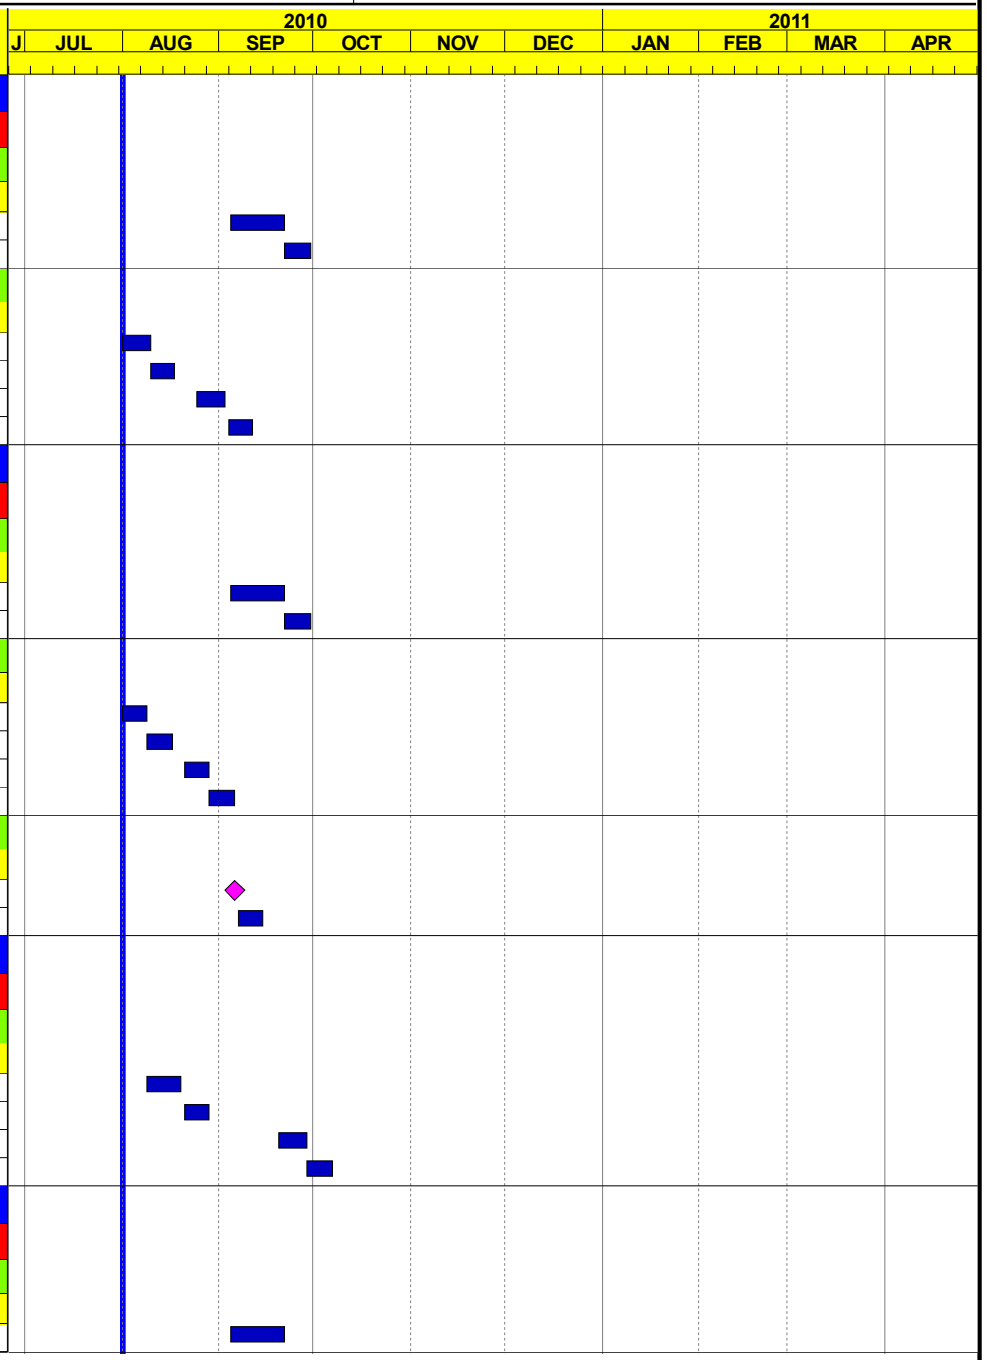


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 2 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DESC-HS011 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| ***Civil Works*** | | | | |
| DESC-HS001 | Work Shop Drawings Submittal | 13 | 01AUG10 | 15AUG10 |
| DESC-HS002 | Approval the work shop drawing | 7 | 16AUG10 | 23AUG10 |
| DESC-HS006 | Reinforcement Details Submittal | 7 | 01SEP10 | 08SEP10 |
| DESC-HS003 | Reinforcment WSD & BBL Approval | 7 | 09SEP10 | 16SEP10 |
| ***Steel Works*** | | | | |
| DESC-HS004 | Work Shop Drawings | 0 | 01SEP10* | |
| DESC-HS005 | Approval the work shop drawing | 7 | 01SEP10 | 08SEP10 |
| ***Milking Parlor*** | | | | |
| ***Building*** | | | | |
| ***Electrical*** | | | | |
| DESD-MP10 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-MP11 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| ***Civil Works*** | | | | |
| DESD-MP001 | Work Shop Drawings Submittal | 10 | 01AUG10 | 11AUG10 |
| DESD-MP002 | Approval the work shop drawing | 7 | 12AUG10 | 19AUG10 |
| DESD-MP006 | Reinforcement Details Submittal | 7 | 25AUG10 | 01SEP10 |
| DESD-MP003 | Reinforcment WSD & BBL Approval | 7 | 02SEP10 | 09SEP10 |
| ***Steel Works*** | | | | |
| DESD-MP004 | Work Shop Drawings | 0 | 04SEP10* | |
| DESD-MP005 | Approval the work shop drawing | 0 | 05SEP10 | 04SEP10 |
| ***Security Building*** | | | | |
| ***Building*** | | | | |
| ***Electrical*** | | | | |
| DESD-SE010 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-SE011 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| ***Civil Works*** | | | | |
| DESD-SE001 | Work Shop Drawings Submittal | 10 | 23SEP10 | 04OCT10 |
| DESD-SE006 | Reinforcement Details Submittal | 10 | 23SEP10 | 04OCT10 |
| DESD-SE002 | Approval the work shop drawing | 7 | 05OCT10 | 12OCT10 |
| DESD-SE003 | Reinforcment WSD & BBL Approval | 7 | 05OCT10 | 12OCT10 |

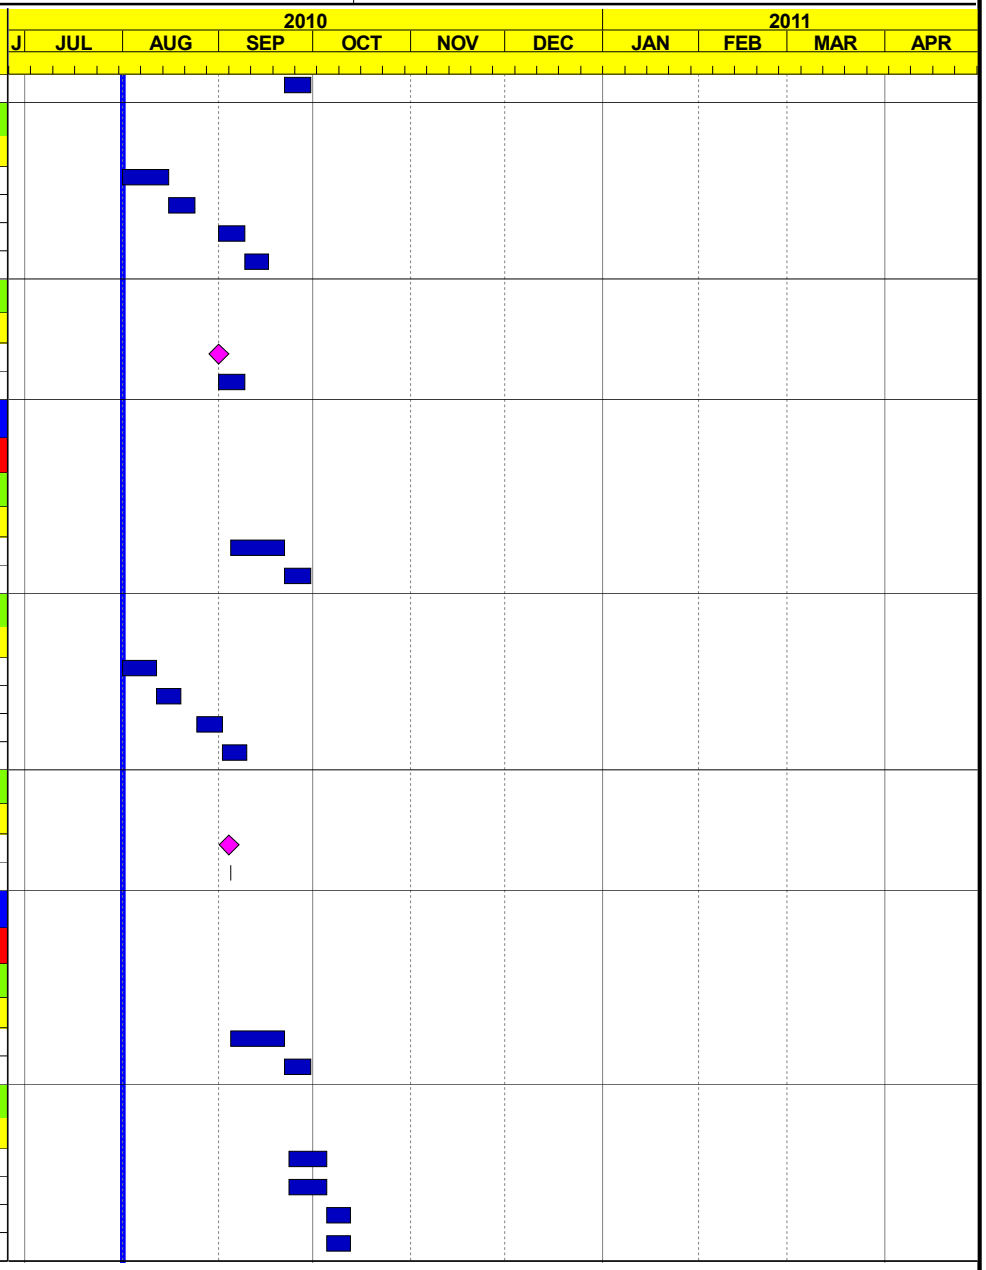


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

© Primavera Systems, Inc.

Early Bar
Progress Bar
Critical Activity

DAFM



General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Social Building** | | | | |
| **Building** | | | | |
| **Electrical** | | | | |
| DESD-SO010 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-SO011 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESD-SO001 | Work Shop Drawings Submittal | 8 | 12AUG10 | 21AUG10 |
| DESD-SO002 | Approval the work shop drawing | 7 | 22AUG10 | 29AUG10 |
| DESD-SO006 | Reinforcement Details Submittal | 8 | 14SEP10 | 22SEP10 |
| DESD-SO003 | Reinforcment WSD & BBL Approval | 7 | 23SEP10 | 30SEP10 |
| **Silage Bunk** | | | | |
| **Building** | | | | |
| **Civil Works** | | | | |
| DESC-SL001 | Work Shop Drawings Submittal | 2 | 01AUG10 | 02AUG10 |
| DESC-SL002 | Approval the work shop drawing | 7 | 03AUG10 | 10AUG10 |
| DESC-SL006 | Reinforcement Details Submittal | 9 | 30AUG10 | 08SEP10 |
| DESC-SL003 | Reinforcment WSD & BBL Approval | 7 | 09SEP10 | 16SEP10 |
| **Weight Building** | | | | |
| **Building** | | | | |
| **Electrical** | | | | |
| **Electrical** | | | | |
| DESC-WB010 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESC-WB011 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESC-WB001 | Work Shop Drawings Submittal | 10 | 29SEP10 | 10OCT10 |
| DESC-WB006 | Reinforcement Details Submittal | 10 | 29SEP10 | 10OCT10 |
| DESC-WB002 | Approval the work shop drawing | 7 | 11OCT10 | 18OCT10 |
| DESC-WB003 | Reinforcment WSD & BBL Approval | 7 | 11OCT10 | 18OCT10 |
| **Work Shop** | | | | |
| **Building** | | | | |
| **Electrical** | | | | |
| **Electrical** | | | | |
| DESD-WS010 | Electrical Work Shop Drawings Submittal | 15 | 05SEP10 | 21SEP10 |
| DESD-WS011 | Electrical Work Shop Drawings Approval | 7 | 22SEP10 | 29SEP10 |
| **Civil Works** | | | | |
| DESD-WS001 | Work Shop Drawings Submittal | 10 | 05SEP10 | 15SEP10 |

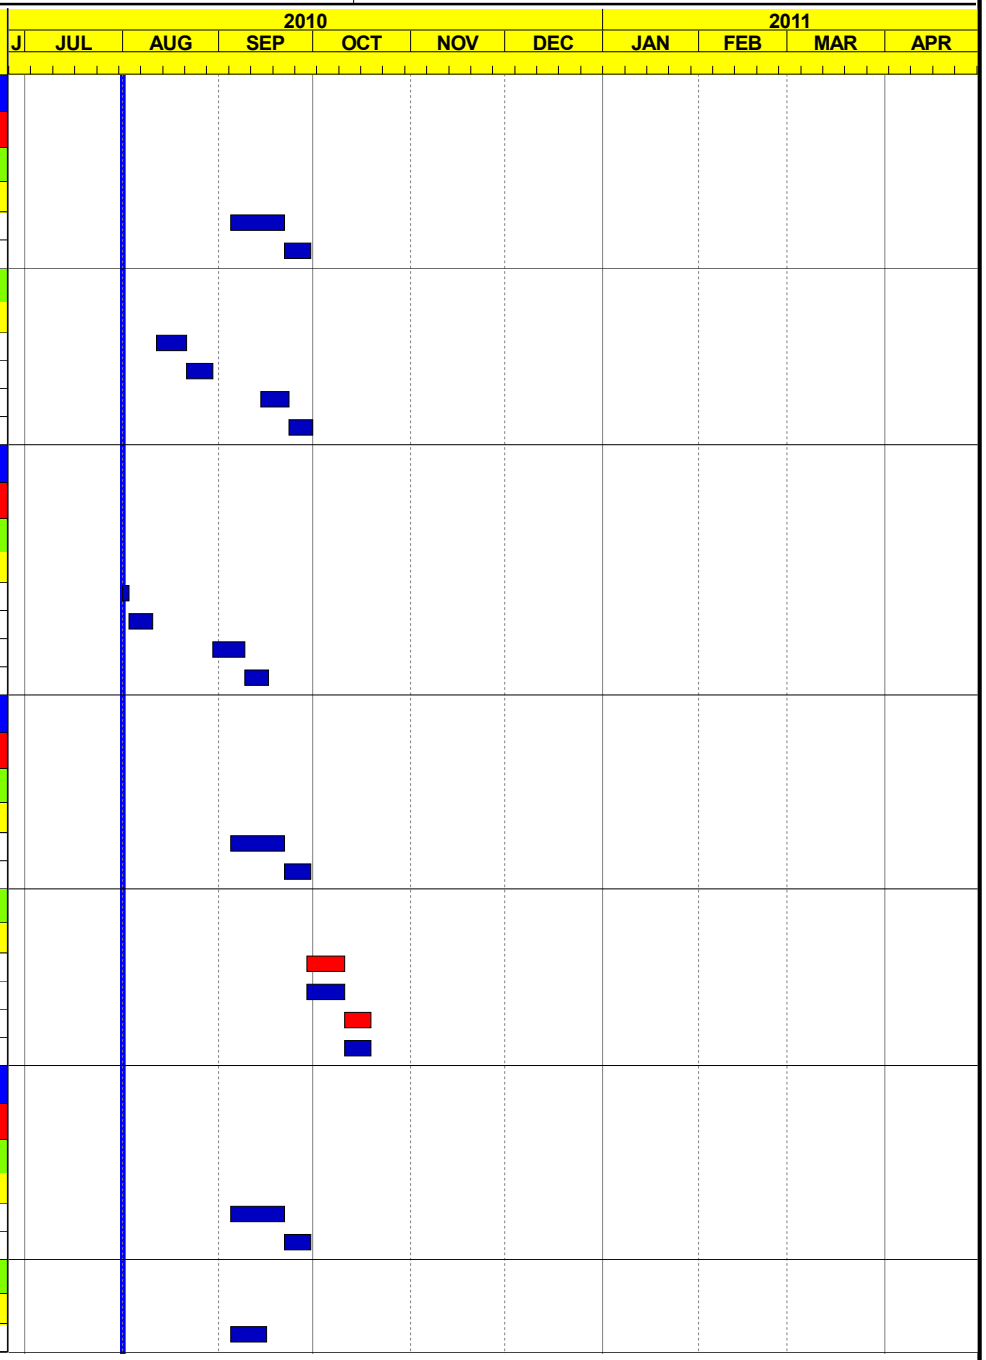


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 4 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DESD-WS006 | Reinforcement Details Submittal | 10 | 05SEP10 | 15SEP10 |
| DESD-WS002 | Approval the work shop drawing | 7 | 16SEP10 | 23SEP10 |
| DESD-WS003 | Reinforcment WSD & BBL Approval | 7 | 16SEP10 | 23SEP10 |
| ***Steel Works*** | | | | |
| DESD-WS004 | Work Shop Drawings | 0 | 05SEP10* | |
| DESD-WS005 | Approval the work shop drawing | 7 | 06SEP10 | 13SEP10 |
| ***Electrical & Transformer Building*** | | | | |
| ***Building*** | | | | |
| ***Civil Works*** | | | | |
| DESD-ET001 | Work Shop Drawings Submittal | 10 | 18SEP10 | 28SEP10 |
| DESD-ET006 | Reinforcement Details Submittal | 10 | 18SEP10 | 28SEP10 |
| DESD-ET002 | fApproval the work shop drawing | 7 | 29SEP10 | 06OCT10 |
| DESD-ET003 | Reinforcment WSD & BBL Approval | 7 | 29SEP10 | 06OCT10 |
| ***Tanks 1, 2, 3 & 4*** | | | | |
| ***Building*** | | | | |
| ***Civil Works*** | | | | |
| DESD-TN001 | Work Shop Drawings Submittal | 8 | 02OCT10 | 10OCT10 |
| DESD-TN006 | Reinforcement Details Submittal | 8 | 02OCT10 | 10OCT10 |
| DESD-TN002 | Approval the work shop drawing | 7 | 11OCT10 | 18OCT10 |
| DESD-TN003 | Reinforcment WSD & BBL Approval | 7 | 11OCT10 | 18OCT10 |
| ***Execution Works*** | | | | |
| ***Site Works*** | | | | |
| ***Site Preparation*** | | | | |
| ***General*** | | | | |
| DCGN-MB001 | Mobilization | 10 | 01AUG10 | 11AUG10 |
| DCGN-MB002 | Electrical Works & Mist System | 79* | 27NOV10 | 26FEB11 |
| ***Cow Island 1 & 2*** | | | | |
| ***Cow Sheds*** | | | | |
| ***Cow Shed 1, 2, 3 & 4*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-CW101 | Excavation | 12 | 17AUG10 | 30AUG10 |
| DCCV-CW107 | Disposal Of Excavated Materials | 20 | 17AUG10 | 08SEP10 |
| DCCV-CW103 | Soil Replacement | 18 | 31AUG10 | 20SEP10 |
| DCCV-CW102 | Filling Around Foundations Up To SOG Level | 16 | 09NOV10 | 27NOV10 |

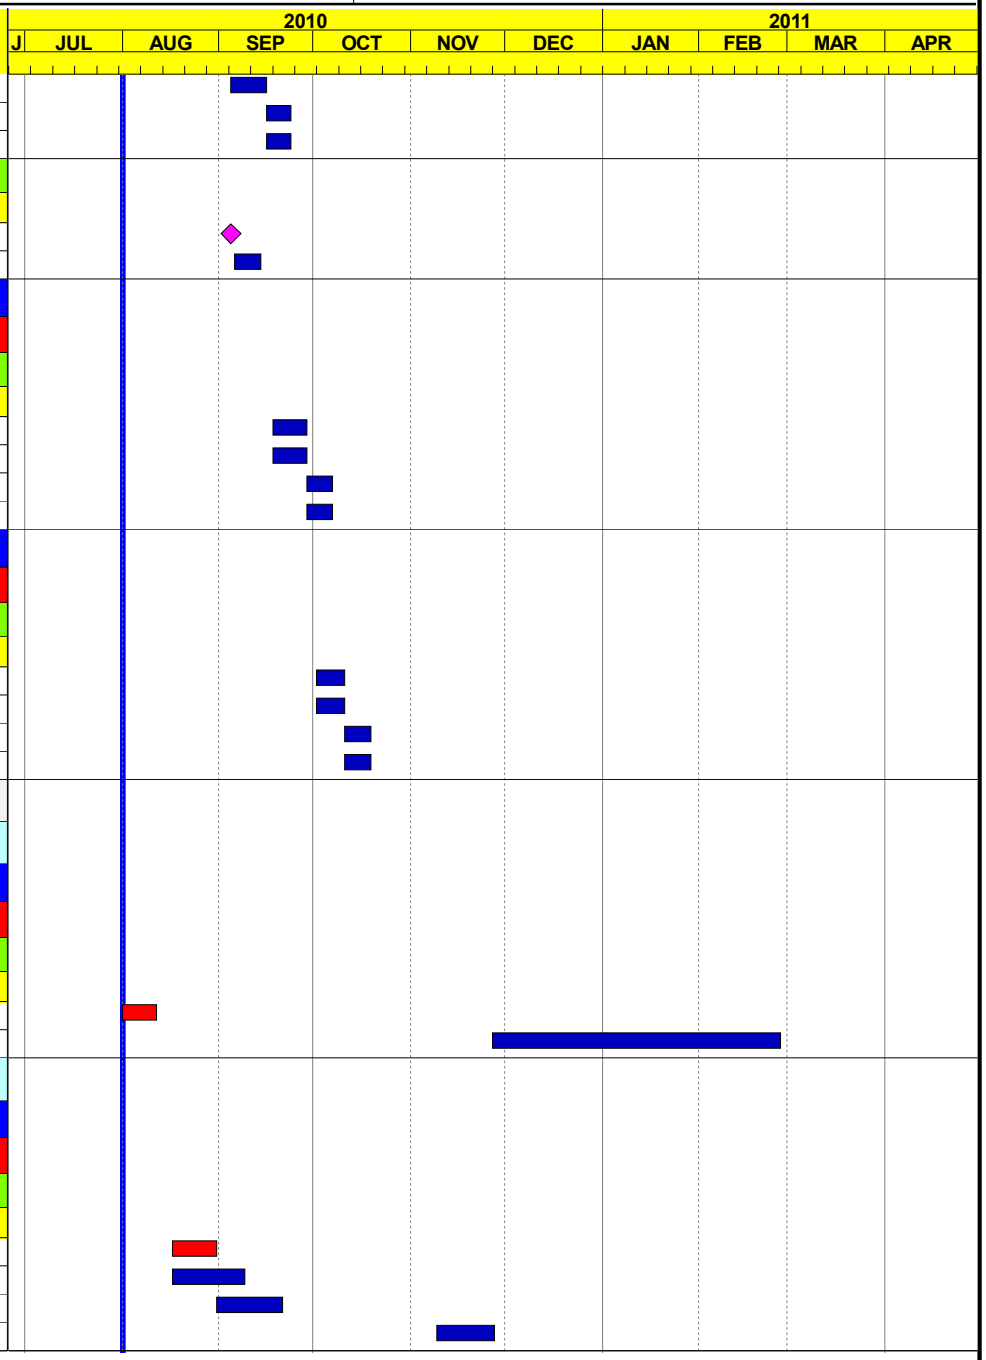


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 5 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Concrete Works** | | | | |
| *Plain Concrete* | | | | |
| DCCV-CW104 | PC Foundation | 12 | 23SEP10 | 06OCT10 |
| DCCV-CW111 | PC Slab On Grade | 8 | 29NOV10 | 07DEC10 |
| *Reinforced Concrete* | | | | |
| DCCV-CW105 | RC Foundation & Semels | 14 | 09OCT10 | 24OCT10 |
| DCCV-CW106 | Columns & Pedestals | 11 | 25OCT10 | 06NOV10 |
| DCCV-CW113 | RC Slab On Grade | 10 | 08DEC10 | 19DEC10 |
| **Metals** | | | | |
| DCCV-CW112 | Anchore Bolts | 8 | 28OCT10 | 06NOV10 |
| DCCV-CW108 | Steel Structure For Skeleton | 15 | 07NOV10 | 23NOV10 |
| DCCV-CW114 | Cladding | 10 | 24NOV10 | 05DEC10 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-CW109 | Water Proofing For Foundations (Cement Slurry) | 2 | 07NOV10 | 08NOV10 |
| DCCV-CW110 | Polyethylene Membrane | 1 | 28NOV10 | 28NOV10 |
| **Electrical** | | | | |
| *Electrical* | | | | |
| DCCV-CW115 | Electrical Works | 19 | 28NOV10 | 19DEC10 |
| **General** | | | | |
| DCGN-CW101 | Start Of Work | 0 | 17AUG10 | |
| DCGN-CW102 | End Of Work | 0 | | 19DEC10 |
| **Feeding Sheds** | | | | |
| **Feeding Shed 1** | | | | |
| **Earth Works** | | | | |
| DCCV-FD101 | Excavation | 6 | 18AUG10 | 24AUG10 |
| DCCV-FD115 | Disposal Of Excavated Materials | 15 | 18AUG10 | 04SEP10 |
| DCCV-FD103 | Soil Replacement | 16 | 25AUG10 | 12SEP10 |
| DCCV-FD102 | Filling Around Foundations Up To SOG Level | 7 | 17OCT10 | 24OCT10 |
| **Concrete Works** | | | | |
| *Plain Concrete* | | | | |
| DCCV-FD104 | PC Foundation | 9 | 13SEP10 | 22SEP10 |
| DCCV-FD106 | PC Slab On Grade | 6 | 26OCT10 | 01NOV10 |
| *Reinforced Concrete* | | | | |
| DCCV-FD105 | RC Foundation & Semels | 13 | 23SEP10 | 07OCT10 |
| DCCV-FD108 | RC Columns & Pedestals | 7 | 09OCT10 | 16OCT10 |
| DCCV-FD107 | RC Slab On Grade | 8 | 02NOV10 | 10NOV10 |

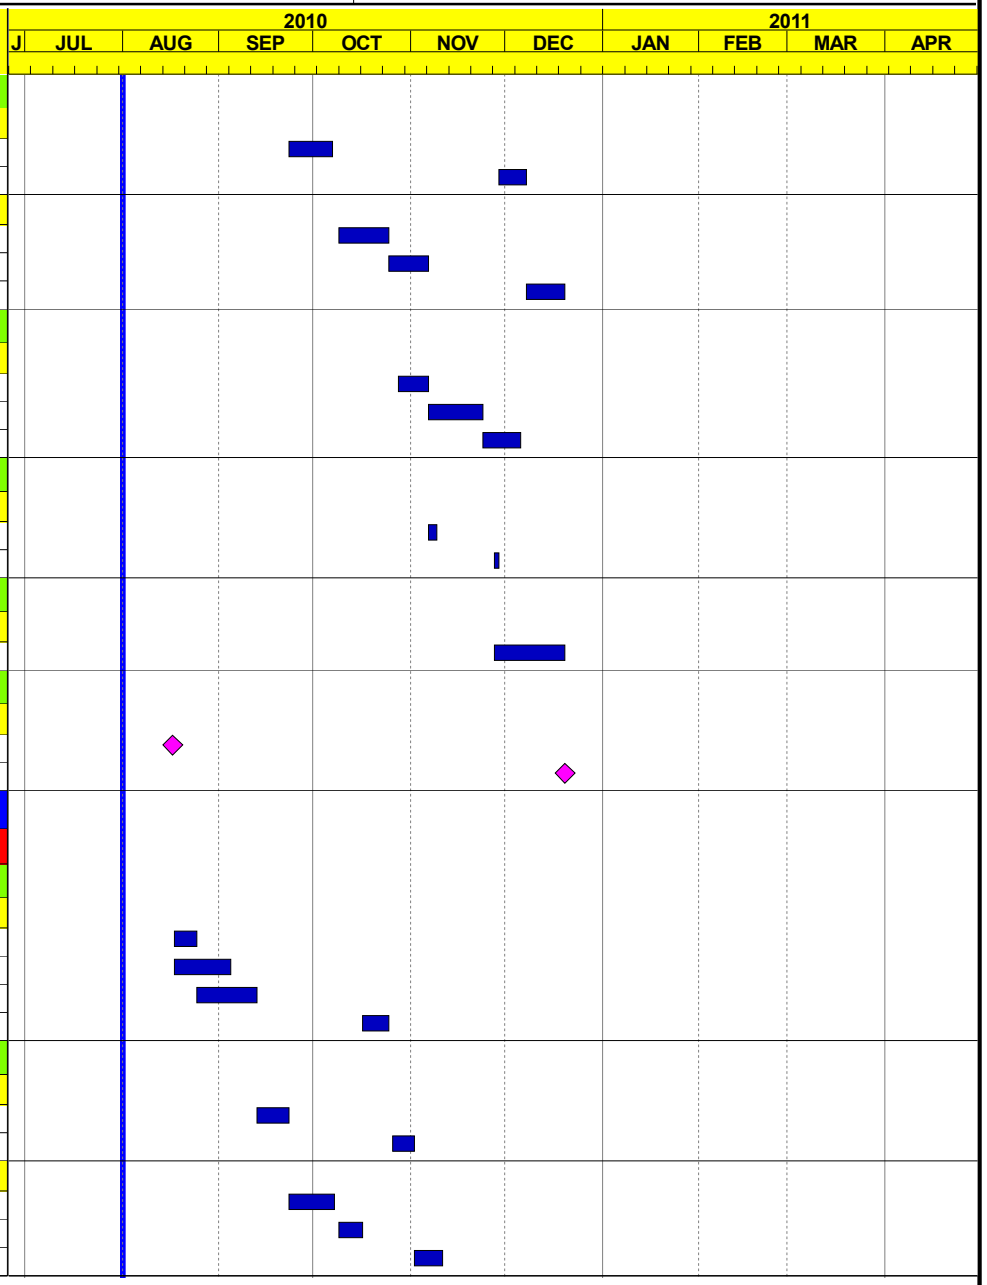


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 6 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama For Trading & Contracting

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| ***Metals*** | | | | |
| DCCV-FD112 | Anchore Bolts | 12 | 03OCT10 | 16OCT10 |
| DCCV-FD109 | Steel Structure For Skeleton | 16 | 17OCT10 | 03NOV10 |
| DCCV-FD113 | Cladding | 19 | 04NOV10 | 25NOV10 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-FD110 | Water Proofing For Foundations (Cement Slurry) | 4 | 12OCT10 | 16OCT10 |
| DCCV-FD111 | Polyethylene Membrane | 1 | 25OCT10 | 25OCT10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-FD114 | Electrical Works | 20 | 27NOV10 | 19DEC10 |
| ***General*** | | | | |
| DCGN-FD101 | Start Of Work | 0 | 18AUG10 | |
| DCGN-FD102 | End Of Work | 0 | | 19DEC10 |
| ***Feeding Shed 2*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-FD201 | Excavation | 6 | 18AUG10 | 24AUG10 |
| DCCV-FD215 | Disposal Of Excavated Materials | 13 | 18AUG10 | 01SEP10 |
| DCCV-FD203 | Soil Replacement | 16 | 25AUG10 | 12SEP10 |
| DCCV-FD202 | Filling Around Foundations Up To SOG Level | 7 | 20OCT10 | 27OCT10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-FD204 | PC Foundation | 9 | 13SEP10 | 22SEP10 |
| DCCV-FD206 | PC Slab On Grade | 6 | 30OCT10 | 04NOV10 |
| ***Reinforced Concrete*** | | | | |
| DCCV-FD205 | RC Foundation & Semels | 13 | 23SEP10 | 07OCT10 |
| DCCV-FD208 | RC Columns & Pedestals | 7 | 09OCT10 | 16OCT10 |
| DCCV-FD207 | RC Slab On Grade | 8 | 06NOV10 | 14NOV10 |
| ***Metals*** | | | | |
| DCCV-FD212 | Anchore Bolts | 14 | 30SEP10 | 16OCT10 |
| DCCV-FD209 | Steel Structure For Skeleton | 16 | 17OCT10 | 03NOV10 |
| DCCV-FD213 | Cladding | 19 | 04NOV10 | 25NOV10 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-FD210 | Water Proofing For Foundations (Cement Slurry) | 3 | 17OCT10 | 19OCT10 |
| DCCV-FD211 | Polyethylene Membrane | 1 | 28OCT10 | 28OCT10 |

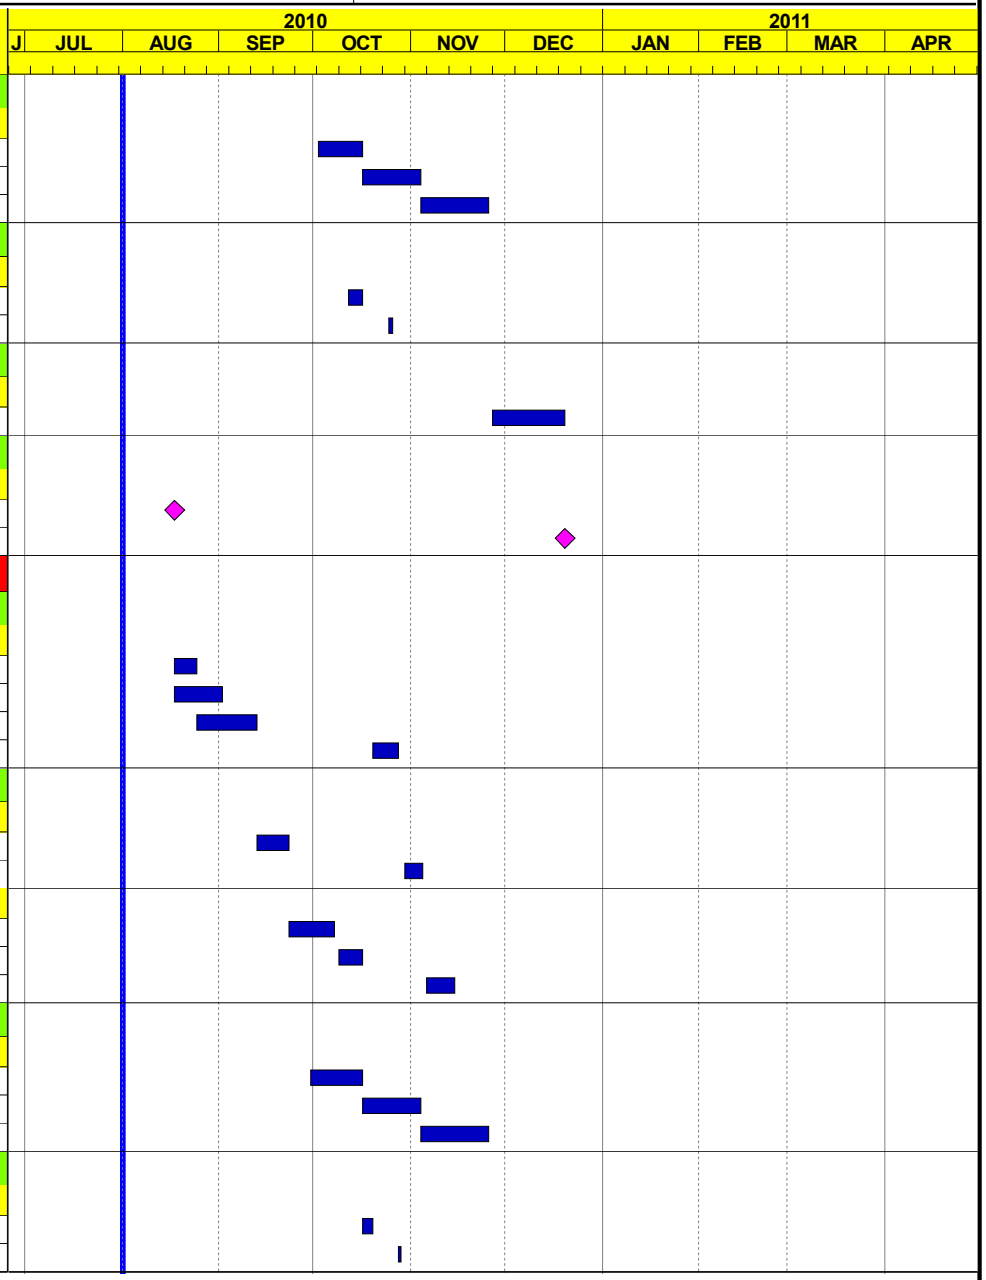


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 7 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Electrical** | | | | |
| ***Electrical*** | | | | |
| DCCV-FD214 | Electrical Works | 20 | 27NOV10 | 19DEC10 |
| **General** | | | | |
| DCGN-FD201 | Start Of Work | 0 | 18AUG10 | |
| DCGN-FD202 | End Of Work | 0 | | 19DEC10 |
| ***Cow Island 3 & 4*** | | | | |
| **Cow Sheds** | | | | |
| **Cow Shed 5, 6, 7 & 8** | | | | |
| **Earth Works** | | | | |
| DCCV-CW201 | Excavation | 12 | 12SEP10 | 25SEP10 |
| DCCV-CW207 | Disposal Of Excavated Materials | 20 | 12SEP10 | 04OCT10 |
| DCCV-CW203 | Soil Replacement | 18 | 26SEP10 | 16OCT10 |
| DCCV-CW202 | Filling Around Foundations Up To SOG Level | 16 | 29DEC10 | 16JAN11 |
| **Concrete Works** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-CW204 | PC Foundation | 12 | 17OCT10 | 30OCT10 |
| DCGN-CW211 | PC Slab On Grade | 8 | 07FEB11 | 15FEB11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-CW205 | RC Foundation & Semels | 14 | 31OCT10 | 15NOV10 |
| DCCV-CW206 | Columns & Pedestals | 11 | 16NOV10 | 28NOV10 |
| DCGN-CW213 | RC Slab On Grade | 10 | 16FEB11 | 27FEB11 |
| **Metals** | | | | |
| DCCV-CW212 | Anchore Bolts | 8 | 20NOV10 | 28NOV10 |
| DCCV-CW208 | Steel Structure For Skeleton | 15 | 01JAN11 | 17JAN11 |
| DCGN-CW214 | Cladding | 10 | 18JAN11 | 29JAN11 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-CW209 | Water Proofing For Foundations (Cement Slurry) | 2 | 29NOV10 | 30NOV10 |
| DCGN-CW210 | Polyethylene Membrane | 1 | 17JAN11 | 17JAN11 |
| **Electrical** | | | | |
| ***Electrical*** | | | | |
| DCGN-CW215 | Electrical Works | 19 | 30JAN11 | 20FEB11 |
| **General** | | | | |
| DCGN-CW201 | Start Of Work | 0 | 12SEP10 | |
| DCGN-CW202 | End Of Work | 0 | | 27FEB11 |

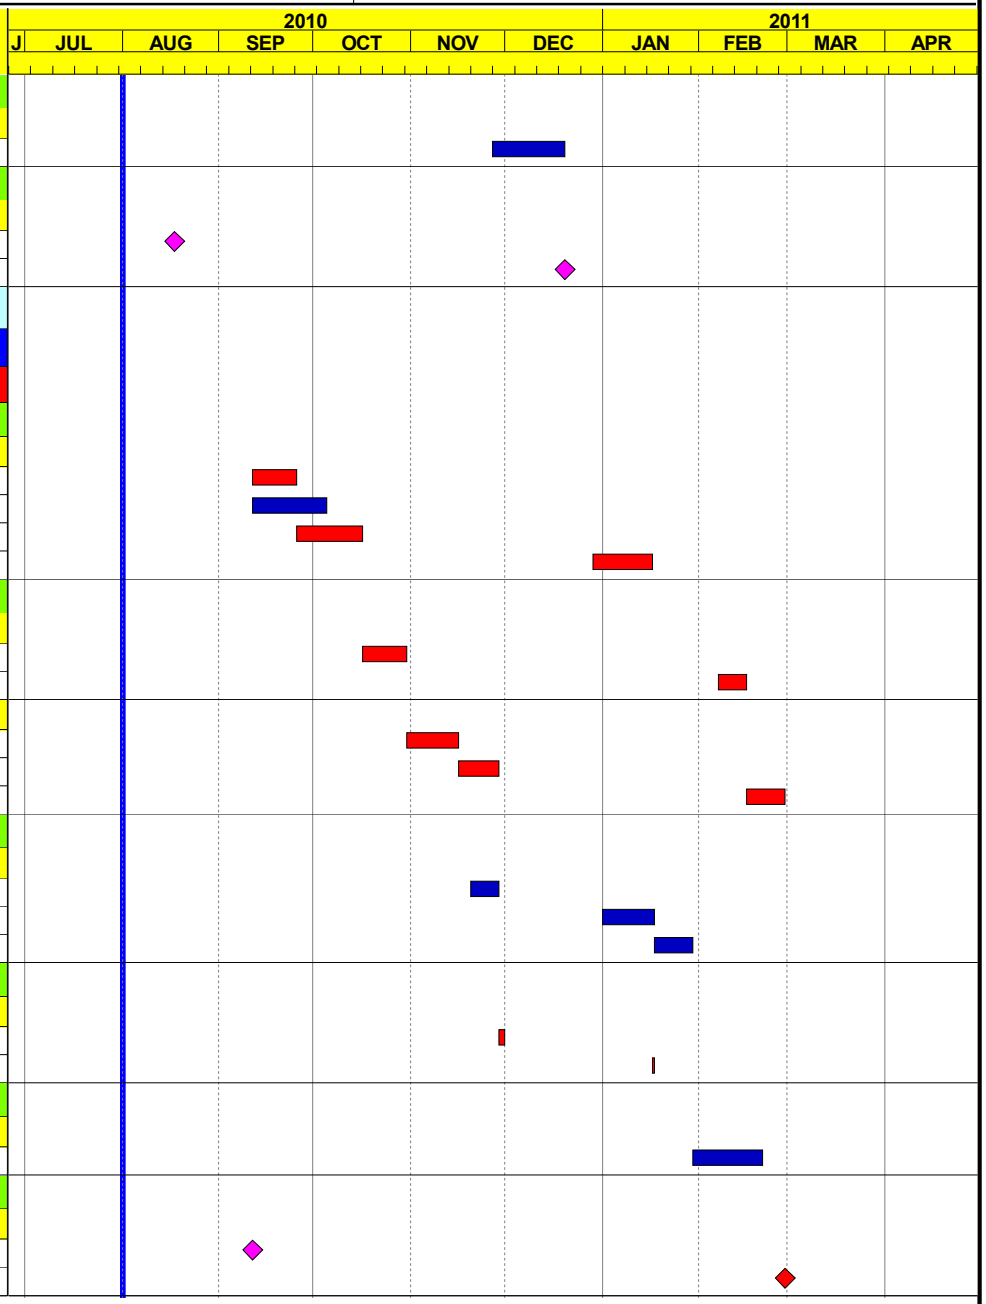


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 8 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Feeding Sheds** | | | | |
| **Feeding Shed 3** | | | | |
| **Earth Works** | | | | |
| DCCV-FD301 | Excavation | 19 | 25AUG10 | 15SEP10 |
| DCCV-FD315 | Disposal Of Excavated Materials | 18 | 25AUG10 | 14SEP10 |
| DCCV-FD303 | Soil Replacement | 16 | 16SEP10 | 04OCT10 |
| DCCV-FD302 | Filling Around Foundations Up To SOG Level | 12 | 24NOV10 | 07DEC10 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-FD304 | PC Foundation | 18 | 05OCT10 | 25OCT10 |
| DCCV-FD306 | PC Slab On Grade | 16 | 09DEC10 | 27DEC10 |
| **Reinforced Concrete** | | | | |
| DCCV-FD305 | RC Foundation & Semels | 17 | 26OCT10 | 14NOV10 |
| DCCV-FD308 | RC Columns & Pedestals | 14 | 15NOV10 | 30NOV10 |
| DCCV-FD307 | RC Slab On Grade | 12 | 01FEB11 | 14FEB11 |
| **Metals** | | | | |
| DCCV-FD312 | Anchore Bolts | 18 | 10NOV10 | 30NOV10 |
| DCCV-FD309 | Steel Structure For Skeleton | 24 | 01DEC10 | 28DEC10 |
| DCCV-FD313 | Cladding | 27 | 29DEC10 | 29JAN11 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-FD310 | Water Proofing For Foundations (Cement Slurry) | 5 | 18NOV10 | 23NOV10 |
| DCCV-FD311 | Polyethylene Membrane | 1 | 08DEC10 | 08DEC10 |
| **Electrical** | | | | |
| **Electrical** | | | | |
| DCCV-FD314 | Electrical Works | 21 | 30JAN11 | 22FEB11 |
| **General** | | | | |
| DCGN-FD301 | Start Of Work | 0 | 25AUG10 | |
| DCGN-FD302 | End Of Work | 0 | | 22FEB11 |
| **Feeding Shed 4** | | | | |
| **Earth Works** | | | | |
| DCCV-FD401 | Excavation | 15 | 06SEP10 | 22SEP10 |
| DCCV-FD415 | Disposal Of Excavated Materials | 17 | 06SEP10 | 25SEP10 |
| DCCV-FD403 | Soil Replacement | 16 | 23SEP10 | 11OCT10 |
| DCCV-FD402 | Filling Around Foundations Up To SOG Level | 8 | 24NOV10 | 02DEC10 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-FD404 | PC Foundation | 16 | 12OCT10 | 30OCT10 |

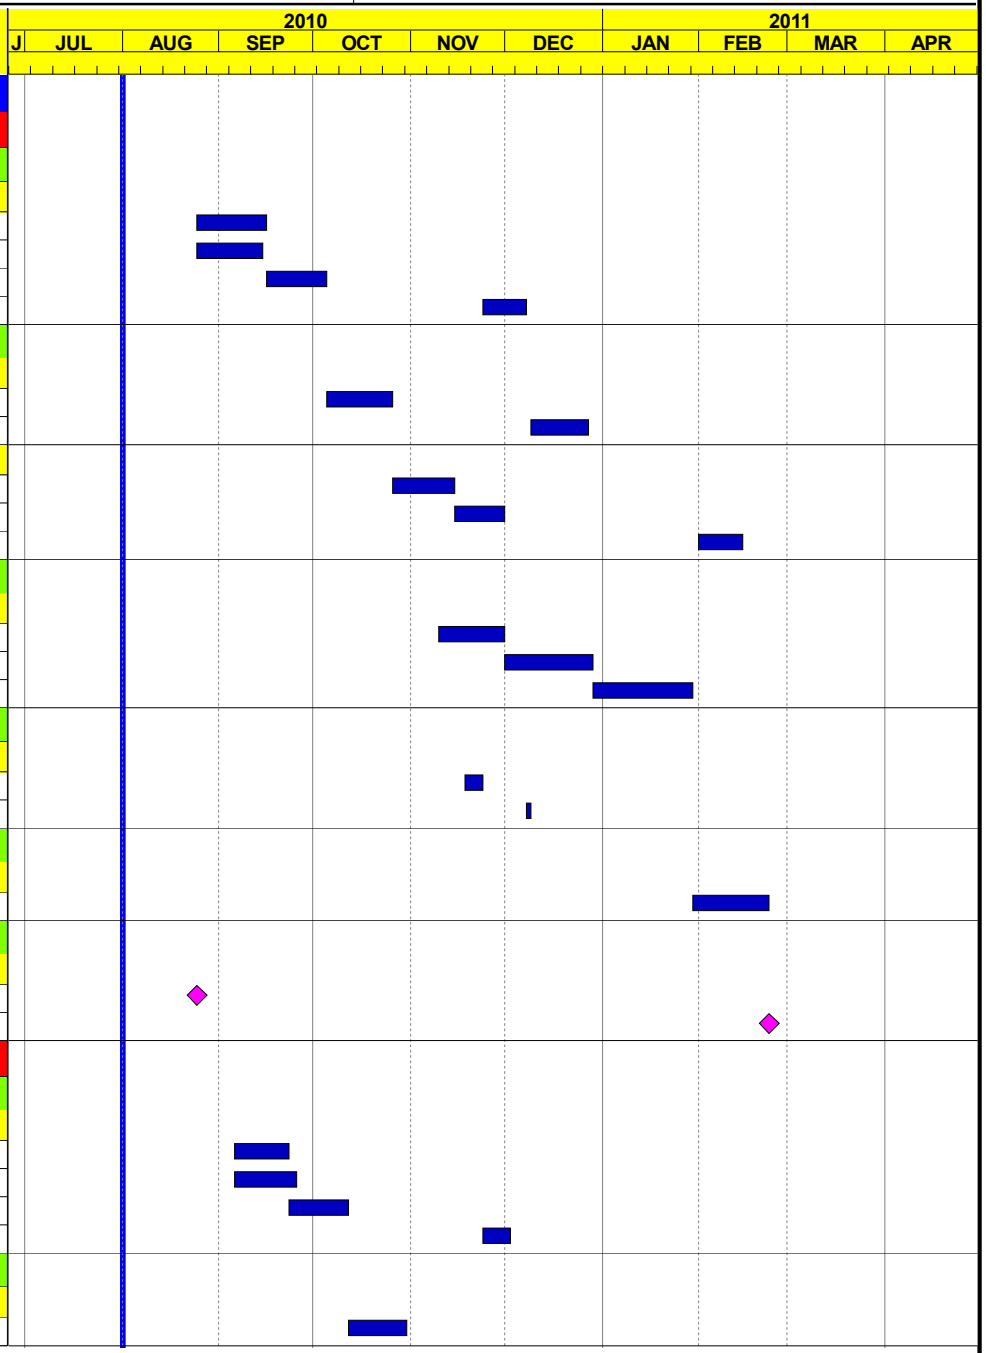


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 9 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCCV-FD406 | PC Slab On Grade | 14 | 26JAN11 | 10FEB11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-FD405 | RC Foundation & Semels | 15 | 31OCT10 | 16NOV10 |
| DCCV-FD408 | RC Columns & Pedestals | 11 | 17NOV10 | 29NOV10 |
| DCCV-FD407 | RC Slab On Grade | 10 | 12FEB11 | 22FEB11 |
| ***Metals*** | | | | |
| DCCV-FD412 | Anchore Bolts | 18 | 09NOV10 | 29NOV10 |
| DCCV-FD409 | Steel Structure For Skeleton | 22 | 30NOV10 | 25DEC10 |
| DCCV-FD413 | Cladding | 27 | 26DEC10 | 25JAN11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-FD410 | Water Proofing For Foundations (Cement Slurry) | 3 | 21NOV10 | 23NOV10 |
| DCCV-FD411 | Polyethylene Membrane | 1 | 04DEC10 | 04DEC10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-FD414 | Electrical Works | 21 | 26JAN11 | 19FEB11 |
| ***General*** | | | | |
| DCGN-FD401 | Start Of Work | 0 | 06SEP10 | |
| DCGN-FD402 | End Of Work | 0 | | 22FEB11 |
| ***Cow Island 5 & 6*** | | | | |
| ***Cow Sheds*** | | | | |
| ***Cow Shed 9, 10, 11 & 12*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-CW301 | Excavation | 12 | 26SEP10 | 09OCT10 |
| DCCV-CW307 | Disposal Of Excavated Materials | 20 | 26SEP10 | 18OCT10 |
| DCCV-CW303 | Soil Replacement | 18 | 10OCT10 | 30OCT10 |
| DCCV-CW302 | Filling Around Foundations Up To SOG Level | 16 | 15DEC10 | 02JAN11 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-CW304 | PC Foundation | 12 | 31OCT10 | 13NOV10 |
| DCCV-CW311 | PC Slab On Grade | 8 | 04JAN11 | 12JAN11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-CW305 | RC Foundation & Semels | 14 | 14NOV10 | 29NOV10 |
| DCCV-CW306 | Columns & Pedestals | 11 | 30NOV10 | 12DEC10 |
| DCCV-CW313 | RC Slab On Grade | 10 | 12FEB11 | 22FEB11 |
| ***Metals*** | | | | |
| DCCV-CW312 | Anchore Bolts | 8 | 04DEC10 | 12DEC10 |
| DCCV-CW308 | Steel Structure For Skeleton | 15 | 05JAN11 | 22JAN11 |

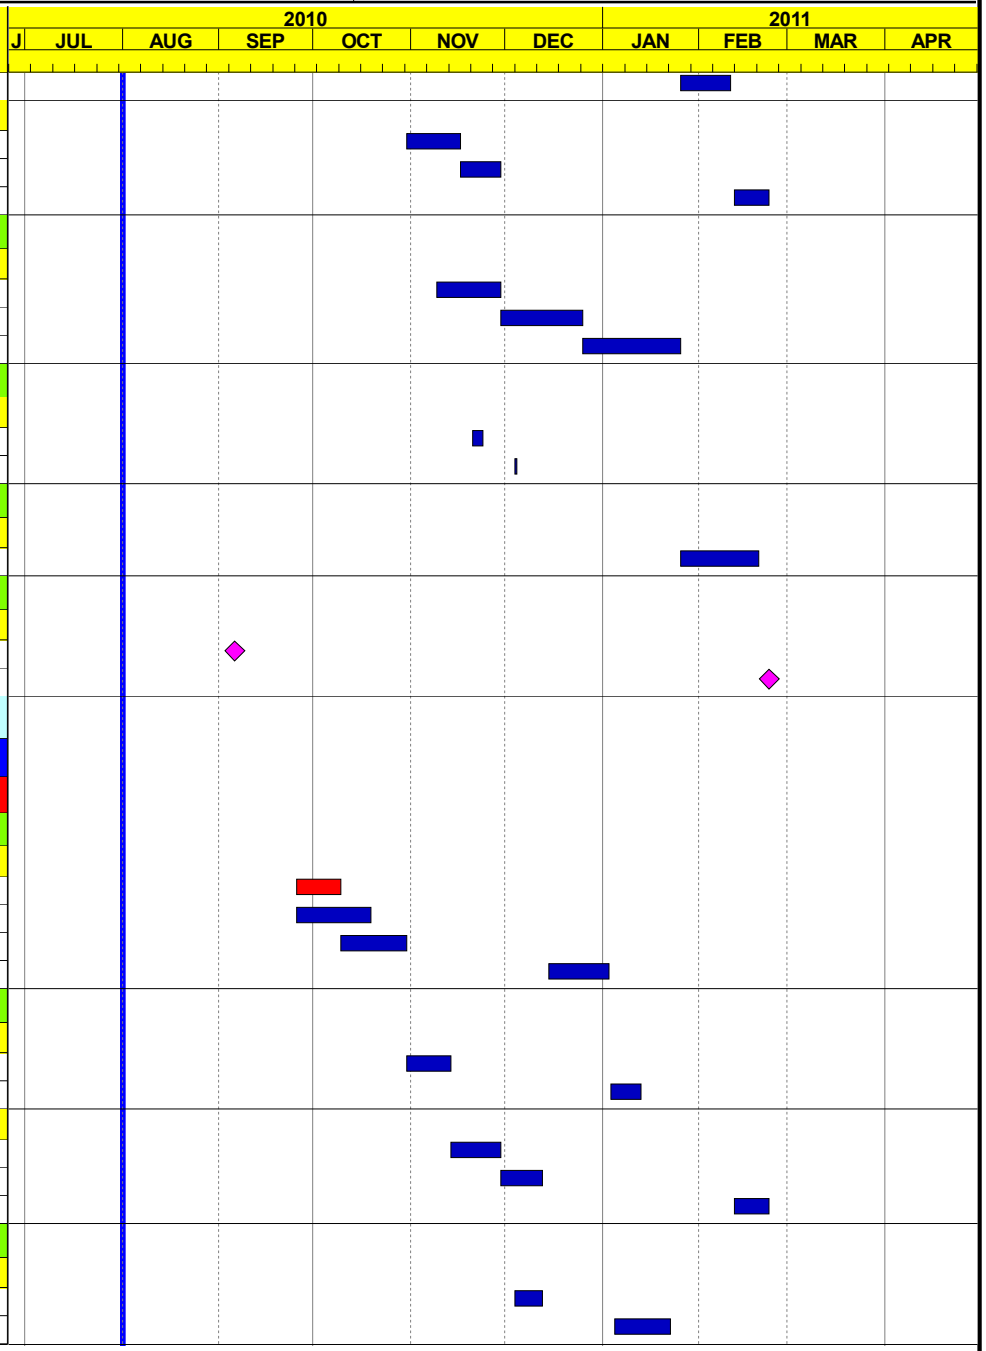


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 10 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCCV-CW314 | Cladding | 10 | 23JAN11 | 02FEB11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-CW309 | Water Proofing For Foundations (Cement Slurry) | 2 | 13DEC10 | 14DEC10 |
| DCCV-CW310 | Polyethylene Membrane | 1 | 03JAN11 | 03JAN11 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-CW315 | Electrical Works | 19 | 03FEB11 | 24FEB11 |
| ***General*** | | | | |
| DCGN-CW301 | Start Of Work | 0 | 26SEP10 | |
| DCGN-CW302 | End Of Work | 0 | | 24FEB11 |
| ***Feeding Sheds*** | | | | |
| ***Feeding Shed 5*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-FD501 | Excavation | 15 | 23SEP10 | 10OCT10 |
| DCCV-FD515 | Disposal Of Excavated Materials | 17 | 23SEP10 | 12OCT10 |
| DCCV-FD503 | Soil Replacement | 16 | 11OCT10 | 28OCT10 |
| DCCV-FD502 | Filling Around Foundations Up To SOG Level | 8 | 09DEC10 | 18DEC10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-FD504 | PC Foundation | 14 | 30OCT10 | 14NOV10 |
| DCCV-FD506 | PC Slab On Grade | 12 | 20DEC10 | 02JAN11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-FD505 | RC Foundation & Semels | 15 | 15NOV10 | 01DEC10 |
| DCCV-FD508 | RC Columns & Pedestals | 11 | 02DEC10 | 14DEC10 |
| DCCV-FD507 | RC Slab On Grade | 10 | 01FEB11 | 12FEB11 |
| ***Metals*** | | | | |
| DCCV-FD512 | Anchore Bolts | 15 | 28NOV10 | 14DEC10 |
| DCCV-FD509 | Steel Structure For Skeleton | 17 | 15DEC10 | 03JAN11 |
| DCCV-FD513 | Cladding | 20 | 04JAN11 | 26JAN11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-FD510 | Water Proofing For Foundations (Cement Slurry) | 3 | 06DEC10 | 08DEC10 |
| DCCV-FD511 | Polyethylene Membrane | 1 | 19DEC10 | 19DEC10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-FD514 | Electrical Works | 20 | 27JAN11 | 19FEB11 |

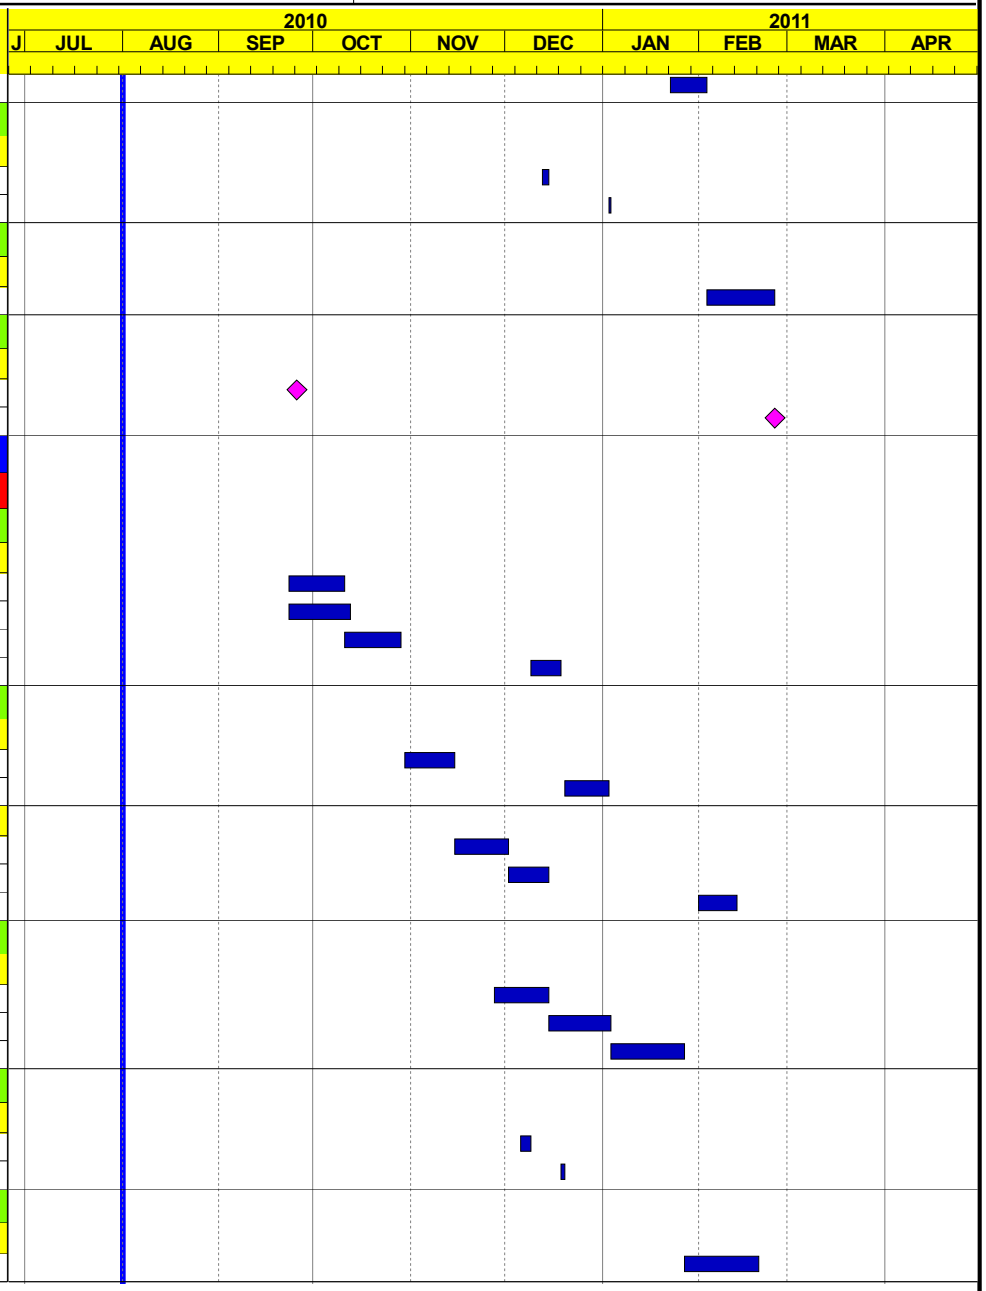


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 11 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama For Trading & Contracting

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **General** | | | | |
| DCGN-FD501 | Start Of Work | 0 | 23SEP10 | |
| DCGN-FD502 | End Of Work | 0 | | 19FEB11 |
| **Fedding Shed 6** | | | | |
| **Earth Works** | | | | |
| DCCV-FD601 | Excavation | 6 | 06NOV10 | 11NOV10 |
| DCCV-FD615 | Disposal Of Excavated Materials | 15 | 06NOV10 | 22NOV10 |
| DCCV-FD603 | Soil Replacement | 16 | 13NOV10 | 30NOV10 |
| DCCV-FD602 | Filling Around Foundations Up To SOG Level | 7 | 04JAN11 | 11JAN11 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-FD604 | PC Foundation | 9 | 01DEC10 | 11DEC10 |
| DCCV-FD606 | PC Slab On Grade | 6 | 13JAN11 | 19JAN11 |
| **Reinforced Concrete** | | | | |
| DCCV-FD605 | RC Foundation & Semels | 13 | 12DEC10 | 26DEC10 |
| DCCV-FD608 | RC Columns & Pedestals | 7 | 27DEC10 | 03JAN11 |
| DCCV-FD607 | RC Slab On Grade | 8 | 20JAN11 | 29JAN11 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-FD610 | Water Proofing For Foundations (Cement Slurry) | 4 | 30DEC10 | 03JAN11 |
| DCCV-FD611 | Polyethylene Membrane | 1 | 12JAN11 | 12JAN11 |
| **Electrical** | | | | |
| **Electrical** | | | | |
| DCCV-FD614 | Electrical Works | 20 | 30JAN11 | 21FEB11 |
| **General** | | | | |
| DCGN-FD601 | Start Of Work | 0 | 13NOV10 | |
| DCGN-FD602 | End Of Work | 0 | | 21FEB11 |
| ***Cow Island 7 & 8*** | | | | |
| **Cow Sheds** | | | | |
| **Cow Shed 13, 14, 15 & 16** | | | | |
| **Earth Works** | | | | |
| DCCV-CW401 | Excavation | 16 | 17OCT10 | 03NOV10 |
| DCCV-CW407 | Disposal Of Excavated Materials | 20 | 17OCT10 | 08NOV10 |
| DCCV-CW403 | Soil Replacement | 18 | 04NOV10 | 24NOV10 |
| DCCV-CW402 | Filling Around Foundations Up To SOG Level | 16 | 10JAN11 | 27JAN11 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-CW404 | PC Foundation | 12 | 25NOV10 | 08DEC10 |

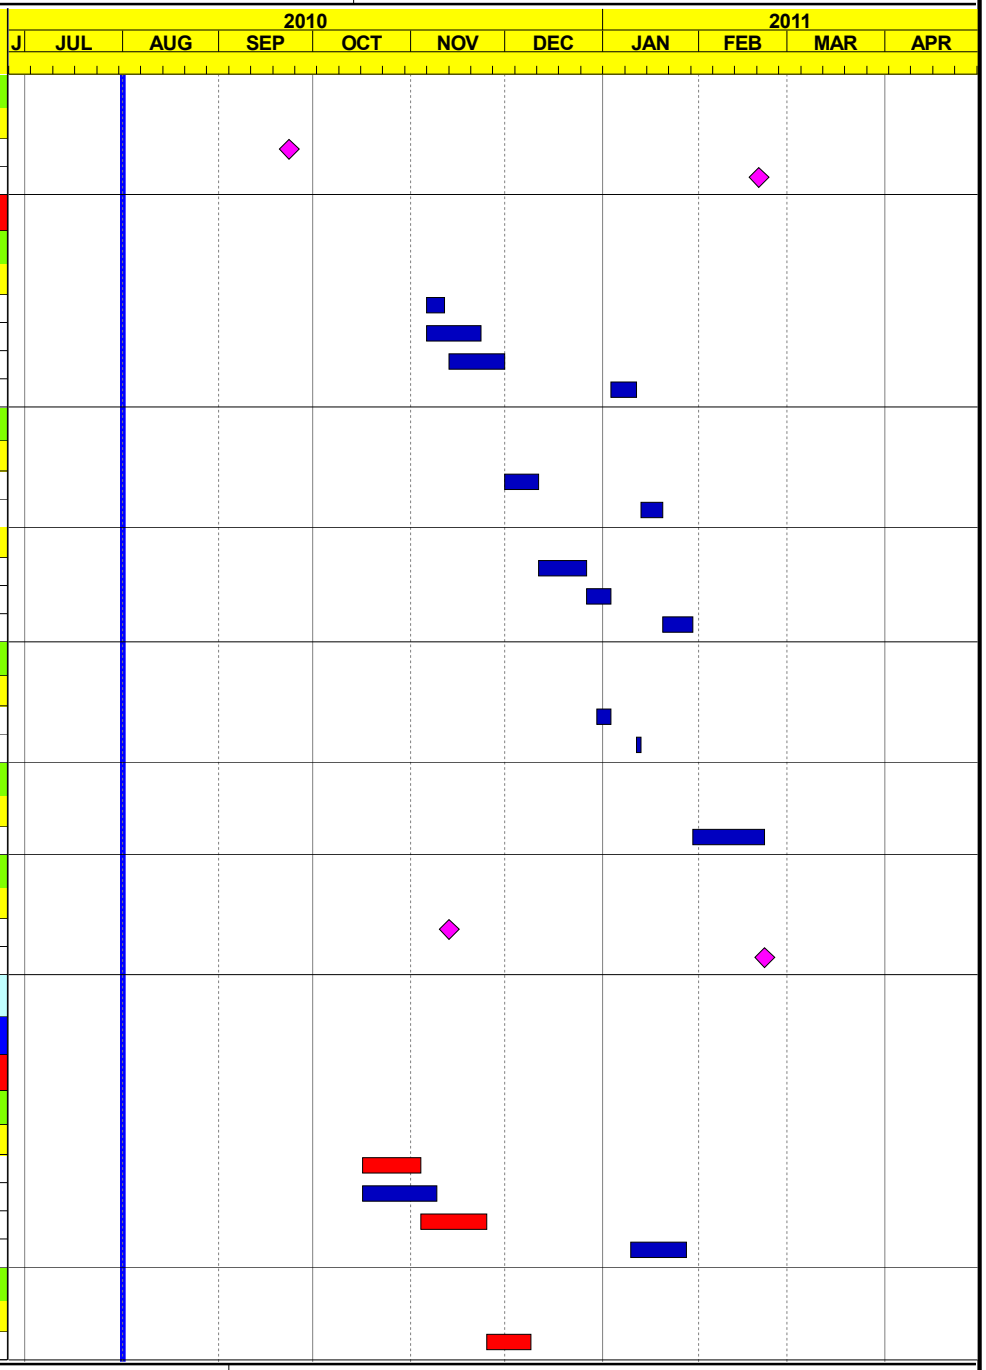


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 12 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCCV-CW411 | PC Slab On Grade | 8 | 30JAN11 | 07FEB11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-CW405 | RC Foundation & Semels | 14 | 09DEC10 | 25DEC10 |
| DCCV-CW406 | Columns & Pedestals | 11 | 26DEC10 | 06JAN11 |
| DCCV-CW413 | RC Slab On Grade | 10 | 08FEB11 | 19FEB11 |
| ***Metals*** | | | | |
| DCCV-CW412 | Anchore Bolts | 8 | 29DEC10 | 06JAN11 |
| DCCV-CW408 | Steel Structure For Skeleton | 15 | 08JAN11 | 24JAN11 |
| DCCV-CW414 | Cladding | 10 | 25JAN11 | 05FEB11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-CW409 | Water Proofing For Foundations (Cement Slurry) | 2 | 08JAN11 | 09JAN11 |
| DCCV-CW410 | Polyethylene Membrane | 1 | 29JAN11 | 29JAN11 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-CW415 | Electrical Works | 19 | 06FEB11 | 27FEB11 |
| ***General*** | | | | |
| DCGN-CW401 | Start Of Work | 0 | 17OCT10 | |
| DCGN-CW402 | End Of Work | 0 | | 27FEB11 |
| ***Feeding Sheds*** | | | | |
| ***Fedding Shed 7*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-FD701 | Excavation | 6 | 10NOV10 | 16NOV10 |
| DCCV-FD715 | Disposal Of Excavated Materials | 15 | 10NOV10 | 27NOV10 |
| DCCV-FD703 | Soil Replacement | 16 | 17NOV10 | 05DEC10 |
| DCCV-FD702 | Filling Around Foundations Up To SOG Level | 7 | 09JAN11 | 16JAN11 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-FD704 | PC Foundation | 9 | 06DEC10 | 15DEC10 |
| DCCV-FD706 | PC Slab On Grade | 6 | 18JAN11 | 24JAN11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-FD705 | RC Foundation & Semels | 13 | 16DEC10 | 30DEC10 |
| DCCV-FD708 | RC Columns & Pedestals | 7 | 01JAN11 | 08JAN11 |
| DCCV-FD707 | RC Slab On Grade | 8 | 25JAN11 | 02FEB11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-FD710 | Water Proofing For Foundations (Cement Slurry) | 4 | 04JAN11 | 08JAN11 |
| DCCV-FD711 | Polyethylene Membrane | 1 | 17JAN11 | 17JAN11 |

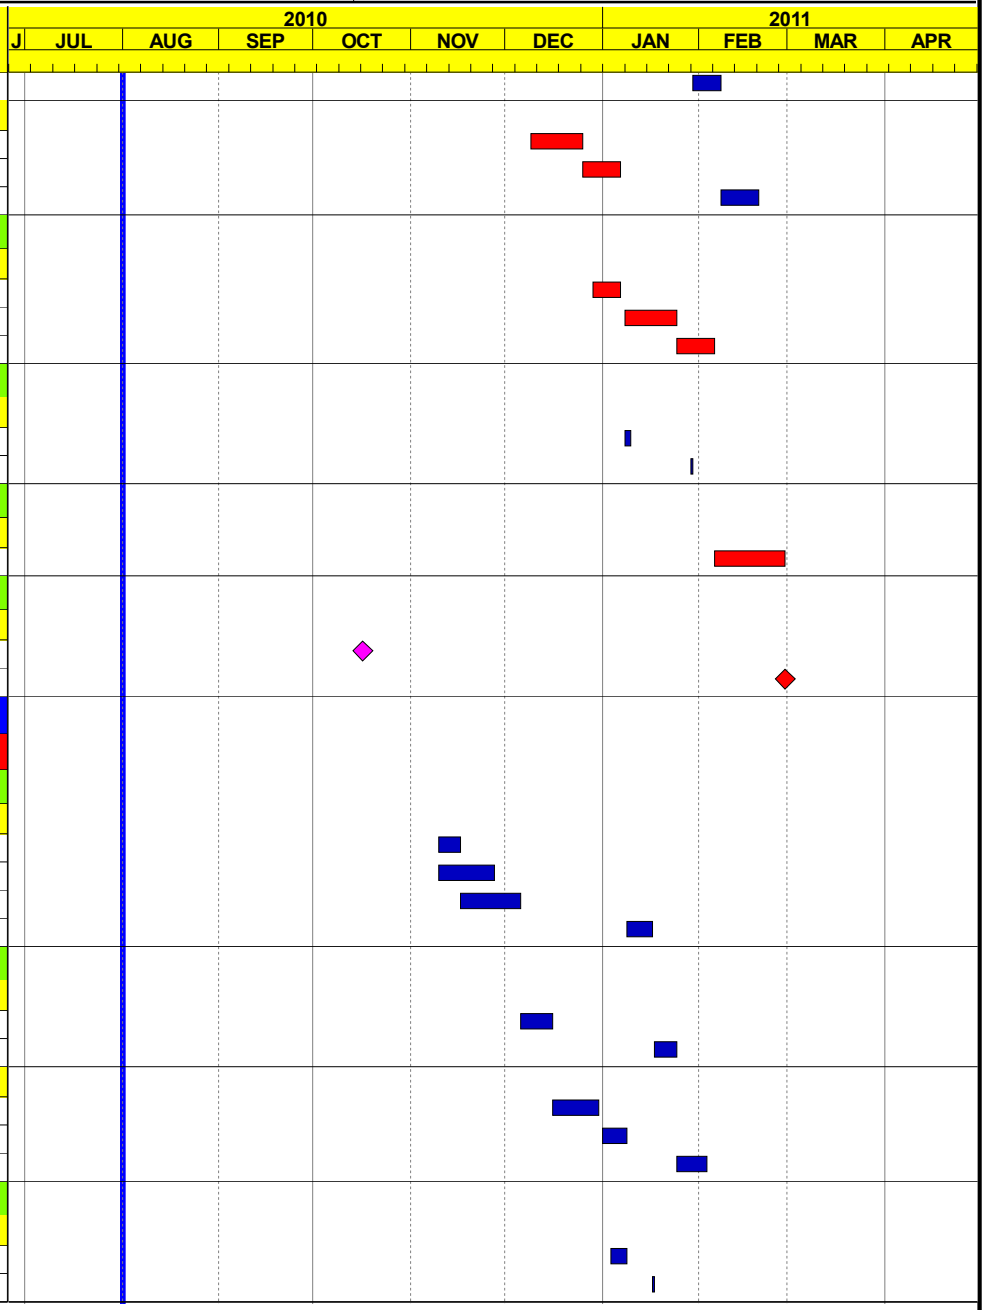


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 13 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Electrical** | | | | |
| *Electrical* | | | | |
| DCCV-FD714 | Electrical Works | 20 | 03FEB11 | 26FEB11 |
| **General** | | | | |
| DCGN-FD701 | Start Of Work | 0 | 10NOV10 | |
| DCGN-FD702 | End Of Work | 0 | | 26FEB11 |
| **Feeding Shed 8** | | | | |
| **Earth Works** | | | | |
| DCCV-FD80` | Excavation | 6 | 10NOV10 | 16NOV10 |
| DCCV-FD815 | Disposal Of Excavated Materials | 15 | 10NOV10 | 27NOV10 |
| DCCV-FD803 | Soil Replacement | 16 | 17NOV10 | 05DEC10 |
| DCCV-FD802 | Filling Around Foundations Up To SOG Level | 7 | 09JAN11 | 16JAN11 |
| **Concrete Works** | | | | |
| *Plain Concrete* | | | | |
| DCCV-FD804 | PC Foundation | 9 | 06DEC10 | 15DEC10 |
| DCCV-FD806 | PC Slab On Grade | 6 | 18JAN11 | 24JAN11 |
| *Reinforced Concrete* | | | | |
| DCCV-FD805 | RC Foundation & Semels | 13 | 16DEC10 | 30DEC10 |
| DCCV-FD808 | RC Columns & Pedestals | 7 | 01JAN11 | 08JAN11 |
| DCCV-FD807 | RC Slab On Grade | 8 | 25JAN11 | 02FEB11 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-FD810 | Water Proofing For Foundations (Cement Slurry) | 4 | 04JAN11 | 08JAN11 |
| DCCV-FD811 | Polyethylene Membrane | 1 | 17JAN11 | 17JAN11 |
| **Electrical** | | | | |
| *Electrical* | | | | |
| DCCV-FD814 | Electrical Works | 20 | 03FEB11 | 26FEB11 |
| **General** | | | | |
| DCGN-FD801 | Start Of Work | 0 | 10NOV10 | |
| DCGN-FD802 | End Of Work | 0 | | 26FEB11 |
| **Checking Building & Kantien** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCCV-CH001 | Excavation | 7 | 01SEP10 | 08SEP10 |
| DCCV-CH035 | Disposal Of Excavated Materials | 10 | 01SEP10 | 12SEP10 |
| DCCV-CH003 | Soil Replacement | 8 | 09SEP10 | 18SEP10 |
| DCCV-CH002 | Filling Around Foundations Up To Ground Level | 7 | 28OCT10 | 04NOV10 |

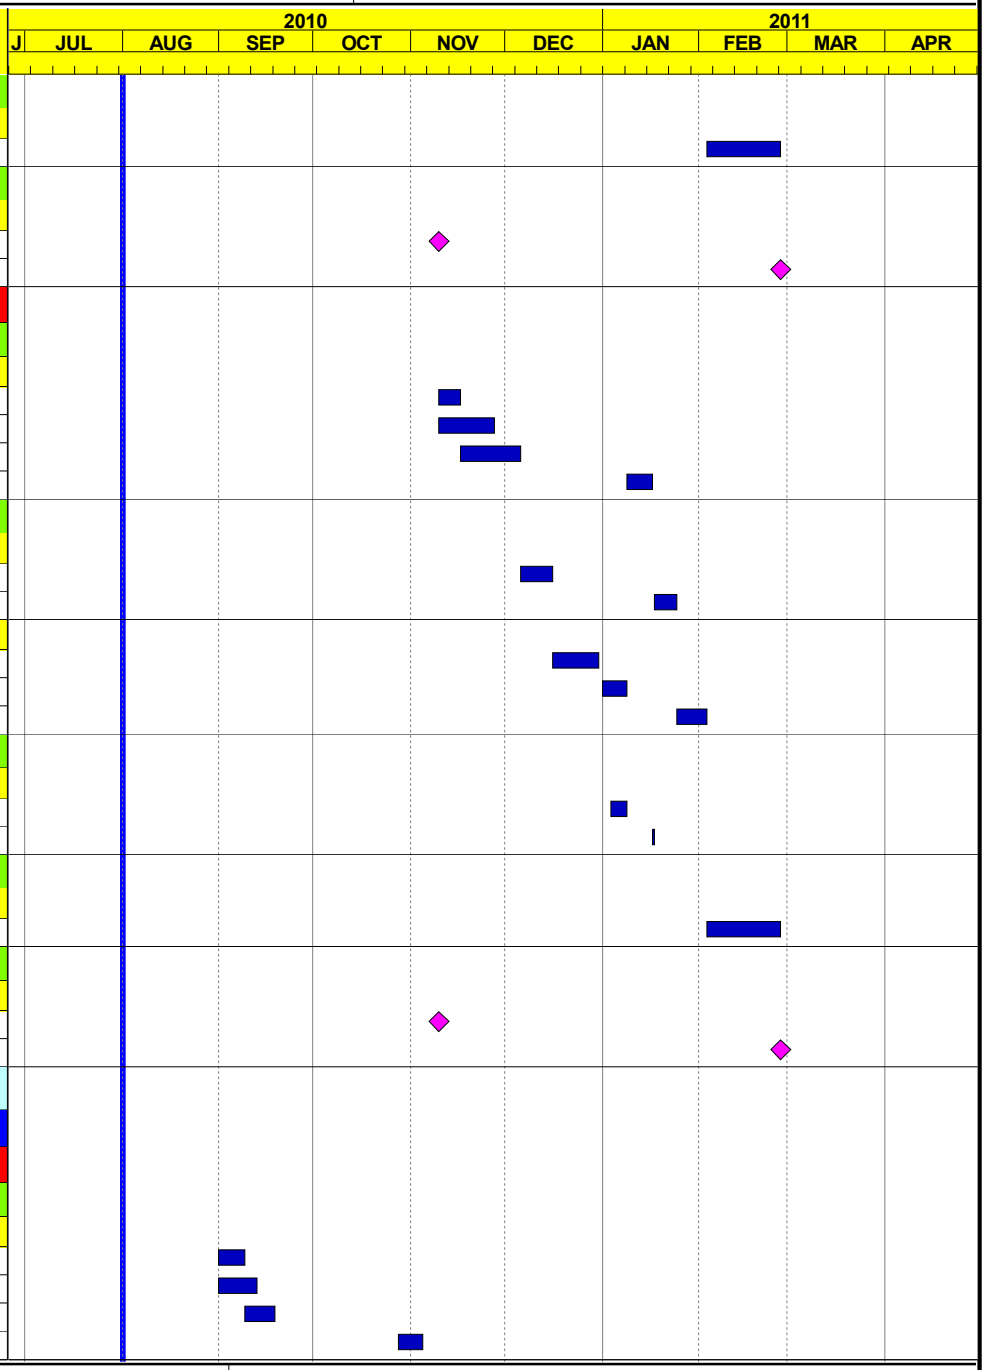


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 14 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Concrete Works** | | | | |
| *Plain Concrete* | | | | |
| DCCV-CH004 | PC Foundation | 10 | 19SEP10 | 29SEP10 |
| DCCV-CH008 | PC Slab On Grade | 6 | 07NOV10 | 13NOV10 |
| *Reinforced Concrete* | | | | |
| DCCV-CH005 | RC Foundation & Semels | 14 | 02OCT10 | 17OCT10 |
| DCCV-CH006 | Columns & Beams | 10 | 18OCT10 | 28OCT10 |
| DCCV-CH007 | RC Slab Slabs | 12 | 30OCT10 | 11NOV10 |
| DCCV-CH033 | RC Slab On Grade | 10 | 27NOV10 | 07DEC10 |
| **Masonary** | | | | |
| DCCV-CH009 | Masonary Works | 18 | 21NOV10 | 11DEC10 |
| **Wood & Plastic** | | | | |
| DCCV-CH010 | MDF Wooden Bench | 1 | 16FEB11 | 16FEB11 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-CH011 | Water Proofing For Foundations (Cement Slurry) | 2 | 26OCT10 | 27OCT10 |
| DCCV-CH021 | Polyethylene Membrane | 1 | 06NOV10 | 06NOV10 |
| DCCV-CH012 | Damp proofing | 4 | 13NOV10 | 16NOV10 |
| DCCV-CH013 | Heat Insulation For Roof | 2 | 17NOV10 | 18NOV10 |
| **Doors & Windows** | | | | |
| DCCV-CH014 | Wooden Doors | 5 | 16FEB11 | 21FEB11 |
| DCCV-CH015 | Aluminum Windows | 5 | 16FEB11 | 21FEB11 |
| **Finishes** | | | | |
| DCCV-CH016 | Internal Plastering | 22 | 12DEC10 | 05JAN11 |
| DCCV-CH017 | External Plastering | 25 | 12DEC10 | 09JAN11 |
| DCCV-CH018 | Wall Tiling For Kitchen & Toilets | 19 | 12DEC10 | 02JAN11 |
| DCCV-CH019 | Flooring For Kitchen & Toilets | 18 | 03JAN11 | 23JAN11 |
| DCCV-CH034 | Flooring | 15 | 06JAN11 | 23JAN11 |
| DCCV-CH022 | External Painting | 22 | 10JAN11 | 03FEB11 |
| DCCV-CH020 | Internal Paiting | 20 | 24JAN11 | 15FEB11 |
| **Specialties** | | | | |
| DCCV-CH023 | Toilet & Bath Accessories | 10 | 24JAN11 | 03FEB11 |
| DCCV-CH024 | Steel Bars For Restaurant | 10 | 16FEB11 | 27FEB11 |
| **Electromechanical Works** | | | | |
| *Fire Fighting* | | | | |
| DCCV-CH030 | Fire Protection | 30 | 12DEC10 | 15JAN11 |
| *HVAC* | | | | |
| DCCV-CH031 | HVAC Works | 30 | 12DEC10 | 15JAN11 |

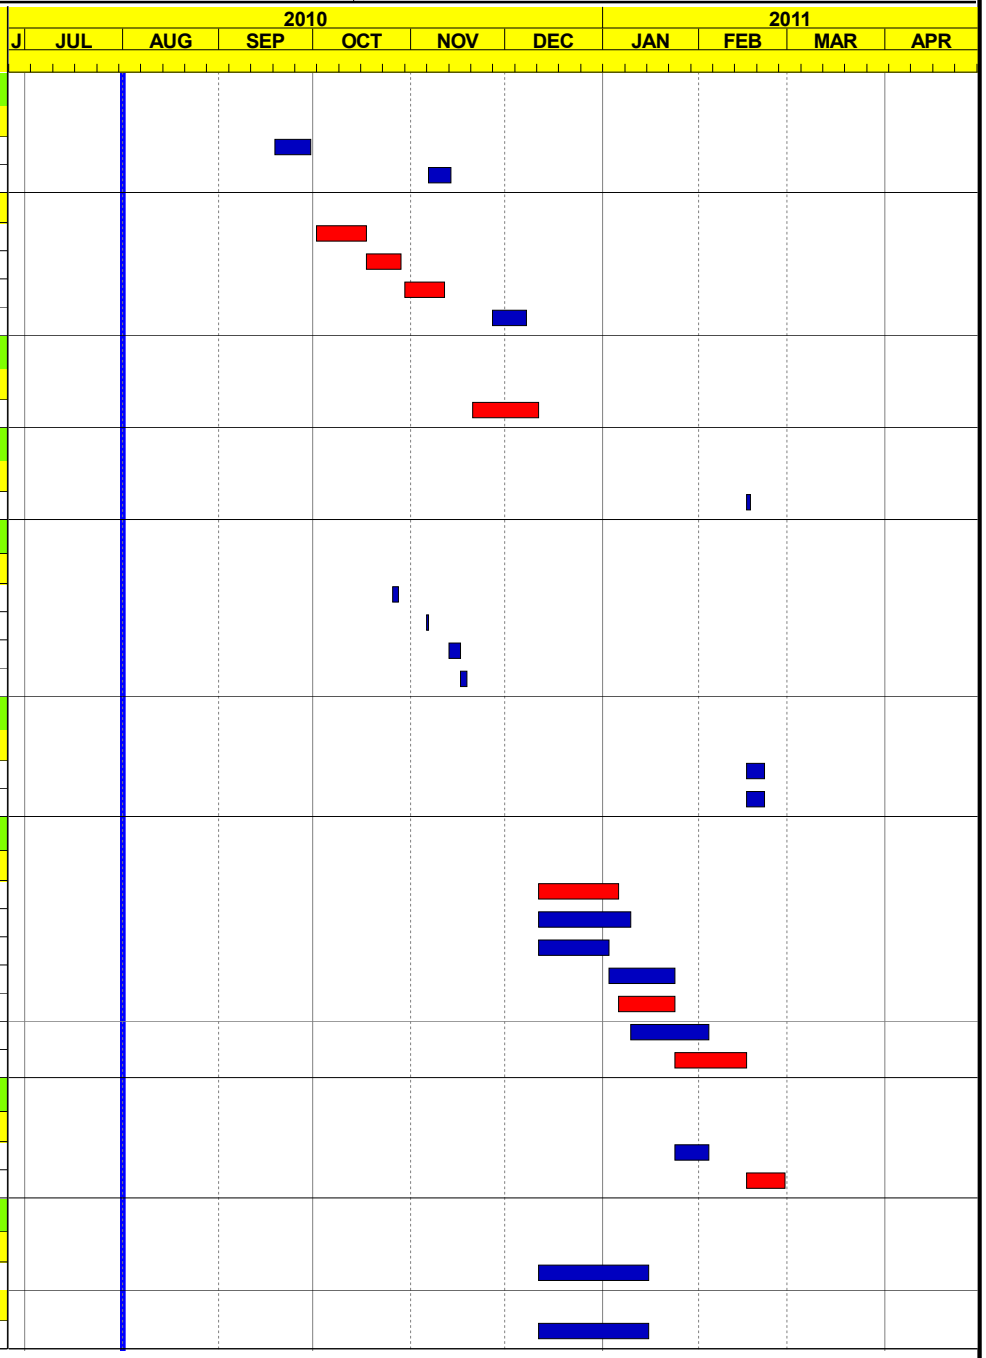


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 15 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama
For Trading & Contracting

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| ***Plumbing*** | | | | |
| DCCV-CH028 | Oil Separator Interceptors | 3 | 01AUG10 | 03AUG10 |
| DCCV-CH026 | Piping Systems (PP) | 6 | 14NOV10 | 20NOV10 |
| DCCV-CH027 | Water & Waste Piping System (UPVC) | 3 | 14NOV10 | 16NOV10 |
| DCCV-CH029 | Roof Storm Water System | 2 | 20NOV10 | 21NOV10 |
| DCCV-CH025 | Plumbing Fixture, Floor Drain & Gully Trap | 5 | 21NOV10 | 25NOV10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-CH032 | Electrical Works | 30 | 12DEC10 | 15JAN11 |
| ***General*** | | | | |
| DCGN-CH001 | Start Of Work | 0 | 01AUG10 | |
| DCGN-CH002 | End Of Work | 0 | | 27FEB11 |
| ***Food Bunk*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-FB001 | Excavation | 9 | 17AUG10 | 26AUG10 |
| DCCV-FB014 | Disposal Of Excavated Materials | 16 | 17AUG10 | 04SEP10 |
| DCCV-FB003 | Soil Replacement | 14 | 28AUG10 | 12SEP10 |
| DCCV-FB002 | Filling Around Foundations Up To SOG Level | 14 | 07NOV10 | 22NOV10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-FB004 | PC Foundation | 12 | 13SEP10 | 26SEP10 |
| DCCV-FB006 | PC Slab On Grade | 7 | 24NOV10 | 01DEC10 |
| ***Reinforced Concrete*** | | | | |
| DCCV-FB005 | RC Foundation & Semels | 15 | 27SEP10 | 13OCT10 |
| DCCV-FB008 | Retaining Walls | 18 | 14OCT10 | 03NOV10 |
| DCCV-FB007 | RC Slab On Grade | 15 | 02DEC10 | 19DEC10 |
| ***Metals*** | | | | |
| DCCV-FB013 | Anchor Bolts | 12 | 21OCT10 | 03NOV10 |
| DCCV-FB009 | Steel Structure For Skeleton | 14 | 04NOV10 | 20NOV10 |
| DCCV-FB010 | Cladding | 25 | 21NOV10 | 19DEC10 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-FB011 | Water Proofing For Foundations (Cement Slurry) | 2 | 04NOV10 | 06NOV10 |
| DCCV-FB012 | Polyethylene Membrane | 1 | 23NOV10 | 23NOV10 |
| ***Finishes*** | | | | |
| DCAR-FB001 | External Plastering For Walls | 8 | 21NOV10 | 29NOV10 |
| DCAR-FB002 | External Painting For Walls | 8 | 30NOV10 | 08DEC10 |

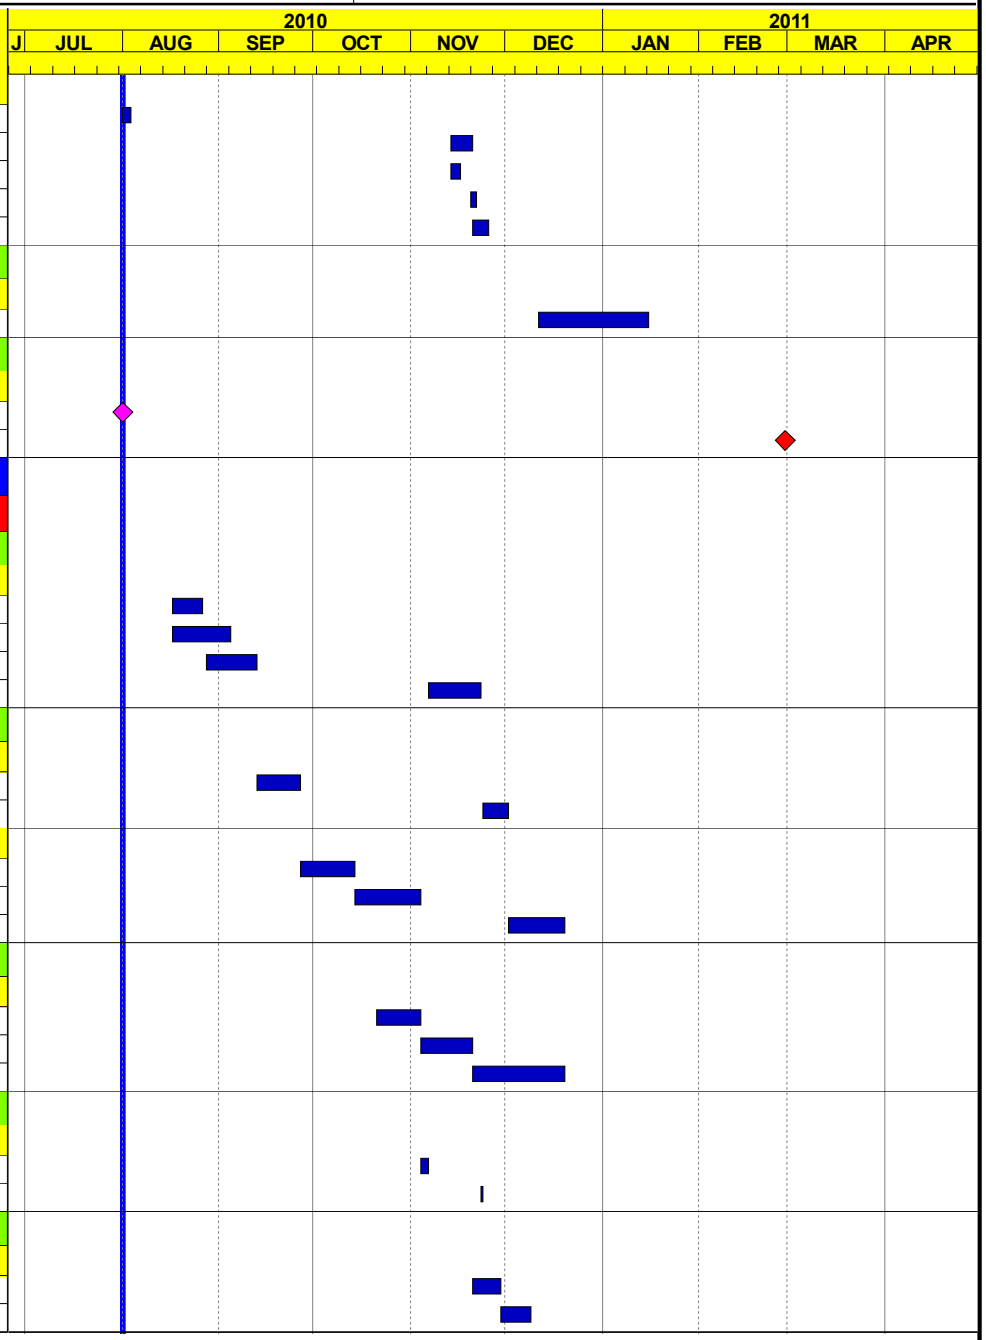


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 16 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCMC-FB014 | Electrical Works | 14 | 21NOV10 | 06DEC10 |
| ***General*** | | | | |
| ***Electrical*** | | | | |
| DCGN-FB001 | Start Of Work | 0 | 17AUG10 | |
| DCGN-FB002 | End Of Work | 0 | | 19DEC10 |
| ***Food Storage Tank*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-MT001 | Excavation | 8 | 29AUG10 | 06SEP10 |
| DCCV-MT017 | Disposal Of Excavated Materials | 12 | 29AUG10 | 11SEP10 |
| DCCV-MT003 | Soil Replacement | 9 | 07SEP10 | 16SEP10 |
| DCCV-MT002 | Filling Around Foundations Up To SOG Level | 5 | 19OCT10 | 24OCT10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-MT004 | PC Foundation | 5 | 18SEP10 | 22SEP10 |
| DCCV-MT006 | PC Slab On Grade | 4 | 25OCT10 | 28OCT10 |
| ***Reinforced Concrete*** | | | | |
| DCCV-MT005 | RC Foundation & Semels | 8 | 07OCT10 | 16OCT10 |
| DCCV-MT008 | Retaining Walls | 10 | 17OCT10 | 27OCT10 |
| DCCV-MT009 | RC Slab | 8 | 28OCT10 | 06NOV10 |
| DCCV-MT007 | RC Slab On Grade | 6 | 07NOV10 | 13NOV10 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-MT011 | Water Proofing For Foundations (Cement Slurry) | 2 | 17OCT10 | 18OCT10 |
| DCCV-MT012 | Polyethylene Membrane | 1 | 25OCT10 | 25OCT10 |
| DCCV-MT013 | Damp Proofing | 3 | 07NOV10 | 09NOV10 |
| DCCV-MT014 | Heat Insulation For Roof | 2 | 10NOV10 | 11NOV10 |
| ***Doors & Windows*** | | | | |
| DCCV-MT010 | Steel Ladder | 1 | 24NOV10 | 24NOV10 |
| DCCV-MT015 | Steel Doors | 2 | 24NOV10 | 25NOV10 |
| DCCV-MT016 | Steel Access Doors | 2 | 24NOV10 | 25NOV10 |
| ***Finishes*** | | | | |
| DCAR-MT001 | External Plastering For Walls | 10 | 13NOV10 | 23NOV10 |
| DCAR-MT002 | External Painting For Walls | 10 | 24NOV10 | 05DEC10 |
| ***General*** | | | | |
| DCGN-MT001 | Start Of Work | 0 | 29AUG10 | |

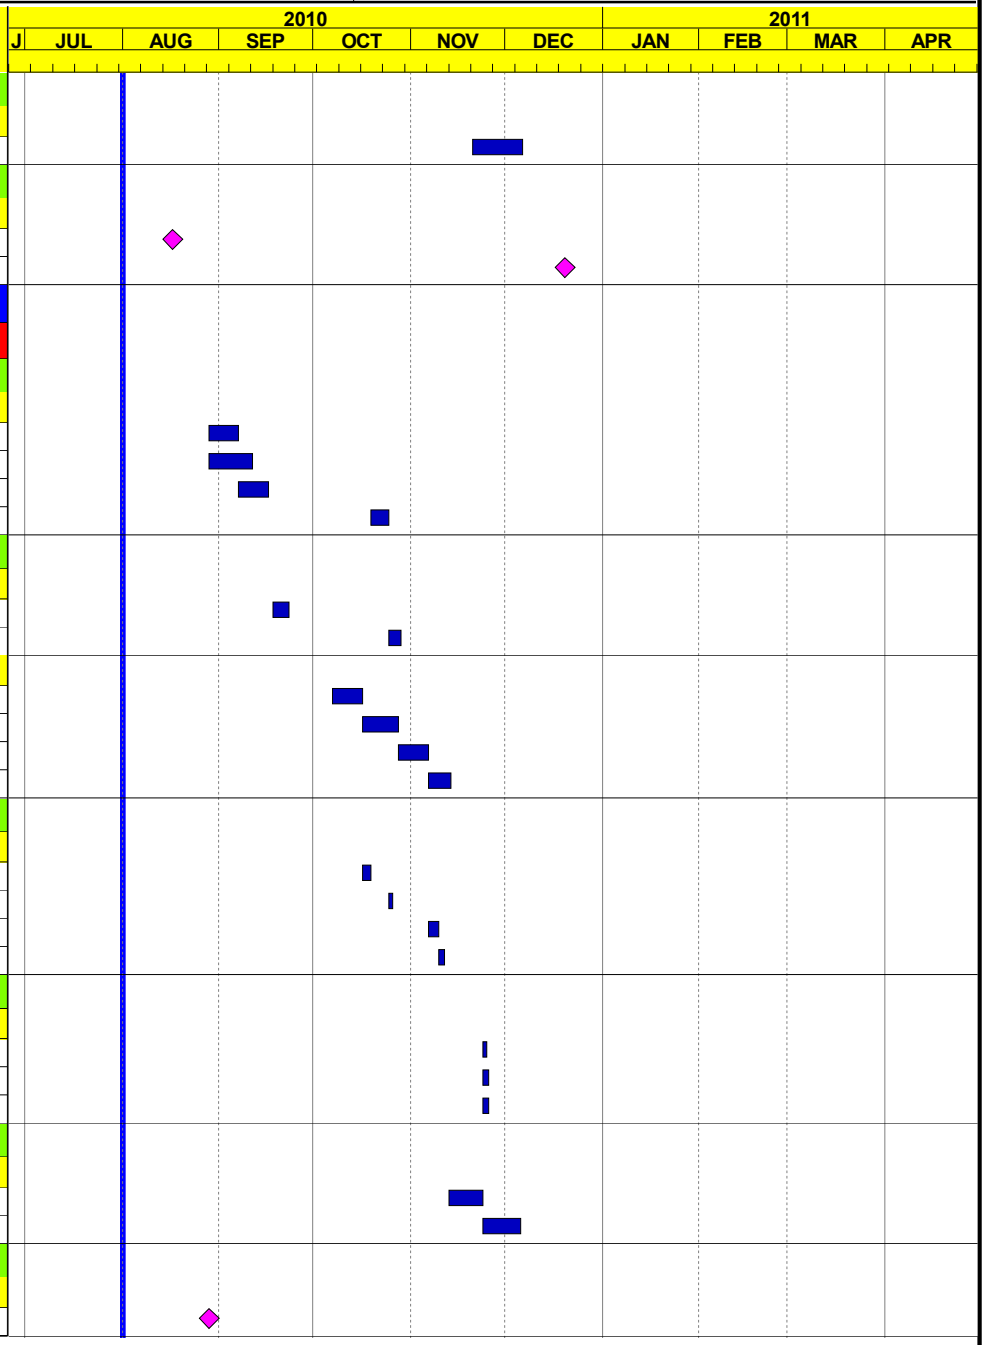


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 17 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCGN-MT002 | End Of Work | 0 | | 05DEC10 |
| **Hospital** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCCV-HS001 | Excavation | 10 | 24AUG10 | 04SEP10 |
| DCCV-HS018 | Disposal Of Excavated Materials | 16 | 24AUG10 | 11SEP10 |
| DCCV-HS003 | Soil Replacement | 8 | 05SEP10 | 13SEP10 |
| DCCV-HS002 | Filling Around Foundations Up To SOG Level | 5 | 14OCT10 | 19OCT10 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-HS004 | PC Foundation | 8 | 14SEP10 | 22SEP10 |
| DCCV-HS006 | PC Slab On Grade | 6 | 21OCT10 | 27OCT10 |
| **Reinforced Concrete** | | | | |
| DCCV-HS005 | RC Foundation & Semels | 7 | 23SEP10 | 30SEP10 |
| DCCV-HS008 | RC Columns & Pedestals | 6 | 02OCT10 | 07OCT10 |
| DCCV-HS009 | RC For Pit (Walls & Floors) | 7 | 02OCT10 | 09OCT10 |
| DCCV-HS007 | RC Slab On Grade | 8 | 28OCT10 | 06NOV10 |
| **Metals** | | | | |
| DCCV-HS017 | Anchor Bolts | 10 | 27SEP10 | 07OCT10 |
| DCCV-HS010 | Steel Structure For Skeleton | 5 | 20OCT10 | 25OCT10 |
| DCCV-HS012 | Galvanized Steel Sandwish Pannel For Walls | 3 | 26OCT10 | 28OCT10 |
| DCCV-HS011 | Cladding | 11 | 30OCT10 | 10NOV10 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-HS013 | Water Proofing For Foundations (Cement Slurry) | 4 | 10OCT10 | 13OCT10 |
| DCCV-HS014 | Polyethylene Membrane | 1 | 20OCT10 | 20OCT10 |
| **Finishes** | | | | |
| DCCV-HS015 | External Plastering For Walls | 8 | 26OCT10 | 03NOV10 |
| DCCV-HS016 | External Painting For Walls | 8 | 26OCT10 | 03NOV10 |
| **Electromechanical Works** | | | | |
| **Plumbing** | | | | |
| DCMC-HS002 | Piping Systems | 8 | 26OCT10 | 03NOV10 |
| DCMC-HS001 | Plumbing Fixture | 6 | 04NOV10 | 10NOV10 |
| DCMC-HS003 | Submersible Pump | 3 | 11NOV10 | 14NOV10 |
| DCMC-HS004 | Trench Drain | 3 | 11NOV10 | 14NOV10 |
| **Electrical** | | | | |
| **Electrical** | | | | |
| DCMC-HS005 | Electrical Works | 20 | 26OCT10 | 17NOV10 |

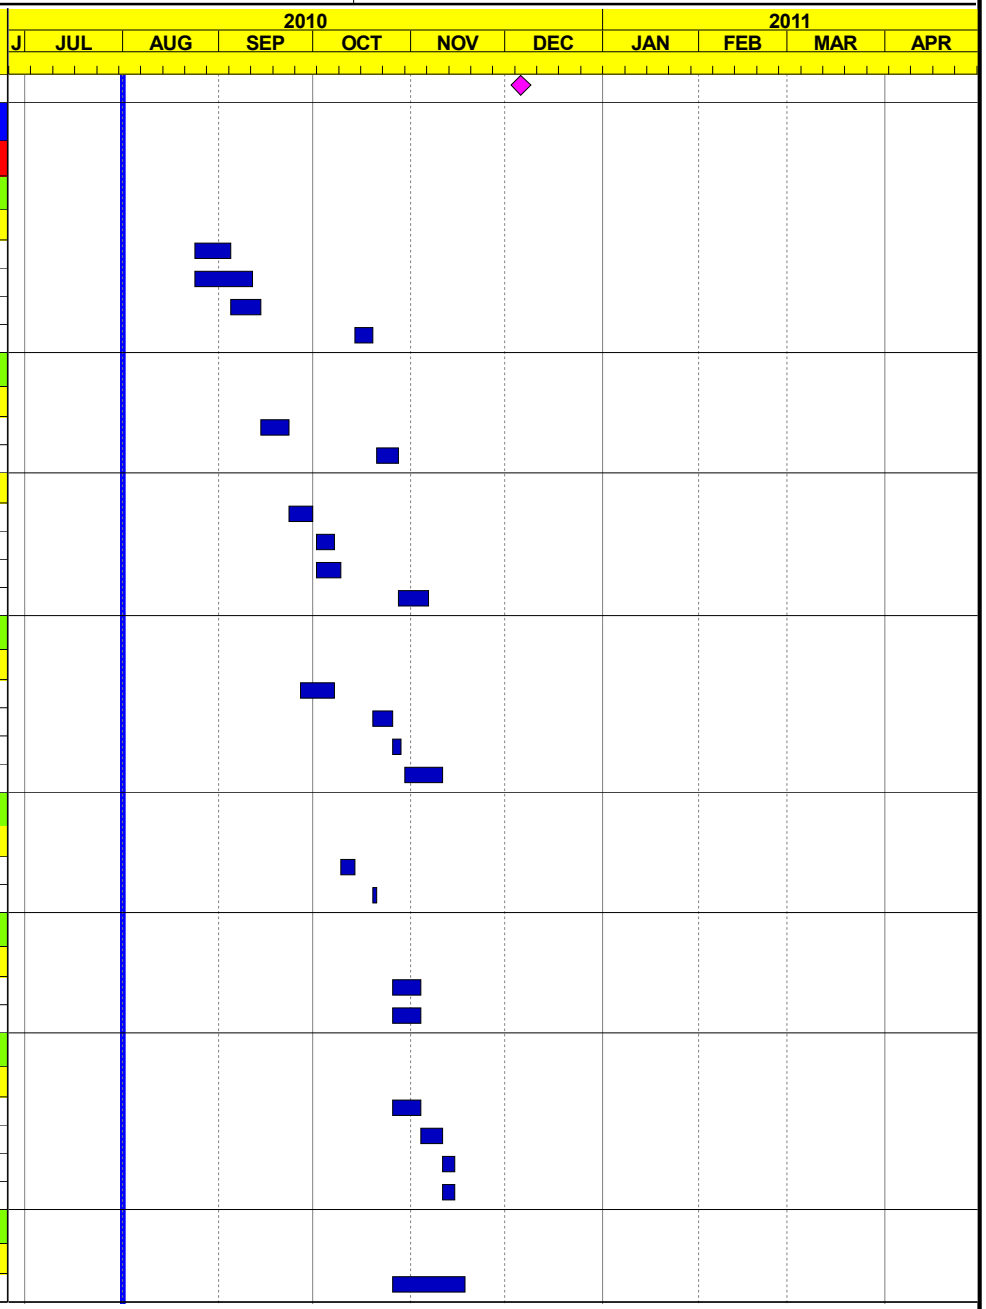


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 18 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **General** | | | | |
| DCGN-HS001 | Start Of Work | 0 | 24AUG10 | |
| DCGN-HS002 | End Of Works | 0 | | 17NOV10 |
| **Milking Parlor** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCCV-MP001 | Excavation | 10 | 21AUG10 | 31AUG10 |
| DCCV-MP011 | Disposal Of Excavated Materials | 15 | 21AUG10 | 06SEP10 |
| DCCV-MP003 | Soil Replacement | 12 | 01SEP10 | 14SEP10 |
| DCCV-MP002 | Filling Around Foundations Up To SOG Level | 10 | 14OCT10 | 25OCT10 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-MP004 | PC Foundation | 6 | 15SEP10 | 21SEP10 |
| DCCV-MP006 | PC Slab On Grade | 5 | 27OCT10 | 01NOV10 |
| **Reinforced Concrete** | | | | |
| DCCV-MP005 | RC Foundation & Semels | 10 | 22SEP10 | 03OCT10 |
| DCCV-MP009 | RC Columns & Pedestals | 12 | 04OCT10 | 17OCT10 |
| DCCV-MP008 | RC For Pit (Walls & Floors) | 12 | 18OCT10 | 31OCT10 |
| DCCV-MP010 | RC For Staircases | 5 | 01NOV10 | 06NOV10 |
| DCCV-MP007 | RC Slab On Grade | 8 | 15NOV10 | 23NOV10 |
| **Masonary** | | | | |
| DCAR-MP011 | Masonary For Walls | 18 | 13OCT10 | 02NOV10 |
| **Metals** | | | | |
| DCCV-MP017 | Anchor Bolts | 12 | 04OCT10 | 17OCT10 |
| DCCV-MP012 | Steel Structure For Skeleton | 18 | 18OCT10 | 07NOV10 |
| DCCV-MP013 | Cladding | 20 | 08NOV10 | 30NOV10 |
| DCCV-MP014 | Galvanized Steel Sandwish Pannel | 10 | 01DEC10 | 12DEC10 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-MP015 | Water Proofing For Foundations (Cement Slurry) | 4 | 10OCT10 | 13OCT10 |
| DCCV-MP016 | Polyethylene Membrane | 1 | 26OCT10 | 26OCT10 |
| **Doors & Windows** | | | | |
| DCAR-MP017 | Steel Doors | 2 | 05DEC10 | 06DEC10 |
| DCAR-MP018 | Wooden Doors | 2 | 05DEC10 | 06DEC10 |
| DCAR-MP019 | Aluminum Windows | 2 | 05DEC10 | 06DEC10 |

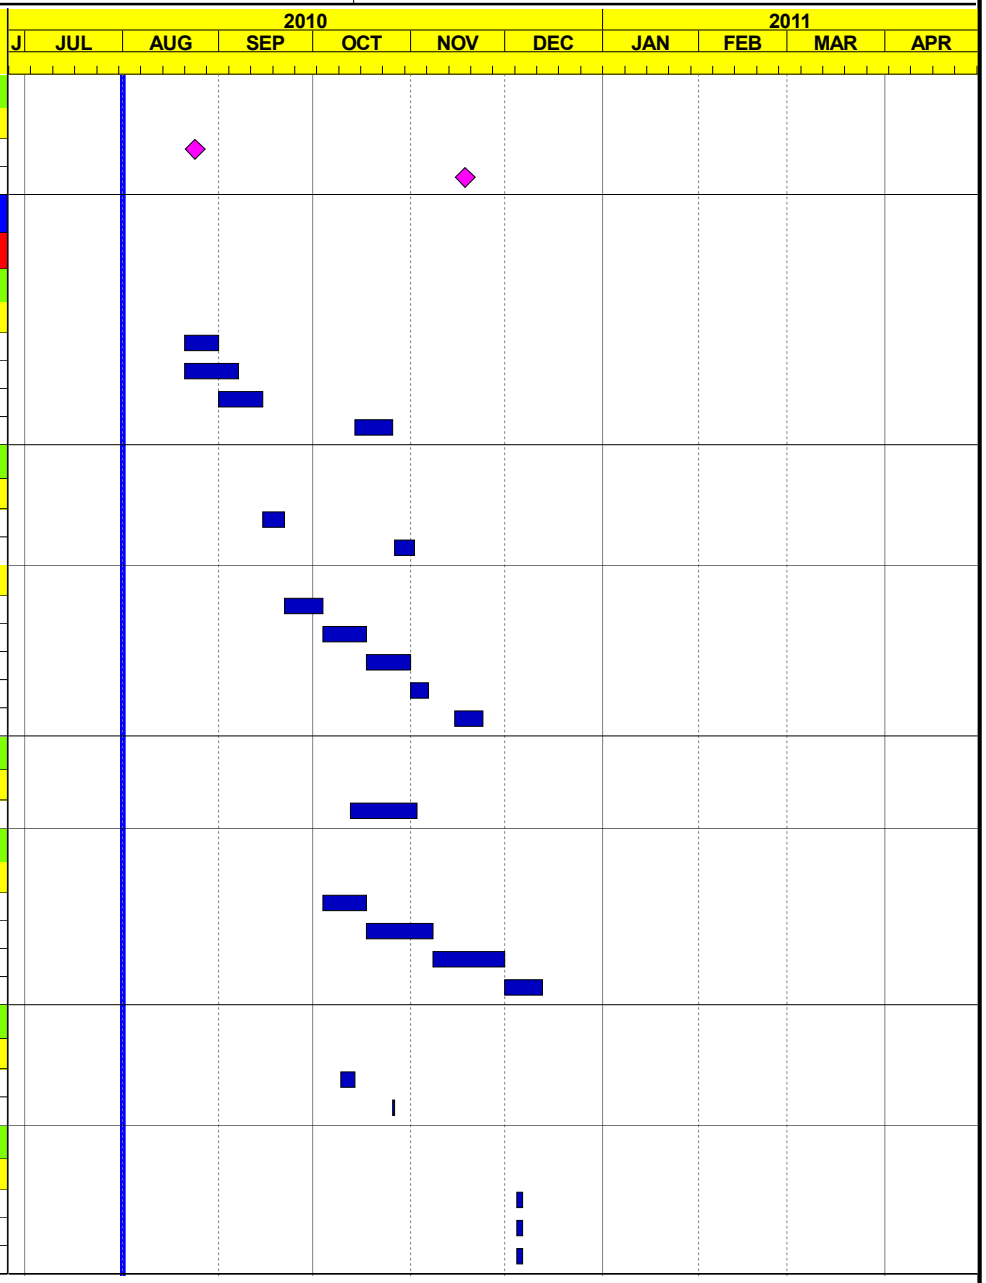


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 19 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Finishes** | | | | |
| DCAR-MP020 | Internal Plastering For Walls | 12 | 03NOV10 | 16NOV10 |
| DCAR-MP021 | External Plastering For Walls | 12 | 03NOV10 | 16NOV10 |
| DCAR-MP023 | Flooring | 7 | 17NOV10 | 24NOV10 |
| DCAR-MP026 | External Painting For Walls | 8 | 17NOV10 | 25NOV10 |
| DCAR-MP025 | Internal Painting For Walls | 8 | 25NOV10 | 04DEC10 |
| DCAR-MP022 | Wall Tiles | 4 | 05DEC10 | 08DEC10 |
| DCAR-MP024 | Tiles For Stairs | 3 | 09DEC10 | 12DEC10 |
| **Specialties** | | | | |
| DCAR-MP027 | Toilet & Bath Accessories | 2 | 05DEC10 | 06DEC10 |
| DCAR-MP028 | Kitchen Vanity Top | 2 | 07DEC10 | 08DEC10 |
| **Electromechanical Works** | | | | |
| ***Fire Fighting*** | | | | |
| DCMC-MP042 | Fire Protection System | 18 | 13DEC10 | 02JAN11 |
| ***HVAC*** | | | | |
| DCMC-MP041 | HVAC Works | 18 | 13DEC10 | 02JAN11 |
| ***Plumbing*** | | | | |
| DCMC-MP030 | Piping Systems (PP) | 5 | 02NOV10 | 07NOV10 |
| DCMC-MP032 | Water & Waste Piping System (UPVC) | 5 | 02NOV10 | 07NOV10 |
| DCMC-MP029 | Plumbing Fixture, Floor Drain & Gully Trap | 6 | 08NOV10 | 14NOV10 |
| DCMC-MP039 | Stainless Steel Submersible Pump | 3 | 24NOV10 | 27NOV10 |
| DCMC-MP040 | Stainless Steel Trench Drain | 2 | 24NOV10 | 25NOV10 |
| DCMC-MP035 | Inspection Chamber | 3 | 28NOV10 | 30NOV10 |
| DCMC-MP031 | Stainless Steel Piping System | 1 | 05DEC10 | 05DEC10 |
| **Electrical** | | | | |
| ***Electrical*** | | | | |
| DCMC-MP043 | Electrical Works | 18 | 13DEC10 | 02JAN11 |
| **General** | | | | |
| DCGN-MP001 | Start Of Work | 0 | 21AUG10 | |
| DCGN-MP002 | End Of Work | 0 | | 02JAN11 |
| **Security Building** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCCV-SC001 | Excavation | 9 | 13OCT10 | 23OCT10 |
| DCCV-SC017 | Disposal Of Excavated Materials | 15 | 13OCT10 | 30OCT10 |
| DCCV-SC003 | Soil Replacement | 12 | 24OCT10 | 06NOV10 |
| DCCV-SC002 | Filling Around Foundations Up To SOG Level | 10 | 16DEC10 | 27DEC10 |

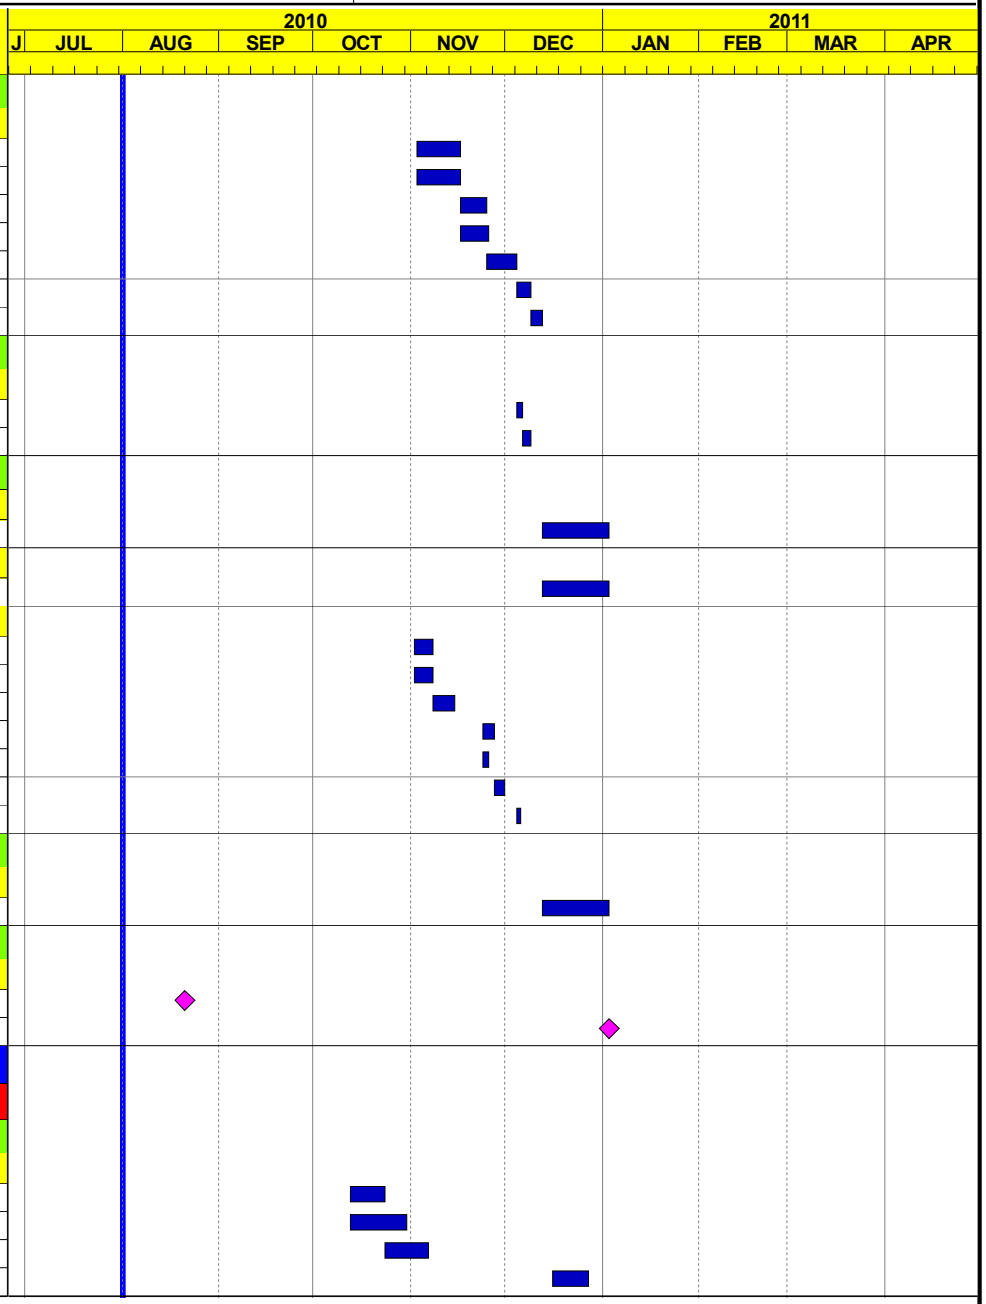


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 20 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Concrete Works** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-SC004 | PC Foundation | 7 | 07NOV10 | 14NOV10 |
| DCCV-SC006 | PC Slab On Grade | 4 | 29DEC10 | 02JAN11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-SC005 | RC Foundation & Semels | 5 | 28NOV10 | 02DEC10 |
| DCCV-SC008 | RC Columns & Beams | 4 | 04DEC10 | 07DEC10 |
| DCCV-SC009 | RC Solid Slabs | 4 | 08DEC10 | 12DEC10 |
| DCCV-SC007 | RC Slab On Grade | 5 | 03JAN11 | 08JAN11 |
| **Masonary** | | | | |
| DCCV-SC010 | Masonary For Walls | 8 | 19DEC10 | 27DEC10 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-SC013 | Damp Proofing | 4 | 13DEC10 | 16DEC10 |
| DCCV-SC011 | Water Proofing For Foundations (Cement Slurry) | 2 | 14DEC10 | 15DEC10 |
| DCCV-SC014 | Heat Insulation For Roof | 2 | 18DEC10 | 19DEC10 |
| DCCV-SC012 | Polyethylene Membrane | 1 | 28DEC10 | 28DEC10 |
| **Doors & Windows** | | | | |
| DCCV-SC015 | Wooden Doors | 2 | 06FEB11 | 07FEB11 |
| DCCV-SC016 | Aluminum Wndows | 2 | 06FEB11 | 07FEB11 |
| **Finishes** | | | | |
| DCAC-SC020 | Wall Tiles For Toilets | 5 | 18DEC10 | 22DEC10 |
| DCAC-SC028 | Flooring For Toilets | 4 | 18DEC10 | 21DEC10 |
| DCAC-SC023 | Roof Flooring | 2 | 20DEC10 | 21DEC10 |
| DCAC-SC024 | Stone Cladding For External Wainscot | 2 | 22DEC10 | 23DEC10 |
| DCAC-SC017 | Internal Plastering For Walls & Ceiling | 12 | 28DEC10 | 10JAN11 |
| DCAC-SC019 | External Plastering For Walls | 12 | 28DEC10 | 10JAN11 |
| DCAC-SC021 | Flooring | 7 | 11JAN11 | 18JAN11 |
| DCAC-SC022 | Marble & Granite For stairs | 6 | 11JAN11 | 17JAN11 |
| DCAC-SC026 | External Painting For Walls | 15 | 11JAN11 | 27JAN11 |
| DCAC-SC025 | Internal Painting For entrance & Security Area | 15 | 19JAN11 | 05FEB11 |
| **Specialties** | | | | |
| DCAC-SC027 | Toilet & Bath Accessories | 3 | 06FEB11 | 08FEB11 |
| **Electromechanical Works** | | | | |
| ***Fire Fighting*** | | | | |
| DCMC-SC037 | Fire Fighting System | 30 | 28DEC10 | 31JAN11 |
| ***HVAC*** | | | | |
| DCMC-SC036 | HVAC Works | 30 | 28DEC10 | 31JAN11 |

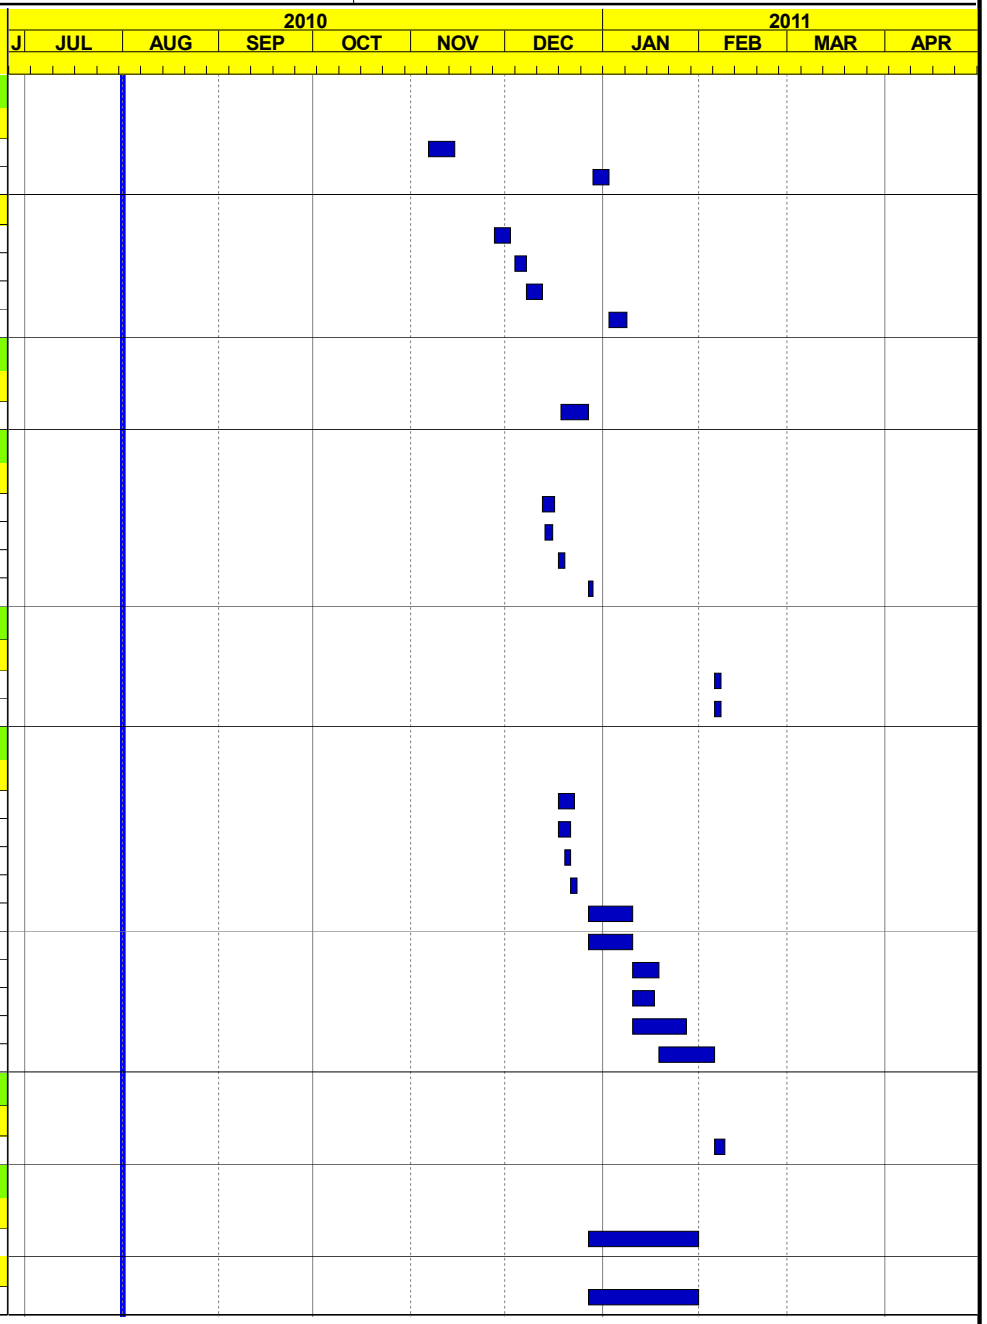


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 21 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama For Trading & Contracting

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| ***Plumbing*** | | | | |
| DCMC-SC029 | Piping Systems (PP) | 6 | 15NOV10 | 21NOV10 |
| DCMC-SC031 | Water & Waste Piping System (UPVC) | 3 | 15NOV10 | 17NOV10 |
| DCMC-SC028 | Plumbing Fixture, Floor Drain & Gully Trap | 5 | 22NOV10 | 27NOV10 |
| DCMC-SC035 | Roof Storm Water System | 2 | 22DEC10 | 23DEC10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCMC-SC038 | Electrical Works | 30 | 28DEC10 | 31JAN11 |
| ***General*** | | | | |
| DCGN-SC001 | Start Of Work | 0 | 13OCT10 | |
| DCGN-SC002 | End Of Work | 0 | | 08FEB11 |
| ***Social Building*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-SO001 | Excavation | 10 | 05SEP10 | 15SEP10 |
| DCCV-SO019 | Disposal Of Excavated Materials | 15 | 05SEP10 | 21SEP10 |
| DCCV-SO003 | Soil Replacement | 12 | 16SEP10 | 29SEP10 |
| DCCV-SO002 | Filling Around Foundations Up To SOG Level | 10 | 14NOV10 | 24NOV10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-SO004 | PC Foundation | 10 | 30SEP10 | 11OCT10 |
| DCCV-SO006 | PC Slab On Grade | 6 | 27NOV10 | 02DEC10 |
| ***Reinforced Concrete*** | | | | |
| DCCV-SO005 | RC Foundation & Semels | 13 | 18OCT10 | 01NOV10 |
| DCCV-SO008 | RC Columns & Beams | 12 | 02NOV10 | 15NOV10 |
| DCCV-SO009 | RC Solid Slabs | 15 | 16NOV10 | 02DEC10 |
| DCCV-SO007 | RC Slab On Grade | 14 | 04DEC10 | 19DEC10 |
| ***Masonary*** | | | | |
| DCCV-SO010 | Masonary for Walls | 16 | 09DEC10 | 27DEC10 |
| ***Metals*** | | | | |
| DCCV-SO011 | Steel Ladder | 1 | 01FEB11 | 01FEB11 |
| ***Wood & Plastic*** | | | | |
| DCCV-SO012 | MDF Wooden Base For Prayer Room | 1 | 02FEB11 | 02FEB11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-SO013 | Water Proofing For Foundations (Cement Slurry) | 4 | 09NOV10 | 13NOV10 |
| DCCV-SO014 | Polyethylene Membrane | 1 | 25NOV10 | 25NOV10 |

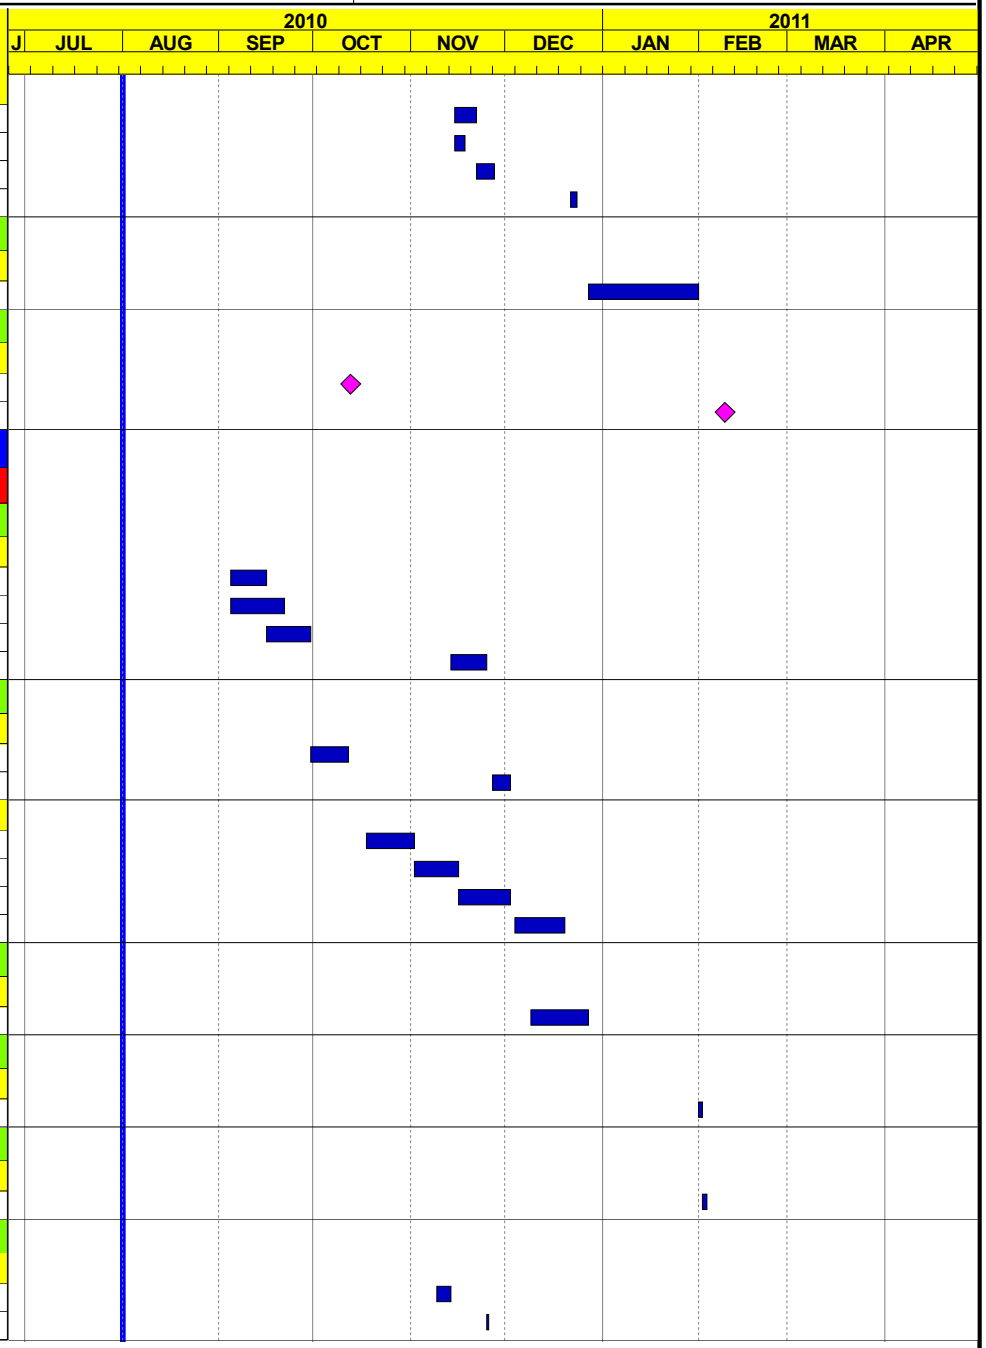


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 22 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCCV-SO015 | Damp Proofing | 3 | 13DEC10 | 15DEC10 |
| DCCV-SO016 | Heat Insulation For Roof | 1 | 16DEC10 | 16DEC10 |
| ***Doors & Windows*** | | | | |
| DCCV-SO017 | Wooden Doors | 2 | 01FEB11 | 02FEB11 |
| DCCV-SO018 | Aluminum Windows | 2 | 01FEB11 | 02FEB11 |
| ***Finishes*** | | | | |
| DCAR-SO020 | Wall Tiles For Kitchen & Toilets | 7 | 16DEC10 | 23DEC10 |
| DCAR-SO023 | Roof Flooring | 10 | 18DEC10 | 28DEC10 |
| DCAR-SO019 | Internal Plastering For Walls & ceiling | 14 | 28DEC10 | 12JAN11 |
| DCAR-SO024 | Stone Cladding For Waincost | 7 | 29DEC10 | 05JAN11 |
| DCAR-SO029 | External Plastering For Walls | 12 | 09JAN11 | 22JAN11 |
| DCAR-SO021 | Floor Tiles | 7 | 13JAN11 | 20JAN11 |
| DCAR-SO022 | Marble & Granite For Stairs & Ramp | 6 | 13JAN11 | 19JAN11 |
| DCAR-SO026 | Internal Painting For Walls & Ceileng | 10 | 22JAN11 | 01FEB11 |
| DCAR-SO027 | External Painting | 8 | 23JAN11 | 31JAN11 |
| DCAR-SO025 | Gypsum Tiles Ceiling | 6 | 02FEB11 | 08FEB11 |
| ***Specialties*** | | | | |
| DCAR-SO028 | Toilet & Bath Accessories | 1 | 02FEB11 | 02FEB11 |
| ***Electromechanical Works*** | | | | |
| ***Fire Fighting*** | | | | |
| DCMC-SO038 | Fire Fighting System | 30 | 28DEC10 | 31JAN11 |
| ***HVAC*** | | | | |
| DCMC-SO039 | HVAC Works | 30 | 28DEC10 | 31JAN11 |
| ***Plumbing*** | | | | |
| DCMC-SO030 | Piping Systems (PP) | 3 | 12OCT10 | 14OCT10 |
| DCMC-SO032 | Water & Waste Piping System (UPVC) | 3 | 12OCT10 | 14OCT10 |
| DCMC-SO029 | Plumbing Fixture, Floor Drain & Gully Trap | 2 | 16OCT10 | 17OCT10 |
| DCMC-SO037 | Roof Storm Water System | 2 | 29DEC10 | 30DEC10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCMC-SO040 | Electrical Works | 30 | 28DEC10 | 31JAN11 |
| ***General*** | | | | |
| DCGN-SO001 | Start Of Work | 0 | 05SEP10 | |
| DCGN-SO002 | End Of Work | 0 | | 08FEB11 |
| ***Silage Bunk*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-SB001 | Excavation | 12 | 21AUG10 | 02SEP10 |

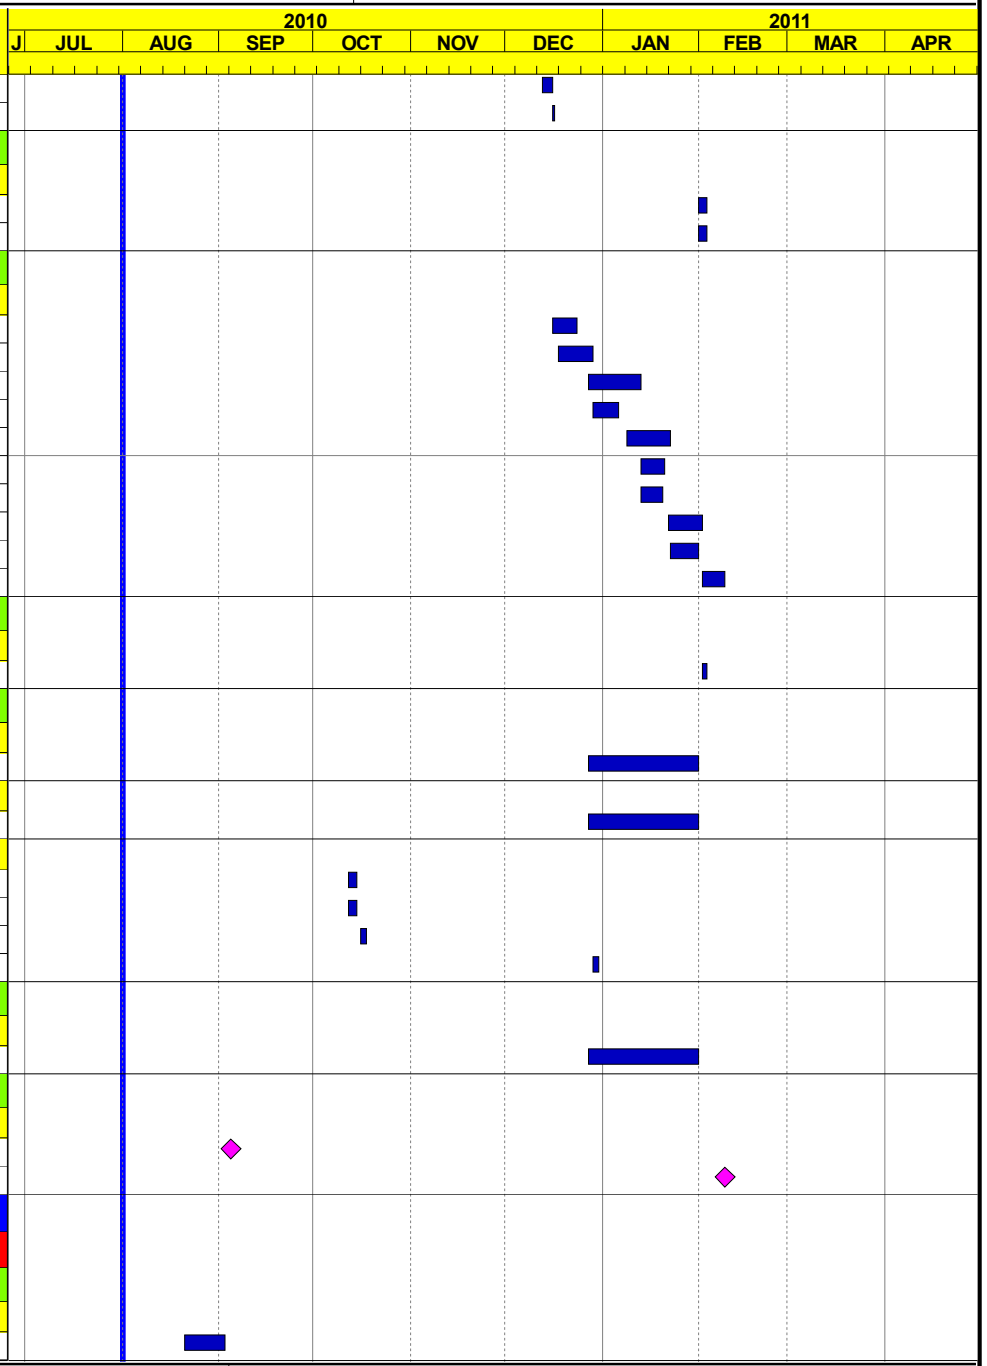


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 23 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama For Trading & Contracting

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCCV-SB012 | Disposal Of Excavated Materials | 23 | 22AUG10 | 16SEP10 |
| DCCV-SB003 | Soil Replacement | 18 | 04SEP10 | 23SEP10 |
| DCCV-SB002 | Filling Around Foundations Up To SOG Level | 13 | 12DEC10 | 26DEC10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-SB004 | PC Foundation | 17 | 25SEP10 | 13OCT10 |
| DCCV-SB006 | PC Slab On Grade | 14 | 27DEC10 | 11JAN11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-SB005 | RC For Strap Footings | 18 | 14OCT10 | 03NOV10 |
| DCCV-SB008 | Retaining Walls | 22 | 04NOV10 | 29NOV10 |
| DCCV-SB007 | RC Slab On Grade | 18 | 12JAN11 | 01FEB11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-SB011 | Expansion Joints For Walls | 5 | 30NOV10 | 05DEC10 |
| DCCV-SB009 | Water Proofing For Foundations (Cement Slurry) | 5 | 06DEC10 | 11DEC10 |
| DCCV-SB010 | Polyethylene Membrane | 1 | 27DEC10 | 27DEC10 |
| ***General*** | | | | |
| DCGN-SB001 | Start Of Work | 0 | 21AUG10 | |
| DCGN-SB002 | End Of Work | 0 | | 01FEB11 |
| ***Weight Building*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-WB001 | Excavation | 10 | 19OCT10 | 30OCT10 |
| DCCV-WB017 | Disposal Of Excavated Materials | 15 | 19OCT10 | 04NOV10 |
| DCCV-WB003 | Soil Replacement | 12 | 31OCT10 | 13NOV10 |
| DCCV-WB002 | Filling Around Foundations Up To SOG Level | 11 | 26DEC10 | 06JAN11 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-WB004 | PC Foundation | 7 | 14NOV10 | 21NOV10 |
| DCCV-WB006 | PC Slab On Grade | 5 | 09JAN11 | 13JAN11 |
| ***Reinforced Concrete*** | | | | |
| DCCV-WB005 | RC Foundation & Semels | 13 | 22NOV10 | 06DEC10 |
| DCCV-WB008 | RC Columns & Beams | 9 | 07DEC10 | 16DEC10 |
| DCCV-WB009 | RC Solid Slabs | 13 | 18DEC10 | 01JAN11 |
| DCCV-WB007 | RC Slab On Grade | 10 | 15JAN11 | 25JAN11 |
| ***Masonary*** | | | | |
| DCCV-WB010 | Masonary for Walls | 17 | 02JAN11 | 20JAN11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-WB011 | Water Proofing For Foundations (Cement Slurry) | 2 | 23DEC10 | 25DEC10 |

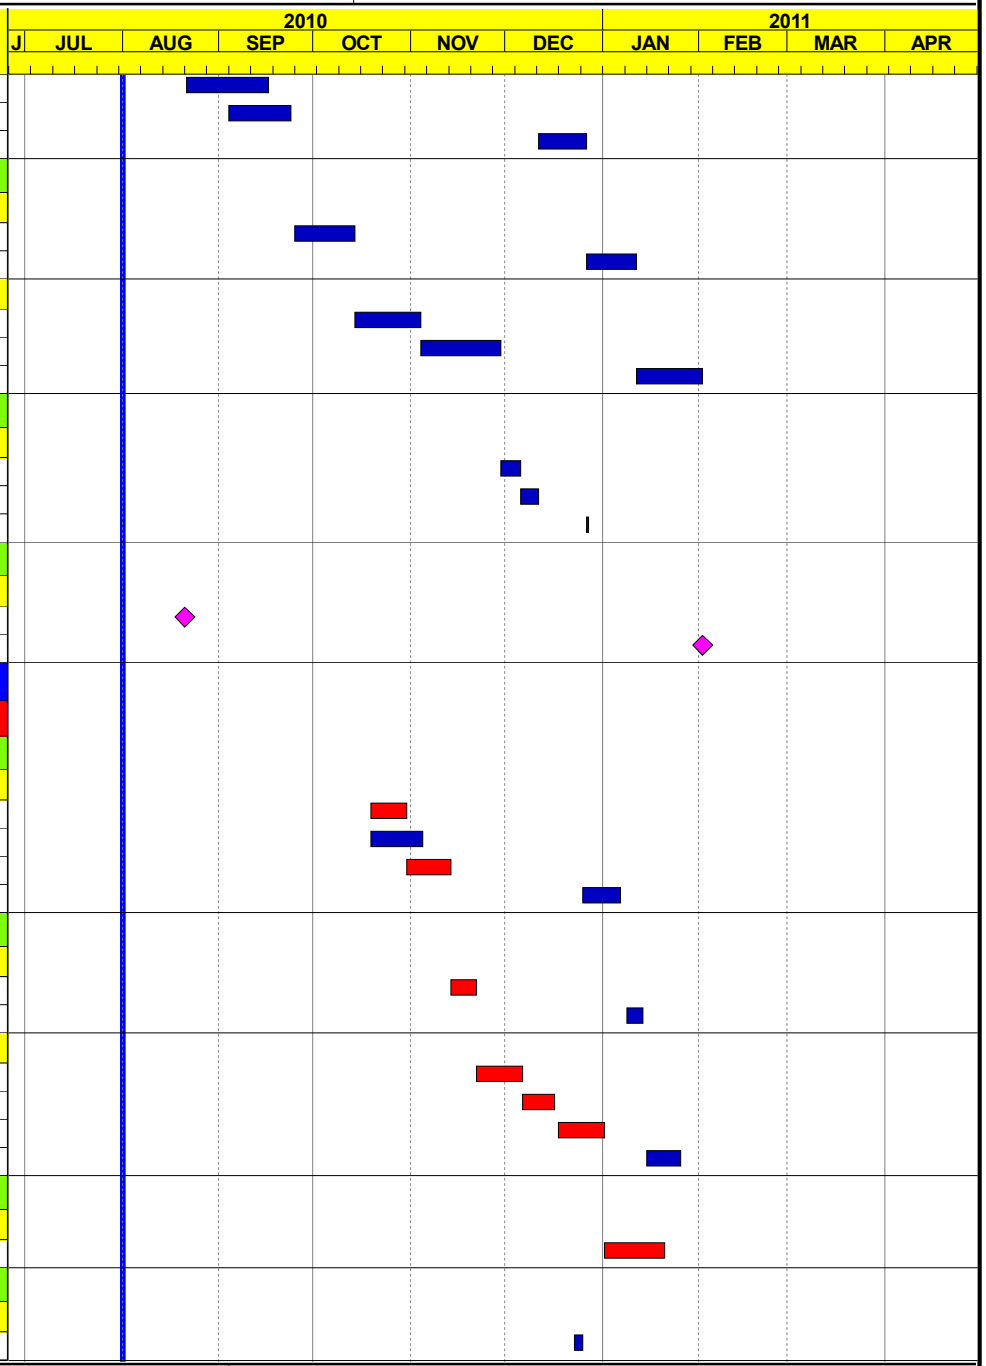


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 24 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCCV-WB013 | Damp Proofing | 4 | 02JAN11 | 05JAN11 |
| DCCV-WB014 | Heat Insulation For Roof | 2 | 06JAN11 | 08JAN11 |
| DCCV-WB012 | Polyethylene Membrane | 1 | 08JAN11 | 08JAN11 |
| ***Doors & Windows*** | | | | |
| DCCV-WB015 | Wooden Doors | 2 | 26FEB11 | 27FEB11 |
| DCCV-WB016 | Aluminum Windows | 2 | 26FEB11 | 27FEB11 |
| ***Finishes*** | | | | |
| DCAR-WB020 | Roof Flooring | 7 | 09JAN11 | 16JAN11 |
| DCAR-WB021 | Stone Cladding For Waincost | 7 | 17JAN11 | 24JAN11 |
| DCAR-WB017 | Internal Plastering For Walls & ceiling | 13 | 22JAN11 | 05FEB11 |
| DCAR-WB018 | External Plastering For Walls | 13 | 22JAN11 | 05FEB11 |
| DCAR-WB019 | Floor Tiles | 8 | 06FEB11 | 14FEB11 |
| DCAR-WB022 | Internal Painting | 17 | 06FEB11 | 24FEB11 |
| DCAR-WB023 | External Painting | 17 | 06FEB11 | 24FEB11 |
| ***Electromechanical Works*** | | | | |
| ***Fire Fighting*** | | | | |
| DCMC-WB025 | Fire Fighting System | 30 | 22JAN11 | 24FEB11 |
| ***HVAC*** | | | | |
| DCMC-WB026 | HVAC Works | 30 | 22JAN11 | 24FEB11 |
| ***Plumbing*** | | | | |
| DCMC-WB024 | Roof Storm Water System | 5 | 17JAN11 | 22JAN11 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCMC-WB027 | Electrical Works | 30 | 22JAN11 | 24FEB11 |
| ***General*** | | | | |
| DCGN-WB001 | Start Of Work | 0 | 19OCT10 | |
| DCGN-WB002 | End Of Work | 0 | | 27FEB11 |
| ***Work Shop*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-WS001 | Excavation | 9 | 25SEP10 | 04OCT10 |
| DCCV-WS025 | Disposal Of Excavated Materials | 16 | 25SEP10 | 12OCT10 |
| DCCV-WS003 | Soil Replacement | 12 | 05OCT10 | 18OCT10 |
| DCCV-WS002 | Filling Around Foundations Up To SOG Level | 8 | 23NOV10 | 01DEC10 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-WS005 | PC Foundation | 6 | 19OCT10 | 25OCT10 |
| DCCV-WS007 | PC Slab On Grade | 6 | 04DEC10 | 09DEC10 |

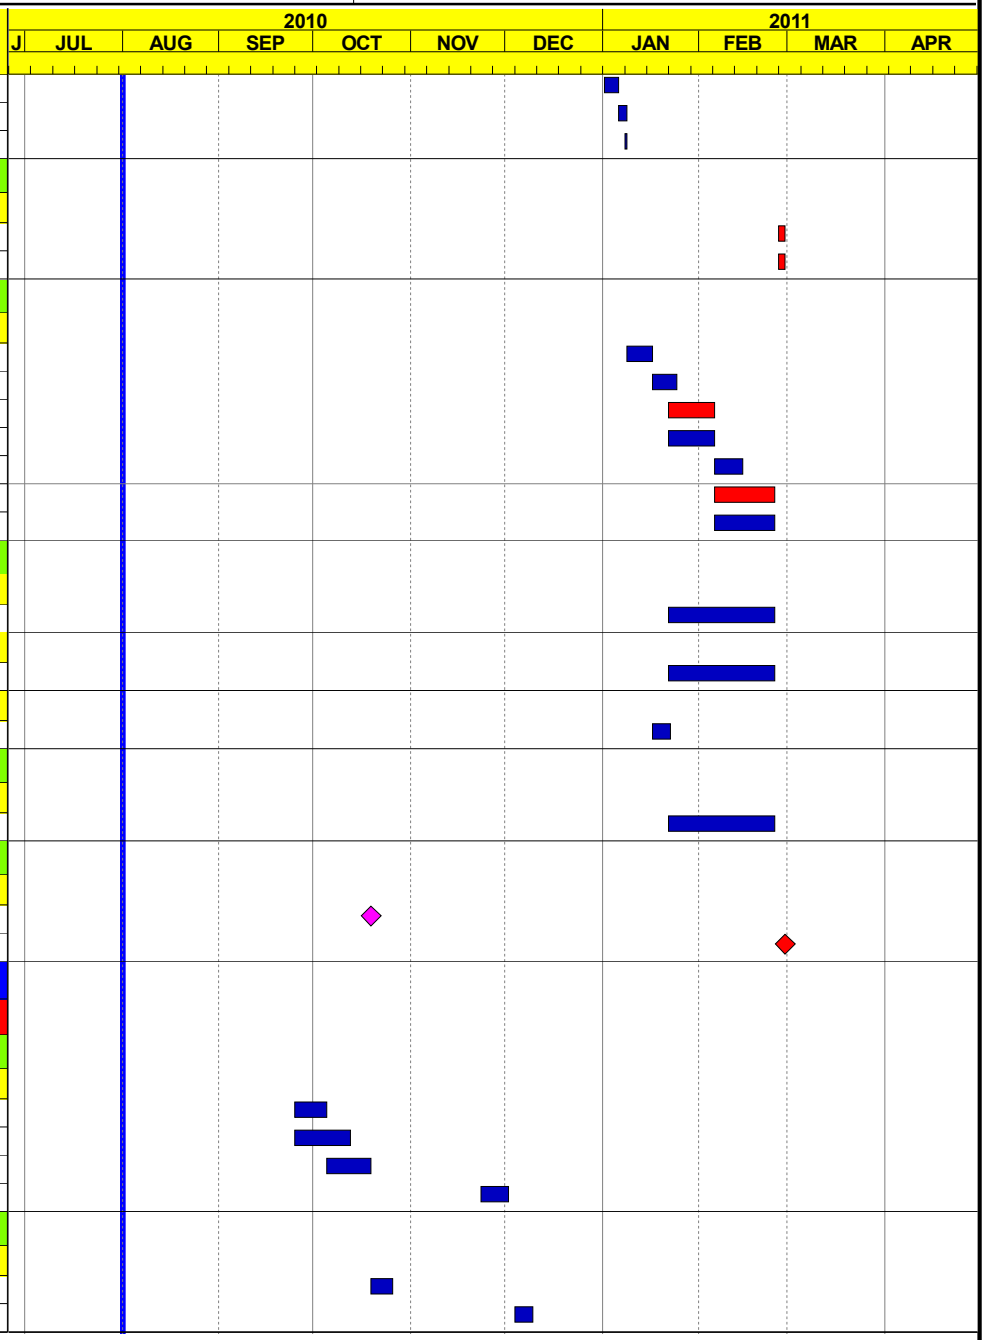


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 25 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama
For Trading & Contracting

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| ***Reinforced Concrete*** | | | | |
| DCCV-WS006 | RC Foundation & Semels | 16 | 26OCT10 | 13NOV10 |
| DCCV-WS009 | RC Columns & Pedestals | 12 | 14NOV10 | 27NOV10 |
| DCCV-WS008 | RC Slab On Grade | 16 | 16DEC10 | 03JAN11 |
| ***Masonary*** | | | | |
| DCCV-WS010 | Masonary for Walls | 14 | 04JAN11 | 19JAN11 |
| ***Metals*** | | | | |
| DCCV-WS031 | Anchor Bolts | 10 | 16NOV10 | 27NOV10 |
| DCCV-WS011 | Steel Structure For Skeleton | 14 | 28NOV10 | 13DEC10 |
| DCCV-WS032 | Cladding | 11 | 14DEC10 | 26DEC10 |
| ***Wood & Plastic*** | | | | |
| DCCV-WS012 | Wooden Bench | 1 | 27DEC10 | 27DEC10 |
| DCCV-WS013 | Wooden Counter | 1 | 27DEC10 | 27DEC10 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-WS014 | Water Proofing For Foundations (Cement Slurry) | 4 | 18NOV10 | 22NOV10 |
| DCCV-WS015 | Polyethylene Membrane | 1 | 02DEC10 | 02DEC10 |
| ***Doors & Windows*** | | | | |
| DCCV-WS016 | Steel Doors | 2 | 27DEC10 | 28DEC10 |
| DCCV-WS017 | Aluminum Windows | 2 | 27DEC10 | 28DEC10 |
| ***Finishes*** | | | | |
| DCCV-WS004 | Gravel Layer For Flooring | 3 | 29DEC10 | 01JAN11 |
| DCCV-WS018 | Internal Plastering For Walls | 15 | 20JAN11 | 06FEB11 |
| DCCV-WS019 | External Plastering For Walls | 15 | 20JAN11 | 06FEB11 |
| DCCV-WS020 | Internal Painting | 15 | 07FEB11 | 23FEB11 |
| DCCV-WS021 | External Painting | 15 | 07FEB11 | 23FEB11 |
| ***Electromechanical Works*** | | | | |
| ***Fire Fighting*** | | | | |
| DCCV-WS028 | Fire Fighting System | 30 | 27DEC10 | 30JAN11 |
| ***HVAC*** | | | | |
| DCCV-WS029 | HVAC Works | 30 | 27DEC10 | 30JAN11 |
| ***Plumbing*** | | | | |
| DCCV-WS023 | Piping Systems (PP) | 3 | 11DEC10 | 13DEC10 |
| DCCV-WS024 | Water & Waste Piping System (UPVC) | 3 | 11DEC10 | 13DEC10 |
| DCCV-WS022 | Plumbing Fixture, Floor Drain & Gully Trap | 2 | 14DEC10 | 15DEC10 |
| ***Electrical*** | | | | |
| ***Electrical*** | | | | |
| DCCV-WS030 | Electrical Works | 30 | 27DEC10 | 30JAN11 |

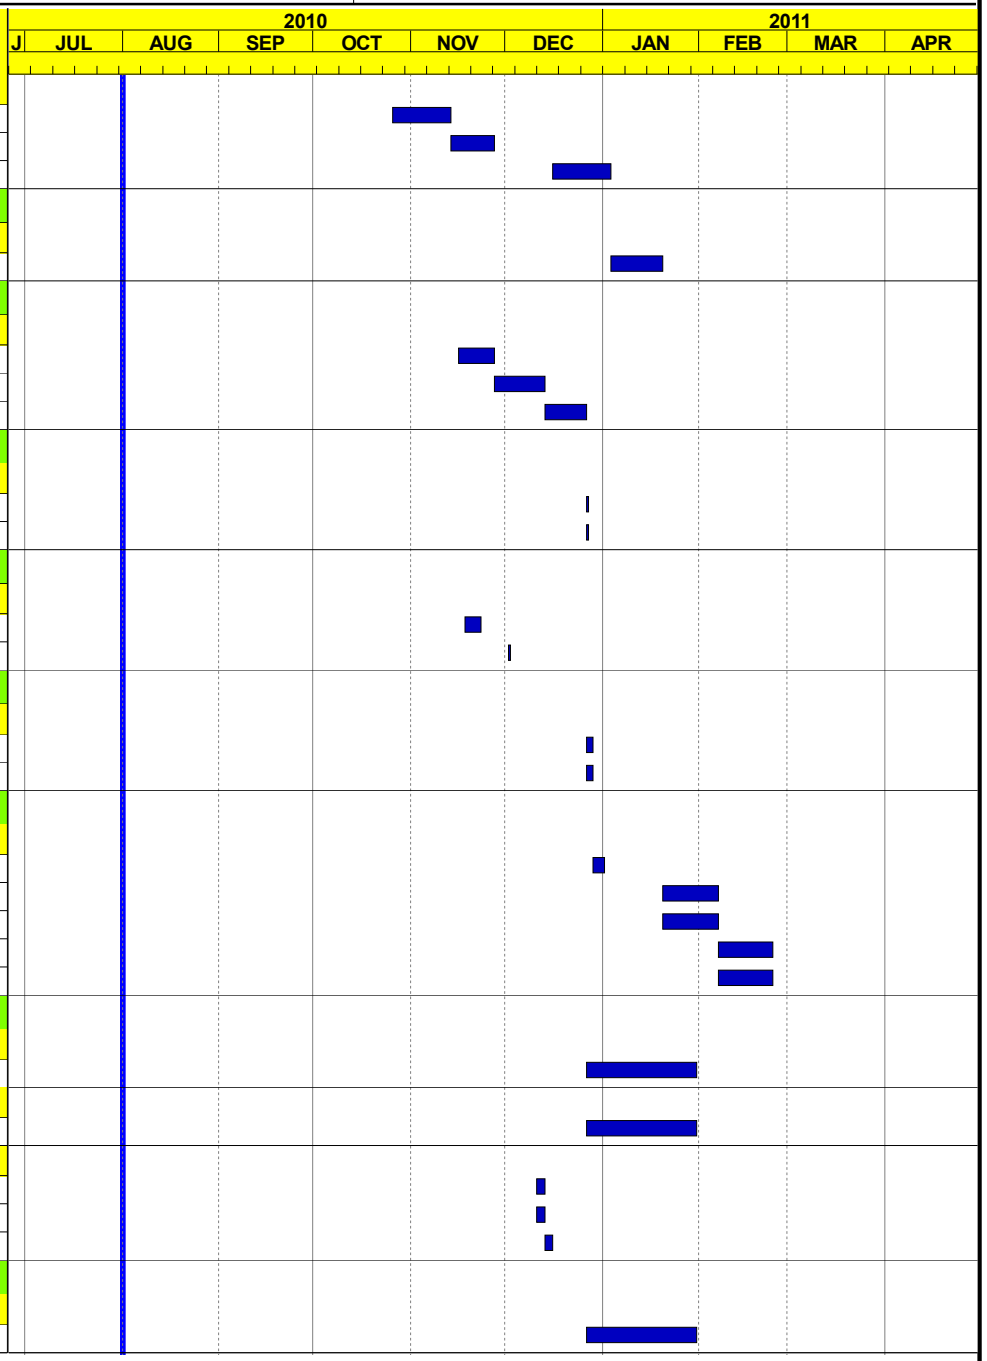


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 26 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **General** | | | | |
| DCGN-WS001 | Start Of Work | 0 | 25SEP10 | |
| DCGN-WS002 | Finish Of Work | 0 | | 23FEB11 |
| **Electrical & Transformer Building** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCCV-TR001 | Excavation | 4 | 07OCT10 | 11OCT10 |
| DCCV-TR004 | Disposal Of Excavated Materials | 13 | 07OCT10 | 21OCT10 |
| DCCV-TR003 | Soil Replacement | 6 | 12OCT10 | 18OCT10 |
| DCCV-TR002 | Filling Around Foundations Up To SOG Level | 5 | 09NOV10 | 14NOV10 |
| **Concrete Works** | | | | |
| **Plain Concrete** | | | | |
| DCCV-TR005 | PC Foundation | 4 | 19OCT10 | 23OCT10 |
| DCCV-TR007 | PC Slab On Grade | 2 | 16NOV10 | 17NOV10 |
| DCCV-TR010 | PC For Layer Under Ramp | 1 | 16NOV10 | 16NOV10 |
| **Reinforced Concrete** | | | | |
| DCCV-TR006 | RC Foundation & Semels | 4 | 24OCT10 | 27OCT10 |
| DCCV-TR009 | RC Columns & Beams | 3 | 28OCT10 | 31OCT10 |
| DCCV-TR012 | RC Solid Slabs | 4 | 01NOV10 | 04NOV10 |
| DCCV-TR008 | RC Slab On Grade | 5 | 18NOV10 | 23NOV10 |
| DCCV-TR011 | RC For Layer Under Ramp | 3 | 18NOV10 | 21NOV10 |
| **Masonary** | | | | |
| DCCV-TR013 | Masonary For Walls | 6 | 28NOV10 | 04DEC10 |
| **Thermal & Moisture Protection** | | | | |
| DCCV-TR014 | Water Proofing For Foundations (Cement Slurry) | 2 | 07NOV10 | 08NOV10 |
| DCCV-TR016 | Damp Proofing | 4 | 10NOV10 | 14NOV10 |
| DCCV-TR015 | Polyethylene Membrane | 1 | 15NOV10 | 15NOV10 |
| DCCV-TR017 | Heat Insulation For Roof | 2 | 15NOV10 | 16NOV10 |
| DCCV-TR018 | Expansion Joints Between S.O.G & Walls | 3 | 24NOV10 | 27NOV10 |
| **Doors & Windows** | | | | |
| DCCV-TR019 | Steel Doors | 1 | 14DEC10 | 14DEC10 |
| **Finishes** | | | | |
| DCAR-TR020 | Internal Plastering For Walls & Ceiling | 4 | 05DEC10 | 08DEC10 |
| DCAR-TR021 | External Plastering For Walls | 4 | 05DEC10 | 08DEC10 |
| DCAR-TR022 | Floor Tiles | 2 | 09DEC10 | 11DEC10 |
| DCAR-TR024 | Internal Painting | 4 | 09DEC10 | 13DEC10 |
| DCAR-TR025 | External Painting | 4 | 09DEC10 | 13DEC10 |

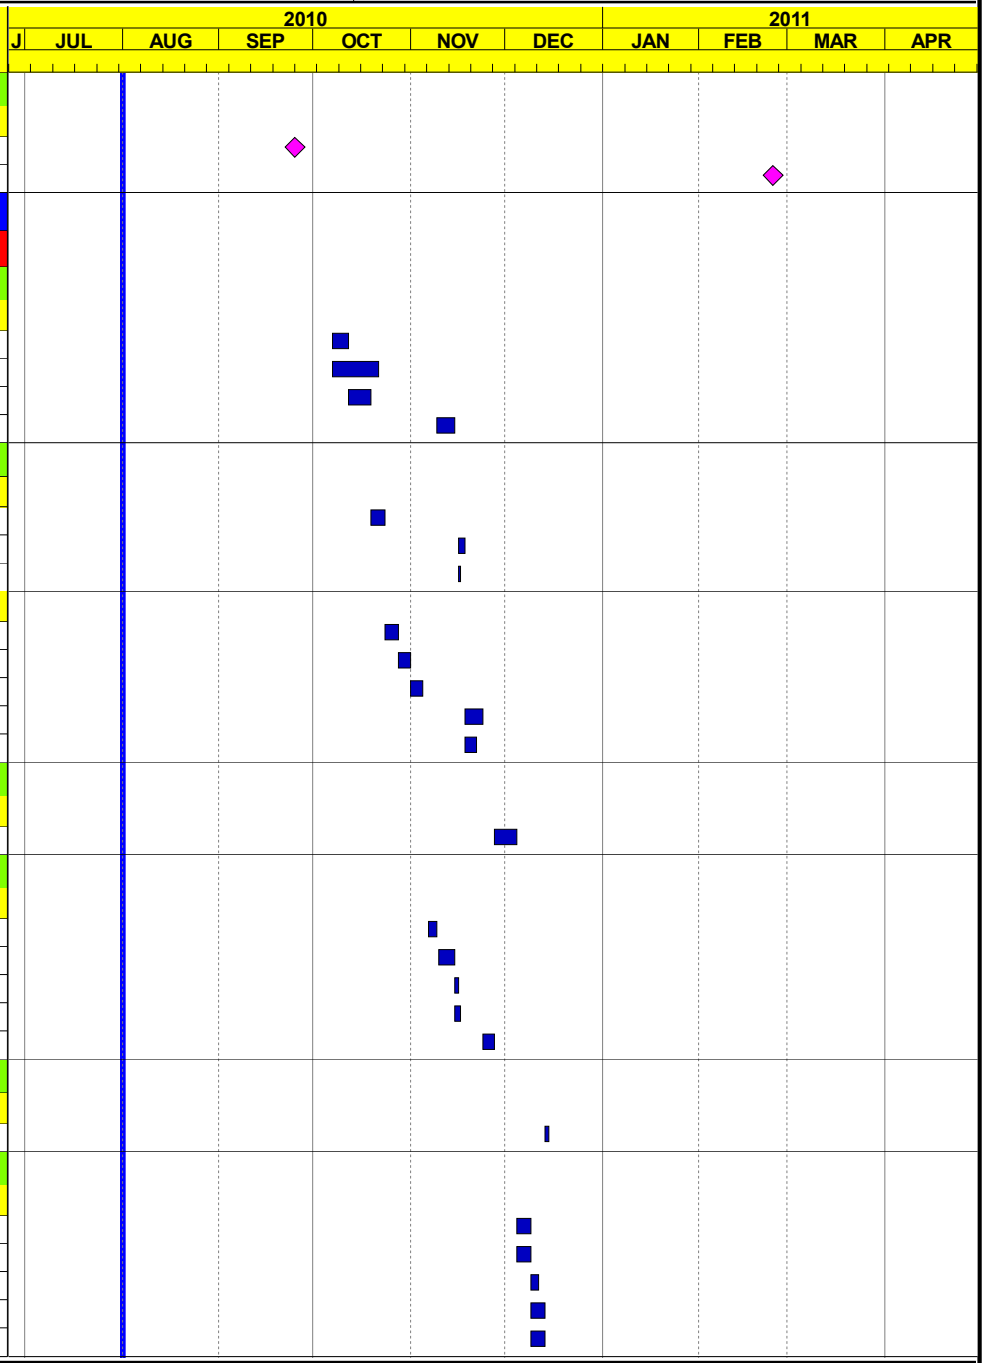


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 27 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

Gama For Trading & Contracting

# Danone Farm In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| DCAR-TR023 | Stone Cladding For Wainscot | 2 | 12DEC10 | 13DEC10 |
| ***General*** | | | | |
| DCGN-TR001 | Start Of Work | 0 | 07OCT10 | |
| DCGN-TR002 | End Of Work | 0 | | 14DEC10 |
| ***Tanks 1, 2, 3 & 4*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCCV-TN001 | Excavation | 26 | 02OCT10 | 31OCT10 |
| DCCV-TN010 | Disposal Of Excavated Materials | 19 | 02OCT10 | 23OCT10 |
| DCCV-TN003 | Soil Replacement | 15 | 01NOV10 | 17NOV10 |
| DCCV-TN002 | Filling Around Foundations Up To SOG Level | 14 | 01JAN11 | 16JAN11 |
| ***Concrete Works*** | | | | |
| ***Plain Concrete*** | | | | |
| DCCV-TN004 | PC For Foundations | 17 | 20NOV10 | 08DEC10 |
| ***Reinforced Concrete*** | | | | |
| DCCV-TN005 | RC Floors | 10 | 09DEC10 | 20DEC10 |
| DCCV-TN006 | RC Walls | 7 | 21DEC10 | 28DEC10 |
| DCCV-TN007 | RC Ceiling | 8 | 29DEC10 | 06JAN11 |
| ***Thermal & Moisture Protection*** | | | | |
| DCCV-TN008 | Polyethylene Membrane | 1 | 18NOV10 | 18NOV10 |
| DCCV-TN009 | Water Profing Epoxy Paints For Tank 3,4 | 2 | 29DEC10 | 30DEC10 |
| ***General*** | | | | |
| DCGN-TN001 | Start Of Work | 0 | 02OCT10 | |
| DCGN-TN002 | End Of Work | 0 | | 06JAN11 |
| ***Water Tank*** | | | | |
| ***Building*** | | | | |
| ***Earth Works*** | | | | |
| DCAR-WW001 | Excavation | 45 | 19OCT10 | 09DEC10 |
| DCAR-WW003 | Disposal Of Excavated Materials | 60 | 19OCT10 | 27DEC10 |
| DCAR-WW002 | Polyethylene Membrane | 31 | 11DEC10 | 15JAN11 |
| ***General*** | | | | |
| DCGN-WW001 | Start Of Work | 0 | 19OCT10 | |
| DCGN-WW002 | End Of Work | 0 | | 15JAN11 |

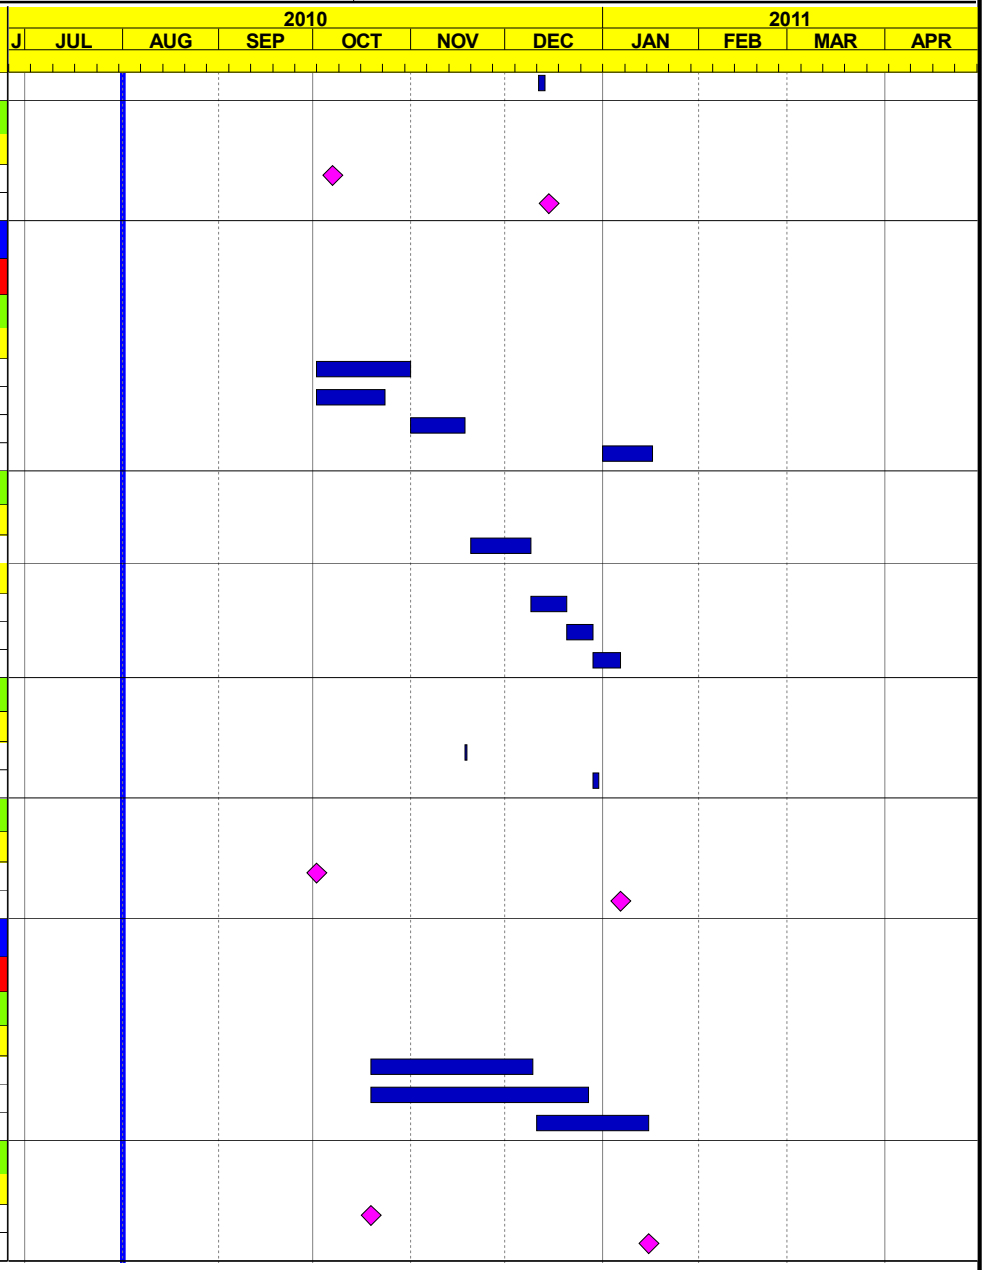


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 28 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.

# Danone Farm
# In Nubariya

**Owner: DANONE DAIRY FARM S.A.E**
**Consultant: EHAF Consulting Engineers**

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish |
|---|---|---|---|---|
| **Waste Tank** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCAR-ST001 | Excavation | 45 | 27NOV10 | 17JAN11 |
| DCAR-ST003 | Disposal Of Excavated Materials | 60 | 27NOV10 | 03FEB11 |
| DCAR-ST002 | Polyethylene Membrane | 31 | 18JAN11 | 22FEB11 |
| **General** | | | | |
| DCGN-ST001 | Start Of Work | 0 | 27NOV10 | |
| DCGN-ST002 | End Of Work | 0 | | 22FEB11 |
| **Landscape** | | | | |
| **Building** | | | | |
| **Earth Works** | | | | |
| DCCV-LS002 | Fences | 136 | 22SEP10 | 27FEB11 |
| DCCV-LS003 | Gates | 60 | 22SEP10 | 30NOV10 |
| DCCV-LS001 | Asphalt Paving | 50 | 26DEC10 | 21FEB11 |
| **Electromechanical Works** | | | | |
| **Plumbing** | | | | |
| DCMC-LS003 | Piping Systems & Valve Box | 60 | 22SEP10 | 30NOV10 |
| DCMC-LS010 | Septic Tank | 15 | 22SEP10 | 09OCT10 |
| DCMC-LS005 | Submersible Pump | 5 | 10OCT10 | 14OCT10 |
| DCMC-LS006 | Trench Drain | 12 | 01DEC10 | 14DEC10 |
| DCMC-LS007 | Floor Cleanout | 4 | 01DEC10 | 05DEC10 |
| DCMC-LS008 | Slow Down Chamber | 6 | 01DEC10 | 07DEC10 |
| DCMC-LS009 | Sump Pit | 4 | 15DEC10 | 19DEC10 |
| **General** | | | | |
| DCGN-LS01 | Start Of Work | 0 | 22SEP10 | |
| DCGN-LS02 | End Of Work | 0 | | 21FEB11 |

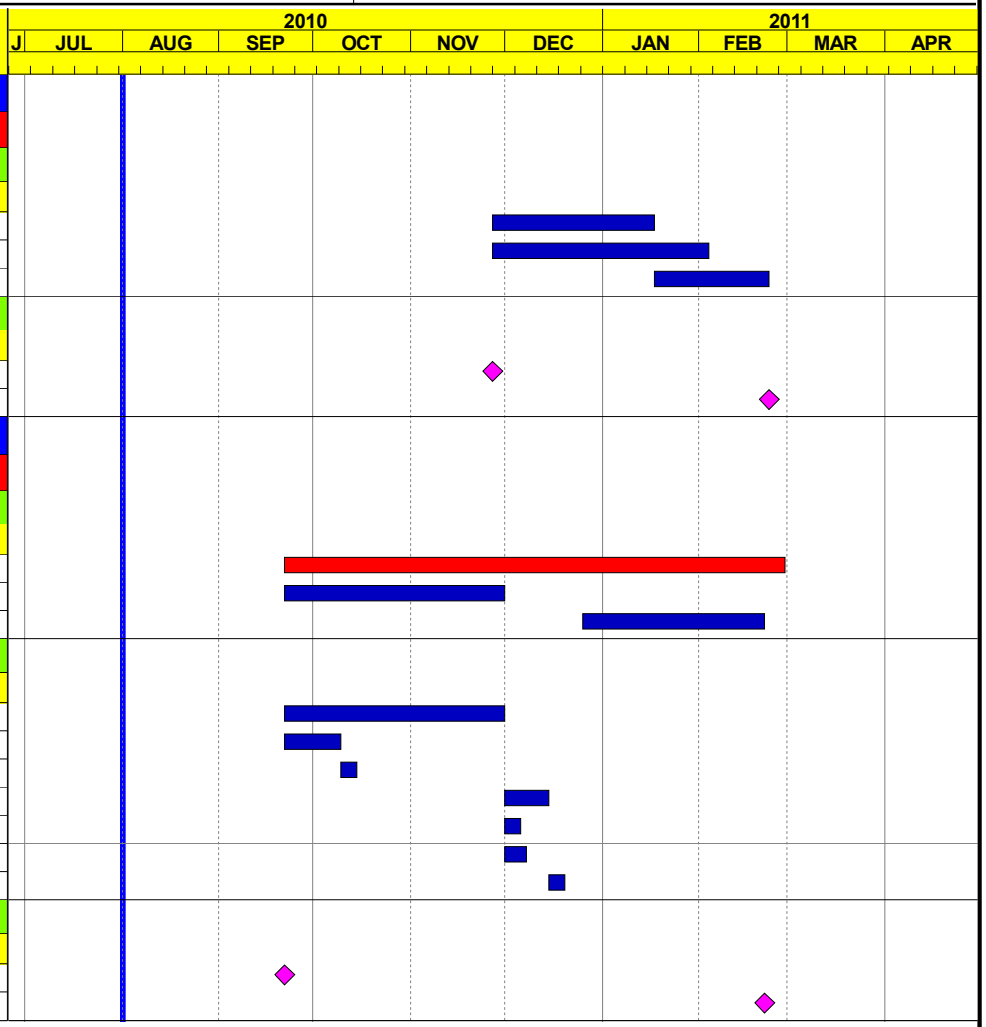


| | |
|---|---|
| Start Date | 01AUG10 |
| Finish Date | 27FEB11 |
| Data Date | 01AUG10 |
| Run Date | 28AUG10 14:57 |

Early Bar
Progress Bar
Critical Activity

DAFM

Sheet 29 of 29

General Layout

| Date | Revision | Checked | Approved |
|---|---|---|---|
| 28AUG10 | Rev. 0 | | |

© Primavera Systems, Inc.
