AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14 CS STORAGE TANKS NO.OF 33 Rev.02(Level VI)		3996h	05-Dec-13	16-Mar-15
CZA-14.1 Pre-Inspection Meeting		0h	05-Dec-13	05-Dec-13
CZA-PIM-1000	Pre Inspection Meeting (SA, PSAL & AZ)	0h	05-Dec-13	
CZA-14.2 SOUTH TANK FARM (STF)		3746h	15-Dec-13	24-Feb-15
CZA-14.2.1 S220-TK-0720(Mixed Xylene/PDEB Inventory Tank Dia 21.28m x Ht 14.70m with IFR)		2136h	15-Dec-13	20-Aug-14
CZA-14.2.1.1 Fabrication Works		362h	15-Dec-13	26-Jan-14
CZA-TK-0720-1000	Cutting of Annular Plates and Bottom Plates	8h	15-Dec-13	15-Dec-13
CZA-TK-0720-1010	Cutting,Bevelling & Rolling Shell No. 1	8h	15-Dec-13	16-Dec-13
CZA-TK-0720-1020	Cutting , Beveling & Rolling Shell No.2	8h	16-Dec-13	17-Dec-13
CZA-TK-0720-1030	Cutting, Fit-up and Weld of Shell Nozzles, Manholes & Other Appurtanances	40h	17-Dec-13	22-Dec-13
CZA-TK-0720-1040	Cutting, Bevelling & Rolling Shell No.3	8h	19-Dec-13	19-Dec-13
CZA-TK-0720-1050	Cutting of Floating Roof Plates	16h	21-Dec-13	22-Dec-13
CZA-TK-0720-1060	Cutting, Fit-up and Welding of Pontoon	80h	22-Dec-13	31-Dec-13
CZA-TK-0720-1070	Cutting of Floating Roof Legs and Manholes	32h	26-Dec-13	30-Dec-13
CZA-TK-0720-1080	Cutting, Bevelling & Rolling Shell No.4	8h	30-Dec-13	31-Dec-13
CZA-TK-0720-1090	Cutting, Bevelling & Rolling Shell No.5	8h	30-Dec-13	31-Dec-13
CZA-TK-0720-1100	Cutting, Bevelling & Rolling Shell No.6	8h	31-Dec-13	01-Jan-14
CZA-TK-0720-1110	Cutting, Bevelling & Rolling Shell no.7	8h	01-Jan-14	02-Jan-14
CZA-TK-0720-1120	Cutting, Fit-up & Welding Roof Structures & Compression Ring	48h	02-Jan-14	07-Jan-14
CZA-TK-0720-1130	Cutting of Roof Plates	16h	08-Jan-14	09-Jan-14
CZA-TK-0720-1140	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	80h	08-Jan-14	16-Jan-14
CZA-TK-0720-1150	Cutting, Fit-up and Welding of Stairways	56h	18-Jan-14	23-Jan-14
CZA-TK-0720-1160	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	21-Jan-14	26-Jan-14
CZA-14.2.1.2 FoundationTakeover		0h	16-Jan-14	16-Jan-14
CZA-TK-0720-1170	Foundation Takeover From Client	0h	16-Jan-14	
CZA-14.2.1.3 Mechanical Erection		1430h	18-Jan-14	03-Jul-14
CZA-14.2.1.3.1 Annular Plates		30h	18-Jan-14	21-Jan-14
CZA-TK-0720-1180	Laying and Fit-up	10h	18-Jan-14	19-Jan-14
CZA-TK-0720-1190	Welding	20h	19-Jan-14	21-Jan-14
CZA-TK-0720-1330	Inspection	30h	18-Jan-14	21-Jan-14
CZA-14.2.1.3.19 Bottom Plates		100h	21-Jan-14	02-Feb-14
CZA-TK-0720-1200	Erection and Fit-up	30h	21-Jan-14	25-Jan-14
CZA-TK-0720-1210	Welding	70h	25-Jan-14	02-Feb-14
CZA-TK-0720-1220	Inspection	100h	21-Jan-14	02-Feb-14
CZA-14.2.1.3.2 Shell No.1		60h	02-Feb-14	09-Feb-14
CZA-TK-0720-1230	Erection and Fit-up	10h	02-Feb-14	03-Feb-14
CZA-TK-0720-1240	Welding	50h	03-Feb-14	09-Feb-14
CZA-TK-0720-1250	Inspection	60h	02-Feb-14	09-Feb-14
CZA-14.2.1.3.3 Shell No.2		60h	09-Feb-14	16-Feb-14
CZA-TK-0720-1260	Erection and Fit-up	10h	09-Feb-14	10-Feb-14
CZA-TK-0720-1270	Welding	50h	10-Feb-14	16-Feb-14
CZA-TK-0720-1280	Inspection	60h	09-Feb-14	16-Feb-14
CZA-14.2.1.3.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		40h	16-Feb-14	20-Feb-14
CZA-TK-0720-1290	Cutting, Installation and Fit-up	10h	16-Feb-14	17-Feb-14
CZA-TK-0720-1300	Welding	30h	17-Feb-14	20-Feb-14
CZA-TK-0720-1310	Inspection	40h	16-Feb-14	20-Feb-14
CZA-14.2.1.3.5 Deck Plates		130h	20-Feb-14	08-Mar-14
CZA-TK-0720-1320	Laying & Fit-up	20h	20-Feb-14	23-Feb-14
CZA-TK-0720-1340	Welding	110h	23-Feb-14	08-Mar-14
CZA-TK-0720-1350	Inspection	130h	20-Feb-14	08-Mar-14
CZA-14.2.1.3.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		100h	08-Mar-14	19-Mar-14
CZA-TK-0720-1360	Cutting of All Holes, Laying & Fit-up	10h	08-Mar-14	09-Mar-14
CZA-TK-0720-1370	Welding of Sleeves and Plates	80h	09-Mar-14	18-Mar-14

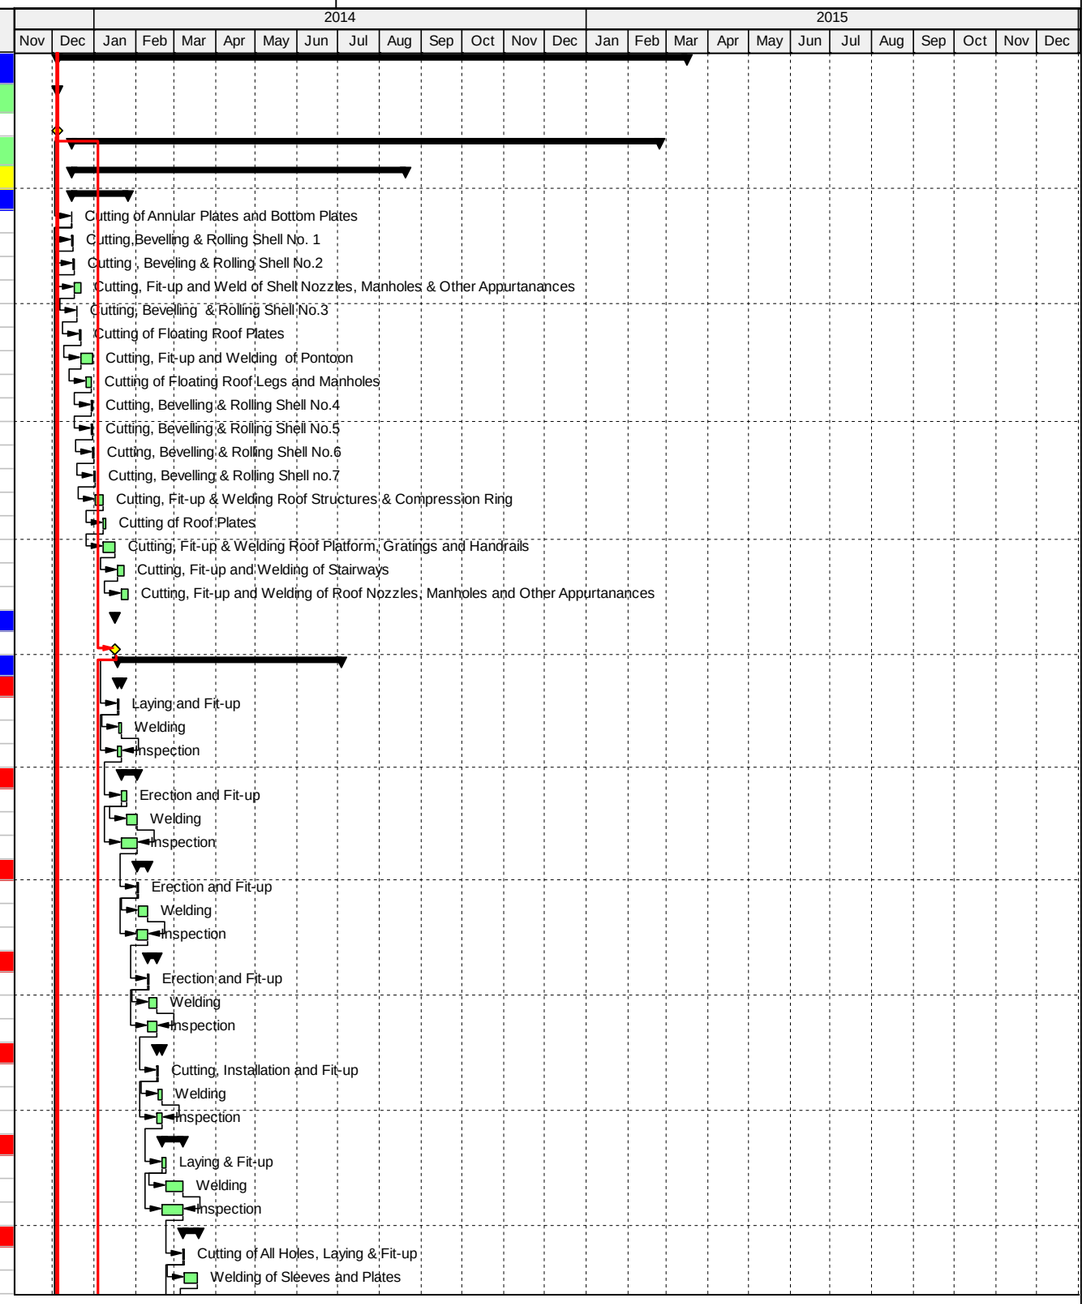

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0720-1380	Installation of Leg Support	10h	18-Mar-14	19-Mar-14
CZA-TK-0720-1390	Inspection	100h	08-Mar-14	19-Mar-14
CZA-14.2.1.3.7 Shell No.3		60h	19-Mar-14	26-Mar-14
CZA-TK-0720-1400	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-0720-1410	Welding	50h	20-Mar-14	26-Mar-14
CZA-TK-0720-1420	Inspection	60h	19-Mar-14	26-Mar-14
CZA-14.2.1.3.8 Shell No.4		60h	26-Mar-14	02-Apr-14
CZA-TK-0720-1430	Erection and Fit-up	10h	26-Mar-14	27-Mar-14
CZA-TK-0720-1440	Welding	50h	27-Mar-14	02-Apr-14
CZA-TK-0720-1450	Inspection	60h	26-Mar-14	02-Apr-14
CZA-14.2.1.3.9 Shell No.5		60h	02-Apr-14	09-Apr-14
CZA-TK-0720-1460	Erection and Fit-up	10h	02-Apr-14	03-Apr-14
CZA-TK-0720-1470	Welding	50h	03-Apr-14	09-Apr-14
CZA-TK-0720-1480	Inspection	60h	02-Apr-14	09-Apr-14
CZA-14.2.1.3.10 Shell No.6		60h	09-Apr-14	16-Apr-14
CZA-TK-0720-1490	Erection and Fit-up	10h	09-Apr-14	10-Apr-14
CZA-TK-0720-1500	Welding	50h	10-Apr-14	16-Apr-14
CZA-TK-0720-1510	Inspection	60h	09-Apr-14	16-Apr-14
CZA-14.2.1.3.11 Shell No.7		70h	16-Apr-14	24-Apr-14
CZA-TK-0720-1520	Erection and Fit-up	10h	16-Apr-14	17-Apr-14
CZA-TK-0720-1530	Welding	50h	17-Apr-14	23-Apr-14
CZA-TK-0720-1540	Inspection	60h	17-Apr-14	24-Apr-14
CZA-14.2.1.3.12 Shell Nozzles and attachements (Upper)		40h	24-Apr-14	29-Apr-14
CZA-TK-0720-1550	Cutting, Installation and Fit-up	20h	24-Apr-14	27-Apr-14
CZA-TK-0720-1560	Welding	20h	27-Apr-14	29-Apr-14
CZA-TK-0720-1570	Inspection	40h	24-Apr-14	29-Apr-14
CZA-14.2.1.3.13 Roof Structure		80h	29-Apr-14	08-May-14
CZA-TK-0720-1580	Erection and Fit-up	30h	29-Apr-14	03-May-14
CZA-TK-0720-1590	Welding	50h	03-May-14	08-May-14
CZA-TK-0720-1600	Inspection	80h	29-Apr-14	08-May-14
CZA-14.2.1.3.14 Roof Plates		90h	08-May-14	19-May-14
CZA-TK-0720-1610	Laying and Fit-up	20h	08-May-14	11-May-14
CZA-TK-0720-1620	Welding	70h	11-May-14	19-May-14
CZA-TK-0720-1630	Inspection	90h	08-May-14	19-May-14
CZA-14.2.1.3.15 Compression Ring		70h	19-May-14	27-May-14
CZA-TK-0720-1640	Laying and Fit-up	10h	19-May-14	20-May-14
CZA-TK-0720-1650	Welding	60h	20-May-14	27-May-14
CZA-TK-0720-1660	Inspection	70h	19-May-14	27-May-14
CZA-14.2.1.3.16 Roof Nozzles, Manholes and Other Appurtanances		50h	27-May-14	02-Jun-14
CZA-TK-0720-1670	Installation and Fit-up	20h	27-May-14	29-May-14
CZA-TK-0720-1680	Welding	30h	29-May-14	02-Jun-14
CZA-TK-0720-1690	Inspection	50h	27-May-14	02-Jun-14
CZA-14.2.1.3.18 Stairway Platform, Handrails and Gratings		110h	02-Jun-14	15-Jun-14
CZA-TK-0720-1700	Erection and Fit-up	30h	02-Jun-14	05-Jun-14
CZA-TK-0720-1710	Welding	80h	05-Jun-14	15-Jun-14
CZA-TK-0720-1720	Inspection	110h	02-Jun-14	15-Jun-14
CZA-14.2.1.3.17 Roof Platform, Handrails and Gratings		120h	15-Jun-14	29-Jun-14
CZA-TK-0720-1730	Erection and Fit-up	30h	15-Jun-14	18-Jun-14
CZA-TK-0720-1740	Welding	90h	18-Jun-14	29-Jun-14
CZA-TK-0720-1750	Inspection	120h	15-Jun-14	29-Jun-14
CZA-14.2.1.3.20 Primary and Secondary Seal		40h	29-Jun-14	03-Jul-14
CZA-TK-0720-1800	Installation of Primary and Secondary Seal	30h	29-Jun-14	02-Jul-14
CZA-TK-0720-1810	Inspection	10h	02-Jul-14	03-Jul-14
CZA-14.2.1.4 Hydrotest		230h	03-Jul-14	30-Jul-14

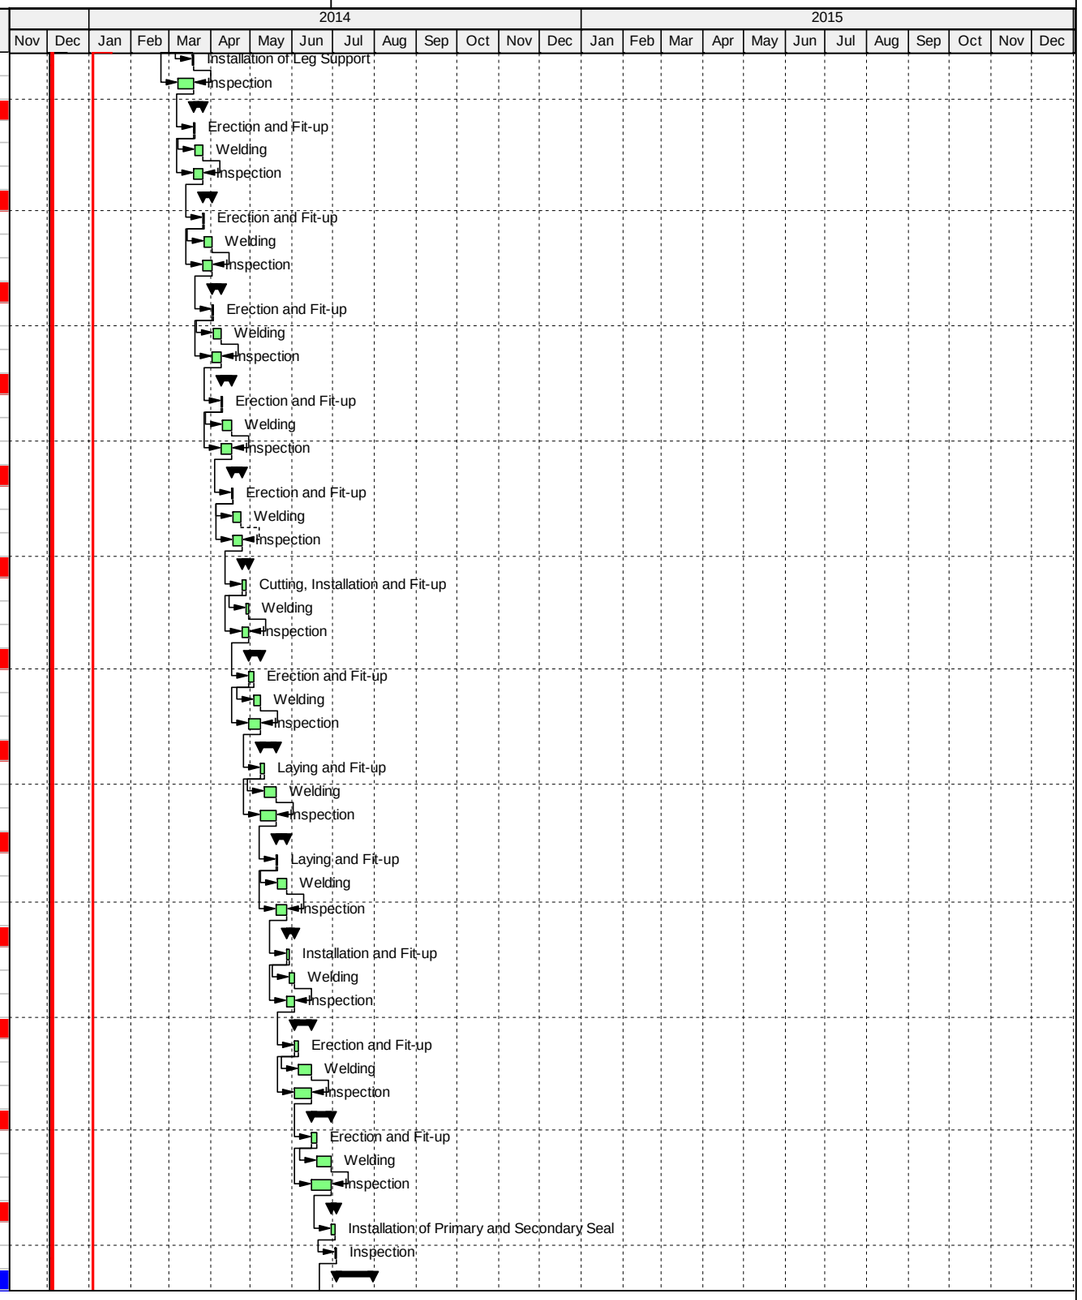

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0720-1760	Filling, Holding and Draining of Water	230h	03-Jul-14	30-Jul-14
CZA-14.2.1.5 Blasting and Painting		110h	30-Jul-14	12-Aug-14
CZA-TK-0720-1770	Blasting and Painting Inside, Outside and Bottom Plates	110h	30-Jul-14	12-Aug-14
CZA-14.2.1.6 Tank Calibration and Handover		70h	12-Aug-14	20-Aug-14
CZA-TK-0720-1780	Tank Calibration	50h	12-Aug-14	18-Aug-14
CZA-TK-0720-1790	Tank Handover	20h	18-Aug-14	20-Aug-14
CZA-14.2.7 S220-TK-0721(Mixed Xylene/PDEB Inventory Tank Dia 21.28m x Ht 14.70 mwith IFR)		2236h	15-Dec-13	01-Sep-14
CZA-14.2.7.1 Fabrication Works		368h	15-Dec-13	26-Jan-14
CZA-TK-0721-1391	Cutting of Annular Plates and Bottom Plates	8h	15-Dec-13	15-Dec-13
CZA-TK-0721-1392	Cutting,Bevelling & Rolling Shell No. 1	8h	15-Dec-13	16-Dec-13
CZA-TK-0721-1393	Cutting , Beveling & Rolling Shell No.2	8h	16-Dec-13	17-Dec-13
CZA-TK-0721-1394	Cutting, Fit-up and Weld of Shell Nozzles, Manholes & Other Appurtanances	40h	17-Dec-13	22-Dec-13
CZA-TK-0721-1395	Cutting, Bevelling & Rolling Shell No.3	8h	19-Dec-13	19-Dec-13
CZA-TK-0721-1396	Cutting of Floating Roof Plates	16h	19-Dec-13	22-Dec-13
CZA-TK-0721-1397	Cutting, Fit-up and Welding of Pontoon	80h	22-Dec-13	31-Dec-13
CZA-TK-0721-1398	Cutting of Floating Roof Legs and Manholes	32h	24-Dec-13	28-Dec-13
CZA-TK-0721-1399	Cutting, Bevelling & Rolling Shell No.4	8h	29-Dec-13	29-Dec-13
CZA-TK-0721-1400	Cutting, Bevelling & Rolling Shell No.5	8h	29-Dec-13	29-Dec-13
CZA-TK-0721-1401	Cutting, Bevelling & Rolling Shell No.6	8h	29-Dec-13	30-Dec-13
CZA-TK-0721-1402	Cutting, Bevelling & Rolling Shell no.7	8h	30-Dec-13	31-Dec-13
CZA-TK-0721-1403	Cutting, Fit-up & Welding Roof Structures & Compression Ring	48h	31-Dec-13	06-Jan-14
CZA-TK-0721-1404	Cutting of Roof Plates	16h	06-Jan-14	07-Jan-14
CZA-TK-0721-1405	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	80h	06-Jan-14	15-Jan-14
CZA-TK-0721-1406	Cutting, Fit-up and Welding of Stairways	56h	15-Jan-14	21-Jan-14
CZA-TK-0721-1407	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	21-Jan-14	26-Jan-14
CZA-14.2.7.2 FoundationTakeover		0h	16-Jan-14	16-Jan-14
CZA-TK-0721-1408	Foundation Takeover From Client	0h	16-Jan-14	
CZA-14.2.7.7 Mechanical Erection		1440h	18-Jan-14	05-Jul-14
CZA-14.2.7.7.1 Annular Plates		30h	18-Jan-14	21-Jan-14
CZA-TK-0721-1409	Laying and Fit-up	10h	18-Jan-14	19-Jan-14
CZA-TK-0721-1410	Welding	20h	19-Jan-14	21-Jan-14
CZA-TK-0721-1411	Inspection	30h	18-Jan-14	21-Jan-14
CZA-14.2.7.7.19 Bottom Plates		100h	21-Jan-14	02-Feb-14
CZA-TK-0721-1412	Erection and Fit-up	30h	21-Jan-14	25-Jan-14
CZA-TK-0721-1413	Welding	70h	25-Jan-14	02-Feb-14
CZA-TK-0721-1414	Inspection	100h	21-Jan-14	02-Feb-14
CZA-14.2.7.7.2 Shell No.1		60h	02-Feb-14	09-Feb-14
CZA-TK-0721-1415	Erection and Fit-up	10h	02-Feb-14	03-Feb-14
CZA-TK-0721-1416	Welding	50h	03-Feb-14	09-Feb-14
CZA-TK-0721-1417	Inspection	60h	02-Feb-14	09-Feb-14
CZA-14.2.7.7.3 Shell No.2		60h	09-Feb-14	16-Feb-14
CZA-TK-0721-1418	Erection and Fit-up	10h	09-Feb-14	10-Feb-14
CZA-TK-0721-1419	Welding	50h	10-Feb-14	16-Feb-14
CZA-TK-0721-1420	Inspection	60h	09-Feb-14	16-Feb-14
CZA-14.2.7.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		50h	16-Feb-14	22-Feb-14
CZA-TK-0721-1421	Cutting, Installation and Fit-up	10h	16-Feb-14	17-Feb-14
CZA-TK-0721-1422	Welding	40h	17-Feb-14	22-Feb-14
CZA-TK-0721-1423	Inspection	50h	16-Feb-14	22-Feb-14
CZA-14.2.7.7.5 Deck Plates		130h	22-Feb-14	09-Mar-14
CZA-TK-0721-1424	Laying & Fit-up	20h	22-Feb-14	24-Feb-14
CZA-TK-0721-1425	Welding	110h	24-Feb-14	09-Mar-14
CZA-TK-0721-1426	Inspection	130h	22-Feb-14	09-Mar-14
CZA-14.2.7.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		100h	09-Mar-14	20-Mar-14
CZA-TK-0721-1427	Cutting of All Holes, Laying and Fit-up	10h	09-Mar-14	10-Mar-14

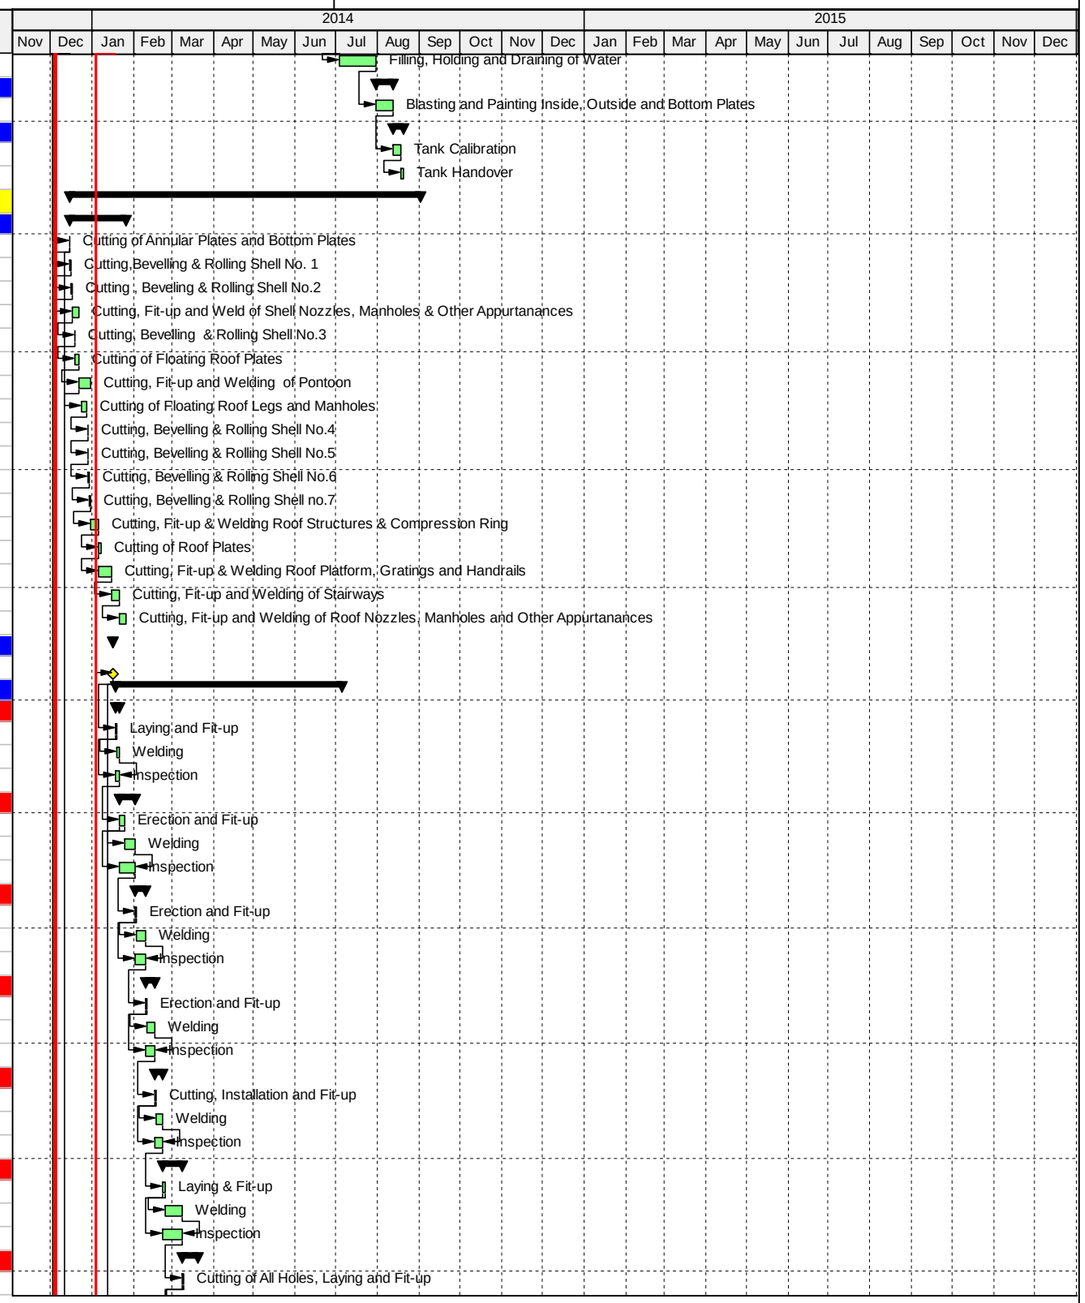

- Actual Level of Effort
- summary
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0721-1428	Welding of Sleeves and Plates	80h	10-Mar-14	19-Mar-14
CZA-TK-0721-1429	Installation of Leg Support	10h	19-Mar-14	20-Mar-14
CZA-TK-0721-1430	Inspection	100h	09-Mar-14	20-Mar-14
CZA-14.2.7.7.7 Shell No.3		**60h**	**20-Mar-14**	**27-Mar-14**
CZA-TK-0721-1431	Erection and Fit-up	10h	20-Mar-14	22-Mar-14
CZA-TK-0721-1432	Welding	50h	22-Mar-14	27-Mar-14
CZA-TK-0721-1433	Inspection	60h	20-Mar-14	27-Mar-14
CZA-14.2.7.7.8 Shell No.4		**60h**	**27-Mar-14**	**03-Apr-14**
CZA-TK-0721-1434	Erection and Fit-up	10h	27-Mar-14	29-Mar-14
CZA-TK-0721-1435	Welding	50h	29-Mar-14	03-Apr-14
CZA-TK-0721-1436	Inspection	60h	27-Mar-14	03-Apr-14
CZA-14.2.7.7.9 Shell No.5		**60h**	**03-Apr-14**	**10-Apr-14**
CZA-TK-0721-1437	Erection and Fit-up	10h	03-Apr-14	05-Apr-14
CZA-TK-0721-1438	Welding	50h	05-Apr-14	10-Apr-14
CZA-TK-0721-1439	Inspection	60h	03-Apr-14	10-Apr-14
CZA-14.2.7.7.10 Shell No.6		**60h**	**10-Apr-14**	**17-Apr-14**
CZA-TK-0721-1440	Erection and Fit-up	10h	10-Apr-14	12-Apr-14
CZA-TK-0721-1441	Welding	50h	12-Apr-14	17-Apr-14
CZA-TK-0721-1442	Inspection	60h	10-Apr-14	17-Apr-14
CZA-14.2.7.7.11 Shell No.7		**70h**	**17-Apr-14**	**26-Apr-14**
CZA-TK-0721-1443	Erection and Fit-up	10h	17-Apr-14	19-Apr-14
CZA-TK-0721-1444	Welding	50h	19-Apr-14	24-Apr-14
CZA-TK-0721-1445	Inspection	60h	19-Apr-14	26-Apr-14
CZA-14.2.7.7.12 Shell Nozzles and attachements (Upper)		**40h**	**26-Apr-14**	**30-Apr-14**
CZA-TK-0721-1446	Cutting, Installation and Fit-up	20h	26-Apr-14	28-Apr-14
CZA-TK-0721-1447	Welding	20h	28-Apr-14	30-Apr-14
CZA-TK-0721-1448	Inspection	40h	26-Apr-14	30-Apr-14
CZA-14.2.7.7.13 Roof Structure		**90h**	**30-Apr-14**	**11-May-14**
CZA-TK-0721-1449	Erection and Fit-up	30h	30-Apr-14	04-May-14
CZA-TK-0721-1450	Welding	60h	04-May-14	11-May-14
CZA-TK-0721-1451	Inspection	90h	30-Apr-14	11-May-14
CZA-14.2.7.7.14 Roof Plates		**90h**	**11-May-14**	**21-May-14**
CZA-TK-0721-1452	Laying and Fit-up	20h	11-May-14	13-May-14
CZA-TK-0721-1453	Welding	70h	13-May-14	21-May-14
CZA-TK-0721-1454	Inspection	90h	11-May-14	21-May-14
CZA-14.2.7.7.15 Compression Ring		**70h**	**21-May-14**	**29-May-14**
CZA-TK-0721-1455	Laying and Fit-up	10h	21-May-14	22-May-14
CZA-TK-0721-1456	Welding	60h	22-May-14	29-May-14
CZA-TK-0721-1457	Inspection	70h	21-May-14	29-May-14
CZA-14.2.7.7.16 Roof Nozzles, Manholes and Other Appurtanances		**60h**	**29-May-14**	**05-Jun-14**
CZA-TK-0721-1458	Installation and Fit-up	20h	29-May-14	01-Jun-14
CZA-TK-0721-1459	Welding	40h	01-Jun-14	05-Jun-14
CZA-TK-0721-1460	Inspection	60h	29-May-14	05-Jun-14
CZA-14.2.7.7.18 Stairway Platform, Handrails and Gratings		**110h**	**05-Jun-14**	**18-Jun-14**
CZA-TK-0721-1461	Erection and Fit-up	30h	05-Jun-14	09-Jun-14
CZA-TK-0721-1462	Welding	80h	09-Jun-14	18-Jun-14
CZA-TK-0721-1463	Inspection	110h	05-Jun-14	18-Jun-14
CZA-14.2.7.7.17 Roof Platform, Handrails and Gratings		**110h**	**18-Jun-14**	**01-Jul-14**
CZA-TK-0721-1464	Erection and Fit-up	30h	18-Jun-14	22-Jun-14
CZA-TK-0721-1465	Welding	80h	22-Jun-14	01-Jul-14
CZA-TK-0721-1466	Inspection	110h	18-Jun-14	01-Jul-14
CZA-14.2.7.7.20 Installation of Primary and Secondary Seal		**30h**	**01-Jul-14**	**05-Jul-14**
CZA-TK-0721-1467	Installation of Primary and Secondary Seal	30h	01-Jul-14	05-Jul-14
CZA-TK-0721-1468	Inspection	10h	03-Jul-14	05-Jul-14

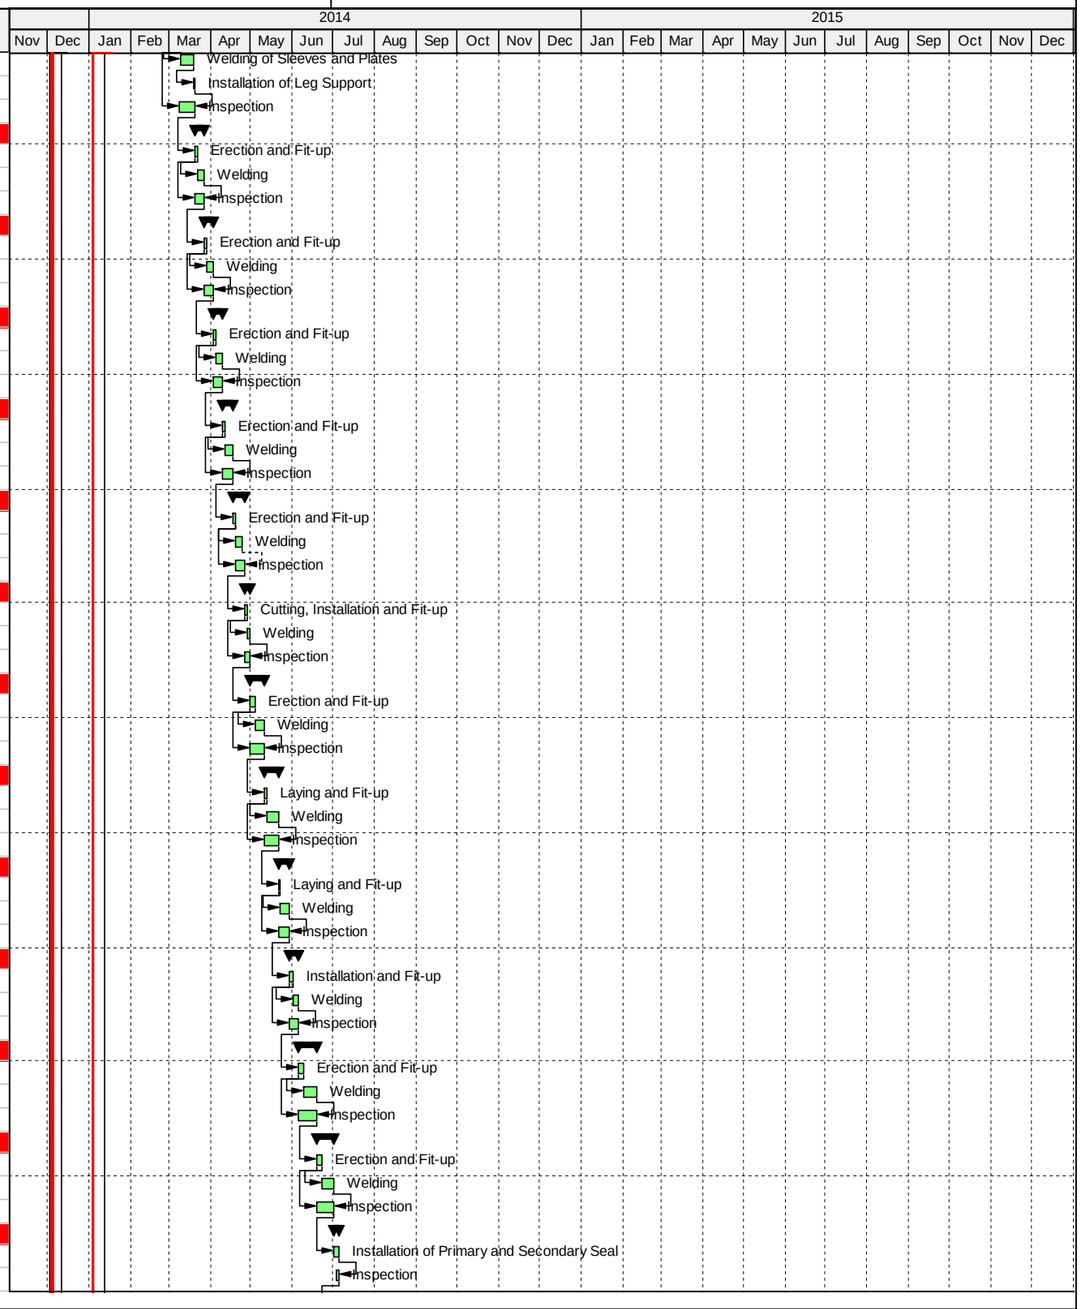

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.2.7.4 Hydrotest		290h	05-Jul-14	07-Aug-14
CZA-TK-0721-1469	Filling, Holding and Draining of Water	290h	05-Jul-14	07-Aug-14
CZA-14.2.7.5 Blasting and Painting		140h	07-Aug-14	24-Aug-14
CZA-TK-0721-1470	Blasting and Painting Inside, Outside and Bottom Plates	140h	07-Aug-14	24-Aug-14
CZA-14.2.7.6 Tank Calibration and Handover		70h	24-Aug-14	01-Sep-14
CZA-TK-0721-1471	Tank Calibration	50h	24-Aug-14	30-Aug-14
CZA-TK-0721-1472	Tank Handover	20h	30-Aug-14	01-Sep-14
CZA-14.2.8 S220-TK-0735(Recovery Methanol Intermediate Tank Dia 29.02m x Ht 19.15mwith IFR)		2708h	24-Dec-13	04-Nov-14
CZA-14.2.8.1 Fabrication Works		368h	24-Dec-13	04-Feb-14
CZA-TK-0735-1431	Cutting of Annular Plates and Bottom Plates	8h	24-Dec-13	24-Dec-13
CZA-TK-0735-1432	Cutting,Bevelling & Rolling Shell No. 7	8h	24-Dec-13	25-Dec-13
CZA-TK-0735-1433	Cutting , Beveling & Rolling Shell No.8	8h	25-Dec-13	26-Dec-13
CZA-TK-0735-1434	Cutting, Fit-up and Weld of Shell Nozzles, Manholes & Other Appurtanances	40h	26-Dec-13	31-Dec-13
CZA-TK-0735-1435	Cutting, Fit-up & Welding Stairway Platform, Gratings and Handrails (Upper Part)	32h	26-Dec-13	30-Dec-13
CZA-TK-0735-1436	Cutting of Deck Plates	16h	30-Dec-13	01-Jan-14
CZA-TK-0735-1437	Cutting, Fit-up and Welding of Pontoon	80h	30-Dec-13	08-Jan-14
CZA-TK-0735-1438	Cutting of Floating Roof Legs and Manholes	32h	08-Jan-14	12-Jan-14
CZA-TK-0735-1439	Cutting, Fit-up & Welding Roof Structures & Compression Ring	40h	12-Jan-14	16-Jan-14
CZA-TK-0735-1440	Cutting of Roof Plates	16h	16-Jan-14	19-Jan-14
CZA-TK-0735-1441	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	19-Jan-14	23-Jan-14
CZA-TK-0735-1442	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	32h	21-Jan-14	25-Jan-14
CZA-TK-0735-1443	Cutting,Bevelling & Rolling Shell No. 6 & 5	8h	25-Jan-14	25-Jan-14
CZA-TK-0735-1444	Cutting,Bevelling & Rolling Shell No. 4 & 3	8h	26-Jan-14	26-Jan-14
CZA-TK-0735-1445	Cutting,Bevelling & Rolling Shell No. 2 & 1	8h	26-Jan-14	27-Jan-14
CZA-TK-0735-1446	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtanances	56h	26-Jan-14	02-Feb-14
CZA-TK-0735-1447	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails (Lower Part)	40h	30-Jan-14	04-Feb-14
CZA-14.2.8.2 FoundationTakeover		0h	25-Jan-14	25-Jan-14
CZA-TK-0735-1448	Foundation Takeover From Client	0h	25-Jan-14	
CZA-14.2.8.7 Mechanical Erection		1780h	26-Jan-14	21-Aug-14
CZA-14.2.8.7.1 Annular Plates		40h	26-Jan-14	30-Jan-14
CZA-TK-0735-1449	Laying and Fit-up	10h	26-Jan-14	27-Jan-14
CZA-TK-0735-1450	Welding	30h	27-Jan-14	30-Jan-14
CZA-TK-0735-1451	Inspection	40h	26-Jan-14	30-Jan-14
CZA-14.2.8.7.2 Bottom Plates		150h	30-Jan-14	17-Feb-14
CZA-TK-0735-1452	Laying and Fit-up	30h	30-Jan-14	03-Feb-14
CZA-TK-0735-1453	Welding	120h	03-Feb-14	17-Feb-14
CZA-TK-0735-1454	Inspection	150h	30-Jan-14	17-Feb-14
CZA-14.2.8.7.3 Shell No.7		80h	17-Feb-14	26-Feb-14
CZA-TK-0735-1455	Erection and Fit-up	20h	17-Feb-14	19-Feb-14
CZA-TK-0735-1456	Welding	60h	19-Feb-14	26-Feb-14
CZA-TK-0735-1457	Inspection	80h	17-Feb-14	26-Feb-14
CZA-14.2.8.7.4 Shell No.8		80h	26-Feb-14	08-Mar-14
CZA-TK-0735-1458	Erection and Fit-up	20h	26-Feb-14	01-Mar-14
CZA-TK-0735-1459	Welding	60h	01-Mar-14	08-Mar-14
CZA-TK-0735-1460	Inspection	80h	26-Feb-14	08-Mar-14
CZA-14.2.8.7.5 Shell Nozzles and Other Attachments		50h	08-Mar-14	13-Mar-14
CZA-TK-0735-1461	Cutting, Installation and Fit-up	20h	08-Mar-14	10-Mar-14
CZA-TK-0735-1462	Welding	30h	10-Mar-14	13-Mar-14
CZA-TK-0735-1463	Inspection	50h	08-Mar-14	13-Mar-14
CZA-14.2.8.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		60h	13-Mar-14	20-Mar-14
CZA-TK-0735-1464	Erection and Fit-up	20h	13-Mar-14	16-Mar-14
CZA-TK-0735-1465	Welding	40h	16-Mar-14	20-Mar-14
CZA-TK-0735-1466	Inspection	60h	13-Mar-14	20-Mar-14
CZA-14.2.8.7.7 Deck Plate		100h	20-Mar-14	01-Apr-14

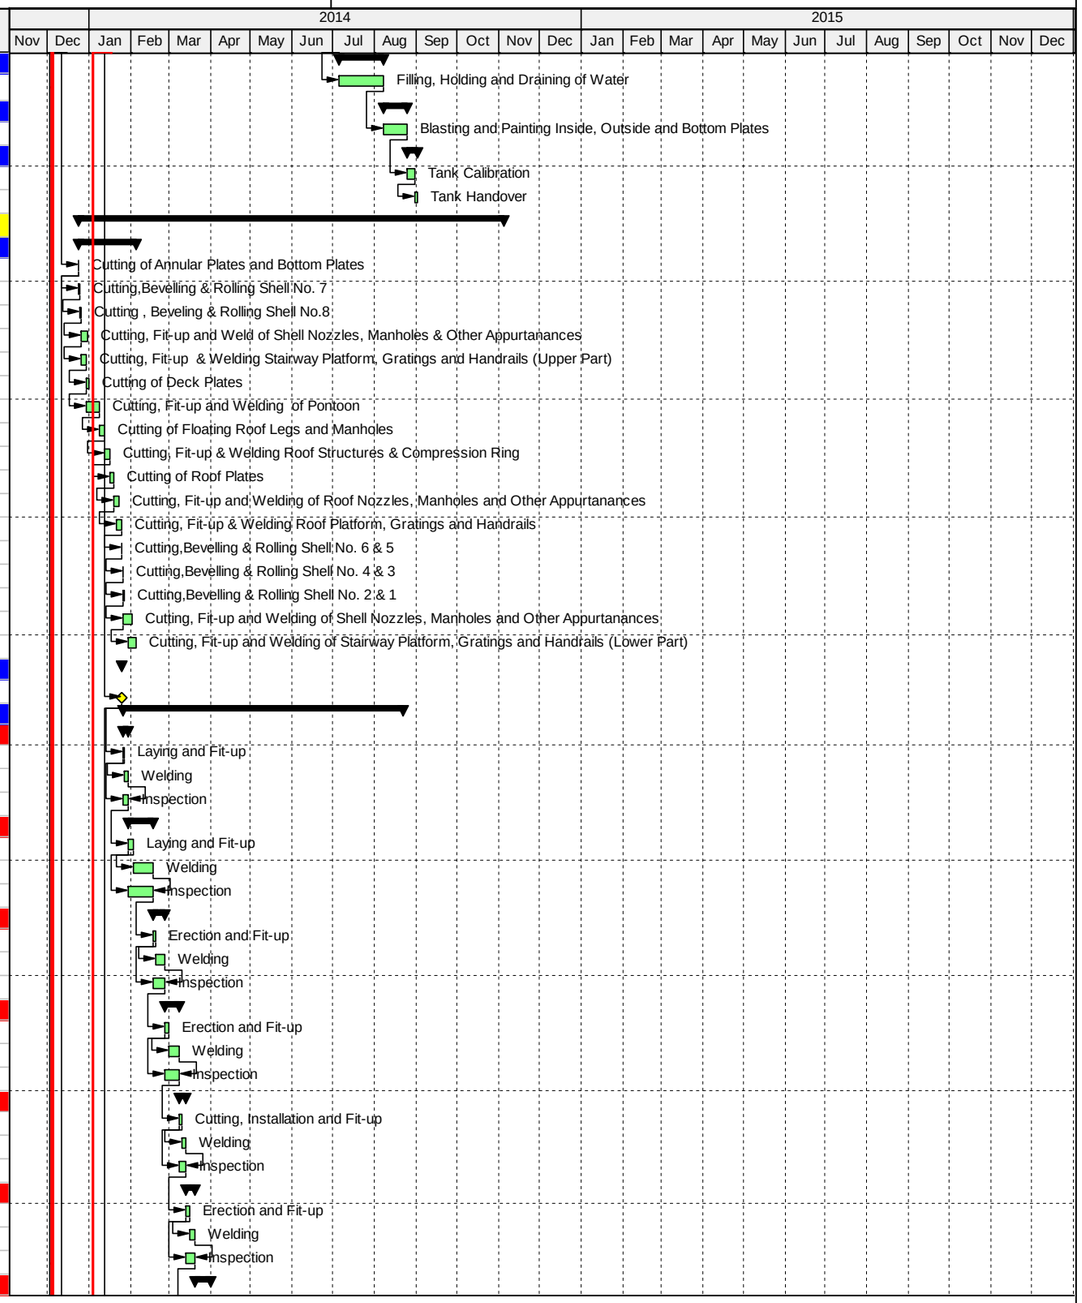

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

Petrofac

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0735-1467	Laying and Fit-up	20h	20-Mar-14	23-Mar-14
CZA-TK-0735-1468	Welding	80h	23-Mar-14	01-Apr-14
CZA-TK-0735-1469	Inspection	100h	20-Mar-14	01-Apr-14
CZA-14.2.8.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**110h**	**01-Apr-14**	**14-Apr-14**
CZA-TK-0735-1470	Laying, Cutting all Holes and Fit-up	30h	01-Apr-14	05-Apr-14
CZA-TK-0735-1471	Welding	80h	01-Apr-14	10-Apr-14
CZA-TK-0735-1472	Inspection	110h	01-Apr-14	14-Apr-14
CZA-14.2.8.7.9 Roof Structure		**60h**	**14-Apr-14**	**21-Apr-14**
CZA-TK-0735-1473	Erection and Fit-up	30h	14-Apr-14	17-Apr-14
CZA-TK-0735-1474	Welding	30h	17-Apr-14	21-Apr-14
CZA-TK-0735-1475	Inspection	60h	14-Apr-14	21-Apr-14
CZA-14.2.8.7.10 Roof Plates		**120h**	**21-Apr-14**	**05-May-14**
CZA-TK-0735-1476	Laying and Fit-up	40h	21-Apr-14	26-Apr-14
CZA-TK-0735-1477	Welding	80h	26-Apr-14	05-May-14
CZA-TK-0735-1478	Inspection	120h	21-Apr-14	05-May-14
CZA-14.2.8.7.11 Compression Ring		**70h**	**05-May-14**	**13-May-14**
CZA-TK-0735-1479	Laying and Fit-up	20h	05-May-14	07-May-14
CZA-TK-0735-1480	Welding	50h	07-May-14	13-May-14
CZA-TK-0735-1481	Inspection	70h	05-May-14	13-May-14
CZA-14.2.8.7.12 Roof Nozzles, Manholes and Other Appurtanances		**60h**	**13-May-14**	**20-May-14**
CZA-TK-0735-1482	Cutting,Installation and Fit-up	20h	13-May-14	15-May-14
CZA-TK-0735-1483	Welding	40h	15-May-14	20-May-14
CZA-TK-0735-1484	Inspection	60h	13-May-14	20-May-14
CZA-14.2.8.7.13 Roof Platform, Gratings and Handrails		**130h**	**20-May-14**	**04-Jun-14**
CZA-TK-0735-1485	Erection and Fit-up	40h	20-May-14	25-May-14
CZA-TK-0735-1486	Welding	90h	25-May-14	04-Jun-14
CZA-TK-0735-1487	Inspection	130h	20-May-14	04-Jun-14
CZA-14.2.8.7.14 Shell No.6		**80h**	**04-Jun-14**	**14-Jun-14**
CZA-TK-0735-1488	Jacking, Erection and Fit-up	20h	04-Jun-14	07-Jun-14
CZA-TK-0735-1489	Welding	60h	07-Jun-14	14-Jun-14
CZA-TK-0735-1490	Inspection	80h	04-Jun-14	14-Jun-14
CZA-14.2.8.7.15 Shell No.5		**80h**	**14-Jun-14**	**23-Jun-14**
CZA-TK-0735-1491	Jacking,Erection and Fit-up	20h	14-Jun-14	16-Jun-14
CZA-TK-0735-1492	Welding	60h	16-Jun-14	23-Jun-14
CZA-TK-0735-1493	Inspection	80h	14-Jun-14	23-Jun-14
CZA-14.2.8.7.16 Shell No.4		**80h**	**23-Jun-14**	**02-Jul-14**
CZA-TK-0735-1494	Jacking,Erection and Fit-up	20h	23-Jun-14	25-Jun-14
CZA-TK-0735-1495	Welding	60h	25-Jun-14	02-Jul-14
CZA-TK-0735-1496	Inspection	80h	23-Jun-14	02-Jul-14
CZA-14.2.8.7.17 Shell No.3		**80h**	**02-Jul-14**	**12-Jul-14**
CZA-TK-0735-1497	Jacking, Erection and Fit-up	20h	02-Jul-14	05-Jul-14
CZA-TK-0735-1498	Welding	60h	05-Jul-14	12-Jul-14
CZA-TK-0735-1499	Inspection	80h	02-Jul-14	12-Jul-14
CZA-14.2.8.7.18 Shell No.2		**80h**	**12-Jul-14**	**21-Jul-14**
CZA-TK-0735-1500	Jacking, Erection and Fit-up	20h	12-Jul-14	14-Jul-14
CZA-TK-0735-1501	Welding	60h	14-Jul-14	21-Jul-14
CZA-TK-0735-1502	Inspection	80h	12-Jul-14	21-Jul-14
CZA-14.2.8.7.19 Shell No.1		**80h**	**21-Jul-14**	**30-Jul-14**
CZA-TK-0735-1503	Jacking, Erection and Fit-up	20h	21-Jul-14	23-Jul-14
CZA-TK-0735-1504	Welding	60h	23-Jul-14	30-Jul-14
CZA-TK-0735-1505	Inspection	80h	21-Jul-14	30-Jul-14
CZA-14.2.8.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**70h**	**30-Jul-14**	**07-Aug-14**
CZA-TK-0735-1506	Lay-out, Cutting, and Fit-up	20h	30-Jul-14	02-Aug-14
CZA-TK-0735-1507	Welding	50h	02-Aug-14	07-Aug-14

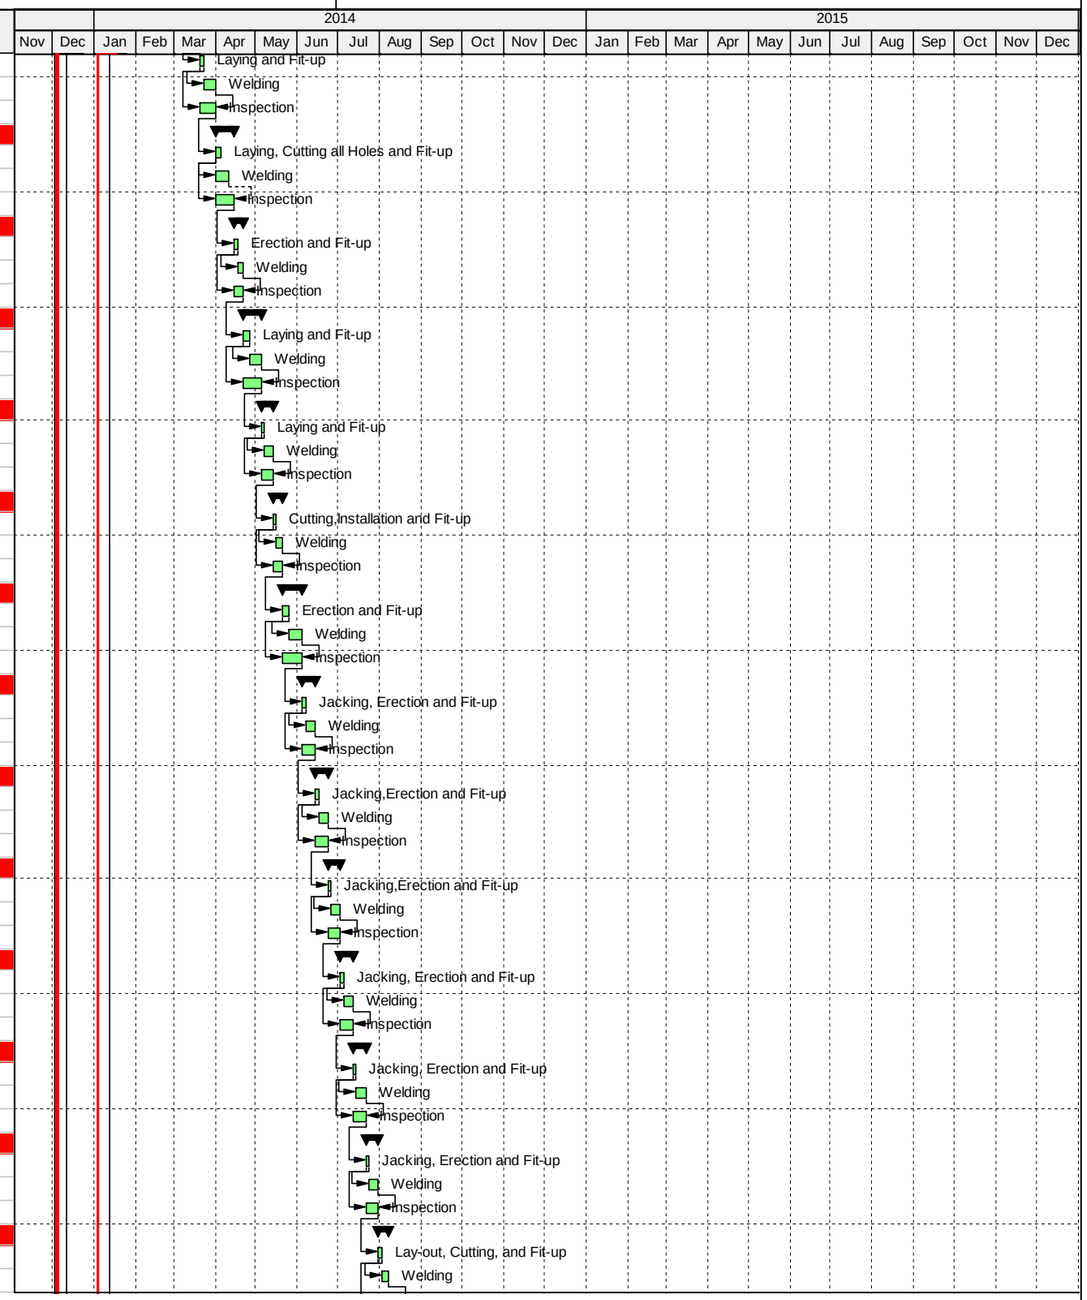

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0735-1508	Inspection	70h	30-Jul-14	07-Aug-14
CZA-14.2.8.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		70h	07-Aug-14	16-Aug-14
CZA-TK-0735-1509	Erection and Fit-up	20h	07-Aug-14	10-Aug-14
CZA-TK-0735-1510	Welding	50h	10-Aug-14	16-Aug-14
CZA-TK-0735-1511	Inspection	70h	07-Aug-14	16-Aug-14
CZA-14.2.8.7.24 Primary and Secondary Seal		50h	16-Aug-14	21-Aug-14
CZA-TK-0735-1512	Installation of Primary and Secondary Seal	40h	16-Aug-14	20-Aug-14
CZA-TK-0735-1513	Inspection	10h	20-Aug-14	21-Aug-14
CZA-14.2.8.4 Hydrotest		380h	21-Aug-14	05-Oct-14
CZA-TK-0735-1514	Filling, Holding and Draining of Water	380h	21-Aug-14	05-Oct-14
CZA-14.2.8.5 Blasting and Painting		190h	05-Oct-14	27-Oct-14
CZA-TK-0735-1515	Blasting and Painting Inside, Outside and Bottom Plates	190h	05-Oct-14	27-Oct-14
CZA-14.2.8.6 Tank Calibration and Handover		70h	27-Oct-14	04-Nov-14
CZA-TK-0735-1516	Tank Calibration	50h	27-Oct-14	02-Nov-14
CZA-TK-0735-1517	Tank Handover	20h	02-Nov-14	04-Nov-14
CZA-14.2.9 S210-TK-0705(Reformate Intermediate Tank Dia 41.94m x Ht 20.10m with IFR)		3348h	24-Dec-13	18-Jan-15
CZA-14.2.9.1 Fabrication Works		360h	24-Dec-13	03-Feb-14
CZA-TK-0705-1470	Cutting of Annular Plates	24h	24-Dec-13	26-Dec-13
CZA-TK-0705-1480	Cutting of Bottom Plates & Compression Ring	24h	24-Dec-13	26-Dec-13
CZA-TK-0705-1490	Cutting, Bevelling & Rolling Shell No.8	16h	24-Dec-13	25-Dec-13
CZA-TK-0705-1500	Cutting, Bevelling and Rolling Shell No.9	16h	24-Dec-13	25-Dec-13
CZA-TK-0705-1510	Cutting of Floating Deck Plate	40h	25-Dec-13	30-Dec-13
CZA-TK-0705-1520	Cutting of Pontoon	80h	28-Dec-13	06-Jan-14
CZA-TK-0705-1530	Cutting, Fit-up, Roof legs and Manholes	56h	29-Dec-13	05-Jan-14
CZA-TK-0705-1540	Cutting, Fit-up, and Welding of Roof Structure	56h	05-Jan-14	11-Jan-14
CZA-TK-0705-1550	Cutting of Roof Plates	16h	12-Jan-14	13-Jan-14
CZA-TK-0705-1560	Cutting, Fit-up, & Welding of Roof Nozzles, Manholes & other Appurtanances	48h	12-Jan-14	16-Jan-14
CZA-TK-0705-1570	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	96h	13-Jan-14	25-Jan-14
CZA-TK-0705-1580	Cutting, Bevelling and Rolling Shell No.7	16h	20-Jan-14	21-Jan-14
CZA-TK-0705-1590	Cutting, Bevelling and Rolling Shell No.6	16h	20-Jan-14	21-Jan-14
CZA-TK-0705-1600	Cutting, Bevelling and Rolling Shell No.5	16h	21-Jan-14	23-Jan-14
CZA-TK-0705-1610	Cutting, Bevelling and Rolling Shell No.4	16h	21-Jan-14	23-Jan-14
CZA-TK-0705-1620	Cutting, Bevelling and Rolling Shell No.3	16h	23-Jan-14	25-Jan-14
CZA-TK-0705-1630	Cutting, Bevelling and Rolling Shell No.2	16h	23-Jan-14	25-Jan-14
CZA-TK-0705-1640	Cutting, Bevelling and Rolling Shell No.1	16h	26-Jan-14	27-Jan-14
CZA-TK-0705-1660	Cutting, Fit-up & Welding of Shell Nozzles, Manholes and Other Appurtanances	56h	27-Jan-14	03-Feb-14
CZA-TK-0705-1670	Cutting, Fit-up & Welding of Stairway Platform, Gratings and Handrails	48h	29-Jan-14	03-Feb-14
CZA-14.2.9.2 FoundationTakeover		0h	25-Jan-14	25-Jan-14
CZA-TK-0705-1680	Foundation Takeover From Client	0h	25-Jan-14	
CZA-14.2.9.7 Mechanical Erection		2120h	26-Jan-14	30-Sep-14
CZA-14.2.9.7.1 Annular Plates		60h	26-Jan-14	02-Feb-14
CZA-TK-0705-1690	Laying and Fit-up	20h	26-Jan-14	28-Jan-14
CZA-TK-0705-1700	Welding	40h	28-Jan-14	02-Feb-14
CZA-TK-0705-1710	Inspection	60h	26-Jan-14	02-Feb-14
CZA-14.2.9.7.2 Bottom Plates		160h	02-Feb-14	20-Feb-14
CZA-TK-0705-1720	Laying and Fit-up	40h	02-Feb-14	06-Feb-14
CZA-TK-0705-1730	Welding	120h	06-Feb-14	20-Feb-14
CZA-TK-0705-1740	Inspection	160h	02-Feb-14	20-Feb-14
CZA-14.2.9.7.3 Shell No.8		80h	20-Feb-14	02-Mar-14
CZA-TK-0705-1750	Erection and Fit-up	20h	20-Feb-14	23-Feb-14
CZA-TK-0705-1760	Welding	60h	23-Feb-14	02-Mar-14
CZA-TK-0705-1770	Inspection	80h	20-Feb-14	02-Mar-14
CZA-14.2.9.7.4 Shell No.9		80h	02-Mar-14	11-Mar-14
CZA-TK-0705-1780	Erection and Fit-up	20h	02-Mar-14	04-Mar-14

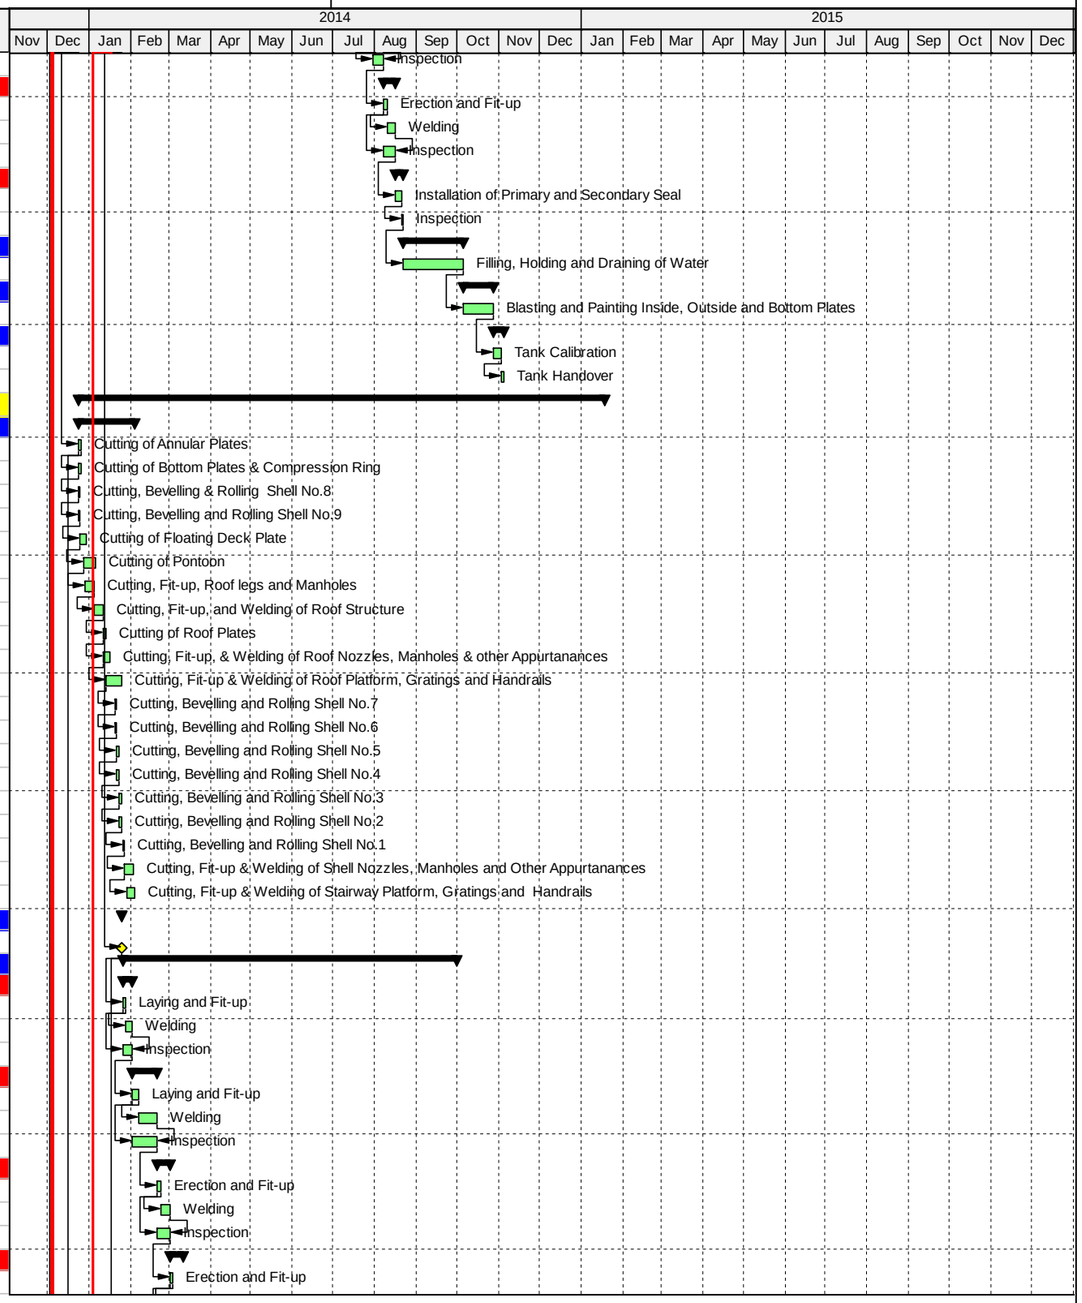

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0705-1790	Welding	60h	04-Mar-14	11-Mar-14
CZA-TK-0705-1800	Inspection	80h	02-Mar-14	11-Mar-14
CZA-14.2.9.7.5 Shell Nozzles and Other Attachments		**70h**	**11-Mar-14**	**19-Mar-14**
CZA-TK-0705-1810	Cutting, Installation and Fit-up	20h	11-Mar-14	13-Mar-14
CZA-TK-0705-1820	Welding	50h	13-Mar-14	19-Mar-14
CZA-TK-0705-1830	Inspection	70h	11-Mar-14	19-Mar-14
CZA-14.2.9.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**100h**	**19-Mar-14**	**31-Mar-14**
CZA-TK-0705-1840	Erection and Fit-up	40h	19-Mar-14	24-Mar-14
CZA-TK-0705-1850	Welding	60h	24-Mar-14	31-Mar-14
CZA-TK-0705-1860	Inspection	100h	19-Mar-14	31-Mar-14
CZA-14.2.9.7.7 Deck Plate		**160h**	**31-Mar-14**	**19-Apr-14**
CZA-TK-0705-1870	Laying and Fit-up	40h	31-Mar-14	05-Apr-14
CZA-TK-0705-1880	Welding	120h	05-Apr-14	19-Apr-14
CZA-TK-0705-1890	Inspection	160h	31-Mar-14	19-Apr-14
CZA-14.2.9.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**120h**	**19-Apr-14**	**03-May-14**
CZA-TK-0705-1900	Laying, Cutting all Holes and Fit-up	40h	19-Apr-14	23-Apr-14
CZA-TK-0705-1910	Welding	110h	19-Apr-14	01-May-14
CZA-TK-0705-1920	Inspection	120h	19-Apr-14	03-May-14
CZA-14.2.9.7.9 Roof Structure		**80h**	**03-May-14**	**12-May-14**
CZA-TK-0705-1930	Erection and Fit-up	30h	03-May-14	06-May-14
CZA-TK-0705-1940	Welding	50h	06-May-14	12-May-14
CZA-TK-0705-1950	Inspection	80h	03-May-14	12-May-14
CZA-14.2.9.7.10 Roof Plates		**120h**	**12-May-14**	**26-May-14**
CZA-TK-0705-1960	Laying and Fit-up	40h	12-May-14	17-May-14
CZA-TK-0705-1970	Welding	80h	17-May-14	26-May-14
CZA-TK-0705-1980	Inspection	120h	12-May-14	26-May-14
CZA-14.2.9.7.11 Compression Ring		**80h**	**26-May-14**	**04-Jun-14**
CZA-TK-0705-2000	Laying and Fit-up	20h	26-May-14	28-May-14
CZA-TK-0705-2010	Welding	60h	28-May-14	04-Jun-14
CZA-TK-0705-2020	Inspection	80h	26-May-14	04-Jun-14
CZA-14.2.9.7.12 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**04-Jun-14**	**12-Jun-14**
CZA-TK-0705-2030	Cutting,Installation and Fit-up	20h	04-Jun-14	07-Jun-14
CZA-TK-0705-2040	Welding	50h	07-Jun-14	12-Jun-14
CZA-TK-0705-2050	Inspection	70h	04-Jun-14	12-Jun-14
CZA-14.2.9.7.13 Roof Platform, Gratings and Handrails		**140h**	**12-Jun-14**	**29-Jun-14**
CZA-TK-0705-2060	Erection and Fit-up	40h	12-Jun-14	17-Jun-14
CZA-TK-0705-2070	Welding	10h	17-Jun-14	18-Jun-14
CZA-TK-0705-2080	Inspection	140h	12-Jun-14	29-Jun-14
CZA-14.2.9.7.14 Shell No.7		**80h**	**29-Jun-14**	**08-Jul-14**
CZA-TK-0705-2090	Jacking, Erection and Fit-up	20h	29-Jun-14	01-Jul-14
CZA-TK-0705-2100	Welding	60h	01-Jul-14	08-Jul-14
CZA-TK-0705-2110	Inspection	80h	29-Jun-14	08-Jul-14
CZA-14.2.9.7.15 Shell No.6		**80h**	**08-Jul-14**	**17-Jul-14**
CZA-TK-0705-2120	Jacking,Erection and Fit-up	20h	08-Jul-14	10-Jul-14
CZA-TK-0705-2130	Welding	60h	10-Jul-14	17-Jul-14
CZA-TK-0705-2140	Inspection	80h	08-Jul-14	17-Jul-14
CZA-14.2.9.7.16 Shell No.5		**80h**	**17-Jul-14**	**27-Jul-14**
CZA-TK-0705-2150	Jacking,Erection and Fit-up	20h	17-Jul-14	20-Jul-14
CZA-TK-0705-2160	Welding	60h	20-Jul-14	27-Jul-14
CZA-TK-0705-2170	Inspection	80h	17-Jul-14	27-Jul-14
CZA-14.2.9.7.17 Shell No.4		**80h**	**27-Jul-14**	**05-Aug-14**
CZA-TK-0705-2180	Jacking, Erection and Fit-up	20h	27-Jul-14	29-Jul-14
CZA-TK-0705-2190	Welding	60h	29-Jul-14	05-Aug-14
CZA-TK-0705-2200	Inspection	80h	27-Jul-14	05-Aug-14

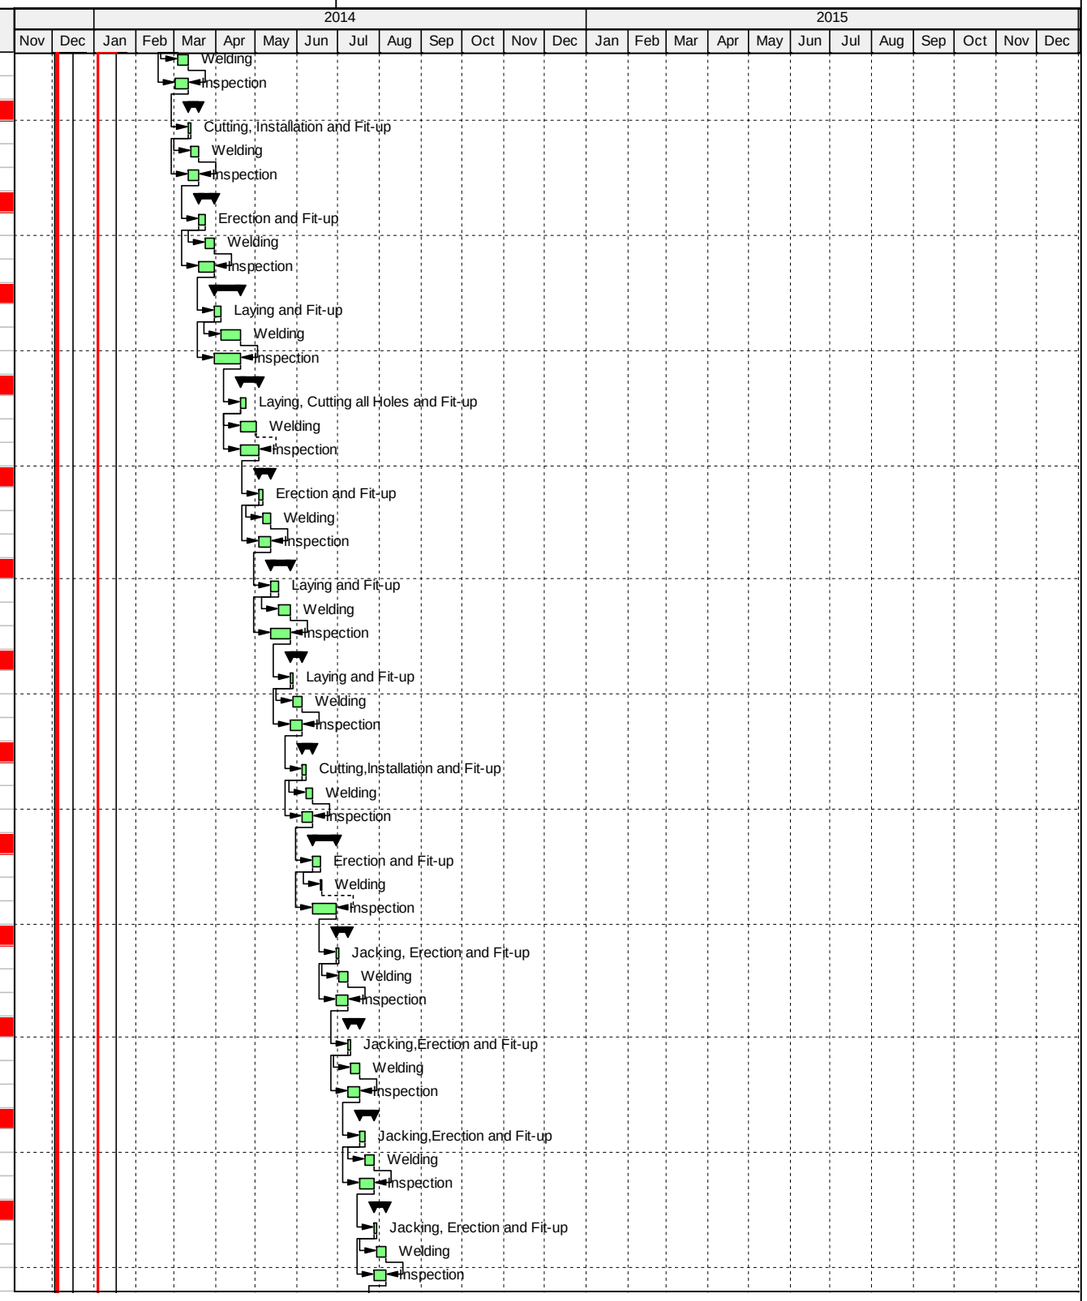

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.2.9.7.18 Shell No.3		**80h**	**05-Aug-14**	**14-Aug-14**
CZA-TK-0705-2210	Jacking, Erection and Fit-up	20h	05-Aug-14	07-Aug-14
CZA-TK-0705-2220	Welding	60h	07-Aug-14	14-Aug-14
CZA-TK-0705-2230	Inspection	80h	05-Aug-14	14-Aug-14
CZA-14.2.9.7.19 Shell No.2		**80h**	**14-Aug-14**	**24-Aug-14**
CZA-TK-0705-2240	Jacking, Erection and Fit-up	20h	14-Aug-14	17-Aug-14
CZA-TK-0705-2250	Welding	60h	17-Aug-14	24-Aug-14
CZA-TK-0705-2260	Inspection	80h	14-Aug-14	24-Aug-14
CZA-14.2.9.7.20 Shell No.1		**80h**	**24-Aug-14**	**02-Sep-14**
CZA-TK-0705-2270	Jacking, Erection and Fit-up	20h	24-Aug-14	26-Aug-14
CZA-TK-0705-2280	Welding	60h	26-Aug-14	02-Sep-14
CZA-TK-0705-2290	Inspection	80h	24-Aug-14	02-Sep-14
CZA-14.2.9.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**70h**	**02-Sep-14**	**10-Sep-14**
CZA-TK-0705-2330	Lay-out, Cutting, and Fit-up	20h	02-Sep-14	04-Sep-14
CZA-TK-0705-2340	Welding	50h	04-Sep-14	10-Sep-14
CZA-TK-0705-2350	Inspection	70h	02-Sep-14	10-Sep-14
CZA-14.2.9.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		**100h**	**10-Sep-14**	**22-Sep-14**
CZA-TK-0705-2360	Erection and Fit-up	30h	10-Sep-14	14-Sep-14
CZA-TK-0705-2370	Welding	70h	14-Sep-14	22-Sep-14
CZA-TK-0705-2380	Inspection	100h	10-Sep-14	22-Sep-14
CZA-14.2.9.7.24 Primary and Secondary Seal		**70h**	**22-Sep-14**	**30-Sep-14**
CZA-TK-0705-2390	Installation of Primary and Secondary Seal	60h	22-Sep-14	29-Sep-14
CZA-TK-0705-2400	Inspection	10h	29-Sep-14	30-Sep-14
CZA-14.2.9.4 Hydrotest		**570h**	**30-Sep-14**	**06-Dec-14**
CZA-TK-0705-2410	Filling, Holding and Draining of Water	570h	30-Sep-14	06-Dec-14
CZA-14.2.9.5 Blasting and Painting		**300h**	**06-Dec-14**	**10-Jan-15**
CZA-TK-0705-2420	Blasting and Painting (Shell, Roof & Bottom)-Outside & Inside	300h	06-Dec-14	10-Jan-15
CZA-14.2.9.6 Tank Calibration and Handover		**70h**	**10-Jan-15**	**18-Jan-15**
CZA-TK-0705-2430	Tank Calibration	50h	10-Jan-15	15-Jan-15
CZA-TK-0705-2440	Tank Handover	20h	15-Jan-15	18-Jan-15
CZA-14.2.2 S210-TK-0700(Heavy Treated Naphtha Intermed Tank Dia 41.94m x Ht 23.15m with IFR)		**3618h**	**29-Dec-13**	**24-Feb-15**
CZA-14.2.2.1 Fabrication Works		**400h**	**29-Dec-13**	**13-Feb-14**
CZA-TK-0700-1000	Cutting of Annular Plates	32h	29-Dec-13	01-Jan-14
CZA-TK-0700-1010	Cutting of Bottom Plates & Compression Ring	32h	29-Dec-13	01-Jan-14
CZA-TK-0700-1020	Cutting, Bevelling & Rolling Shell No.9	16h	31-Dec-13	01-Jan-14
CZA-TK-0700-1030	Cutting, Bevelling and Rolling Shell No.10	16h	31-Dec-13	01-Jan-14
CZA-TK-0700-1040	Cutting of Floating Deck Plate	56h	02-Jan-14	08-Jan-14
CZA-TK-0700-1050	Cutting of Pontoon	80h	04-Jan-14	13-Jan-14
CZA-TK-0700-1060	Cutting, Fit-up, Roof legs and Manholes	56h	06-Jan-14	12-Jan-14
CZA-TK-0700-1070	Cutting, Fit-up, and Welding of Roof Structure	56h	12-Jan-14	19-Jan-14
CZA-TK-0700-1080	Cutting of Roof Plates	16h	19-Jan-14	20-Jan-14
CZA-TK-0700-1090	Cutting, Fit-up, & Welding of Roof Nozzles, Manholes & other Appurtanances	56h	21-Jan-14	27-Jan-14
CZA-TK-0700-1100	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	120h	23-Jan-14	06-Feb-14
CZA-TK-0700-1110	Cutting, Bevelling and Rolling Shell No.8	16h	30-Jan-14	01-Feb-14
CZA-TK-0700-1120	Cutting, Bevelling and Rolling Shell No.7	16h	30-Jan-14	01-Feb-14
CZA-TK-0700-1130	Cutting, Bevelling and Rolling Shell No.6	16h	01-Feb-14	03-Feb-14
CZA-TK-0700-1140	Cutting, Bevelling and Rolling Shell No.5	16h	01-Feb-14	03-Feb-14
CZA-TK-0700-1150	Cutting, Bevelling and Rolling Shell No.4	16h	03-Feb-14	04-Feb-14
CZA-TK-0700-1160	Cutting, Bevelling and Rolling Shell No.3	16h	03-Feb-14	04-Feb-14
CZA-TK-0700-1170	Cutting, Bevelling and Rolling Shell No.2	16h	04-Feb-14	06-Feb-14
CZA-TK-0700-1180	Cutting, Bevelling and Rolling Shell No.1	16h	04-Feb-14	06-Feb-14
CZA-TK-0700-1190	Cutting, Fit-up & Welding of Shell Nozzles, Manholes and Other Appurtanances	64h	06-Feb-14	13-Feb-14
CZA-TK-0700-1200	Cutting, Fit-up & Welding of Stairway Platform, Gratings and Handrails	48h	08-Feb-14	12-Feb-14
CZA-14.2.2.2 FoundationTakeover		**0h**	**30-Jan-14**	**30-Jan-14**

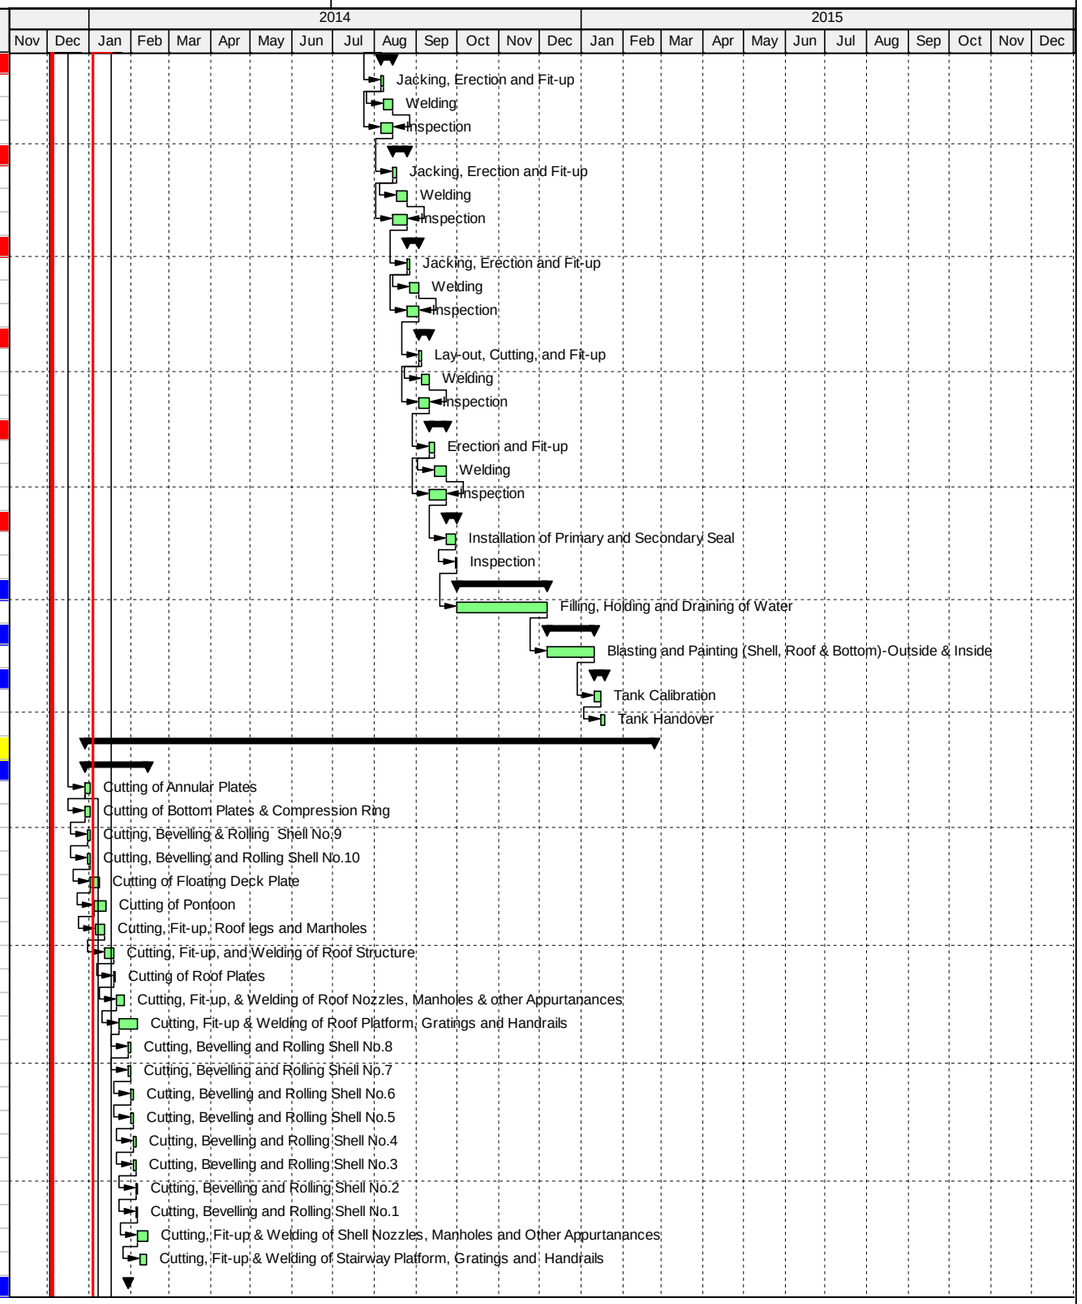

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0700-1210	Foundation Takeover From Client	0h	30-Jan-14	
CZA-14.2.2.3 Mechanical Erection		**2180h**	**01-Feb-14**	**13-Oct-14**
CZA-14.2.2.3.1 Annular Plates		**60h**	**01-Feb-14**	**08-Feb-14**
CZA-TK-0700-1220	Laying and Fit-up	20h	01-Feb-14	03-Feb-14
CZA-TK-0700-1230	Welding	40h	03-Feb-14	08-Feb-14
CZA-TK-0700-1240	Inspection	60h	01-Feb-14	08-Feb-14
CZA-14.2.2.3.2 Bottom Plates		**160h**	**08-Feb-14**	**26-Feb-14**
CZA-TK-0700-1250	Laying and Fit-up	40h	08-Feb-14	12-Feb-14
CZA-TK-0700-1260	Welding	120h	12-Feb-14	26-Feb-14
CZA-TK-0700-1270	Inspection	160h	08-Feb-14	26-Feb-14
CZA-14.2.2.3.3 Shell No.9		**80h**	**26-Feb-14**	**08-Mar-14**
CZA-TK-0700-1280	Erection and Fit-up	20h	26-Feb-14	01-Mar-14
CZA-TK-0700-1290	Welding	60h	01-Mar-14	08-Mar-14
CZA-TK-0700-1300	Inspection	80h	26-Feb-14	08-Mar-14
CZA-14.2.2.3.4 Shell No.10		**80h**	**08-Mar-14**	**17-Mar-14**
CZA-TK-0700-1310	Erection and Fit-up	20h	08-Mar-14	10-Mar-14
CZA-TK-0700-1320	Welding	60h	10-Mar-14	17-Mar-14
CZA-TK-0700-1330	Inspection	80h	08-Mar-14	17-Mar-14
CZA-14.2.2.3.5 Shell Nozzles and Other Attachments		**70h**	**17-Mar-14**	**25-Mar-14**
CZA-TK-0700-1340	Cutting, Installation and Fit-up	20h	17-Mar-14	19-Mar-14
CZA-TK-0700-1350	Welding	50h	19-Mar-14	25-Mar-14
CZA-TK-0700-1360	Inspection	70h	17-Mar-14	25-Mar-14
CZA-14.2.2.3.6 Stairway Platform, Handrails and Gratings (Upper Part)		**80h**	**25-Mar-14**	**03-Apr-14**
CZA-TK-0700-1370	Erection and Fit-up	30h	25-Mar-14	29-Mar-14
CZA-TK-0700-1380	Welding	50h	29-Mar-14	03-Apr-14
CZA-TK-0700-1390	Inspection	80h	25-Mar-14	03-Apr-14
CZA-14.2.2.3.7 Deck Plate		**150h**	**03-Apr-14**	**21-Apr-14**
CZA-TK-0700-1400	Laying and Fit-up	40h	03-Apr-14	08-Apr-14
CZA-TK-0700-1410	Welding	110h	08-Apr-14	21-Apr-14
CZA-TK-0700-1420	Inspection	150h	03-Apr-14	21-Apr-14
CZA-14.2.2.3.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**140h**	**21-Apr-14**	**07-May-14**
CZA-TK-0700-1430	Laying, Cutting all Holes and Fit-up	40h	21-Apr-14	26-Apr-14
CZA-TK-0700-1440	Welding	100h	21-Apr-14	03-May-14
CZA-TK-0700-1450	Inspection	140h	21-Apr-14	07-May-14
CZA-14.2.2.3.9 Roof Structure		**60h**	**07-May-14**	**14-May-14**
CZA-TK-0700-1460	Erection and Fit-up	30h	07-May-14	11-May-14
CZA-TK-0700-1470	Welding	30h	11-May-14	14-May-14
CZA-TK-0700-1480	Inspection	60h	07-May-14	14-May-14
CZA-14.2.2.3.10 Roof Plates		**120h**	**14-May-14**	**28-May-14**
CZA-TK-0700-1490	Laying and Fit-up	40h	14-May-14	19-May-14
CZA-TK-0700-1500	Welding	80h	19-May-14	28-May-14
CZA-TK-0700-1510	Inspection	120h	14-May-14	28-May-14
CZA-14.2.2.3.11 Compression Ring		**80h**	**28-May-14**	**07-Jun-14**
CZA-TK-0700-1520	Laying and Fit-up	20h	28-May-14	31-May-14
CZA-TK-0700-1530	Welding	60h	31-May-14	07-Jun-14
CZA-TK-0700-1540	Inspection	80h	28-May-14	07-Jun-14
CZA-14.2.2.3.12 Roof Nozzles, Manholes and Other Appurtanances		**80h**	**07-Jun-14**	**16-Jun-14**
CZA-TK-0700-1550	Cutting,Installation and Fit-up	20h	07-Jun-14	09-Jun-14
CZA-TK-0700-1560	Welding	60h	09-Jun-14	16-Jun-14
CZA-TK-0700-1570	Inspection	80h	07-Jun-14	16-Jun-14
CZA-14.2.2.3.13 Roof Platform, Gratings and Handrails		**140h**	**16-Jun-14**	**02-Jul-14**
CZA-TK-0700-1580	Erection and Fit-up	40h	16-Jun-14	21-Jun-14
CZA-TK-0700-1590	Welding	100h	21-Jun-14	02-Jul-14
CZA-TK-0700-1600	Inspection	140h	16-Jun-14	02-Jul-14

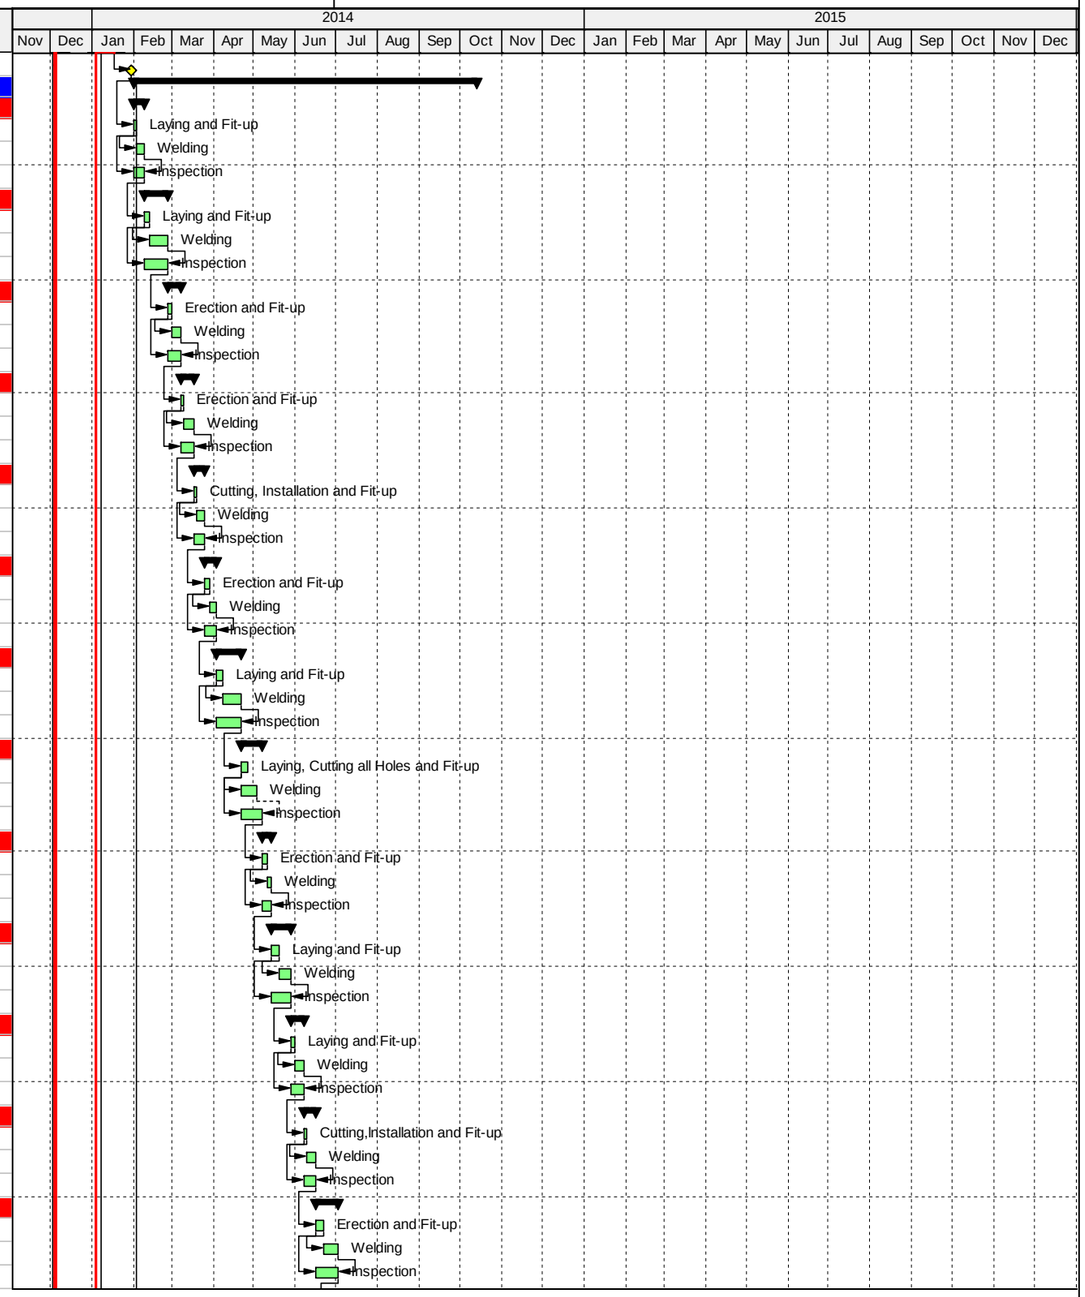

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.2.2.3.14 Shell No.8		80h	02-Jul-14	12-Jul-14
CZA-TK-0700-1610	Jacking, Erection and Fit-up	20h	02-Jul-14	05-Jul-14
CZA-TK-0700-1620	Welding	60h	05-Jul-14	12-Jul-14
CZA-TK-0700-1630	Inspection	80h	02-Jul-14	12-Jul-14
CZA-14.2.2.3.15 Shell No.7		80h	12-Jul-14	21-Jul-14
CZA-TK-0700-1640	Jacking,Erection and Fit-up	20h	12-Jul-14	14-Jul-14
CZA-TK-0700-1650	Welding	60h	14-Jul-14	21-Jul-14
CZA-TK-0700-1660	Inspection	80h	12-Jul-14	21-Jul-14
CZA-14.2.2.3.16 Shell No.6		80h	21-Jul-14	30-Jul-14
CZA-TK-0700-1670	Jacking,Erection and Fit-up	20h	21-Jul-14	23-Jul-14
CZA-TK-0700-1680	Welding	60h	23-Jul-14	30-Jul-14
CZA-TK-0700-1690	Inspection	80h	21-Jul-14	30-Jul-14
CZA-14.2.2.3.17 Shell No.5		80h	30-Jul-14	09-Aug-14
CZA-TK-0700-1700	Jacking, Erection and Fit-up	20h	30-Jul-14	02-Aug-14
CZA-TK-0700-1710	Welding	60h	02-Aug-14	09-Aug-14
CZA-TK-0700-1720	Inspection	80h	30-Jul-14	09-Aug-14
CZA-14.2.2.3.18 Shell No.4		80h	09-Aug-14	18-Aug-14
CZA-TK-0700-1730	Jacking, Erection and Fit-up	20h	09-Aug-14	11-Aug-14
CZA-TK-0700-1740	Welding	60h	11-Aug-14	18-Aug-14
CZA-TK-0700-1750	Inspection	80h	09-Aug-14	18-Aug-14
CZA-14.2.2.3.19 Shell No.3		80h	18-Aug-14	27-Aug-14
CZA-TK-0700-1760	Jacking, Erection and Fit-up	20h	18-Aug-14	20-Aug-14
CZA-TK-0700-1770	Welding	60h	20-Aug-14	27-Aug-14
CZA-TK-0700-1780	Inspection	80h	18-Aug-14	27-Aug-14
CZA-14.2.2.3.20 Shell No.2		80h	27-Aug-14	06-Sep-14
CZA-TK-0700-1790	Jacking, Erection and Fit-up	20h	27-Aug-14	30-Aug-14
CZA-TK-0700-1800	Welding	60h	30-Aug-14	06-Sep-14
CZA-TK-0700-1810	Inspection	80h	27-Aug-14	06-Sep-14
CZA-14.2.2.3.21 Shell No.1		80h	06-Sep-14	15-Sep-14
CZA-TK-0700-1820	Jacking, Erection and Fit-up	20h	06-Sep-14	08-Sep-14
CZA-TK-0700-1830	Welding	60h	08-Sep-14	15-Sep-14
CZA-TK-0700-1840	Inspection	80h	06-Sep-14	15-Sep-14
CZA-14.2.2.3.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		70h	15-Sep-14	23-Sep-14
CZA-TK-0700-1850	Lay-out, Cutting, and Fit-up	20h	15-Sep-14	17-Sep-14
CZA-TK-0700-1860	Welding	50h	17-Sep-14	23-Sep-14
CZA-TK-0700-1870	Inspection	70h	15-Sep-14	23-Sep-14
CZA-14.2.2.3.23 Stairway Platform, Handrails and Gratings (Lower Part)		100h	23-Sep-14	05-Oct-14
CZA-TK-0700-1880	Erection and Fit-up	30h	23-Sep-14	27-Sep-14
CZA-TK-0700-1890	Welding	70h	27-Sep-14	05-Oct-14
CZA-TK-0700-1900	Inspection	100h	23-Sep-14	05-Oct-14
CZA-14.2.2.3.24 Primary and Secondary Seal		70h	05-Oct-14	13-Oct-14
CZA-TK-0700-1910	Installation of Primary and Secondary Seal	60h	05-Oct-14	12-Oct-14
CZA-TK-0700-1920	Inspection	10h	12-Oct-14	13-Oct-14
CZA-14.2.2.4 Hydrotest		720h	13-Oct-14	05-Jan-15
CZA-TK-0700-1930	Filling, Holding and Draining of Water	720h	13-Oct-14	05-Jan-15
CZA-14.2.2.5 Blasting and Painting		360h	05-Jan-15	16-Feb-15
CZA-TK-0700-1940	Blasting and Painting (Shell, Roof & Bottom)-Outside & Inside	360h	05-Jan-15	16-Feb-15
CZA-14.2.2.6 Tank Calibration and Handover		70h	16-Feb-15	24-Feb-15
CZA-TK-0700-1950	Tank Calibration	50h	16-Feb-15	22-Feb-15
CZA-TK-0700-1960	Tank Handover	20h	22-Feb-15	24-Feb-15
CZA-14.2.3 S220-TK-0710(C9/C10 Aromatics Intermediate Tank Dia 29.02m x Ht 18.10with IFR)		2642h	20-Jan-14	24-Nov-14
CZA-14.2.3.1 Fabrication Works		352h	20-Jan-14	02-Mar-14
CZA-TK-0710-1000	Cutting of Annular Plates	16h	20-Jan-14	21-Jan-14
CZA-TK-0710-1010	Cutting of Bottom Plates	16h	20-Jan-14	21-Jan-14

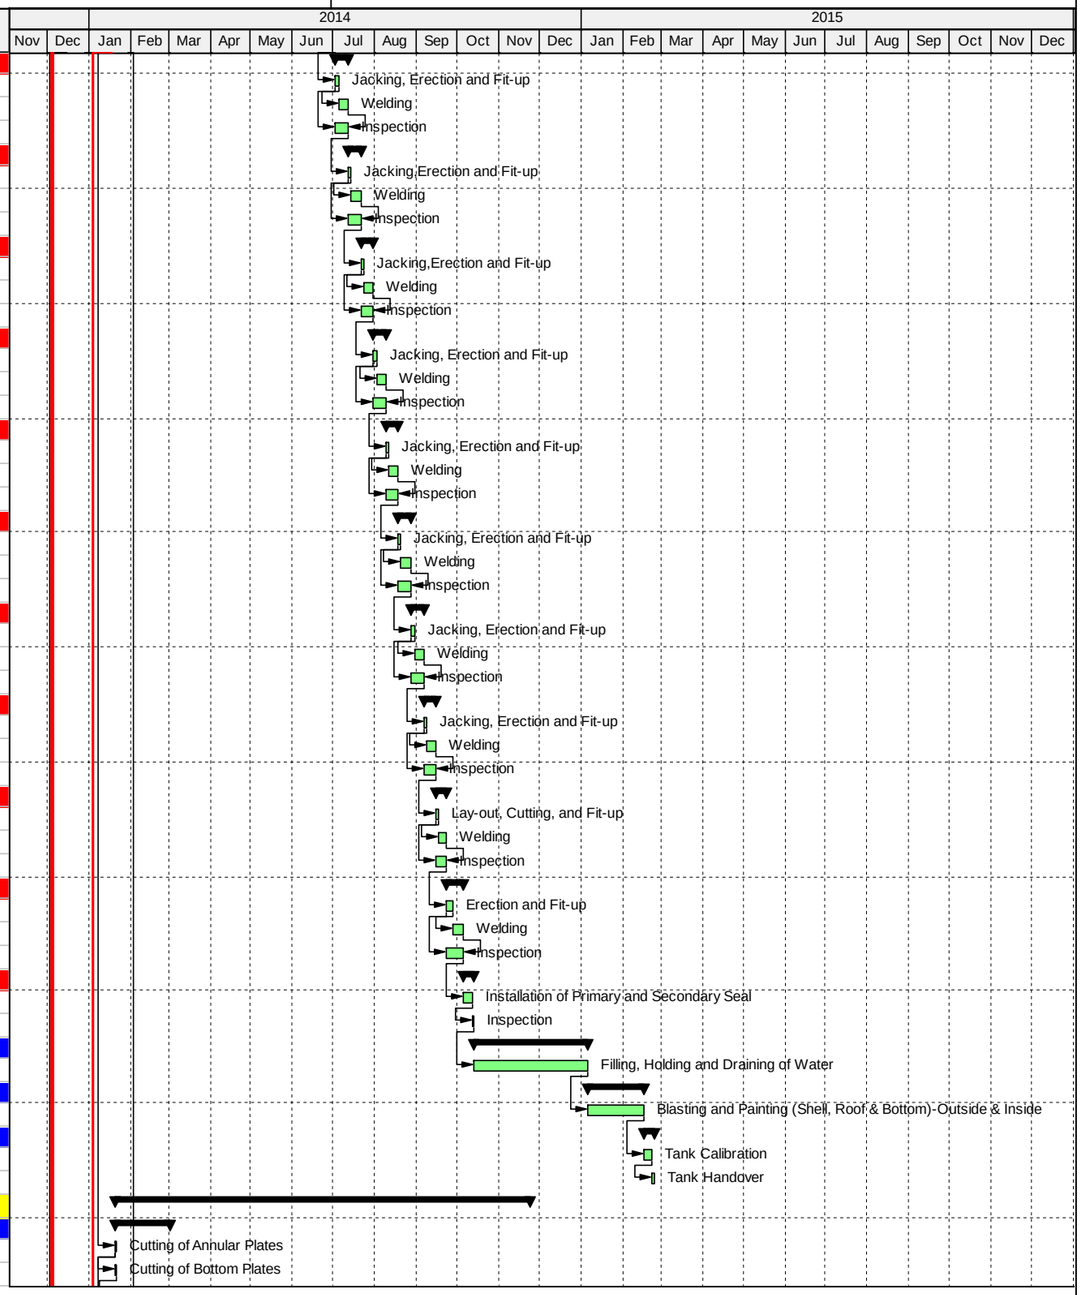

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0710-1020	Cutting, Beveling & Rolling Shell No.7	8h	21-Jan-14	22-Jan-14
CZA-TK-0710-1030	Cutting, Bevelling & Rolling Shell No.8	8h	21-Jan-14	22-Jan-14
CZA-TK-0710-1040	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails (Upper Part)	56h	22-Jan-14	29-Jan-14
CZA-TK-0710-1050	Cutting of Deck Plate	16h	29-Jan-14	30-Jan-14
CZA-TK-0710-1060	Cutting of Pontoon, Legs and Other Appurtanances	56h	30-Jan-14	06-Feb-14
CZA-TK-0710-1070	Cutting of Compression Ring	16h	06-Feb-14	08-Feb-14
CZA-TK-0710-1080	Cutting, Fit-up and Welding of Roof Structure	40h	09-Feb-14	12-Feb-14
CZA-TK-0710-1090	Cutting of Roof Plates	8h	13-Feb-14	13-Feb-14
CZA-TK-0710-1100	Cutting of Roof Nozzles, Manholes and Other Appurtanances	40h	13-Feb-14	17-Feb-14
CZA-TK-0710-1110	Cutting, Fit-up and welding of Roof Platform, Gratings and Handrails	8h	18-Feb-14	18-Feb-14
CZA-TK-0710-1120	Cutting, Bevelling & Rolling of Shell No.7	8h	18-Feb-14	18-Feb-14
CZA-TK-0710-1130	Cutting, Bevelling & Rolling of Shell No.6	8h	18-Feb-14	19-Feb-14
CZA-TK-0710-1140	Cutting, Bevelling & Rolling of Shell No.5	8h	19-Feb-14	20-Feb-14
CZA-TK-0710-1150	Cutting, Bevelling & Rolling of Shell No.4	8h	20-Feb-14	22-Feb-14
CZA-TK-0710-1160	Cutting, Bevelling & Rolling of Shell No.3	8h	22-Feb-14	22-Feb-14
CZA-TK-0710-1170	Cutting, Bevelling & Rolling of Shell No.2	8h	23-Feb-14	23-Feb-14
CZA-TK-0710-1180	Cutting, Bevelling & Rolling of Shell No.1	8h	23-Feb-14	23-Feb-14
CZA-TK-0710-1190	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	40h	23-Feb-14	27-Feb-14
CZA-TK-0710-1191	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails (Lower Part)	56h	23-Feb-14	02-Mar-14
CZA-14.2.3.2 Foundation Takeover		**0h**	**15-Feb-14**	**15-Feb-14**
CZA-TK-0710-1200	Foundation Takeover from Client	0h	15-Feb-14	
CZA-14.2.3.7 Mechanical Erection		**1810h**	**16-Feb-14**	**15-Sep-14**
CZA-14.2.3.7.1 Annular Plates		**40h**	**16-Feb-14**	**20-Feb-14**
CZA-TK-0710-1210	Laying and Fit-up	10h	16-Feb-14	17-Feb-14
CZA-TK-0710-1220	Welding	30h	17-Feb-14	20-Feb-14
CZA-TK-0710-1230	Inspection	40h	16-Feb-14	20-Feb-14
CZA-14.2.3.7.2 Bottom Plates		**70h**	**20-Feb-14**	**01-Mar-14**
CZA-TK-0710-1240	Laying and Fit-up	20h	20-Feb-14	23-Feb-14
CZA-TK-0710-1250	Welding	50h	23-Feb-14	01-Mar-14
CZA-TK-0710-1260	Inspection	70h	20-Feb-14	01-Mar-14
CZA-14.2.3.7.3 Shell No.7		**70h**	**01-Mar-14**	**09-Mar-14**
CZA-TK-0710-1270	Erection and Fit-up	10h	01-Mar-14	02-Mar-14
CZA-TK-0710-1280	Welding	60h	02-Mar-14	09-Mar-14
CZA-TK-0710-1290	Inspection	70h	01-Mar-14	09-Mar-14
CZA-14.2.3.7.4 Shell No.8		**70h**	**09-Mar-14**	**17-Mar-14**
CZA-TK-0710-1300	Erection and Fit-up	10h	09-Mar-14	10-Mar-14
CZA-TK-0710-1310	Welding	60h	10-Mar-14	17-Mar-14
CZA-TK-0710-1320	Inspection	70h	09-Mar-14	17-Mar-14
CZA-14.2.3.7.5 Shell Nozzles and Other Attachments		**50h**	**17-Mar-14**	**23-Mar-14**
CZA-TK-0710-1330	Cutting, Installation and Fit-up	20h	17-Mar-14	19-Mar-14
CZA-TK-0710-1340	Welding	30h	19-Mar-14	23-Mar-14
CZA-TK-0710-1350	Inspection	50h	17-Mar-14	23-Mar-14
CZA-14.2.3.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**80h**	**23-Mar-14**	**01-Apr-14**
CZA-TK-0710-1360	Erection and Fit-up	20h	23-Mar-14	25-Mar-14
CZA-TK-0710-1370	Welding	60h	25-Mar-14	01-Apr-14
CZA-TK-0710-1380	Inspection	80h	23-Mar-14	01-Apr-14
CZA-14.2.3.7.7 Deck Plate		**130h**	**01-Apr-14**	**16-Apr-14**
CZA-TK-0710-1390	Laying and Fit-up	30h	01-Apr-14	05-Apr-14
CZA-TK-0710-1400	Welding	100h	05-Apr-14	16-Apr-14
CZA-TK-0710-1410	Inspection	130h	01-Apr-14	16-Apr-14
CZA-14.2.3.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**140h**	**16-Apr-14**	**03-May-14**
CZA-TK-0710-1420	Laying, Cutting all Holes and Fit-up	40h	16-Apr-14	21-Apr-14
CZA-TK-0710-1430	Welding	100h	16-Apr-14	28-Apr-14
CZA-TK-0710-1440	Inspection	140h	16-Apr-14	03-May-14

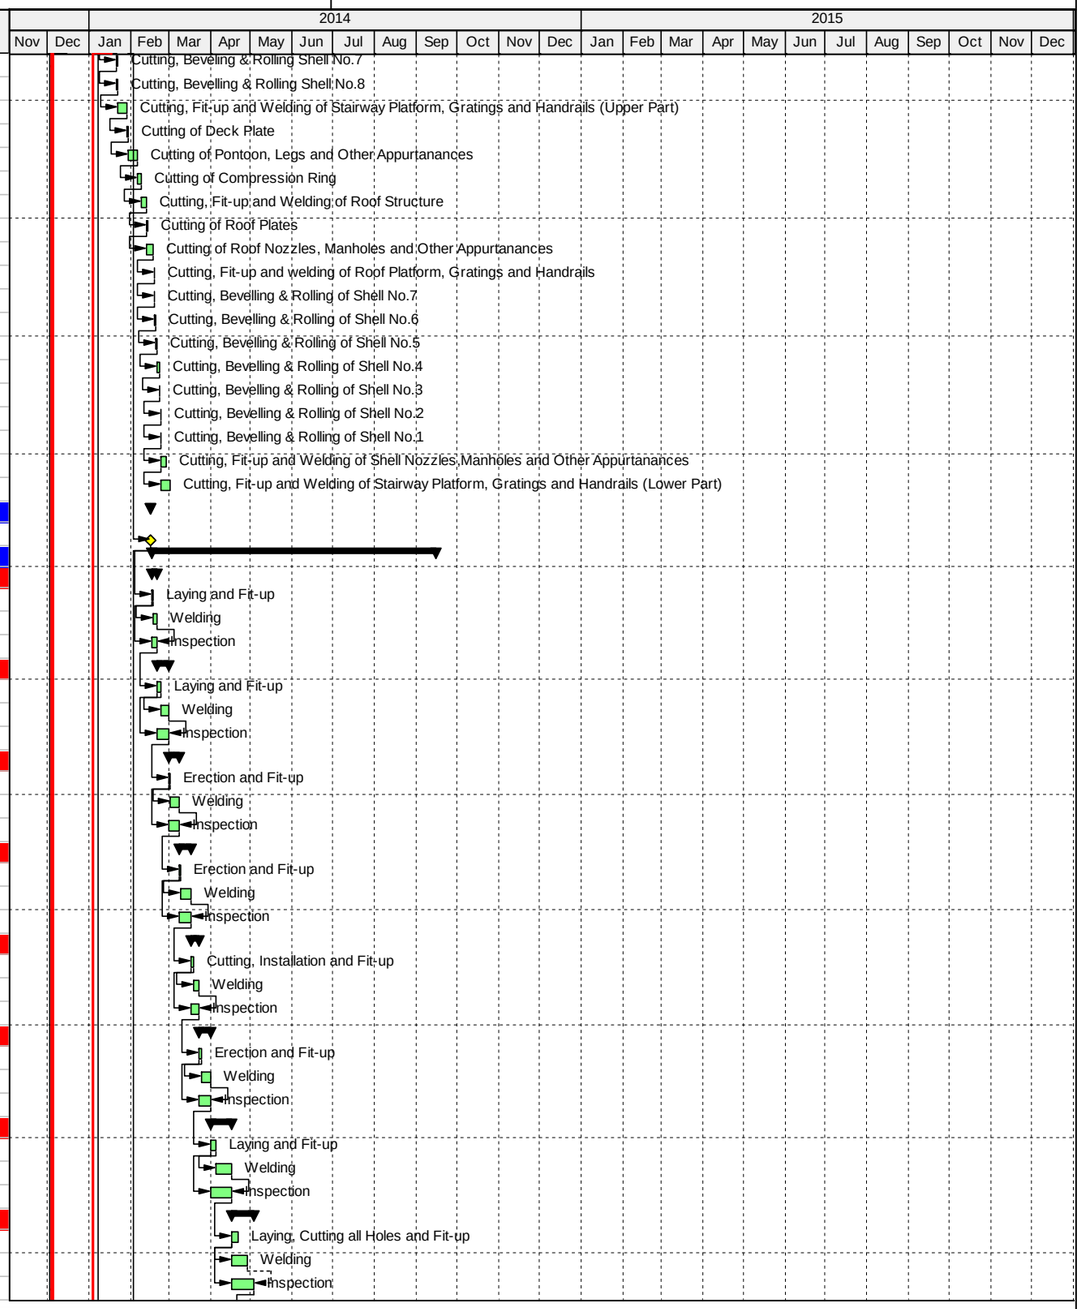

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone
- summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.2.3.7.9	**Roof Structure**	100h	03-May-14	14-May-14
CZA-TK-0710-1450	Erection and Fit-up	30h	03-May-14	06-May-14
CZA-TK-0710-1460	Welding	70h	06-May-14	14-May-14
CZA-TK-0710-1470	Inspection	100h	03-May-14	14-May-14
CZA-14.2.3.7.10	**Roof Plates**	100h	14-May-14	26-May-14
CZA-TK-0710-1480	Laying and Fit-up	30h	14-May-14	18-May-14
CZA-TK-0710-1490	Welding	70h	18-May-14	26-May-14
CZA-TK-0710-1500	Inspection	100h	14-May-14	26-May-14
CZA-14.2.3.7.11	**Compression Ring**	90h	26-May-14	05-Jun-14
CZA-TK-0710-1510	Laying and Fit-up	30h	26-May-14	29-May-14
CZA-TK-0710-1520	Welding	60h	29-May-14	05-Jun-14
CZA-TK-0710-1530	Inspection	90h	26-May-14	05-Jun-14
CZA-14.2.3.7.12	**Roof Nozzles, Manholes and Other Appurtanances**	90h	05-Jun-14	16-Jun-14
CZA-TK-0710-1540	Cutting,Installation and Fit-up	30h	05-Jun-14	09-Jun-14
CZA-TK-0710-1550	Welding	60h	09-Jun-14	16-Jun-14
CZA-TK-0710-1560	Inspection	90h	05-Jun-14	16-Jun-14
CZA-14.2.3.7.13	**Roof Platform, Gratings and Handrails**	170h	16-Jun-14	06-Jul-14
CZA-TK-0710-1570	Erection and Fit-up	50h	16-Jun-14	22-Jun-14
CZA-TK-0710-1580	Welding	120h	22-Jun-14	06-Jul-14
CZA-TK-0710-1590	Inspection	170h	16-Jun-14	06-Jul-14
CZA-14.2.3.7.14	**Shell No.6**	70h	06-Jul-14	14-Jul-14
CZA-TK-0710-1600	Jacking, Erection and Fit-up	10h	06-Jul-14	07-Jul-14
CZA-TK-0710-1610	Welding	60h	07-Jul-14	14-Jul-14
CZA-TK-0710-1620	Inspection	70h	06-Jul-14	14-Jul-14
CZA-14.2.3.7.15	**Shell No.5**	70h	14-Jul-14	22-Jul-14
CZA-TK-0710-1630	Jacking,Erection and Fit-up	10h	14-Jul-14	15-Jul-14
CZA-TK-0710-1640	Welding	60h	15-Jul-14	22-Jul-14
CZA-TK-0710-1650	Inspection	70h	14-Jul-14	22-Jul-14
CZA-14.2.3.7.16	**Shell No.4**	70h	22-Jul-14	30-Jul-14
CZA-TK-0710-1660	Jacking,Erection and Fit-up	10h	22-Jul-14	23-Jul-14
CZA-TK-0710-1670	Welding	60h	23-Jul-14	30-Jul-14
CZA-TK-0710-1680	Inspection	70h	22-Jul-14	30-Jul-14
CZA-14.2.3.7.17	**Shell No.3**	70h	30-Jul-14	07-Aug-14
CZA-TK-0710-1690	Jacking, Erection and Fit-up	10h	30-Jul-14	31-Jul-14
CZA-TK-0710-1700	Welding	60h	31-Jul-14	07-Aug-14
CZA-TK-0710-1710	Inspection	70h	30-Jul-14	07-Aug-14
CZA-14.2.3.7.18	**Shell No.2**	70h	07-Aug-14	16-Aug-14
CZA-TK-0710-1720	Jacking, Erection and Fit-up	10h	07-Aug-14	09-Aug-14
CZA-TK-0710-1730	Welding	60h	09-Aug-14	16-Aug-14
CZA-TK-0710-1740	Inspection	70h	07-Aug-14	16-Aug-14
CZA-14.2.3.7.19	**Shell No.1**	70h	16-Aug-14	24-Aug-14
CZA-TK-0710-1750	Jacking, Erection and Fit-up	10h	16-Aug-14	17-Aug-14
CZA-TK-0710-1760	Welding	60h	17-Aug-14	24-Aug-14
CZA-TK-0710-1770	Inspection	70h	16-Aug-14	24-Aug-14
CZA-14.2.3.7.22	**Shell Nozzles, Manholes , Attachments and Other Appurtanances**	70h	24-Aug-14	01-Sep-14
CZA-TK-0710-1780	Lay-out, Cutting, and Fit-up	20h	24-Aug-14	26-Aug-14
CZA-TK-0710-1790	Welding	50h	26-Aug-14	01-Sep-14
CZA-TK-0710-1800	Inspection	70h	24-Aug-14	01-Sep-14
CZA-14.2.3.7.23	**Stairway Platform, Handrails and Gratings (Lower Part)**	70h	01-Sep-14	09-Sep-14
CZA-TK-0710-1810	Erection and Fit-up	20h	01-Sep-14	03-Sep-14
CZA-TK-0710-1820	Welding	50h	03-Sep-14	09-Sep-14
CZA-TK-0710-1830	Inspection	70h	01-Sep-14	09-Sep-14
CZA-14.2.3.7.24	**Primary and Secondary Seal**	50h	09-Sep-14	15-Sep-14
CZA-TK-0710-1840	Installation of Primary and Secondary Seal	40h	09-Sep-14	14-Sep-14

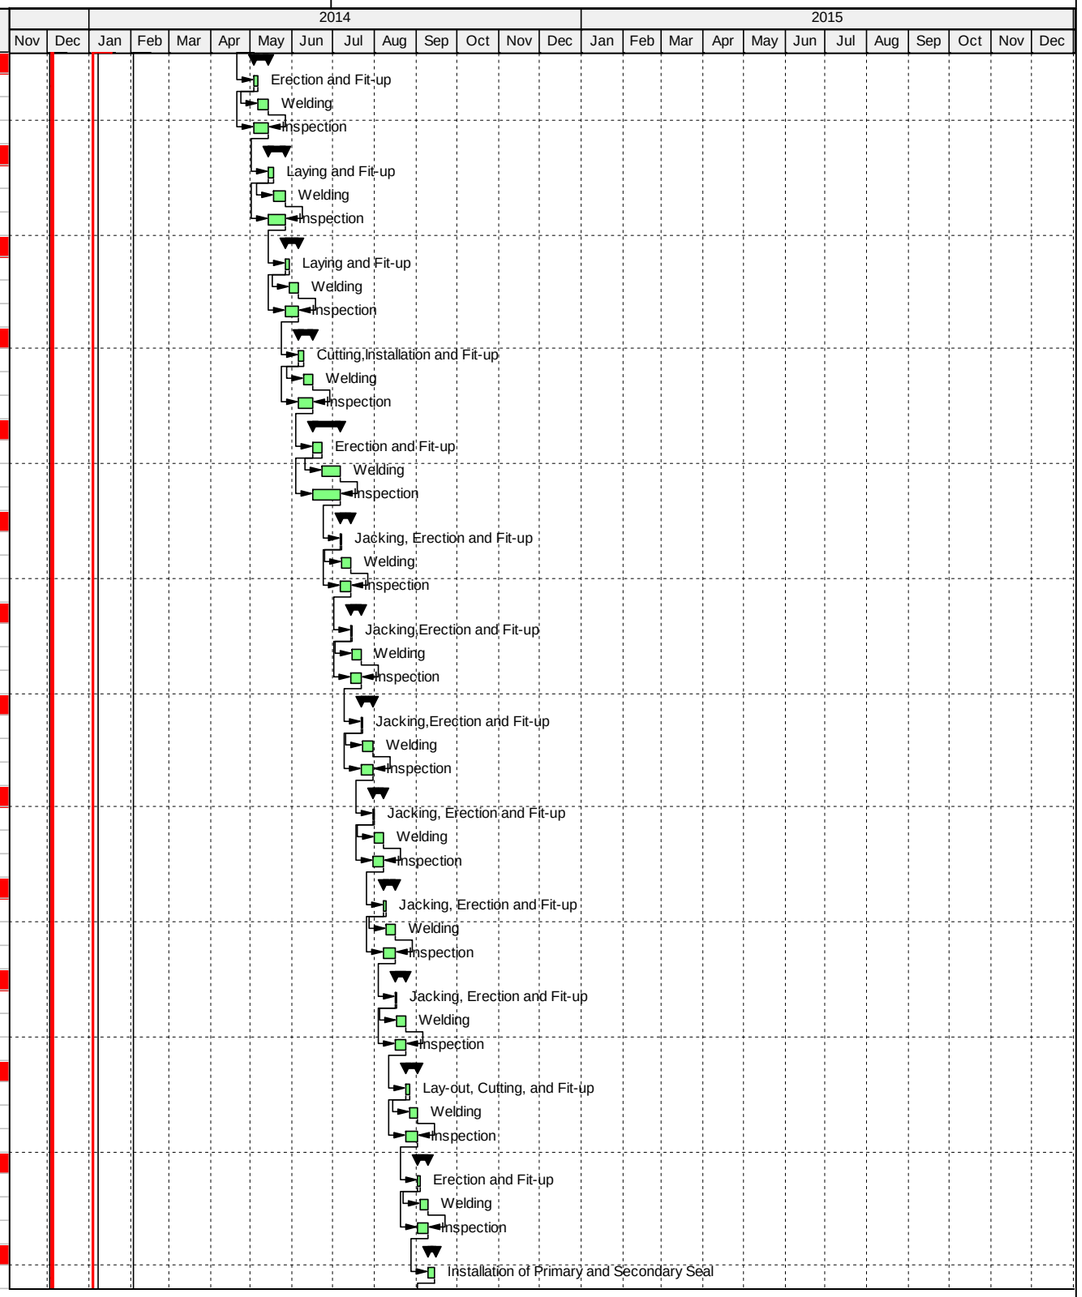

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0710-1850	Inspection	10h	14-Sep-14	15-Sep-14
CZA-14.2.3.4 Hydrotest		350h	15-Sep-14	26-Oct-14
CZA-TK-0710-1860	Filling,Holding and Draining of Water	350h	15-Sep-14	26-Oct-14
CZA-14.2.3.5 Blasting and Painting		180h	26-Oct-14	16-Nov-14
CZA-TK-0710-1870	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	180h	26-Oct-14	16-Nov-14
CZA-14.2.3.6 Tank Calibration and Handover		70h	16-Nov-14	24-Nov-14
CZA-TK-0710-1880	Tank Calibration	50h	16-Nov-14	22-Nov-14
CZA-TK-0710-1890	Tank Handover	20h	22-Nov-14	24-Nov-14
CZA-14.2.4 S220-TK-0725(P-Xylene Intermediate Tank Dia 19.35m x Ht 12.50with IFR)		1822h	20-Jan-14	20-Aug-14
CZA-14.2.4.1 Fabrication Works		360h	20-Jan-14	03-Mar-14
CZA-TK-0725-1450	Cutting of Annular Plates	8h	20-Jan-14	20-Jan-14
CZA-TK-0725-1460	Cutting of Bottom Plates	8h	20-Jan-14	20-Jan-14
CZA-TK-0725-1470	Cutting, Beveling & Rolling Shell No.1	8h	21-Jan-14	21-Jan-14
CZA-TK-0725-1480	Cutting, Bevelling & Rolling Shell No.2	8h	21-Jan-14	21-Jan-14
CZA-TK-0725-1490	Cutting, Fit-up & Welding of Shell Nozzle, Manholes and Other Appurtanances	40h	21-Jan-14	26-Jan-14
CZA-TK-0725-1500	Cutting, Bevelling and Rolling Shell No.3	16h	26-Jan-14	28-Jan-14
CZA-TK-0725-1510	Cutting of Floating Deck Plate	40h	28-Jan-14	02-Feb-14
CZA-TK-0725-1520	Cutting, Fit-up and Welding of Pontoon	56h	02-Feb-14	08-Feb-14
CZA-TK-0725-1530	Cutting of Floating Legs and Manholes	8h	09-Feb-14	09-Feb-14
CZA-TK-0725-1540	Cutting, Bevelling & Rolling of Shell No.4	8h	09-Feb-14	10-Feb-14
CZA-TK-0725-1550	Cutting, Bevelling & Rolling of Shell No.5	8h	09-Feb-14	10-Feb-14
CZA-TK-0725-1560	Cutting, Bevelling & Rolling of Shell No.6	8h	10-Feb-14	11-Feb-14
CZA-TK-0725-1590	Cutting & Rolling of Compression Ring	24h	11-Feb-14	13-Feb-14
CZA-TK-0725-1600	Cutting, Fit-up and Welding of roof Structure	24h	13-Feb-14	17-Feb-14
CZA-TK-0725-1610	Cutting of Roof Plates	16h	17-Feb-14	18-Feb-14
CZA-TK-0725-1620	Cutting,Fit-up & Welding of roof Platform, Gratings and Handrails	80h	18-Feb-14	27-Feb-14
CZA-TK-0725-1630	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	20-Feb-14	26-Feb-14
CZA-TK-0725-1640	Cutting, Fit-up and Welding of Roof Nozzles,Manholes and Other Appurtanances	56h	24-Feb-14	03-Mar-14
CZA-14.2.4.2 Foundation Takeover		0h	15-Feb-14	15-Feb-14
CZA-TK-0725-1650	Foundation Takeover from Client	0h	15-Feb-14	
CZA-14.2.4.7 Mechanical Erection		1260h	16-Feb-14	13-Jul-14
CZA-14.2.4.7.1 Annular Plates		30h	16-Feb-14	19-Feb-14
CZA-TK-0725-1660	Laying and Fit-up	10h	16-Feb-14	17-Feb-14
CZA-TK-0725-1670	Welding	20h	17-Feb-14	19-Feb-14
CZA-TK-0725-1680	Inspection	30h	16-Feb-14	19-Feb-14
CZA-14.2.4.7.19 Bottom Plates		60h	19-Feb-14	26-Feb-14
CZA-TK-0725-1690	Erection and Fit-up	20h	19-Feb-14	22-Feb-14
CZA-TK-0725-1700	Welding	40h	22-Feb-14	26-Feb-14
CZA-TK-0725-1710	Inspection	60h	19-Feb-14	26-Feb-14
CZA-14.2.4.7.2 Shell No.1		50h	26-Feb-14	04-Mar-14
CZA-TK-0725-1720	Erection and Fit-up	10h	26-Feb-14	27-Feb-14
CZA-TK-0725-1730	Welding	40h	27-Feb-14	04-Mar-14
CZA-TK-0725-1740	Inspection	50h	26-Feb-14	04-Mar-14
CZA-14.2.4.7.3 Shell No.2		50h	04-Mar-14	10-Mar-14
CZA-TK-0725-1750	Erection and Fit-up	10h	04-Mar-14	05-Mar-14
CZA-TK-0725-1760	Welding	40h	05-Mar-14	10-Mar-14
CZA-TK-0725-1770	Inspection	50h	04-Mar-14	10-Mar-14
CZA-14.2.4.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		50h	10-Mar-14	16-Mar-14
CZA-TK-0725-1780	Cutting, Installation and Fit-up	10h	10-Mar-14	11-Mar-14
CZA-TK-0725-1790	Welding	40h	11-Mar-14	16-Mar-14
CZA-TK-0725-1800	Inspection	50h	10-Mar-14	16-Mar-14
CZA-14.2.4.7.5 Deck Plates		100h	16-Mar-14	27-Mar-14
CZA-TK-0725-1810	Laying & Fit-up	20h	16-Mar-14	18-Mar-14
CZA-TK-0725-1820	Welding	80h	18-Mar-14	27-Mar-14

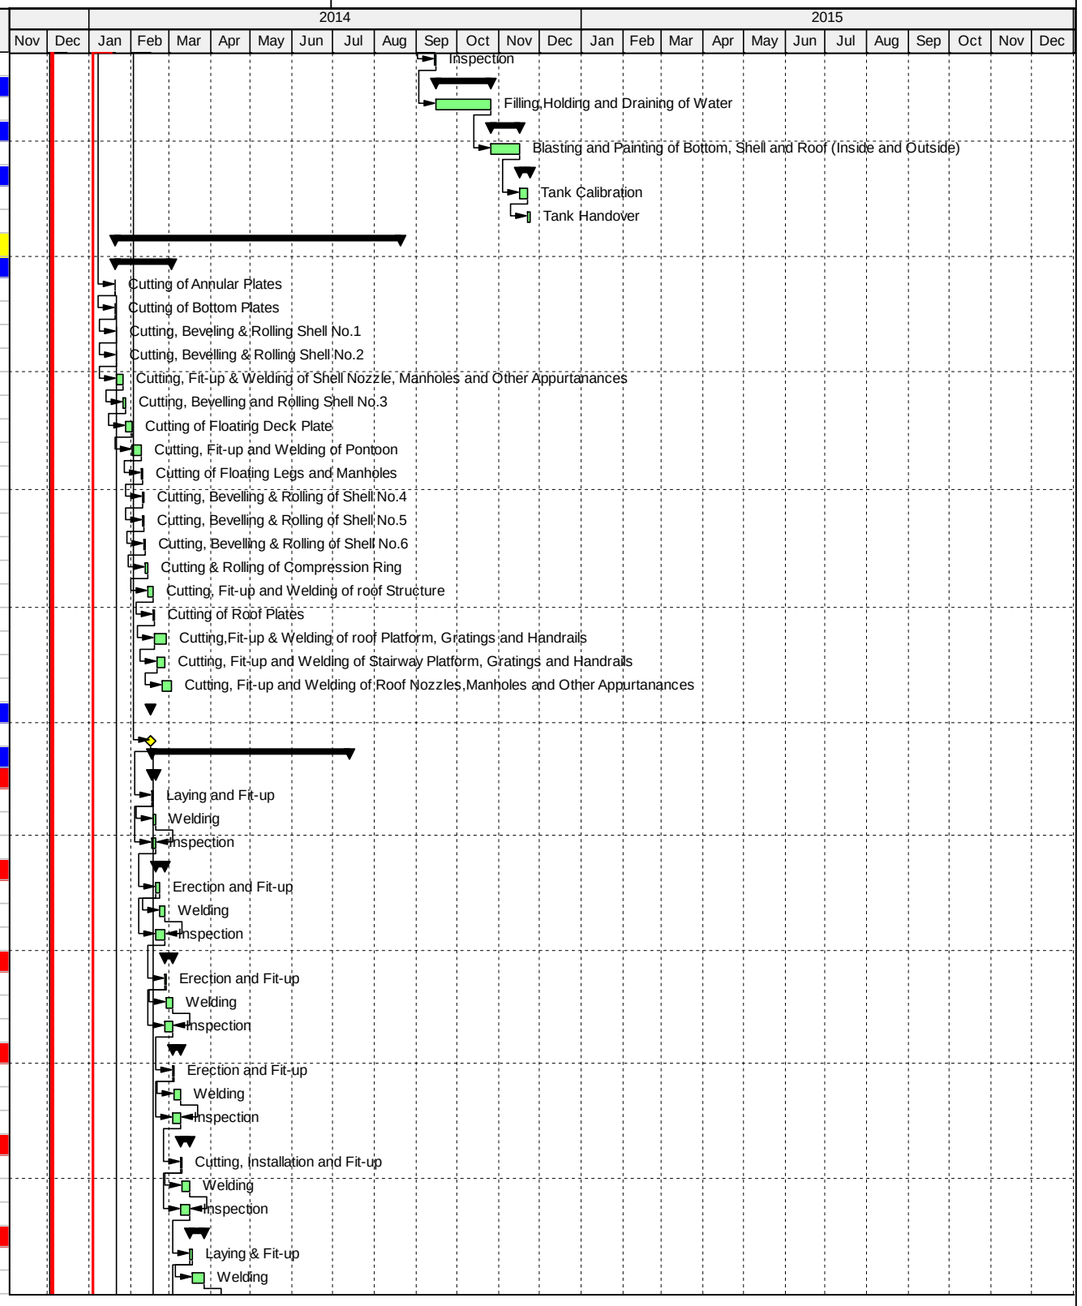

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0725-1830	Inspection	100h	16-Mar-14	27-Mar-14
CZA-14.2.4.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		**90h**	**27-Mar-14**	**07-Apr-14**
CZA-TK-0725-1840	Cutting of All Holes, Laying & Fit-up	20h	27-Mar-14	30-Mar-14
CZA-TK-0725-1850	Welding of Sleeves and Plates	60h	30-Mar-14	06-Apr-14
CZA-TK-0725-1860	Installation of Leg Support	10h	06-Apr-14	07-Apr-14
CZA-TK-0725-1870	Inspection	90h	27-Mar-14	07-Apr-14
CZA-14.2.4.7.7 Shell No.3		**50h**	**07-Apr-14**	**13-Apr-14**
CZA-TK-0725-1880	Erection and Fit-up	10h	07-Apr-14	08-Apr-14
CZA-TK-0725-1890	Welding	40h	08-Apr-14	13-Apr-14
CZA-TK-0725-1900	Inspection	50h	07-Apr-14	13-Apr-14
CZA-14.2.4.7.8 Shell No.4		**50h**	**13-Apr-14**	**19-Apr-14**
CZA-TK-0725-2000	Erection and Fit-up	10h	13-Apr-14	14-Apr-14
CZA-TK-0725-2010	Welding	40h	14-Apr-14	19-Apr-14
CZA-TK-0725-2020	Inspection	50h	13-Apr-14	19-Apr-14
CZA-14.2.4.7.9 Shell No.5		**50h**	**19-Apr-14**	**24-Apr-14**
CZA-TK-0725-2030	Erection and Fit-up	10h	19-Apr-14	20-Apr-14
CZA-TK-0725-2040	Welding	40h	20-Apr-14	24-Apr-14
CZA-TK-0725-2050	Inspection	50h	19-Apr-14	24-Apr-14
CZA-14.2.4.7.10 Shell No.6		**50h**	**24-Apr-14**	**30-Apr-14**
CZA-TK-0725-2060	Erection and Fit-up	10h	24-Apr-14	26-Apr-14
CZA-TK-0725-2070	Welding	40h	26-Apr-14	30-Apr-14
CZA-TK-0725-2080	Inspection	50h	24-Apr-14	30-Apr-14
CZA-14.2.4.7.12 Shell Nozzles and attachements (Upper)		**60h**	**30-Apr-14**	**07-May-14**
CZA-TK-0725-2090	Cutting, Installation and Fit-up	20h	30-Apr-14	03-May-14
CZA-TK-0725-2100	Welding	40h	03-May-14	07-May-14
CZA-TK-0725-2110	Inspection	60h	30-Apr-14	07-May-14
CZA-14.2.4.7.13 Roof Structure		**90h**	**07-May-14**	**18-May-14**
CZA-TK-0725-2120	Erection and Fit-up	30h	07-May-14	11-May-14
CZA-TK-0725-2130	Welding	60h	11-May-14	18-May-14
CZA-TK-0725-2140	Inspection	90h	07-May-14	18-May-14
CZA-14.2.4.7.14 Roof Plates		**60h**	**18-May-14**	**25-May-14**
CZA-TK-0725-2150	Laying and Fit-up	20h	18-May-14	20-May-14
CZA-TK-0725-2160	Welding	40h	20-May-14	25-May-14
CZA-TK-0725-2170	Inspection	60h	18-May-14	25-May-14
CZA-14.2.4.7.15 Compression Ring		**60h**	**25-May-14**	**01-Jun-14**
CZA-TK-0725-2180	Laying and Fit-up	20h	25-May-14	27-May-14
CZA-TK-0725-2190	Welding	40h	27-May-14	01-Jun-14
CZA-TK-0725-2200	Inspection	60h	25-May-14	01-Jun-14
CZA-14.2.4.7.16 Roof Nozzles, Manholes and Other Appurtanances		**50h**	**01-Jun-14**	**07-Jun-14**
CZA-TK-0725-2210	Installation and Fit-up	20h	01-Jun-14	03-Jun-14
CZA-TK-0725-2220	Welding	30h	03-Jun-14	07-Jun-14
CZA-TK-0725-2230	Inspection	50h	01-Jun-14	07-Jun-14
CZA-14.2.4.7.18 Stairway Platform, Handrails and Gratings		**150h**	**07-Jun-14**	**24-Jun-14**
CZA-TK-0725-2240	Erection and Fit-up	40h	07-Jun-14	11-Jun-14
CZA-TK-0725-2250	Welding	110h	11-Jun-14	24-Jun-14
CZA-TK-0725-2260	Inspection	150h	07-Jun-14	24-Jun-14
CZA-14.2.4.7.17 Roof Platform, Handrails and Gratings		**120h**	**24-Jun-14**	**08-Jul-14**
CZA-TK-0725-2270	Erection and Fit-up	30h	24-Jun-14	28-Jun-14
CZA-TK-0725-2280	Welding	90h	28-Jun-14	08-Jul-14
CZA-TK-0725-2290	Inspection	120h	24-Jun-14	08-Jul-14
CZA-14.2.4.7.20 Primary and Secondary Seal		**40h**	**08-Jul-14**	**13-Jul-14**
CZA-TK-0725-2300	Installation of Primary and Secondary Seal	30h	08-Jul-14	12-Jul-14
CZA-TK-0725-2310	Inspection	10h	12-Jul-14	13-Jul-14
CZA-14.2.4.4 Hydrotest		**170h**	**13-Jul-14**	**02-Aug-14**

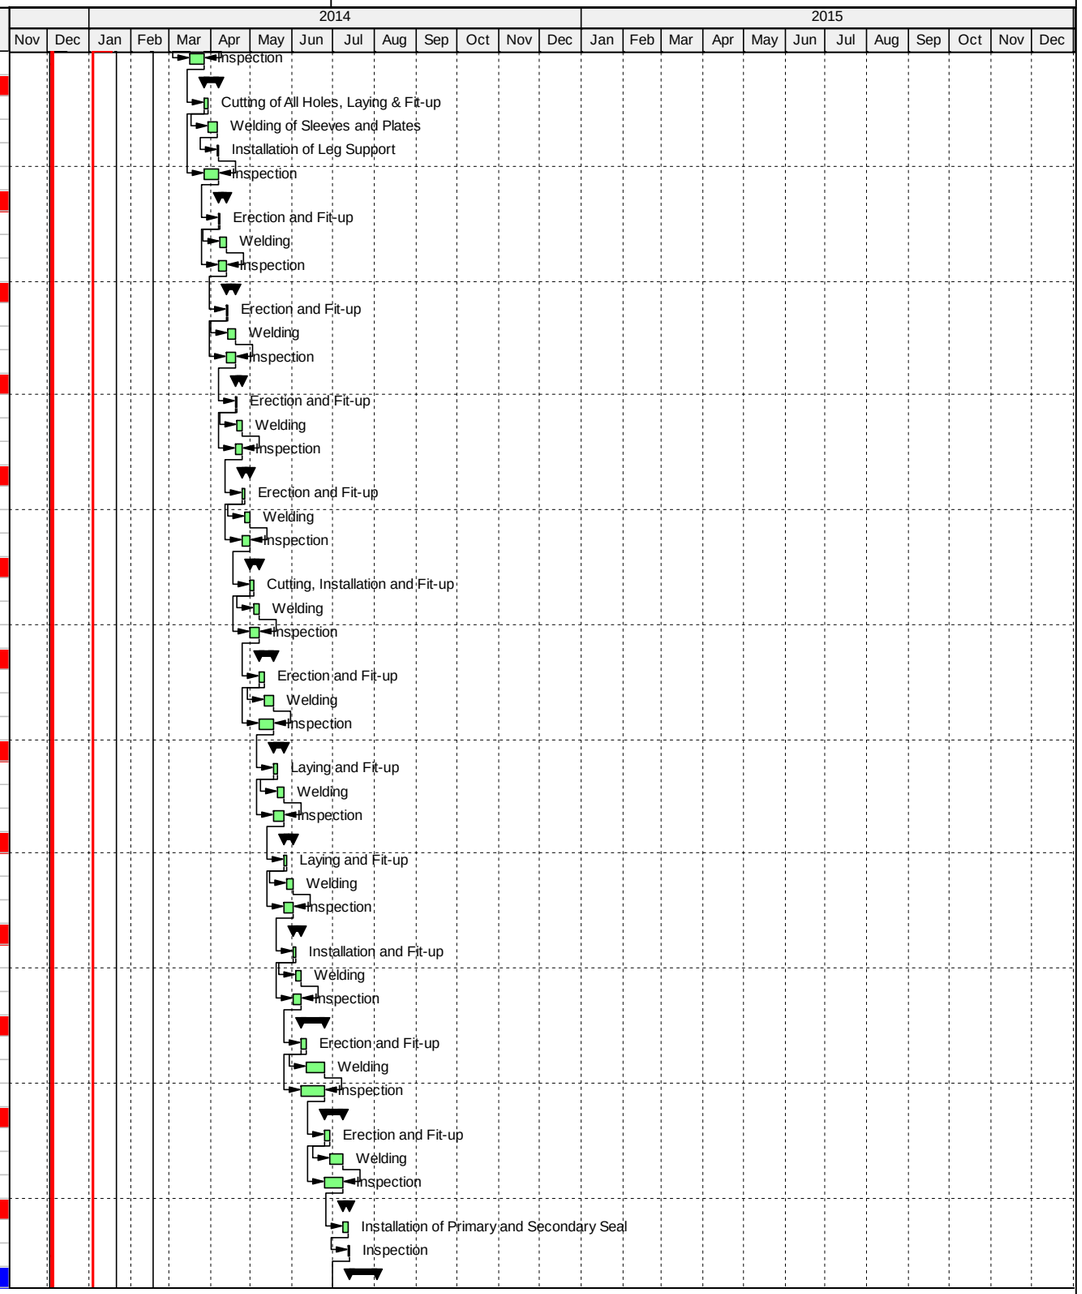

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0725-2320	Filling,Holding and Draining of Water	170h	13-Jul-14	02-Aug-14
CZA-14.2.4.5 Blasting and Painting		**90h**	**02-Aug-14**	**12-Aug-14**
CZA-TK-0725-2330	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	90h	02-Aug-14	12-Aug-14
CZA-14.2.4.6 Tank Calibration and Handover		**70h**	**12-Aug-14**	**20-Aug-14**
CZA-TK-0725-2340	Tank Calibration	50h	12-Aug-14	18-Aug-14
CZA-TK-0725-2350	Tank Handover	20h	18-Aug-14	20-Aug-14
CZA-14.2.5 S220-TK-0715(Toluence Intermediate Tank Dia 29.02m x Ht 18.40m with IFR)		**2342h**	**03-Feb-14**	**03-Nov-14**
CZA-14.2.5.1 Fabrication Works		**320h**	**03-Feb-14**	**12-Mar-14**
CZA-TK-0715-1650	Cutting of Annular Plates	8h	03-Feb-14	03-Feb-14
CZA-TK-0715-1660	Cutting of Bottom Plates	8h	03-Feb-14	03-Feb-14
CZA-TK-0715-1670	Cutting, Beveling & Rolling Shell No.7	8h	04-Feb-14	04-Feb-14
CZA-TK-0715-1680	Cutting, Bevelling & Rolling Shell No.8	8h	04-Feb-14	04-Feb-14
CZA-TK-0715-1690	Cutting, Fit-up & Welding of Shell Nozzle, Manholes and Other Appurtanances (Upper I	40h	04-Feb-14	09-Feb-14
CZA-TK-0715-1700	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails (upper Part)	56h	05-Feb-14	12-Feb-14
CZA-TK-0715-1710	Cutting of Floating Deck Plate	40h	12-Feb-14	17-Feb-14
CZA-TK-0715-1720	Cutting, Fit-up and Welding of Pontoon	56h	13-Feb-14	20-Feb-14
CZA-TK-0715-1730	Cutting of Floating Legs and Manholes	56h	16-Feb-14	22-Feb-14
CZA-TK-0715-1740	Cutting, Fit-up and Welding of roof Structure	40h	23-Feb-14	26-Feb-14
CZA-TK-0715-1750	Cutting of Roof Plates	16h	23-Feb-14	24-Feb-14
CZA-TK-0715-1760	Cutting & Rolling of Compression Ring	16h	23-Feb-14	24-Feb-14
CZA-TK-0715-1770	Cutting, Fit-up and Welding of Roof Nozzles,Manholes and Other Appurtanances	40h	23-Feb-14	26-Feb-14
CZA-TK-0715-1780	Cutting,Fit-up & Welding of roof Platform, Gratings and Handrails	56h	23-Feb-14	01-Mar-14
CZA-TK-0715-1790	Cutting, Bevelling & Rolling Shell No.6 & 5	8h	01-Mar-14	02-Mar-14
CZA-TK-0715-1800	Cutting, Bevelling & Rolling Shell No.4 & 3	8h	02-Mar-14	03-Mar-14
CZA-TK-0715-1810	Cutting, Bevelling & Rolling Shell No.2	8h	03-Mar-14	03-Mar-14
CZA-TK-0715-1820	Cutting, Bevelling & Rolling Shell No.1	8h	04-Mar-14	04-Mar-14
CZA-TK-0715-1830	Cutting, Fit-up & Welding of Shell Nozzle, Manholes and Other Appurtanances (Lower I	56h	05-Mar-14	12-Mar-14
CZA-TK-0715-1840	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails (Lower Part)	40h	08-Mar-14	12-Mar-14
CZA-14.2.5.2 Foundation Takeover		**0h**	**02-Mar-14**	**02-Mar-14**
CZA-TK-0715-1850	Foundation Takeover from Client	0h	02-Mar-14	
CZA-14.2.5.7 Mechanical Erection		**1480h**	**02-Mar-14**	**21-Aug-14**
CZA-14.2.5.7.1 Annular Plates		**30h**	**02-Mar-14**	**05-Mar-14**
CZA-TK-0715-1860	Laying and Fit-up	10h	02-Mar-14	03-Mar-14
CZA-TK-0715-1870	Welding	20h	03-Mar-14	05-Mar-14
CZA-TK-0715-1880	Inspection	30h	02-Mar-14	05-Mar-14
CZA-14.2.5.7.2 Bottom Plates		**30h**	**05-Mar-14**	**09-Mar-14**
CZA-TK-0715-1890	Laying and Fit-up	10h	05-Mar-14	06-Mar-14
CZA-TK-0715-1900	Welding	20h	06-Mar-14	09-Mar-14
CZA-TK-0715-1910	Inspection	30h	05-Mar-14	09-Mar-14
CZA-14.2.5.7.3 Shell No.7		**50h**	**09-Mar-14**	**15-Mar-14**
CZA-TK-0715-1920	Erection and Fit-up	10h	09-Mar-14	10-Mar-14
CZA-TK-0715-1930	Welding	40h	10-Mar-14	15-Mar-14
CZA-TK-0715-1940	Inspection	50h	09-Mar-14	15-Mar-14
CZA-14.2.5.7.4 Shell No.8		**50h**	**15-Mar-14**	**20-Mar-14**
CZA-TK-0715-1950	Erection and Fit-up	10h	15-Mar-14	16-Mar-14
CZA-TK-0715-1960	Welding	40h	16-Mar-14	20-Mar-14
CZA-TK-0715-1970	Inspection	50h	15-Mar-14	20-Mar-14
CZA-14.2.5.7.5 Shell Nozzles and Other Attachments		**60h**	**20-Mar-14**	**27-Mar-14**
CZA-TK-0715-1980	Cutting, Installation and Fit-up	20h	20-Mar-14	23-Mar-14
CZA-TK-0715-1990	Welding	40h	23-Mar-14	27-Mar-14
CZA-TK-0715-2000	Inspection	40h	23-Mar-14	27-Mar-14
CZA-14.2.5.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**50h**	**27-Mar-14**	**02-Apr-14**
CZA-TK-0715-2010	Erection and Fit-up	20h	27-Mar-14	30-Mar-14
CZA-TK-0715-2020	Welding	30h	30-Mar-14	02-Apr-14

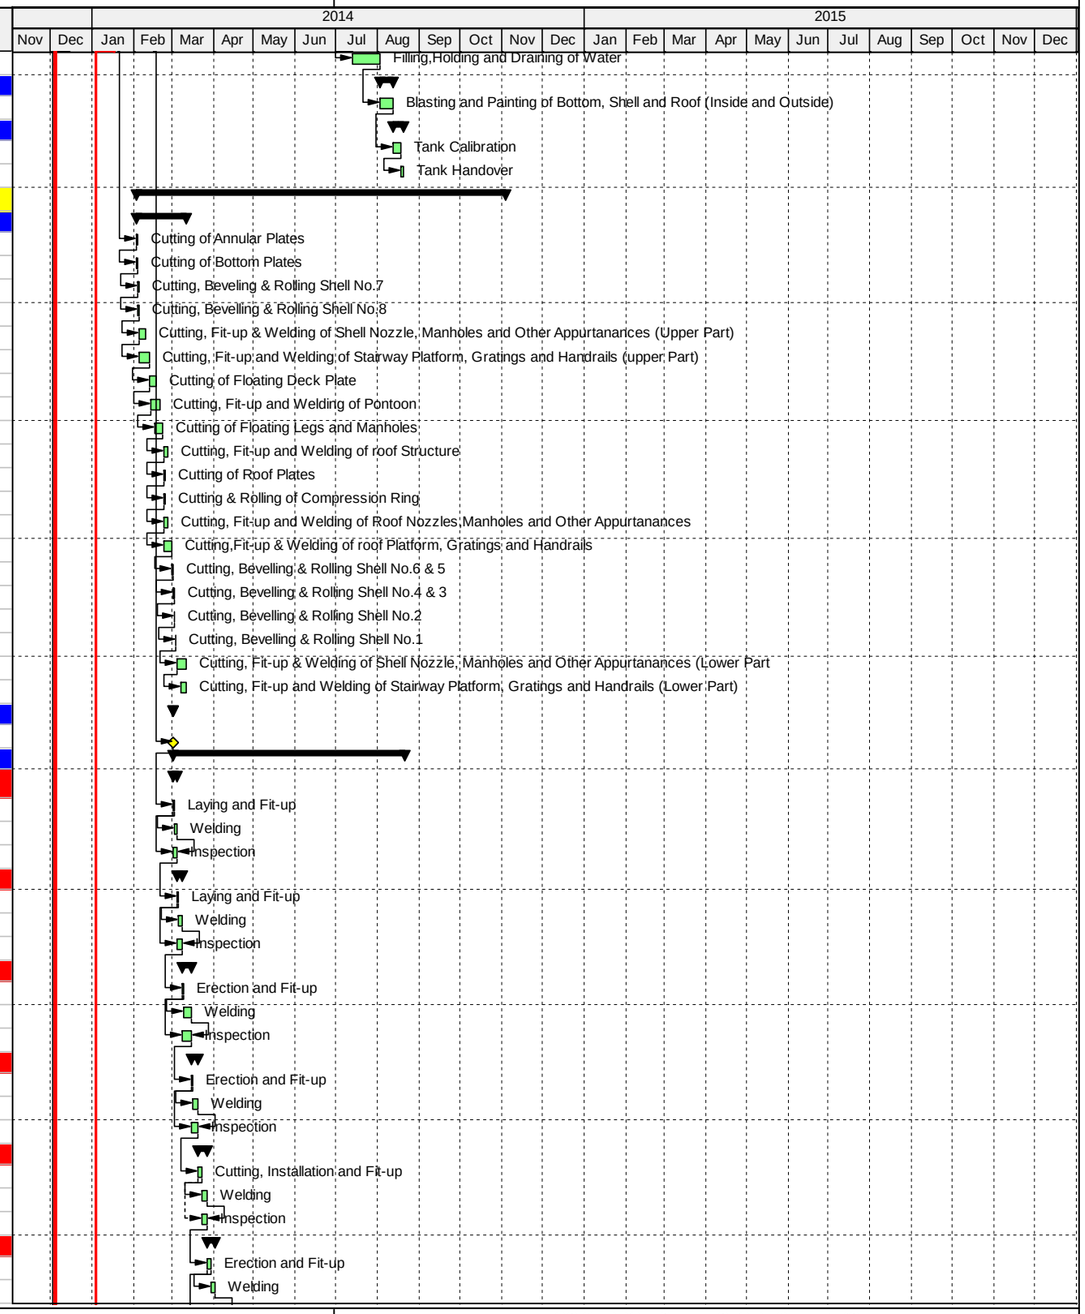

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0715-2030	Inspection	50h	27-Mar-14	02-Apr-14
CZA-14.2.5.7.7 Deck Plate		**100h**	**02-Apr-14**	**14-Apr-14**
CZA-TK-0715-2040	Laying and Fit-up	20h	02-Apr-14	05-Apr-14
CZA-TK-0715-2050	Welding	80h	05-Apr-14	14-Apr-14
CZA-TK-0715-2060	Inspection	100h	02-Apr-14	14-Apr-14
CZA-14.2.5.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**100h**	**14-Apr-14**	**26-Apr-14**
CZA-TK-0715-2070	Laying, Cutting all Holes and Fit-up	20h	14-Apr-14	16-Apr-14
CZA-TK-0715-2080	Welding	80h	14-Apr-14	23-Apr-14
CZA-TK-0715-2090	Inspection	100h	14-Apr-14	26-Apr-14
CZA-14.2.5.7.9 Roof Structure		**100h**	**26-Apr-14**	**07-May-14**
CZA-TK-0715-2100	Erection and Fit-up	20h	26-Apr-14	28-Apr-14
CZA-TK-0715-2110	Welding	80h	28-Apr-14	07-May-14
CZA-TK-0715-2120	Inspection	100h	26-Apr-14	07-May-14
CZA-14.2.5.7.10 Roof Plates		**100h**	**07-May-14**	**19-May-14**
CZA-TK-0715-2130	Laying and Fit-up	30h	07-May-14	11-May-14
CZA-TK-0715-2140	Welding	70h	11-May-14	19-May-14
CZA-TK-0715-2150	Inspection	100h	07-May-14	19-May-14
CZA-14.2.5.7.11 Compression Ring		**90h**	**19-May-14**	**29-May-14**
CZA-TK-0715-2160	Laying and Fit-up	30h	19-May-14	22-May-14
CZA-TK-0715-2170	Welding	60h	22-May-14	29-May-14
CZA-TK-0715-2180	Inspection	90h	19-May-14	29-May-14
CZA-14.2.5.7.12 Roof Nozzles, Manholes and Other Appurtanances		**90h**	**29-May-14**	**09-Jun-14**
CZA-TK-0715-1290	Cutting,Installation and Fit-up	30h	29-May-14	02-Jun-14
CZA-TK-0715-1300	Welding	60h	02-Jun-14	09-Jun-14
CZA-TK-0715-1310	Inspection	90h	29-May-14	09-Jun-14
CZA-14.2.5.7.13 Roof Platform, Gratings and Handrails		**150h**	**09-Jun-14**	**26-Jun-14**
CZA-TK-0715-1320	Erection and Fit-up	50h	09-Jun-14	15-Jun-14
CZA-TK-0715-1330	Welding	100h	15-Jun-14	26-Jun-14
CZA-TK-0715-1640	Inspection	150h	09-Jun-14	26-Jun-14
CZA-14.2.5.7.14 Shell No.6		**50h**	**26-Jun-14**	**02-Jul-14**
CZA-TK-0715-1340	Jacking, Erection and Fit-up	10h	26-Jun-14	28-Jun-14
CZA-TK-0715-1350	Welding	40h	28-Jun-14	02-Jul-14
CZA-TK-0715-1360	Inspection	50h	26-Jun-14	02-Jul-14
CZA-14.2.5.7.15 Shell No.5		**50h**	**02-Jul-14**	**08-Jul-14**
CZA-TK-0715-1370	Jacking,Erection and Fit-up	10h	02-Jul-14	03-Jul-14
CZA-TK-0715-1380	Welding	40h	03-Jul-14	08-Jul-14
CZA-TK-0715-1390	Inspection	50h	02-Jul-14	08-Jul-14
CZA-14.2.5.7.16 Shell No.4		**50h**	**08-Jul-14**	**14-Jul-14**
CZA-TK-0715-1400	Jacking,Erection and Fit-up	10h	08-Jul-14	09-Jul-14
CZA-TK-0715-1410	Welding	40h	09-Jul-14	14-Jul-14
CZA-TK-0715-1420	Inspection	50h	08-Jul-14	14-Jul-14
CZA-14.2.5.7.17 Shell No.3		**50h**	**14-Jul-14**	**20-Jul-14**
CZA-TK-0715-1430	Jacking, Erection and Fit-up	10h	14-Jul-14	15-Jul-14
CZA-TK-0715-1440	Welding	40h	15-Jul-14	20-Jul-14
CZA-TK-0715-1450	Inspection	50h	14-Jul-14	20-Jul-14
CZA-14.2.5.7.18 Shell No.2		**50h**	**20-Jul-14**	**26-Jul-14**
CZA-TK-0715-1460	Jacking, Erection and Fit-up	10h	20-Jul-14	21-Jul-14
CZA-TK-0715-1470	Welding	40h	21-Jul-14	26-Jul-14
CZA-TK-0715-1480	Inspection	50h	20-Jul-14	26-Jul-14
CZA-14.2.5.7.19 Shell No.1		**50h**	**26-Jul-14**	**31-Jul-14**
CZA-TK-0715-1490	Jacking, Erection and Fit-up	10h	26-Jul-14	27-Jul-14
CZA-TK-0715-1500	Welding	40h	27-Jul-14	31-Jul-14
CZA-TK-0715-1510	Inspection	50h	26-Jul-14	31-Jul-14
CZA-14.2.5.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**70h**	**31-Jul-14**	**09-Aug-14**

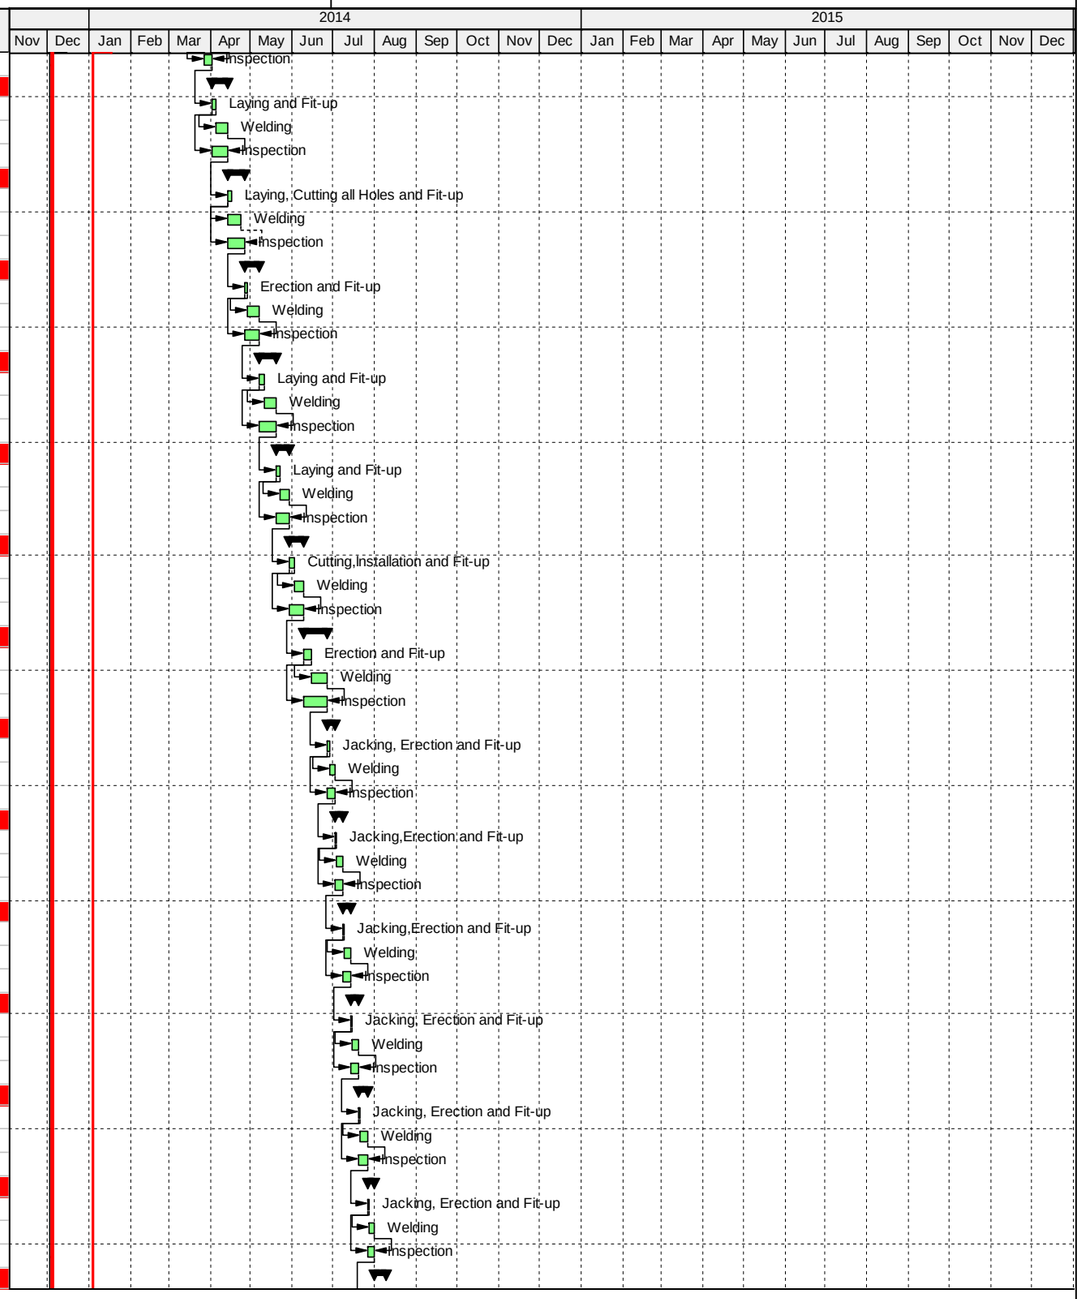

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0715-1520	Lay-out, Cutting, and Fit-up	20h	31-Jul-14	03-Aug-14
CZA-TK-0715-1530	Welding	50h	03-Aug-14	09-Aug-14
CZA-TK-0715-1540	Inspection	70h	31-Jul-14	09-Aug-14
CZA-14.2.5.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		70h	09-Aug-14	17-Aug-14
CZA-TK-0715-1550	Erection and Fit-up	20h	09-Aug-14	11-Aug-14
CZA-TK-0715-1560	Welding	50h	11-Aug-14	17-Aug-14
CZA-TK-0715-1570	Inspection	70h	09-Aug-14	17-Aug-14
CZA-14.2.5.7.24 Primary and Secondary Seal		40h	17-Aug-14	21-Aug-14
CZA-TK-0715-1580	Installation of Primary and Secondary Seal	30h	17-Aug-14	20-Aug-14
CZA-TK-0715-1590	Inspection	10h	20-Aug-14	21-Aug-14
CZA-14.2.5.4 Hydrotest		370h	21-Aug-14	04-Oct-14
CZA-TK-0715-1600	Filling,Holding and Draining of Water	370h	21-Aug-14	04-Oct-14
CZA-14.2.5.5 Blasting and Painting		190h	04-Oct-14	26-Oct-14
CZA-TK-0715-1610	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	190h	04-Oct-14	26-Oct-14
CZA-14.2.5.6 Tank Calibration and Handover		70h	26-Oct-14	03-Nov-14
CZA-TK-0715-1620	Tank Calibration	50h	26-Oct-14	01-Nov-14
CZA-TK-0715-1630	Tank Handover	20h	01-Nov-14	03-Nov-14
CZA-14.5 UTILITY AREA (UTL)		2958h	15-Dec-13	24-Nov-14
CZA-14.5.3 C240-TK-2400(Potable Water Tank Dia 6.75m x Ht 7.85m)		802h	15-Dec-13	18-Mar-14
CZA-14.5.3.1 Fabrication Works		168h	15-Dec-13	02-Jan-14
CZA-TK-2400-1000	Cutting of Bottom Plates	8h	15-Dec-13	15-Dec-13
CZA-TK-2400-1010	Cutting, Bevelling and Rolling Shell No.1	8h	15-Dec-13	15-Dec-13
CZA-TK-2400-1020	Cutting, Bevelling & Rolling Shell No.2	8h	15-Dec-13	15-Dec-13
CZA-TK-2400-1030	Cutting, Fit-up and Welding of Shell Nozzles. Manholes and Othe Appurtanances	32h	15-Dec-13	18-Dec-13
CZA-TK-2400-1040	Cutting, Bevelling & Rolling Shell No.3	8h	19-Dec-13	19-Dec-13
CZA-TK-2400-1050	Cutting, Bevelling & Rolling Shell No.4	8h	19-Dec-13	19-Dec-13
CZA-TK-2400-1060	Cutting, Bevelling and Rolling of Curb Angle	24h	22-Dec-13	24-Dec-13
CZA-TK-2400-1070	Cutting, Fit-up and Welding of Roof Structure	40h	22-Dec-13	26-Dec-13
CZA-TK-2400-1080	Cutting of Roof Plates	8h	26-Dec-13	28-Dec-13
CZA-TK-2400-1090	Cutting, Fit-up and Welding of Roof Structure, Gratings and Handrails	56h	28-Dec-13	02-Jan-14
CZA-TK-2400-1100	Cutting,Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	32h	29-Dec-13	01-Jan-14
CZA-14.5.3.2 FoundationTakeover		0h	16-Jan-14	16-Jan-14
CZA-TK-2400-1110	Foundation Takeover From Client	0h	16-Jan-14	
CZA-14.5.3.7 Mechanical Erection		302h	16-Jan-14	20-Feb-14
CZA-14.5.3.7.19 Bottom Plates		20h	16-Jan-14	18-Jan-14
CZA-TK-2400-1120	Erection and Fit-up	10h	16-Jan-14	16-Jan-14
CZA-TK-2400-1130	Welding	10h	18-Jan-14	18-Jan-14
CZA-TK-2400-1140	Inspection	20h	16-Jan-14	18-Jan-14
CZA-14.5.3.7.2 Shell No.1		40h	19-Jan-14	22-Jan-14
CZA-TK-2400-1150	Erection and Fit-up	10h	19-Jan-14	19-Jan-14
CZA-TK-2400-1160	Inspection	20h	21-Jan-14	22-Jan-14
CZA-TK-2400-1170	Welding	30h	20-Jan-14	22-Jan-14
CZA-14.5.3.7.3 Shell No.2		20h	23-Jan-14	25-Jan-14
CZA-TK-2400-1180	Erection and Fit-up	10h	23-Jan-14	23-Jan-14
CZA-TK-2400-1190	Welding	10h	25-Jan-14	25-Jan-14
CZA-TK-2400-1200	Inspection	20h	23-Jan-14	25-Jan-14
CZA-14.5.3.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		30h	26-Jan-14	28-Jan-14
CZA-TK-2400-1210	Cutting, Installation and Fit-up	10h	26-Jan-14	26-Jan-14
CZA-TK-2400-1220	Welding	20h	27-Jan-14	28-Jan-14
CZA-TK-2400-1230	Inspection	30h	26-Jan-14	28-Jan-14
CZA-14.5.3.7.7 Shell No.3		20h	29-Jan-14	30-Jan-14
CZA-TK-2400-1240	Erection and Fit-up	10h	29-Jan-14	29-Jan-14
CZA-TK-2400-1250	Welding	10h	30-Jan-14	30-Jan-14
CZA-TK-2400-1260	Inspection	20h	29-Jan-14	30-Jan-14

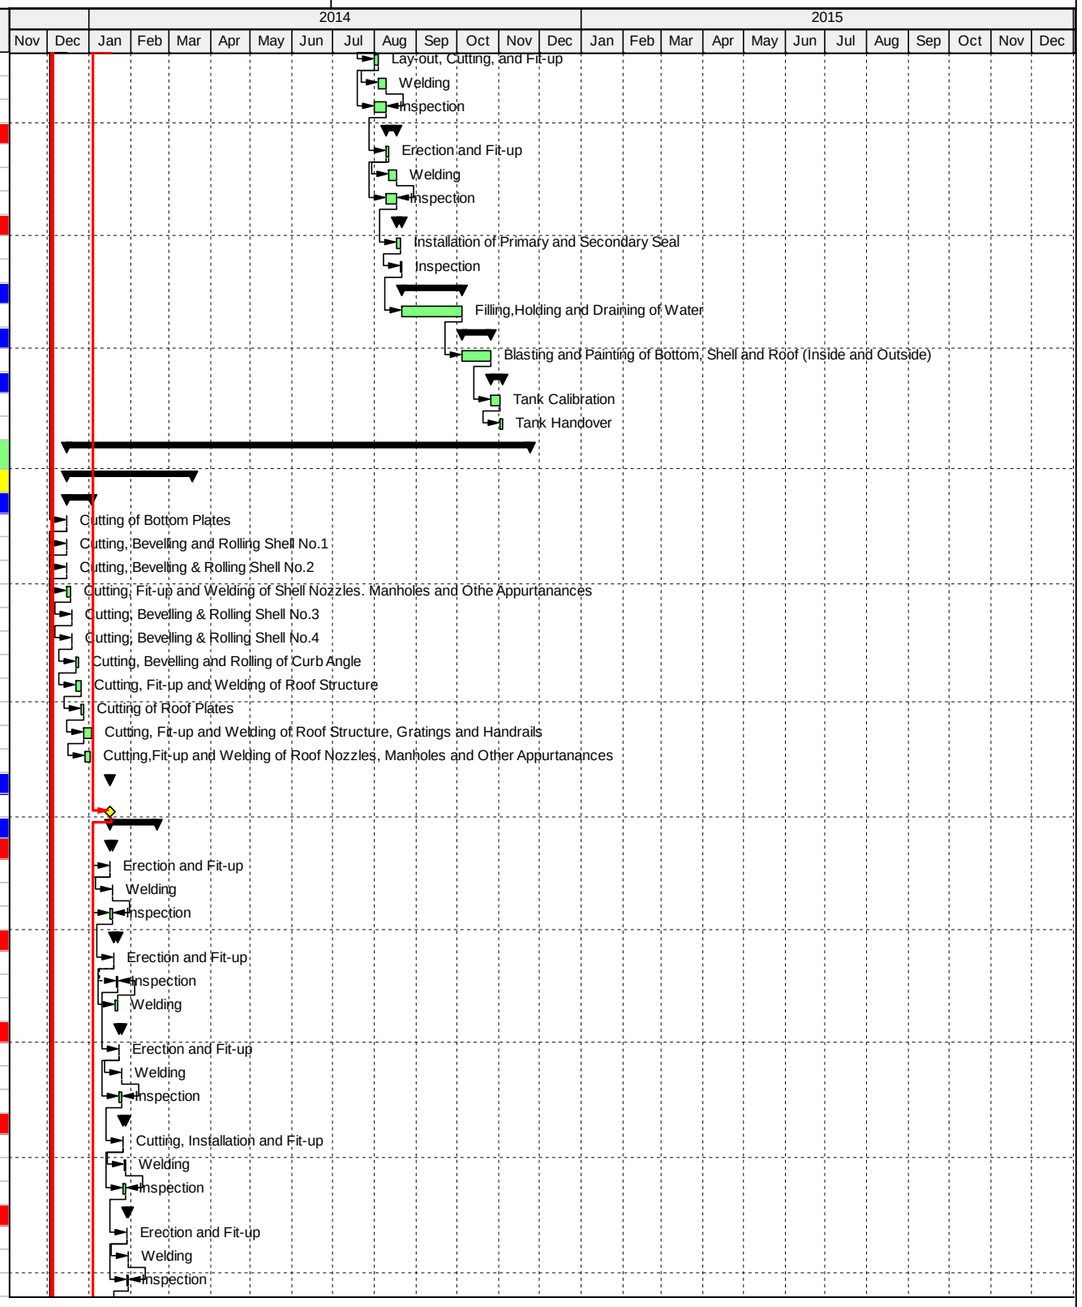

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.5.3.7.8 Shell No.4		20h	01-Feb-14	02-Feb-14
CZA-TK-2400-1270	Erection and Fit-up	10h	01-Feb-14	01-Feb-14
CZA-TK-2400-1280	Welding	10h	02-Feb-14	02-Feb-14
CZA-TK-2400-1290	Inspection	20h	01-Feb-14	02-Feb-14
CZA-14.5.3.7.12 Shell Nozzles and attachements (Upper)		20h	03-Feb-14	04-Feb-14
CZA-TK-2400-1300	Cutting, Installation and Fit-up	10h	03-Feb-14	03-Feb-14
CZA-TK-2400-1310	Welding	10h	04-Feb-14	04-Feb-14
CZA-TK-2400-1320	Inspection	20h	03-Feb-14	04-Feb-14
CZA-14.5.3.7.15 Curb Angle		20h	05-Feb-14	06-Feb-14
CZA-TK-2400-1330	Erection and Fit-up	10h	05-Feb-14	05-Feb-14
CZA-TK-2400-1340	Welding	10h	06-Feb-14	06-Feb-14
CZA-TK-2400-1350	Inspection	20h	05-Feb-14	06-Feb-14
CZA-14.5.3.7.14 Roof Plates		20h	08-Feb-14	09-Feb-14
CZA-TK-2400-1390	Laying and Fit-up	10h	08-Feb-14	08-Feb-14
CZA-TK-2400-1400	Welding	10h	09-Feb-14	09-Feb-14
CZA-TK-2400-1410	Inspection	20h	08-Feb-14	09-Feb-14
CZA-14.5.3.7.16 Roof Nozzles, Manholes and Other Appurtanances		50h	10-Feb-14	15-Feb-14
CZA-TK-2400-1420	Installation and Fit-up	20h	10-Feb-14	11-Feb-14
CZA-TK-2400-1430	Welding	30h	12-Feb-14	15-Feb-14
CZA-TK-2400-1440	Inspection	50h	10-Feb-14	15-Feb-14
CZA-14.5.3.7.17 Roof Platform, Handrails and Gratings		50h	11-Feb-14	17-Feb-14
CZA-TK-2400-1450	Erection and Fit-up	10h	11-Feb-14	12-Feb-14
CZA-TK-2400-1460	Welding	40h	12-Feb-14	17-Feb-14
CZA-TK-2400-1470	Inspection	50h	11-Feb-14	17-Feb-14
CZA-14.5.3.7.18 Stairway Platform, Handrails and Gratings		60h	13-Feb-14	20-Feb-14
CZA-TK-2400-1480	Erection and Fit-up	20h	13-Feb-14	16-Feb-14
CZA-TK-2400-1490	Welding	40h	16-Feb-14	20-Feb-14
CZA-TK-2400-1500	Inspection	60h	13-Feb-14	20-Feb-14
CZA-14.5.3.4 Hydrotest		100h	20-Feb-14	04-Mar-14
CZA-TK-2400-1510	Filling, Holding and Draining of Water	100h	20-Feb-14	04-Mar-14
CZA-14.5.3.5 Blasting and Painting		50h	04-Mar-14	10-Mar-14
CZA-TK-2400-1520	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	50h	04-Mar-14	10-Mar-14
CZA-14.5.3.6 Tank Calibration and Handover		70h	10-Mar-14	18-Mar-14
CZA-TK-2400-1530	Tank Calibration	50h	10-Mar-14	16-Mar-14
CZA-TK-2400-1540	Tank Handover	20h	16-Mar-14	18-Mar-14
CZA-14.5.7 C240-TK-2401(Potable Water Tank Dia 6.75m x Ht 7.85m)		782h	15-Dec-13	16-Mar-14
CZA-14.5.7.1 Fabrication Works		168h	15-Dec-13	02-Jan-14
CZA-TK-2401-1270	Cutting of Bottom Plates	8h	15-Dec-13	15-Dec-13
CZA-TK-2401-1280	Cutting, Bevelling and Rolling Shell No.1	8h	15-Dec-13	15-Dec-13
CZA-TK-2401-1290	Cutting, Bevelling & Rolling Shell No.2	8h	15-Dec-13	15-Dec-13
CZA-TK-2401-1300	Cutting, Fit-up and Welding of Shell Nozzles. Manholes and Othe Appurtanances	32h	15-Dec-13	18-Dec-13
CZA-TK-2401-1310	Cutting, Bevelling & Rolling Shell No.3	8h	19-Dec-13	19-Dec-13
CZA-TK-2401-1320	Cutting, Bevelling & Rolling Shell No.4	8h	19-Dec-13	19-Dec-13
CZA-TK-2401-1330	Cutting, Bevelling and Rolling of Curb Angle	24h	22-Dec-13	24-Dec-13
CZA-TK-2401-1340	Cutting, Fit-up and Welding of Roof Structure	40h	22-Dec-13	26-Dec-13
CZA-TK-2401-1350	Cutting of Roof Plates	8h	26-Dec-13	28-Dec-13
CZA-TK-2401-1360	Cutting, Fit-up and Welding of Roof Structure, Gratings and Handrails	56h	28-Dec-13	02-Jan-14
CZA-TK-2401-1370	Cutting,Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	32h	29-Dec-13	01-Jan-14
CZA-14.5.7.2 FoundationTakeover		0h	16-Jan-14	16-Jan-14
CZA-TK-2401-1380	Foundation Takeover From Client	0h	16-Jan-14	
CZA-14.5.7.7 Mechanical Erection		282h	16-Jan-14	18-Feb-14
CZA-14.5.7.7.19 Bottom Plates		20h	16-Jan-14	18-Jan-14
CZA-TK-2401-1390	Erection and Fit-up	10h	16-Jan-14	16-Jan-14
CZA-TK-2401-1400	Welding	10h	18-Jan-14	18-Jan-14

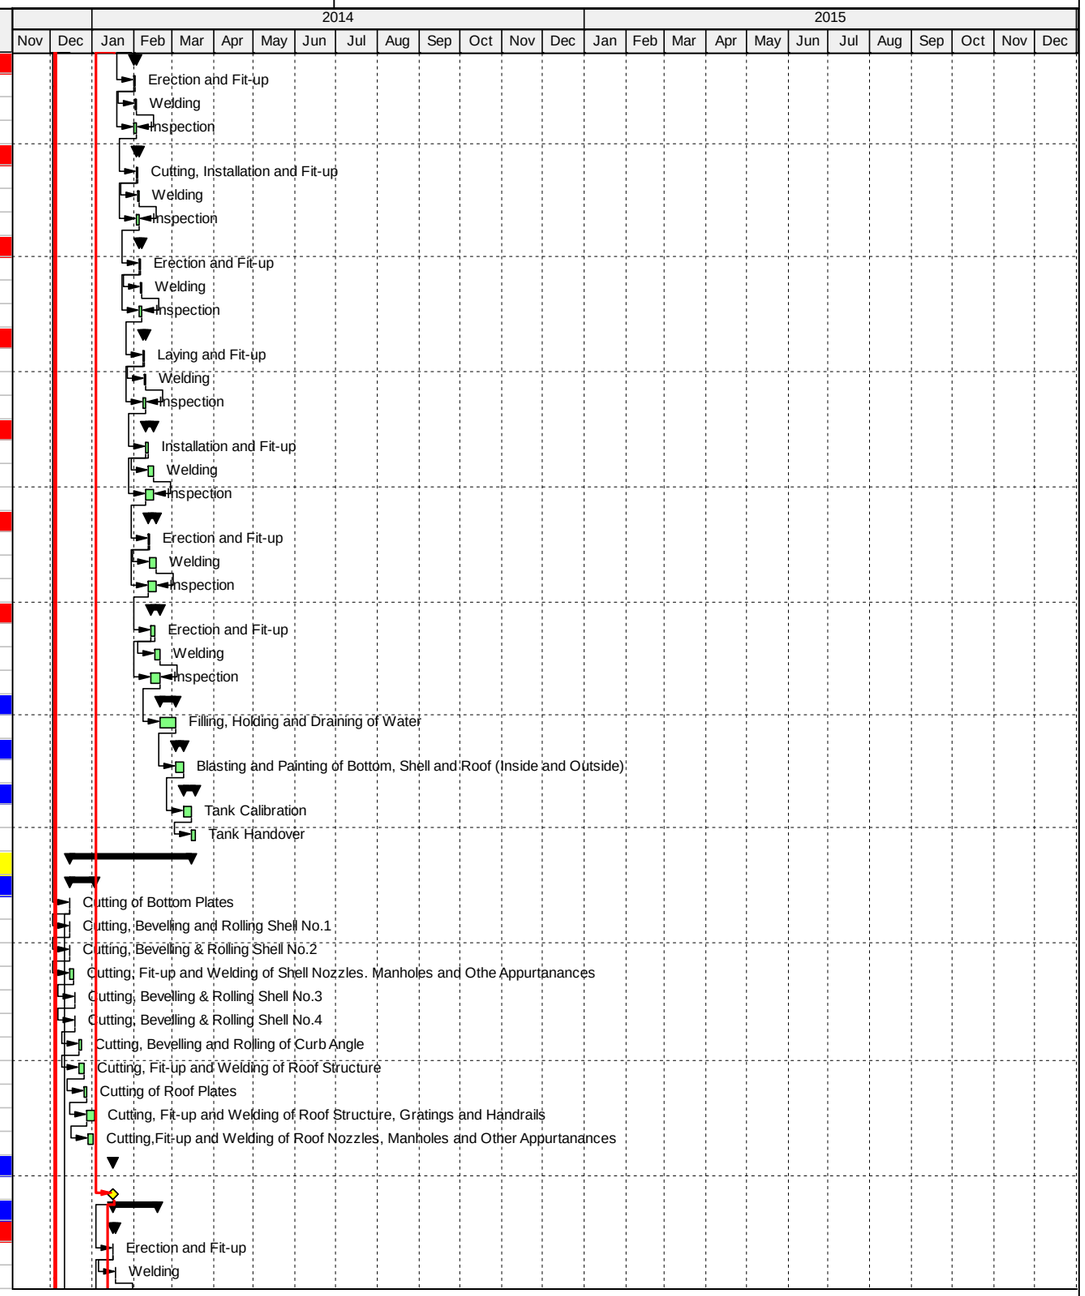

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone
- summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-2401-1410	Inspection	20h	16-Jan-14	18-Jan-14
CZA-14.5.7.7.2 Shell No.1		20h	19-Jan-14	20-Jan-14
CZA-TK-2401-1420	Erection and Fit-up	10h	19-Jan-14	19-Jan-14
CZA-TK-2401-1430	Welding	10h	20-Jan-14	20-Jan-14
CZA-TK-2401-1440	Inspection	20h	19-Jan-14	20-Jan-14
CZA-14.5.7.7.3 Shell No.2		20h	21-Jan-14	22-Jan-14
CZA-TK-2401-1450	Erection and Fit-up	10h	21-Jan-14	21-Jan-14
CZA-TK-2401-1460	Welding	10h	22-Jan-14	22-Jan-14
CZA-TK-2401-1470	Inspection	20h	21-Jan-14	22-Jan-14
CZA-14.5.7.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		30h	23-Jan-14	26-Jan-14
CZA-TK-2401-1480	Cutting, Installation and Fit-up	10h	23-Jan-14	23-Jan-14
CZA-TK-2401-1490	Welding	20h	25-Jan-14	26-Jan-14
CZA-TK-2401-1500	Inspection	30h	23-Jan-14	26-Jan-14
CZA-14.5.7.7.7 Shell No.3		20h	27-Jan-14	28-Jan-14
CZA-TK-2401-1510	Erection and Fit-up	10h	27-Jan-14	27-Jan-14
CZA-TK-2401-1520	Welding	10h	28-Jan-14	28-Jan-14
CZA-TK-2401-1530	Inspection	20h	27-Jan-14	28-Jan-14
CZA-14.5.7.7.8 Shell No.4		20h	29-Jan-14	30-Jan-14
CZA-TK-2401-1540	Erection and Fit-up	10h	29-Jan-14	29-Jan-14
CZA-TK-2401-1550	Welding	10h	30-Jan-14	30-Jan-14
CZA-TK-2401-1560	Inspection	20h	29-Jan-14	30-Jan-14
CZA-14.5.7.7.12 Shell Nozzles and attachements (Upper)		20h	01-Feb-14	02-Feb-14
CZA-TK-2401-1570	Cutting, Installation and Fit-up	10h	01-Feb-14	01-Feb-14
CZA-TK-2401-1580	Welding	10h	02-Feb-14	02-Feb-14
CZA-TK-2401-1590	Inspection	20h	01-Feb-14	02-Feb-14
CZA-14.5.7.7.15 Curb Angle		20h	03-Feb-14	04-Feb-14
CZA-TK-2401-1600	Erection and Fit-up	10h	03-Feb-14	03-Feb-14
CZA-TK-2401-1610	Welding	10h	04-Feb-14	04-Feb-14
CZA-TK-2401-1620	Inspection	20h	03-Feb-14	04-Feb-14
CZA-14.5.7.7.14 Roof Plates		20h	05-Feb-14	06-Feb-14
CZA-TK-2401-1660	Laying and Fit-up	10h	05-Feb-14	05-Feb-14
CZA-TK-2401-1670	Welding	10h	06-Feb-14	06-Feb-14
CZA-TK-2401-1680	Inspection	20h	05-Feb-14	06-Feb-14
CZA-14.5.7.7.16 Roof Nozzles, Manholes and Other Appurtanances		50h	08-Feb-14	12-Feb-14
CZA-TK-2401-1690	Installation and Fit-up	20h	08-Feb-14	09-Feb-14
CZA-TK-2401-1700	Welding	30h	10-Feb-14	12-Feb-14
CZA-TK-2401-1710	Inspection	50h	08-Feb-14	12-Feb-14
CZA-14.5.7.7.17 Roof Platform, Handrails and Gratings		60h	09-Feb-14	16-Feb-14
CZA-TK-2401-1720	Erection and Fit-up	20h	09-Feb-14	11-Feb-14
CZA-TK-2401-1730	Welding	40h	11-Feb-14	16-Feb-14
CZA-TK-2401-1740	Inspection	60h	09-Feb-14	16-Feb-14
CZA-14.5.7.7.18 Stairway Platform, Handrails and Gratings		60h	11-Feb-14	18-Feb-14
CZA-TK-2401-1750	Erection and Fit-up	20h	11-Feb-14	13-Feb-14
CZA-TK-2401-1760	Welding	40h	13-Feb-14	18-Feb-14
CZA-TK-2401-1770	Inspection	60h	11-Feb-14	18-Feb-14
CZA-14.5.7.4 Hydrotest		100h	18-Feb-14	02-Mar-14
CZA-TK-2401-1780	Filling, Holding and Draining of Water	100h	18-Feb-14	02-Mar-14
CZA-14.5.7.5 Blasting and Painting		50h	02-Mar-14	08-Mar-14
CZA-TK-2401-1790	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	50h	02-Mar-14	08-Mar-14
CZA-14.5.7.6 Tank Calibration and Handover		70h	08-Mar-14	16-Mar-14
CZA-TK-2401-1800	Tank Calibration	50h	08-Mar-14	13-Mar-14
CZA-TK-2401-1810	Tank Handover	20h	13-Mar-14	16-Mar-14
CZA-14.5.1 C230-TK-2310(Fire Water Tank Dia 31.93m x Ht 18.50m)		2848h	24-Dec-13	20-Nov-14
CZA-14.5.1.2 Fabrication Works		360h	24-Dec-13	03-Feb-14

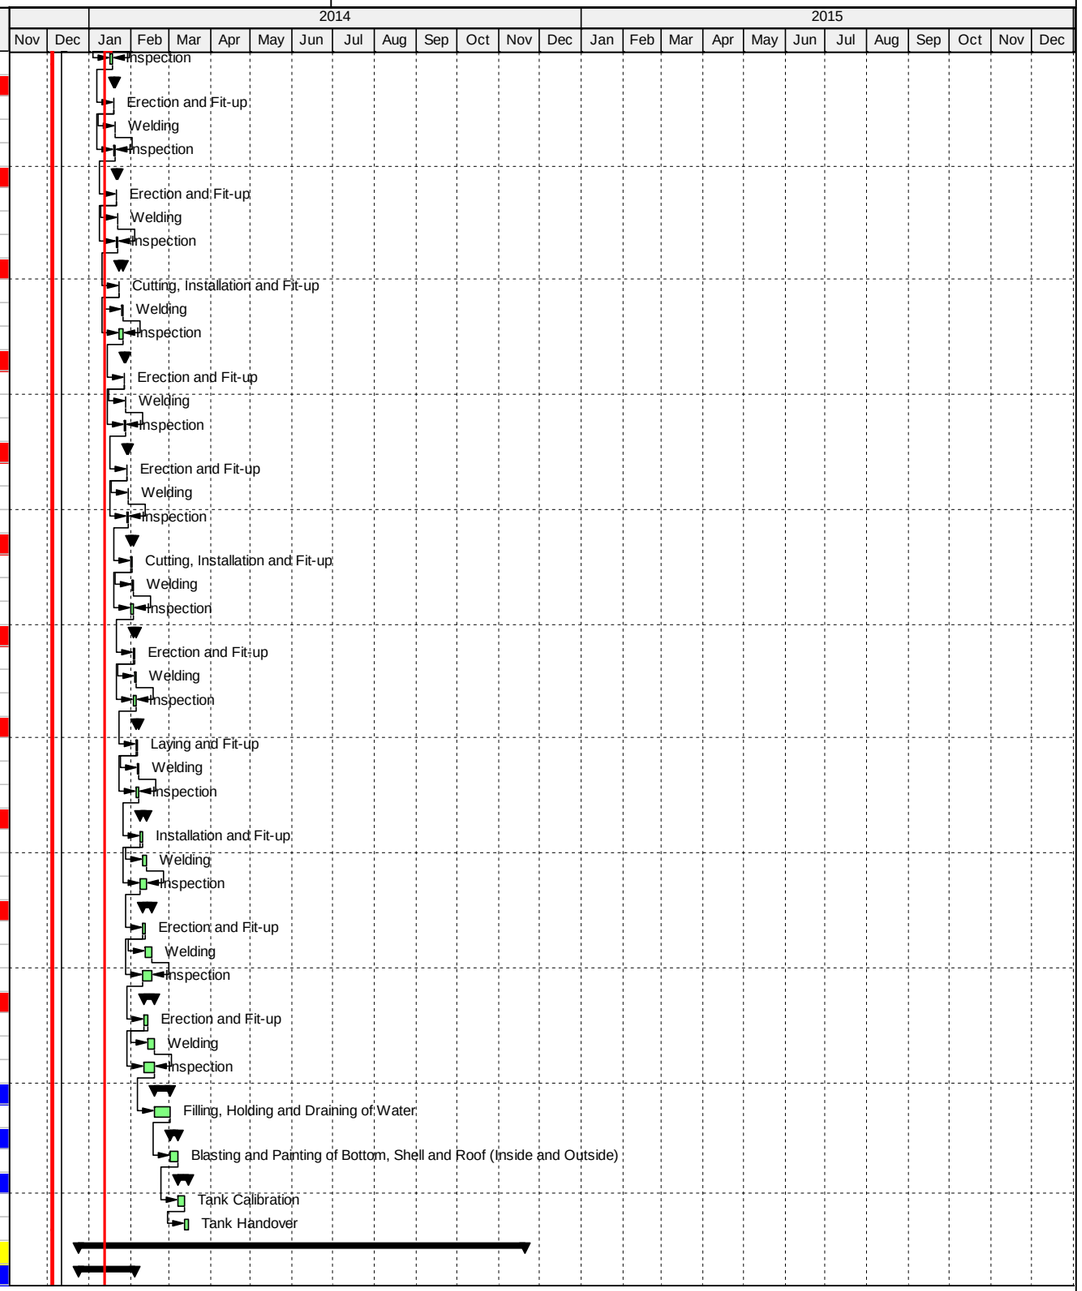

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-2310-1000	Cutting of Annular Plate	8h	24-Dec-13	24-Dec-13
CZA-TK-2310-1010	Cutting of Bottom Plates	8h	24-Dec-13	25-Dec-13
CZA-TK-2310-1020	Cutting, Bevelling & Rolling of Shell No.7	8h	25-Dec-13	26-Dec-13
CZA-TK-2310-1030	Cutting, Fit-up and Rolling of Shell No.8	8h	26-Dec-13	28-Dec-13
CZA-TK-2310-1040	Cutting of Compression Ring & Stairways Gratings and Handrails	48h	28-Dec-13	01-Jan-14
CZA-TK-2310-1050	Cutting, Fit-up and Welding Roof Structure	32h	29-Dec-13	01-Jan-14
CZA-TK-2310-1060	Cutting of Roof Plates	24h	01-Jan-14	04-Jan-14
CZA-TK-2310-1070	Cutting, Fit-up, Welding of Roof Nozzles, Manholes and Other Appurtances	48h	04-Jan-14	09-Jan-14
CZA-TK-2310-1080	Cutting, Fit-up and Welding of Roof Platform, Gratings and Handrails	80h	09-Jan-14	19-Jan-14
CZA-TK-2310-1090	Cutting, Bevelling and Rolling Shell No.6	8h	19-Jan-14	20-Jan-14
CZA-TK-2310-1100	Cutting, Bevelling and Rolling Shell No.5	8h	20-Jan-14	20-Jan-14
CZA-TK-2310-1110	Cutting, Bevelling and Rolling Shell No.4	8h	21-Jan-14	21-Jan-14
CZA-TK-2310-1120	Cutting, Bevelling and Rolling Shell No.3	8h	21-Jan-14	22-Jan-14
CZA-TK-2310-1130	Cutting, Bevelling and Rolling Shell No.2	8h	22-Jan-14	23-Jan-14
CZA-TK-2310-1140	Cutting, Bevelling and Rolling Shell No.1	8h	23-Jan-14	25-Jan-14
CZA-TK-2310-1150	Cutting, Fit-up & Welding of Shell Nozzles, Manholes and other Appurtanances	48h	25-Jan-14	29-Jan-14
CZA-TK-2310-1160	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	48h	29-Jan-14	03-Feb-14
CZA-14.5.1.4 Foundation Takeover		0h	25-Jan-14	25-Jan-14
CZA-TK-2310-1170	Foundation Takeover From Client	0h	25-Jan-14	
CZA-14.5.1.7 Mechanical Erection		1840h	26-Jan-14	28-Aug-14
CZA-14.5.1.7.1 Annular Plates		50h	26-Jan-14	01-Feb-14
CZA-TK-2310-1180	Laying and Fit-up	10h	26-Jan-14	27-Jan-14
CZA-TK-2310-1190	Welding	40h	27-Jan-14	01-Feb-14
CZA-TK-2310-1200	Inspection	50h	26-Jan-14	01-Feb-14
CZA-14.5.1.7.2 Bottom Plates		160h	01-Feb-14	19-Feb-14
CZA-TK-2310-1210	Laying and Fit-up	40h	01-Feb-14	05-Feb-14
CZA-TK-2310-1220	Welding	120h	05-Feb-14	19-Feb-14
CZA-TK-2310-1230	Inspection	160h	01-Feb-14	19-Feb-14
CZA-14.5.1.7.3 Shell No.7		90h	19-Feb-14	02-Mar-14
CZA-TK-2310-1240	Erection and Fit-up	20h	19-Feb-14	22-Feb-14
CZA-TK-2310-1250	Welding	70h	22-Feb-14	02-Mar-14
CZA-TK-2310-1260	Inspection	90h	19-Feb-14	02-Mar-14
CZA-14.5.1.7.4 Shell No.8		90h	02-Mar-14	12-Mar-14
CZA-TK-2310-1270	Erection and Fit-up	20h	02-Mar-14	04-Mar-14
CZA-TK-2310-1280	Welding	70h	04-Mar-14	12-Mar-14
CZA-TK-2310-1290	Inspection	90h	02-Mar-14	12-Mar-14
CZA-14.5.1.7.5 Shell Nozzles and Other Attachments		60h	12-Mar-14	19-Mar-14
CZA-TK-2310-1300	Cutting, Installation and Fit-up	20h	12-Mar-14	15-Mar-14
CZA-TK-2310-1310	Welding	40h	15-Mar-14	19-Mar-14
CZA-TK-2310-1320	Inspection	60h	12-Mar-14	19-Mar-14
CZA-14.5.1.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		50h	19-Mar-14	25-Mar-14
CZA-TK-2310-1330	Erection and Fit-up	20h	19-Mar-14	22-Mar-14
CZA-TK-2310-1340	Welding	30h	22-Mar-14	25-Mar-14
CZA-TK-2310-1350	Inspection	50h	19-Mar-14	25-Mar-14
CZA-14.5.1.7.9 Roof Structure		160h	25-Mar-14	13-Apr-14
CZA-TK-2310-1360	Erection and Fit-up	40h	25-Mar-14	30-Mar-14
CZA-TK-2310-1370	Welding	120h	30-Mar-14	13-Apr-14
CZA-TK-2310-1380	Inspection	160h	25-Mar-14	13-Apr-14
CZA-14.5.1.7.10 Roof Plates		120h	13-Apr-14	27-Apr-14
CZA-TK-2310-1390	Laying and Fit-up	20h	13-Apr-14	15-Apr-14
CZA-TK-2310-1400	Welding	100h	15-Apr-14	27-Apr-14
CZA-TK-2310-1410	Inspection	120h	13-Apr-14	27-Apr-14
CZA-14.5.1.7.11 Compression Ring		120h	27-Apr-14	11-May-14
CZA-TK-2310-1420	Laying and Fit-up	20h	27-Apr-14	29-Apr-14

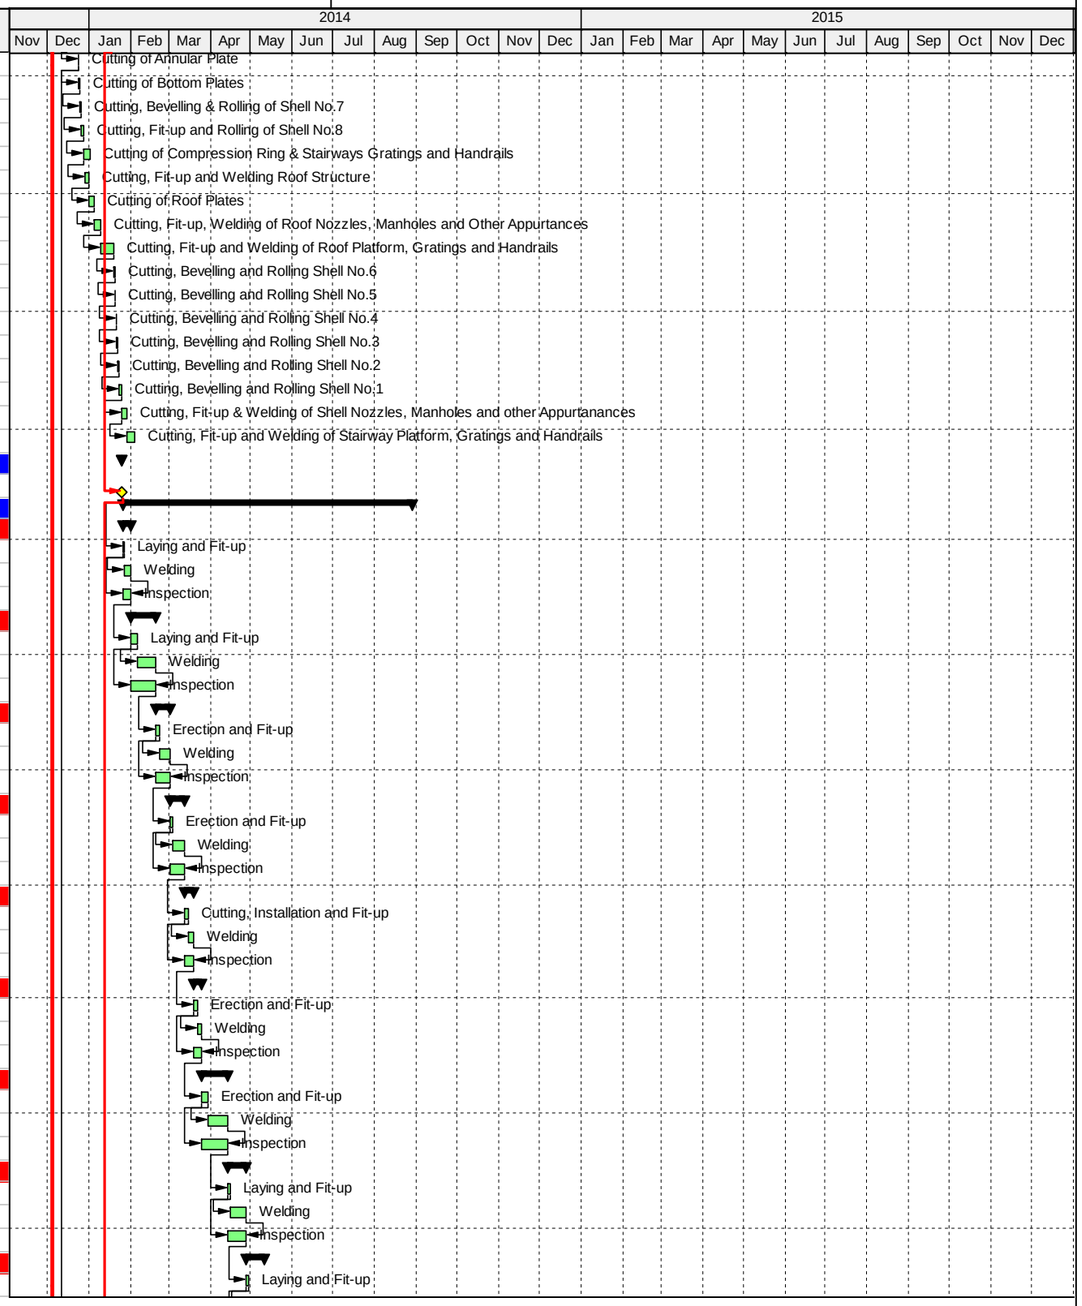

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone
- summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-2310-1430	Welding	100h	29-Apr-14	11-May-14
CZA-TK-2310-1440	Inspection	120h	27-Apr-14	11-May-14
CZA-14.5.1.7.12 Roof Nozzles, Manholes and Other Appurtanances		**90h**	**11-May-14**	**21-May-14**
CZA-TK-2310-1450	Cutting,Installation and Fit-up	30h	11-May-14	14-May-14
CZA-TK-2310-1460	Welding	60h	14-May-14	21-May-14
CZA-TK-2310-1470	Inspection	90h	11-May-14	21-May-14
CZA-14.5.1.7.13 Roof Platform, Gratings and Handrails		**140h**	**21-May-14**	**07-Jun-14**
CZA-TK-2310-1480	Erection and Fit-up	40h	21-May-14	26-May-14
CZA-TK-2310-1490	Welding	100h	26-May-14	07-Jun-14
CZA-TK-2310-1500	Inspection	140h	21-May-14	07-Jun-14
CZA-14.5.1.7.14 Shell No.6		**90h**	**07-Jun-14**	**17-Jun-14**
CZA-TK-2310-1510	Jacking, Erection and Fit-up	20h	07-Jun-14	09-Jun-14
CZA-TK-2310-1520	Welding	70h	09-Jun-14	17-Jun-14
CZA-TK-2310-1530	Inspection	90h	07-Jun-14	17-Jun-14
CZA-14.5.1.7.15 Shell No.5		**90h**	**17-Jun-14**	**28-Jun-14**
CZA-TK-2310-1540	Jacking,Erection and Fit-up	20h	17-Jun-14	19-Jun-14
CZA-TK-2310-1550	Welding	70h	19-Jun-14	28-Jun-14
CZA-TK-2310-1560	Inspection	90h	17-Jun-14	28-Jun-14
CZA-14.5.1.7.16 Shell No.4		**90h**	**28-Jun-14**	**08-Jul-14**
CZA-TK-2310-1570	Jacking,Erection and Fit-up	20h	28-Jun-14	30-Jun-14
CZA-TK-2310-1580	Welding	70h	30-Jun-14	08-Jul-14
CZA-TK-2310-1590	Inspection	90h	28-Jun-14	08-Jul-14
CZA-14.5.1.7.17 Shell No.3		**90h**	**08-Jul-14**	**19-Jul-14**
CZA-TK-2310-1600	Jacking, Erection and Fit-up	20h	08-Jul-14	10-Jul-14
CZA-TK-2310-1610	Welding	70h	10-Jul-14	19-Jul-14
CZA-TK-2310-1620	Inspection	90h	08-Jul-14	19-Jul-14
CZA-14.5.1.7.18 Shell No.2		**90h**	**19-Jul-14**	**29-Jul-14**
CZA-TK-2310-1630	Jacking, Erection and Fit-up	20h	19-Jul-14	21-Jul-14
CZA-TK-2310-1640	Welding	70h	21-Jul-14	29-Jul-14
CZA-TK-2310-1650	Inspection	90h	19-Jul-14	29-Jul-14
CZA-14.5.1.7.19 Shell No.1		**90h**	**29-Jul-14**	**09-Aug-14**
CZA-TK-2310-1660	Jacking, Erection and Fit-up	20h	29-Jul-14	31-Jul-14
CZA-TK-2310-1670	Welding	70h	31-Jul-14	09-Aug-14
CZA-TK-2310-1680	Inspection	90h	29-Jul-14	09-Aug-14
CZA-14.5.1.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**120h**	**09-Aug-14**	**23-Aug-14**
CZA-TK-2310-1690	Lay-out, Cutting, and Fit-up	40h	09-Aug-14	13-Aug-14
CZA-TK-2310-1700	Welding	80h	13-Aug-14	23-Aug-14
CZA-TK-2310-1710	Inspection	120h	09-Aug-14	23-Aug-14
CZA-14.5.1.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		**90h**	**18-Aug-14**	**28-Aug-14**
CZA-TK-2310-1720	Erection and Fit-up	20h	18-Aug-14	20-Aug-14
CZA-TK-2310-1730	Welding	70h	20-Aug-14	28-Aug-14
CZA-TK-2310-1740	Inspection	90h	18-Aug-14	28-Aug-14
CZA-14.5.1.6 Hydrotest		**430h**	**28-Aug-14**	**18-Oct-14**
CZA-TK-2310-1750	Filling, Holding and Draining of Water	430h	28-Aug-14	18-Oct-14
CZA-14.5.1.8 Blasting and Painting		**220h**	**18-Oct-14**	**12-Nov-14**
CZA-TK-2310-1760	Blasting and Painting of Shell, Bottom and Roof (Inside and Outside)	220h	18-Oct-14	12-Nov-14
CZA-14.5.1.9 Tank Calibration and Handover		**70h**	**12-Nov-14**	**20-Nov-14**
CZA-TK-2310-1770	Tank Calibration	50h	12-Nov-14	18-Nov-14
CZA-TK-2310-1780	Tank Handover	20h	18-Nov-14	20-Nov-14
CZA-14.5.2 C230-TK-2311(Fire Water Tank Dia 31.93m x Ht 18.50m)		**2878h**	**24-Dec-13**	**24-Nov-14**
CZA-14.5.2.2 Fabrication Works		**360h**	**24-Dec-13**	**03-Feb-14**
CZA-TK-2311-1380	Cutting of Annular Plate	8h	24-Dec-13	24-Dec-13
CZA-TK-2311-1390	Cutting of Bottom Plates	8h	24-Dec-13	25-Dec-13
CZA-TK-2311-1400	Cutting, Bevelling & Rolling of Shell No.7	8h	25-Dec-13	26-Dec-13

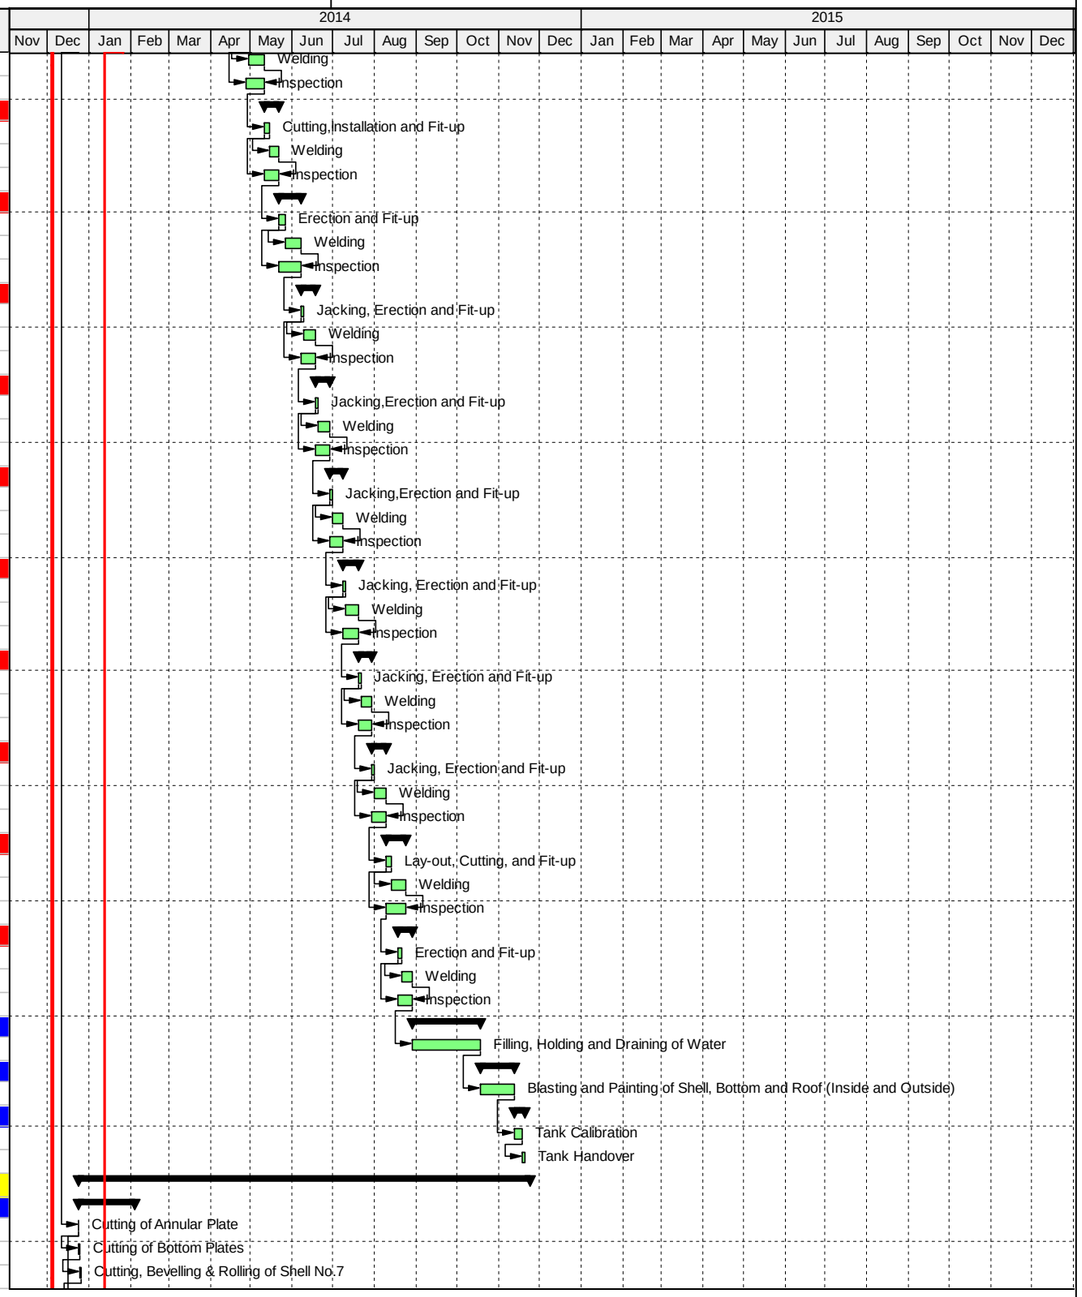

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-2311-1410	Cutting, Fit-up and Rolling of Shell No.8	8h	26-Dec-13	28-Dec-13
CZA-TK-2311-1420	Cutting of Compression Ring & Stairway	40h	29-Dec-13	01-Jan-14
CZA-TK-2311-1430	Cutting, Fit-up and Welding Roof Structure	32h	29-Dec-13	01-Jan-14
CZA-TK-2311-1440	Cutting of Roof Plates	24h	01-Jan-14	04-Jan-14
CZA-TK-2311-1450	Cutting, Fit-up, Welding of Roof Nozzles, Manholes and Other Appurtances	48h	04-Jan-14	09-Jan-14
CZA-TK-2311-1460	Cutting, Fit-up and Welding of Roof Platform, Gratings and Handrails	80h	09-Jan-14	19-Jan-14
CZA-TK-2311-1470	Cutting, Bevelling and Rolling Shell No.6	8h	19-Jan-14	20-Jan-14
CZA-TK-2311-1480	Cutting, Bevelling and Rolling Shell No.5	8h	20-Jan-14	20-Jan-14
CZA-TK-2311-1490	Cutting, Bevelling and Rolling Shell No.4	8h	21-Jan-14	21-Jan-14
CZA-TK-2311-1500	Cutting, Bevelling and Rolling Shell No.3	8h	21-Jan-14	22-Jan-14
CZA-TK-2311-1510	Cutting, Bevelling and Rolling Shell No.2	8h	22-Jan-14	23-Jan-14
CZA-TK-2311-1520	Cutting, Bevelling and Rolling Shell No.1	8h	23-Jan-14	25-Jan-14
CZA-TK-2311-1530	Cutting, Fit-up & Welding of Shell Nozzles, Manholes and other Appurtanances	48h	25-Jan-14	29-Jan-14
CZA-TK-2311-1540	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	48h	29-Jan-14	03-Feb-14
CZA-14.5.2.4 Foundation Takeover		**0h**	**25-Jan-14**	**25-Jan-14**
CZA-TK-2311-1550	Foundation Takeover From Client	0h	25-Jan-14	
CZA-14.5.2.7 Mechanical Erection		**1870h**	**26-Jan-14**	**01-Sep-14**
CZA-14.5.2.7.1 Annular Plates		**50h**	**26-Jan-14**	**01-Feb-14**
CZA-TK-2311-1560	Laying and Fit-up	10h	26-Jan-14	27-Jan-14
CZA-TK-2311-1570	Welding	40h	27-Jan-14	01-Feb-14
CZA-TK-2311-1580	Inspection	50h	26-Jan-14	01-Feb-14
CZA-14.5.2.7.2 Bottom Plates		**160h**	**01-Feb-14**	**19-Feb-14**
CZA-TK-2311-1590	Laying and Fit-up	40h	01-Feb-14	05-Feb-14
CZA-TK-2311-1600	Welding	120h	05-Feb-14	19-Feb-14
CZA-TK-2311-1610	Inspection	160h	01-Feb-14	19-Feb-14
CZA-14.5.2.7.3 Shell No.7		**90h**	**19-Feb-14**	**02-Mar-14**
CZA-TK-2311-1620	Erection and Fit-up	20h	19-Feb-14	22-Feb-14
CZA-TK-2311-1630	Welding	70h	22-Feb-14	02-Mar-14
CZA-TK-2311-1640	Inspection	90h	19-Feb-14	02-Mar-14
CZA-14.5.2.7.4 Shell No.8		**90h**	**02-Mar-14**	**12-Mar-14**
CZA-TK-2311-1650	Erection and Fit-up	20h	02-Mar-14	04-Mar-14
CZA-TK-2311-1660	Welding	70h	04-Mar-14	12-Mar-14
CZA-TK-2311-1670	Inspection	90h	02-Mar-14	12-Mar-14
CZA-14.5.2.7.5 Shell Nozzles and Other Attachments		**60h**	**12-Mar-14**	**19-Mar-14**
CZA-TK-2311-1680	Cutting, Installation and Fit-up	20h	12-Mar-14	15-Mar-14
CZA-TK-2311-1690	Welding	40h	15-Mar-14	19-Mar-14
CZA-TK-2311-1700	Inspection	60h	12-Mar-14	19-Mar-14
CZA-14.5.2.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**60h**	**19-Mar-14**	**26-Mar-14**
CZA-TK-2311-1710	Erection and Fit-up	20h	19-Mar-14	22-Mar-14
CZA-TK-2311-1720	Welding	40h	22-Mar-14	26-Mar-14
CZA-TK-2311-1730	Inspection	60h	19-Mar-14	26-Mar-14
CZA-14.5.2.7.9 Roof Structure		**160h**	**26-Mar-14**	**14-Apr-14**
CZA-TK-2311-1740	Erection and Fit-up	40h	26-Mar-14	31-Mar-14
CZA-TK-2311-1750	Welding	120h	31-Mar-14	14-Apr-14
CZA-TK-2311-1760	Inspection	160h	26-Mar-14	14-Apr-14
CZA-14.5.2.7.10 Roof Plates		**120h**	**14-Apr-14**	**28-Apr-14**
CZA-TK-2311-1770	Laying and Fit-up	20h	14-Apr-14	16-Apr-14
CZA-TK-2311-1780	Welding	10h	16-Apr-14	17-Apr-14
CZA-TK-2311-1790	Inspection	120h	14-Apr-14	28-Apr-14
CZA-14.5.2.7.11 Compression Ring		**120h**	**28-Apr-14**	**12-May-14**
CZA-TK-2311-1800	Laying and Fit-up	20h	28-Apr-14	30-Apr-14
CZA-TK-2311-1810	Welding	100h	30-Apr-14	12-May-14
CZA-TK-2311-1820	Inspection	120h	28-Apr-14	12-May-14
CZA-14.5.2.7.12 Roof Nozzles, Manholes and Other Appurtanances		**100h**	**12-May-14**	**24-May-14**

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone
- summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

Petrofac

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-2311-1830	Cutting,Installation and Fit-up	30h	12-May-14	15-May-14
CZA-TK-2311-1840	Welding	70h	15-May-14	24-May-14
CZA-TK-2311-1850	Inspection	100h	12-May-14	24-May-14
CZA-14.5.2.7.13 Roof Platform, Gratings and Handrails		**140h**	**24-May-14**	**09-Jun-14**
CZA-TK-2311-1860	Erection and Fit-up	40h	24-May-14	28-May-14
CZA-TK-2311-1870	Welding	100h	28-May-14	09-Jun-14
CZA-TK-2311-1880	Inspection	140h	24-May-14	09-Jun-14
CZA-14.5.2.7.14 Shell No.6		**90h**	**09-Jun-14**	**19-Jun-14**
CZA-TK-2311-1890	Jacking, Erection and Fit-up	20h	09-Jun-14	11-Jun-14
CZA-TK-2311-1900	Welding	70h	11-Jun-14	19-Jun-14
CZA-TK-2311-1910	Inspection	90h	09-Jun-14	19-Jun-14
CZA-14.5.2.7.15 Shell No.5		**90h**	**19-Jun-14**	**30-Jun-14**
CZA-TK-2311-1920	Jacking,Erection and Fit-up	20h	19-Jun-14	22-Jun-14
CZA-TK-2311-1930	Welding	70h	22-Jun-14	30-Jun-14
CZA-TK-2311-1940	Inspection	90h	19-Jun-14	30-Jun-14
CZA-14.5.2.7.16 Shell No.4		**90h**	**30-Jun-14**	**10-Jul-14**
CZA-TK-2311-1950	Jacking,Erection and Fit-up	20h	30-Jun-14	02-Jul-14
CZA-TK-2311-1960	Welding	70h	02-Jul-14	10-Jul-14
CZA-TK-2311-1970	Inspection	90h	30-Jun-14	10-Jul-14
CZA-14.5.2.7.17 Shell No.3		**90h**	**10-Jul-14**	**21-Jul-14**
CZA-TK-2311-1980	Jacking, Erection and Fit-up	20h	10-Jul-14	13-Jul-14
CZA-TK-2311-1990	Welding	70h	13-Jul-14	21-Jul-14
CZA-TK-2311-2000	Inspection	90h	10-Jul-14	21-Jul-14
CZA-14.5.2.7.18 Shell No.2		**90h**	**21-Jul-14**	**31-Jul-14**
CZA-TK-2311-2010	Jacking, Erection and Fit-up	20h	21-Jul-14	23-Jul-14
CZA-TK-2311-2020	Welding	70h	23-Jul-14	31-Jul-14
CZA-TK-2311-2030	Inspection	90h	21-Jul-14	31-Jul-14
CZA-14.5.2.7.19 Shell No.1		**90h**	**31-Jul-14**	**11-Aug-14**
CZA-TK-2311-2040	Jacking, Erection and Fit-up	20h	31-Jul-14	03-Aug-14
CZA-TK-2311-2050	Welding	70h	03-Aug-14	11-Aug-14
CZA-TK-2311-2060	Inspection	90h	31-Jul-14	11-Aug-14
CZA-14.5.2.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**120h**	**11-Aug-14**	**25-Aug-14**
CZA-TK-2311-2070	Lay-out, Cutting, and Fit-up	40h	11-Aug-14	16-Aug-14
CZA-TK-2311-2080	Welding	80h	16-Aug-14	25-Aug-14
CZA-TK-2311-2090	Inspection	120h	11-Aug-14	25-Aug-14
CZA-14.5.2.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		**100h**	**20-Aug-14**	**01-Sep-14**
CZA-TK-2311-2100	Erection and Fit-up	30h	20-Aug-14	24-Aug-14
CZA-TK-2311-2110	Welding	70h	24-Aug-14	01-Sep-14
CZA-TK-2311-2120	Inspection	100h	20-Aug-14	01-Sep-14
CZA-14.5.2.6 Hydrotest		**430h**	**01-Sep-14**	**21-Oct-14**
CZA-TK-2311-2130	Filling, Holding and Draining of Water	430h	01-Sep-14	21-Oct-14
CZA-14.5.2.8 Blasting and Painting		**220h**	**21-Oct-14**	**16-Nov-14**
CZA-TK-2311-2140	Blasting and Painting of Shell, Bottom and Roof (Inside and Outside)	220h	21-Oct-14	16-Nov-14
CZA-14.5.2.9 Tank Calibration and Handover		**70h**	**16-Nov-14**	**24-Nov-14**
CZA-TK-2311-2150	Tank Calibration	50h	16-Nov-14	22-Nov-14
CZA-TK-2311-2160	Tank Handover	20h	22-Nov-14	24-Nov-14
CZA-14.5.4 C320-TK-3201(Slop Oil Storage Tank Dia 11.0m x Ht 15m with IFR)		**1466h**	**29-Dec-13**	**17-Jun-14**
CZA-14.5.4.1 Fabrication Works		**352h**	**29-Dec-13**	**08-Feb-14**
CZA-TK-3201-1000	Cutting of Annular	8h	29-Dec-13	29-Dec-13
CZA-TK-3201-1010	Cutting of Bottom Plates	8h	29-Dec-13	30-Dec-13
CZA-TK-3201-1020	Cutting, Bevelling and Rolling No.1	8h	30-Dec-13	31-Dec-13
CZA-TK-3201-1030	Cutting, Bevelling and Rolling No.2	8h	31-Dec-13	01-Jan-14
CZA-TK-3201-1040	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtances	56h	01-Jan-14	07-Jan-14
CZA-TK-3201-1050	Cutting, Bevelling & Rolling No.3	8h	07-Jan-14	08-Jan-14

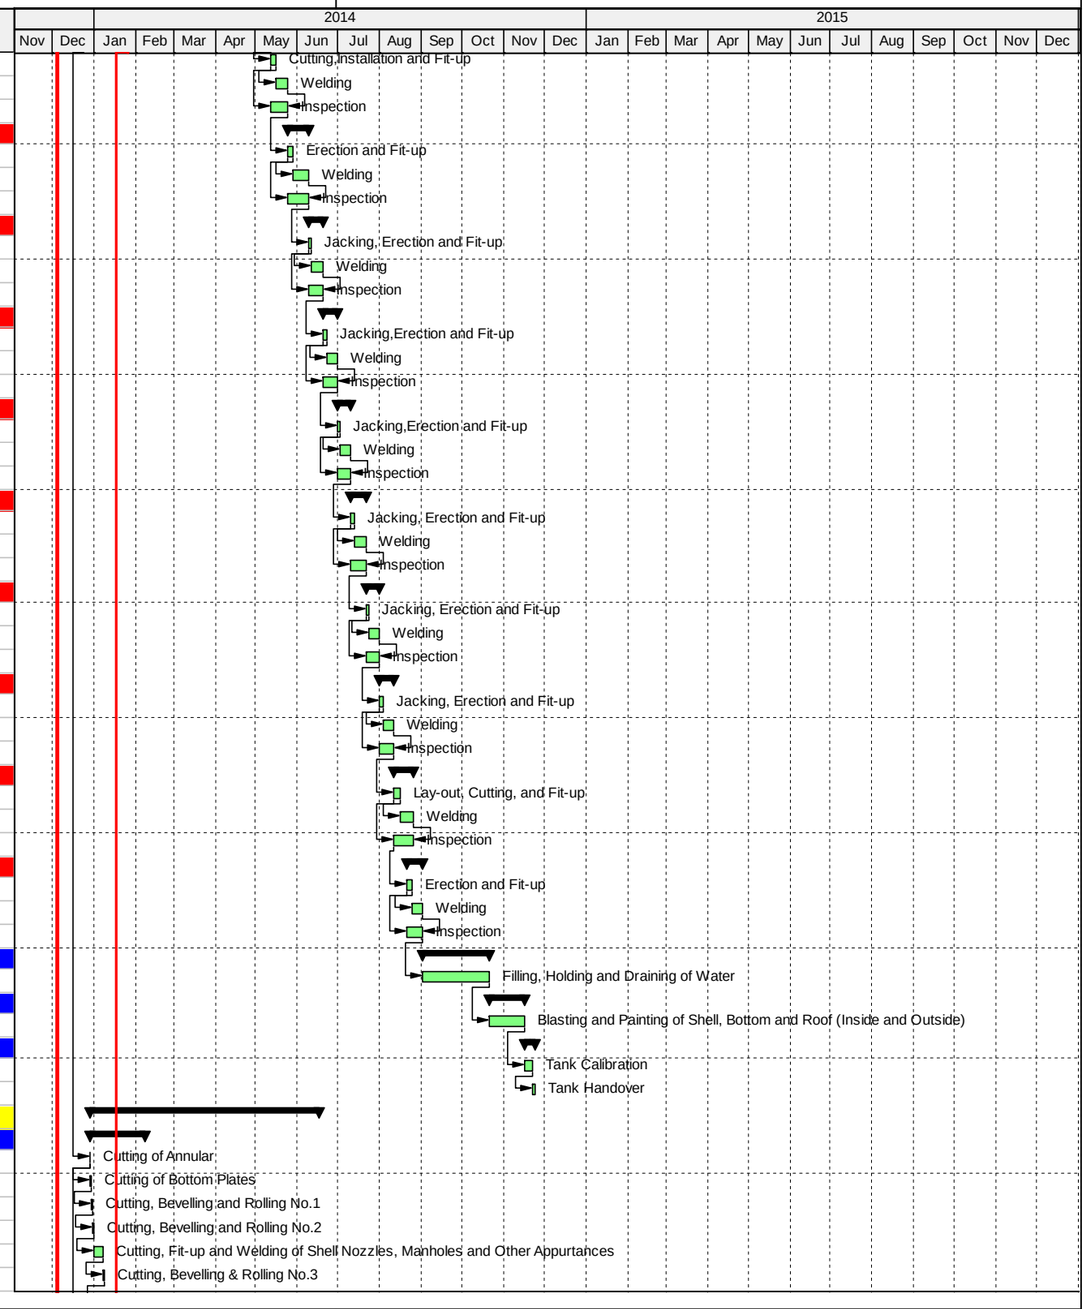

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-3201-1090	Cutting, Bevelling & Rolling of Shell No.4	8h	08-Jan-14	09-Jan-14
CZA-TK-3201-1100	Cutting, Bevelling & Rolling of Shell No.5	8h	09-Jan-14	11-Jan-14
CZA-TK-3201-1110	Cutting, Bevelling & Rolling of Shell No.6	8h	11-Jan-14	11-Jan-14
CZA-TK-3201-1120	Cutting, Bevelling & Rolling of Shell No.7	8h	12-Jan-14	12-Jan-14
CZA-TK-3201-1130	Cutting, Fit-up and Welding Curb Angle	24h	12-Jan-14	15-Jan-14
CZA-TK-3201-1140	Cutting, Fit-up and Welding of Roof Structure	40h	15-Jan-14	20-Jan-14
CZA-TK-3201-1150	Cutting,Fit-up and Welding of Roof Plates	8h	20-Jan-14	20-Jan-14
CZA-TK-3201-1160	Cutting, Fit-up and Welding of Roof Platform, Gratings and Handrails	56h	21-Jan-14	27-Jan-14
CZA-TK-3201-1170	Cutting, Fit-up & Welding of Roof Nozzles,Manholes and Other Appurtances	40h	27-Jan-14	01-Feb-14
CZA-TK-3201-1180	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	01-Feb-14	08-Feb-14
CZA-14.5.4.2 Foundation Takeover		**0h**	**30-Jan-14**	**30-Jan-14**
CZA-TK-3201-1190	Foundation Takeover from Client	0h	30-Jan-14	
CZA-14.5.4.7 Mechanical Erection		**890h**	**01-Feb-14**	**15-May-14**
CZA-14.5.4.7.1 Annular Plates		**30h**	**01-Feb-14**	**04-Feb-14**
CZA-TK-3201-1200	Laying and Fit-up	10h	01-Feb-14	02-Feb-14
CZA-TK-3201-1210	Welding	20h	02-Feb-14	04-Feb-14
CZA-TK-3201-1220	Inspection	30h	01-Feb-14	04-Feb-14
CZA-14.5.4.7.19 Bottom Plates		**40h**	**04-Feb-14**	**09-Feb-14**
CZA-TK-3201-1230	Erection and Fit-up	10h	04-Feb-14	05-Feb-14
CZA-TK-3201-1240	Welding	30h	05-Feb-14	09-Feb-14
CZA-TK-3201-1250	Inspection	40h	04-Feb-14	09-Feb-14
CZA-14.5.4.7.2 Shell No.1		**30h**	**09-Feb-14**	**12-Feb-14**
CZA-TK-3201-1260	Erection and Fit-up	10h	09-Feb-14	10-Feb-14
CZA-TK-3201-1270	Welding	20h	10-Feb-14	12-Feb-14
CZA-TK-3201-1280	Inspection	30h	09-Feb-14	12-Feb-14
CZA-14.5.4.7.3 Shell No.2		**30h**	**12-Feb-14**	**16-Feb-14**
CZA-TK-3201-1290	Erection and Fit-up	10h	12-Feb-14	13-Feb-14
CZA-TK-3201-1300	Welding	20h	13-Feb-14	16-Feb-14
CZA-TK-3201-1310	Inspection	30h	12-Feb-14	16-Feb-14
CZA-14.5.4.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**60h**	**16-Feb-14**	**23-Feb-14**
CZA-TK-3201-1320	Cutting, Installation and Fit-up	20h	16-Feb-14	18-Feb-14
CZA-TK-3201-1330	Welding	40h	18-Feb-14	23-Feb-14
CZA-TK-3201-1340	Inspection	60h	16-Feb-14	23-Feb-14
CZA-14.5.4.7.7 Shell No.3		**30h**	**23-Feb-14**	**26-Feb-14**
CZA-TK-3201-1350	Erection and Fit-up	10h	23-Feb-14	24-Feb-14
CZA-TK-3201-1360	Welding	20h	24-Feb-14	26-Feb-14
CZA-TK-3201-1370	Inspection	30h	23-Feb-14	26-Feb-14
CZA-14.5.4.7.8 Shell No.4		**30h**	**26-Feb-14**	**02-Mar-14**
CZA-TK-3201-1380	Erection and Fit-up	10h	26-Feb-14	27-Feb-14
CZA-TK-3201-1390	Welding	20h	27-Feb-14	02-Mar-14
CZA-TK-3201-1400	Inspection	30h	26-Feb-14	02-Mar-14
CZA-14.5.4.7.9 Shell No.5		**30h**	**02-Mar-14**	**05-Mar-14**
CZA-TK-3201-1410	Erection and Fit-up	10h	02-Mar-14	03-Mar-14
CZA-TK-3201-1420	Welding	20h	03-Mar-14	05-Mar-14
CZA-TK-3201-1430	Inspection	30h	02-Mar-14	05-Mar-14
CZA-14.5.4.7.10 Shell No.6		**30h**	**05-Mar-14**	**09-Mar-14**
CZA-TK-3201-1440	Erection and Fit-up	10h	05-Mar-14	06-Mar-14
CZA-TK-3201-1450	Welding	20h	06-Mar-14	09-Mar-14
CZA-TK-3201-1460	Inspection	30h	05-Mar-14	09-Mar-14
CZA-14.5.4.7.11 Shell No.7		**40h**	**09-Mar-14**	**13-Mar-14**
CZA-TK-3201-1470	Erection and Fit-up	10h	09-Mar-14	10-Mar-14
CZA-TK-3201-1480	Welding	20h	10-Mar-14	12-Mar-14
CZA-TK-3201-1490	Inspection	30h	10-Mar-14	13-Mar-14
CZA-14.5.4.7.12 Shell Nozzles and attachements (Upper)		**50h**	**13-Mar-14**	**19-Mar-14**

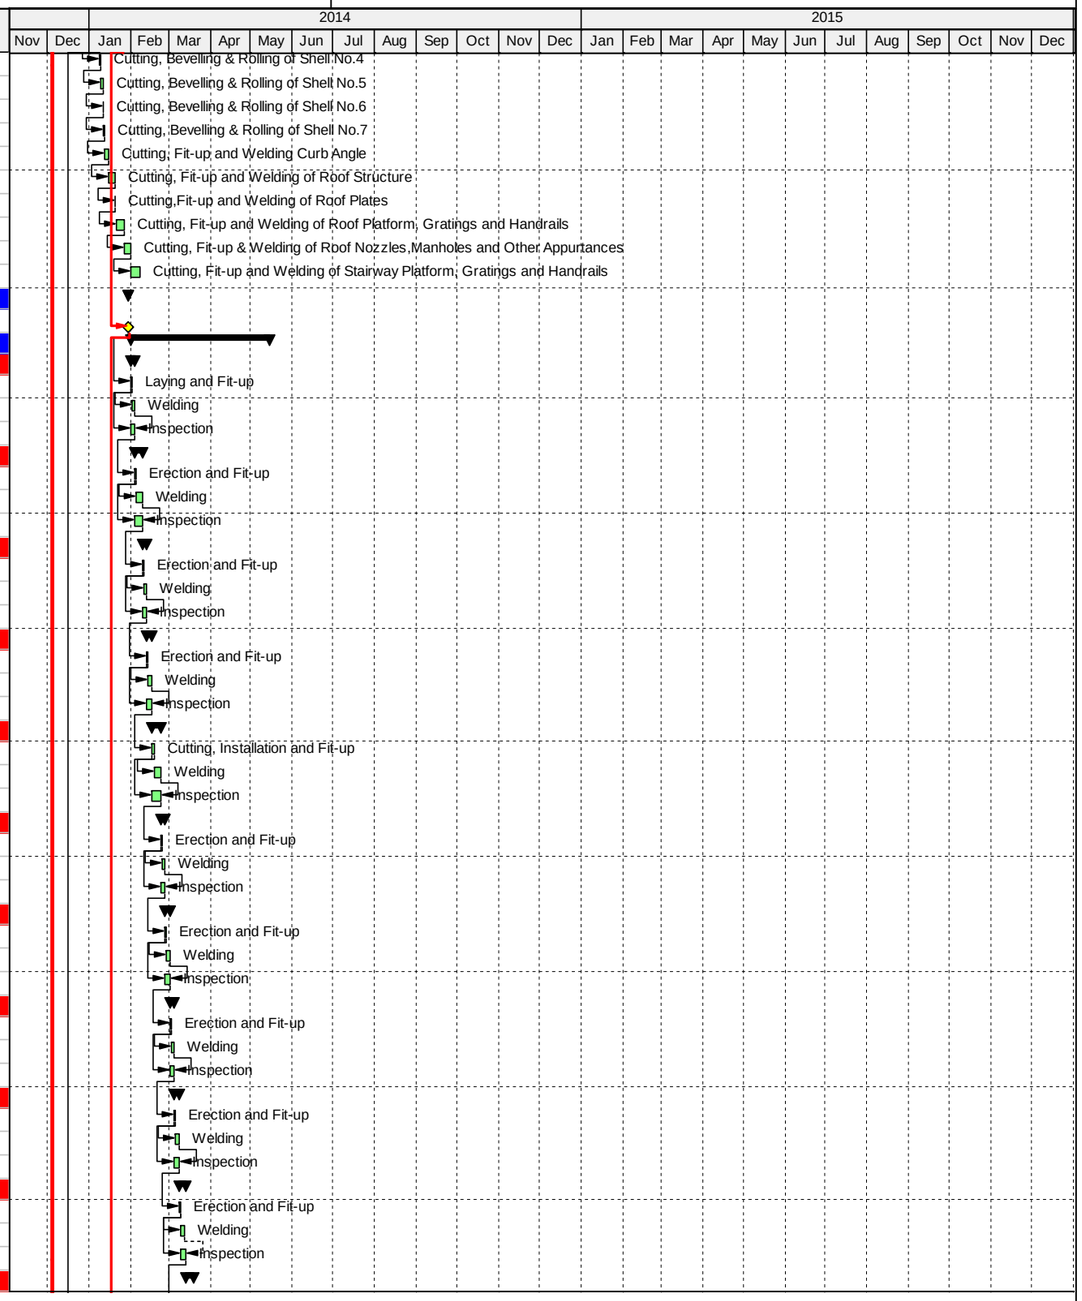

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-3201-1500	Cutting, Installation and Fit-up	20h	13-Mar-14	16-Mar-14
CZA-TK-3201-1520	Welding	30h	16-Mar-14	19-Mar-14
CZA-TK-3201-1530	Inspection	50h	13-Mar-14	19-Mar-14
CZA-14.5.4.7.13 Curb Angle		**30h**	**19-Mar-14**	**23-Mar-14**
CZA-TK-3201-1540	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-3201-1550	Welding	20h	20-Mar-14	23-Mar-14
CZA-TK-3201-1560	Inspection	30h	19-Mar-14	23-Mar-14
CZA-14.5.4.7.14 Roof Structure		**70h**	**23-Mar-14**	**31-Mar-14**
CZA-TK-3201-1570	Laying and Fit-up	20h	23-Mar-14	25-Mar-14
CZA-TK-3201-1580	Welding	50h	25-Mar-14	31-Mar-14
CZA-TK-3201-1590	Inspection	70h	23-Mar-14	31-Mar-14
CZA-14.5.4.7.15 Roof Plates		**40h**	**31-Mar-14**	**05-Apr-14**
CZA-TK-3201-1600	Laying and Fit-up	10h	31-Mar-14	01-Apr-14
CZA-TK-3201-1610	Welding	30h	01-Apr-14	05-Apr-14
CZA-TK-3201-1620	Inspection	40h	31-Mar-14	05-Apr-14
CZA-14.5.4.7.16 Roof Nozzles, Manholes and Other Appurtanances		**50h**	**05-Apr-14**	**10-Apr-14**
CZA-TK-3201-1630	Installation and Fit-up	20h	05-Apr-14	07-Apr-14
CZA-TK-3201-1640	Welding	30h	07-Apr-14	10-Apr-14
CZA-TK-3201-1650	Inspection	50h	05-Apr-14	10-Apr-14
CZA-14.5.4.7.18 Stairway Platform, Handrails and Gratings		**150h**	**10-Apr-14**	**28-Apr-14**
CZA-TK-3201-1660	Erection and Fit-up	50h	10-Apr-14	16-Apr-14
CZA-TK-3201-1670	Welding	100h	16-Apr-14	28-Apr-14
CZA-TK-3201-1680	Inspection	150h	10-Apr-14	28-Apr-14
CZA-14.5.4.7.17 Roof Platform, Handrails and Gratings		**150h**	**28-Apr-14**	**15-May-14**
CZA-TK-3201-1690	Erection and Fit-up	50h	28-Apr-14	04-May-14
CZA-TK-3201-1700	Welding	100h	04-May-14	15-May-14
CZA-TK-3201-1710	Inspection	150h	28-Apr-14	15-May-14
CZA-14.5.4.4 Hydrotest		**140h**	**15-May-14**	**01-Jun-14**
CZA-TK-3201-1720	Filling, Holding and Draining of Water	140h	15-May-14	01-Jun-14
CZA-14.5.4.5 Blasting and Painting		**70h**	**01-Jun-14**	**09-Jun-14**
CZA-TK-3201-1730	Blasting and Painting of Bottom, Shell and Roof (Inside & Outside)	70h	01-Jun-14	09-Jun-14
CZA-14.5.4.6 Tank Calibration & Handover		**70h**	**09-Jun-14**	**17-Jun-14**
CZA-TK-3201-1740	Tank Calibration	50h	09-Jun-14	15-Jun-14
CZA-TK-3201-1750	Tank Handover	20h	15-Jun-14	17-Jun-14
CZA-14.5.5 C320-TK-3208(Aqueous Waste Tank Dia 14m x Ht 14m)		**1526h**	**29-Dec-13**	**24-Jun-14**
CZA-14.5.5.1 Fabrication Works		**288h**	**29-Dec-13**	**30-Jan-14**
CZA-TK-3208-1200	Cutting of Annular	8h	29-Dec-13	29-Dec-13
CZA-TK-3208-1210	Cutting of Bottom Plates	8h	29-Dec-13	29-Dec-13
CZA-TK-3208-1220	Cutting, Bevelling and Rolling No.1	8h	29-Dec-13	30-Dec-13
CZA-TK-3208-1230	Cutting, Bevelling and Rolling No.2	8h	30-Dec-13	31-Dec-13
CZA-TK-3208-1240	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtances	32h	31-Dec-13	04-Jan-14
CZA-TK-3208-1250	Cutting, Bevelling & Rolling of Shell No.3	8h	04-Jan-14	05-Jan-14
CZA-TK-3208-1290	Cutting, Bevelling & Rolling of Shell No.4	8h	05-Jan-14	06-Jan-14
CZA-TK-3208-1300	Cutting, Bevelling & Rolling of Shell No.5	8h	05-Jan-14	06-Jan-14
CZA-TK-3208-1310	Cutting, Bevelling & Rolling of Shell No.6	8h	06-Jan-14	06-Jan-14
CZA-TK-3208-1320	Cutting, Bevelling & Rolling of Shell No.7	8h	06-Jan-14	06-Jan-14
CZA-TK-3208-1330	Cutting, Fit-up and Welding Curb Angle	16h	07-Jan-14	08-Jan-14
CZA-TK-3208-1340	Cutting, Fit-up and Welding of Roof Structure	40h	08-Jan-14	13-Jan-14
CZA-TK-3208-1350	Cutting,Fit-up and Welding of Roof Plates	8h	13-Jan-14	14-Jan-14
CZA-TK-3208-1360	Cutting, Fit-up and Welding of Roof Platform, Gratings and Handrails	56h	14-Jan-14	20-Jan-14
CZA-TK-3208-1370	Cutting, Fit-up & Welding of Roof Nozzles,Manholes and Other Appurtances	32h	21-Jan-14	25-Jan-14
CZA-TK-3208-1380	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	25-Jan-14	30-Jan-14
CZA-14.5.5.2 Foundation Takeover		**0h**	**30-Jan-14**	**30-Jan-14**
CZA-TK-3208-1390	Foundation Takeover from Client	0h	30-Jan-14	

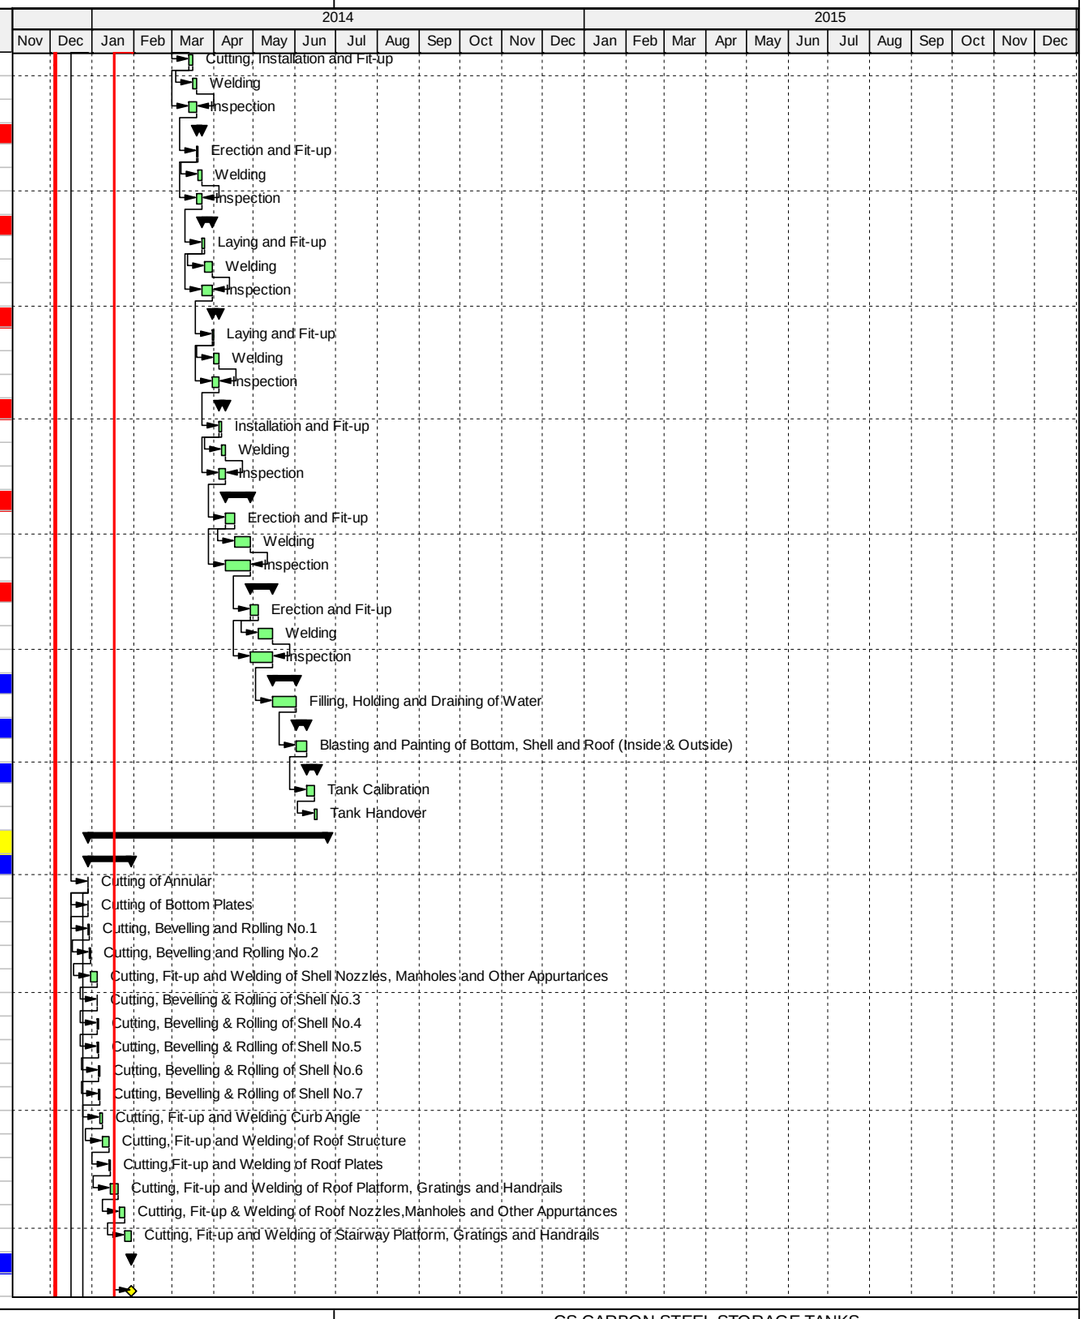

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.5.5.7 Mechanical Erection		**930h**	**01-Feb-14**	**20-May-14**
CZA-14.5.5.7.1 Annular Plates		**30h**	**01-Feb-14**	**04-Feb-14**
CZA-TK-3208-1400	Laying and Fit-up	10h	01-Feb-14	02-Feb-14
CZA-TK-3208-1410	Welding	20h	02-Feb-14	04-Feb-14
CZA-TK-3208-1420	Inspection	30h	01-Feb-14	04-Feb-14
CZA-14.5.5.7.19 Bottom Plates		**50h**	**04-Feb-14**	**10-Feb-14**
CZA-TK-3208-1430	Erection and Fit-up	10h	04-Feb-14	05-Feb-14
CZA-TK-3208-1440	Welding	40h	05-Feb-14	10-Feb-14
CZA-TK-3208-1450	Inspection	50h	04-Feb-14	10-Feb-14
CZA-14.5.5.7.2 Shell No.1		**40h**	**10-Feb-14**	**15-Feb-14**
CZA-TK-3208-1460	Erection and Fit-up	10h	10-Feb-14	11-Feb-14
CZA-TK-3208-1470	Welding	30h	11-Feb-14	15-Feb-14
CZA-TK-3208-1480	Inspection	40h	10-Feb-14	15-Feb-14
CZA-14.5.5.7.3 Shell No.2		**40h**	**15-Feb-14**	**19-Feb-14**
CZA-TK-3208-1490	Erection and Fit-up	10h	15-Feb-14	16-Feb-14
CZA-TK-3208-1500	Welding	30h	16-Feb-14	19-Feb-14
CZA-TK-3208-1510	Inspection	40h	15-Feb-14	19-Feb-14
CZA-14.5.5.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**50h**	**19-Feb-14**	**25-Feb-14**
CZA-TK-3208-1520	Cutting, Installation and Fit-up	20h	19-Feb-14	22-Feb-14
CZA-TK-3208-1530	Welding	30h	22-Feb-14	25-Feb-14
CZA-TK-3208-1540	Inspection	50h	19-Feb-14	25-Feb-14
CZA-14.5.5.7.7 Shell No.3		**40h**	**25-Feb-14**	**02-Mar-14**
CZA-TK-3208-1550	Erection and Fit-up	10h	25-Feb-14	26-Feb-14
CZA-TK-3208-1560	Welding	30h	26-Feb-14	02-Mar-14
CZA-TK-3208-1570	Inspection	40h	25-Feb-14	02-Mar-14
CZA-14.5.5.7.8 Shell No.4		**40h**	**02-Mar-14**	**06-Mar-14**
CZA-TK-3208-1580	Erection and Fit-up	10h	02-Mar-14	03-Mar-14
CZA-TK-3208-1590	Welding	30h	03-Mar-14	06-Mar-14
CZA-TK-3208-1600	Inspection	40h	02-Mar-14	06-Mar-14
CZA-14.5.5.7.9 Shell No.5		**40h**	**06-Mar-14**	**11-Mar-14**
CZA-TK-3208-1610	Erection and Fit-up	10h	06-Mar-14	08-Mar-14
CZA-TK-3208-1620	Welding	30h	08-Mar-14	11-Mar-14
CZA-TK-3208-1630	Inspection	40h	06-Mar-14	11-Mar-14
CZA-14.5.5.7.10 Shell No.6		**40h**	**11-Mar-14**	**16-Mar-14**
CZA-TK-3208-1640	Erection and Fit-up	10h	11-Mar-14	12-Mar-14
CZA-TK-3208-1650	Welding	30h	12-Mar-14	16-Mar-14
CZA-TK-3208-1660	Inspection	40h	11-Mar-14	16-Mar-14
CZA-14.5.5.7.11 Shell No.7		**40h**	**16-Mar-14**	**20-Mar-14**
CZA-TK-3208-1670	Erection and Fit-up	10h	16-Mar-14	17-Mar-14
CZA-TK-3208-1680	Welding	30h	17-Mar-14	20-Mar-14
CZA-TK-3208-1690	Inspection	40h	16-Mar-14	20-Mar-14
CZA-14.5.5.7.12 Shell Nozzles and attachements (Upper)		**50h**	**20-Mar-14**	**26-Mar-14**
CZA-TK-3208-1700	Cutting, Installation and Fit-up	20h	20-Mar-14	23-Mar-14
CZA-TK-3208-1710	Welding	30h	23-Mar-14	26-Mar-14
CZA-TK-3208-1720	Inspection	50h	20-Mar-14	26-Mar-14
CZA-14.5.5.7.13 Curb Angle		**40h**	**26-Mar-14**	**31-Mar-14**
CZA-TK-3208-1730	Erection and Fit-up	10h	26-Mar-14	27-Mar-14
CZA-TK-3208-1740	Welding	30h	27-Mar-14	31-Mar-14
CZA-TK-3208-1750	Inspection	40h	26-Mar-14	31-Mar-14
CZA-14.5.5.7.14 Roof Structure		**80h**	**31-Mar-14**	**09-Apr-14**
CZA-TK-3208-1760	Laying and Fit-up	20h	31-Mar-14	02-Apr-14
CZA-TK-3208-1770	Welding	60h	02-Apr-14	09-Apr-14
CZA-TK-3208-1780	Inspection	80h	31-Mar-14	09-Apr-14
CZA-14.5.5.7.15 Roof Plates		**40h**	**09-Apr-14**	**14-Apr-14**

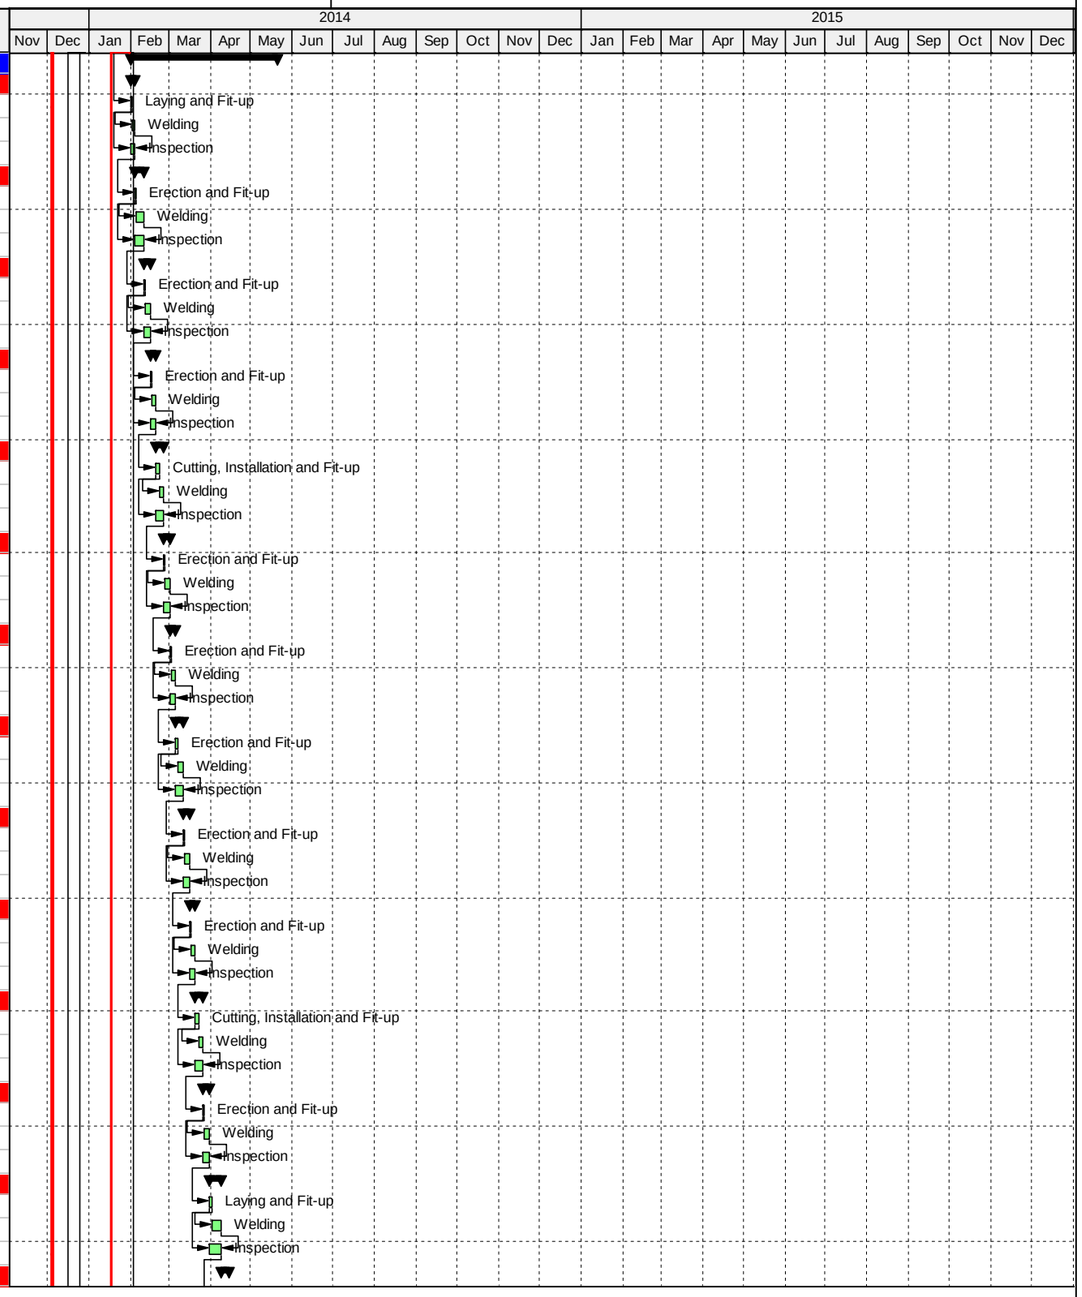

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-3208-1790	Laying and Fit-up	10h	09-Apr-14	10-Apr-14
CZA-TK-3208-1800	Welding	30h	10-Apr-14	14-Apr-14
CZA-TK-3208-1810	Inspection	40h	09-Apr-14	14-Apr-14
CZA-14.5.5.7.16 Roof Nozzles, Manholes and Other Appurtanances		60h	14-Apr-14	21-Apr-14
CZA-TK-3208-1820	Installation and Fit-up	20h	14-Apr-14	16-Apr-14
CZA-TK-3208-1830	Welding	40h	16-Apr-14	21-Apr-14
CZA-TK-3208-1840	Inspection	60h	14-Apr-14	21-Apr-14
CZA-14.5.5.7.18 Stairway Platform, Handrails and Gratings		130h	21-Apr-14	06-May-14
CZA-TK-3208-1850	Erection and Fit-up	30h	21-Apr-14	24-Apr-14
CZA-TK-3208-1860	Welding	100h	24-Apr-14	06-May-14
CZA-TK-3208-1870	Inspection	130h	21-Apr-14	06-May-14
CZA-14.5.5.7.17 Roof Platform, Handrails and Gratings		120h	06-May-14	20-May-14
CZA-TK-3208-1880	Erection and Fit-up	30h	06-May-14	10-May-14
CZA-TK-3208-1890	Welding	90h	10-May-14	20-May-14
CZA-TK-3208-1900	Inspection	120h	06-May-14	20-May-14
CZA-14.5.5.4 Hydrotest		150h	20-May-14	07-Jun-14
CZA-TK-3208-1910	Filling, Holding and Draining of Water	150h	20-May-14	07-Jun-14
CZA-14.5.5.5 Blasting and Painting		80h	07-Jun-14	16-Jun-14
CZA-TK-3208-1920	Blasting and Painting of Bottom, Shell and Roof (Inside & Outside)	80h	07-Jun-14	16-Jun-14
CZA-14.5.5.6 Tank Calibration & Handover		70h	16-Jun-14	24-Jun-14
CZA-TK-3208-1930	Tank Calibration	50h	16-Jun-14	22-Jun-14
CZA-TK-3208-1940	Tank Handover	20h	22-Jun-14	24-Jun-14
CZA-14.5.6 C320-TK-3202(Cumane Waste Tank Dia 4m x Ht 4.6m)		714h	07-Jan-14	31-Mar-14
CZA-14.5.6.1 Fabrication Works		128h	07-Jan-14	21-Jan-14
CZA-TK-3202-1410	Cutting of Bottom Plates	8h	07-Jan-14	07-Jan-14
CZA-TK-3202-1420	Cutting, Bevelling and Rolling No.1	8h	07-Jan-14	08-Jan-14
CZA-TK-3202-1430	Cutting, Bevelling and Rolling No.2	8h	08-Jan-14	09-Jan-14
CZA-TK-3202-1440	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtances	32h	09-Jan-14	13-Jan-14
CZA-TK-3202-1450	Cutting, Bevelling and Rolling Curb Angle	8h	13-Jan-14	14-Jan-14
CZA-TK-3202-1520	Cutting,Fit-up and Welding of Roof Plates	8h	14-Jan-14	15-Jan-14
CZA-TK-3202-1530	Cutting, Fit-up and Welding of Roof Platform, Gratings and Handrails	40h	14-Jan-14	19-Jan-14
CZA-TK-3202-1540	Cutting, Fit-up & Welding of Roof Nozzles,Manholes and Other Appurtances	32h	14-Jan-14	18-Jan-14
CZA-TK-3202-1550	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	48h	16-Jan-14	21-Jan-14
CZA-14.5.6.2 Foundation Takeover		0h	15-Feb-14	15-Feb-14
CZA-TK-3202-1560	Foundation Takeover from Client	0h	15-Feb-14	
CZA-14.5.6.7 Mechanical Erection		160h	16-Feb-14	06-Mar-14
CZA-14.5.6.7.19 Bottom Plates		20h	16-Feb-14	18-Feb-14
CZA-TK-3202-1570	Erection and Fit-up	10h	16-Feb-14	17-Feb-14
CZA-TK-3202-1580	Welding	10h	17-Feb-14	18-Feb-14
CZA-TK-3202-1590	Inspection	20h	16-Feb-14	18-Feb-14
CZA-14.5.6.7.2 Shell No.1		20h	18-Feb-14	20-Feb-14
CZA-TK-3202-1600	Erection and Fit-up	10h	18-Feb-14	19-Feb-14
CZA-TK-3202-1610	Welding	10h	19-Feb-14	20-Feb-14
CZA-TK-3202-1620	Inspection	20h	18-Feb-14	20-Feb-14
CZA-14.5.6.7.3 Shell No.2		20h	20-Feb-14	23-Feb-14
CZA-TK-3202-1630	Erection and Fit-up	10h	20-Feb-14	22-Feb-14
CZA-TK-3202-1640	Welding	10h	22-Feb-14	23-Feb-14
CZA-TK-3202-1650	Inspection	20h	20-Feb-14	23-Feb-14
CZA-14.5.6.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		20h	20-Feb-14	23-Feb-14
CZA-TK-3202-1660	Cutting, Installation and Fit-up	10h	20-Feb-14	22-Feb-14
CZA-TK-3202-1670	Welding	10h	22-Feb-14	23-Feb-14
CZA-TK-3202-1680	Inspection	20h	20-Feb-14	23-Feb-14
CZA-14.5.6.7.12 Shell Nozzles and attachements (Upper)		20h	20-Feb-14	23-Feb-14
CZA-TK-3202-1690	Cutting, Installation and Fit-up	10h	20-Feb-14	22-Feb-14

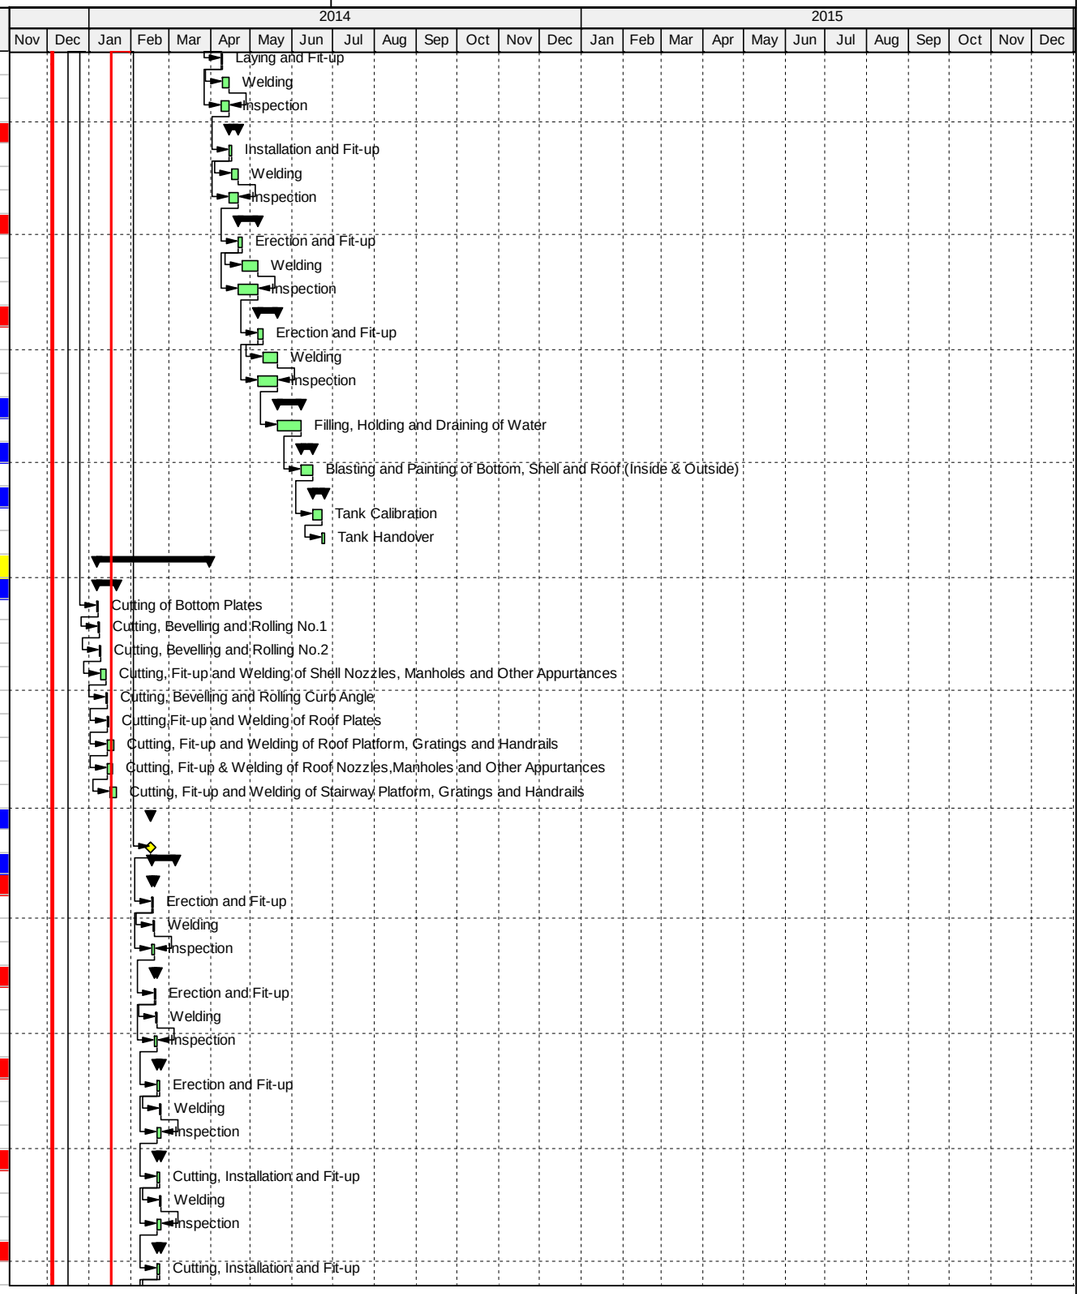

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-3202-1700	Welding	10h	22-Feb-14	23-Feb-14
CZA-TK-3202-1710	Inspection	20h	20-Feb-14	23-Feb-14
CZA-14.5.6.7.14 Curb Angle		20h	23-Feb-14	25-Feb-14
CZA-TK-3202-1720	Laying and Fit-up	10h	23-Feb-14	24-Feb-14
CZA-TK-3202-1730	Welding	10h	24-Feb-14	25-Feb-14
CZA-TK-3202-1740	Inspection	20h	23-Feb-14	25-Feb-14
CZA-14.5.6.7.15 Roof Plates		30h	25-Feb-14	01-Mar-14
CZA-TK-3202-1750	Laying and Fit-up	10h	25-Feb-14	26-Feb-14
CZA-TK-3202-1760	Welding	20h	26-Feb-14	01-Mar-14
CZA-TK-3202-1770	Inspection	30h	25-Feb-14	01-Mar-14
CZA-14.5.6.7.16 Roof Nozzles, Manholes and Other Appurtanances		30h	01-Mar-14	04-Mar-14
CZA-TK-3202-1780	Installation and Fit-up	10h	01-Mar-14	02-Mar-14
CZA-TK-3202-1790	Welding	20h	02-Mar-14	04-Mar-14
CZA-TK-3202-1800	Inspection	30h	01-Mar-14	04-Mar-14
CZA-14.5.6.7.18 Stairway Platform, Handrails and Gratings		50h	01-Mar-14	06-Mar-14
CZA-TK-3202-1810	Erection and Fit-up	20h	01-Mar-14	03-Mar-14
CZA-TK-3202-1820	Welding	30h	03-Mar-14	06-Mar-14
CZA-TK-3202-1830	Inspection	50h	01-Mar-14	06-Mar-14
CZA-14.5.6.7.17 Roof Platform, Handrails and Gratings		50h	01-Mar-14	06-Mar-14
CZA-TK-3202-1840	Erection and Fit-up	20h	01-Mar-14	03-Mar-14
CZA-TK-3202-1850	Welding	30h	03-Mar-14	06-Mar-14
CZA-TK-3202-1860	Inspection	50h	01-Mar-14	06-Mar-14
CZA-14.5.6.4 Hydrotest		90h	06-Mar-14	17-Mar-14
CZA-TK-3202-1870	Filling, Holding and Draining of Water	90h	06-Mar-14	17-Mar-14
CZA-14.5.6.5 Blasting and Painting		50h	17-Mar-14	23-Mar-14
CZA-TK-3202-1880	Blasting and Painting of Bottom, Shell and Roof (Inside & Outside)	50h	17-Mar-14	23-Mar-14
CZA-14.5.6.6 Tank Calibration & Handover		70h	23-Mar-14	31-Mar-14
CZA-TK-3202-1890	Tank Calibration	50h	23-Mar-14	29-Mar-14
CZA-TK-3202-1900	Tank Handover	20h	29-Mar-14	31-Mar-14
CZA-14.3 NORTH TANK FARM(NTF)		3382h	29-Dec-13	27-Jan-15
CZA-14.3.1 S210-TK-0510 (Extender Oil-1 Feed Tank Dia 11.61m x Ht 13.05m)		1700h	29-Dec-13	14-Jul-14
CZA-14.3.1.1 Fabrication Works		250h	29-Dec-13	26-Jan-14
CZA-TK-0510-1000	Cutting of Annular Plate	8h	29-Dec-13	29-Dec-13
CZA-TK-0510-1010	Cutting of Bottom Plates	8h	29-Dec-13	30-Dec-13
CZA-TK-0510-1020	Cutting, Bevelling & Rolling of Shell No.1	8h	30-Dec-13	31-Dec-13
CZA-TK-0510-1030	Cutting, Bevelling & Rolling of Shell No.2	8h	31-Dec-13	01-Jan-14
CZA-TK-0510-1040	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	24h	01-Jan-14	04-Jan-14
CZA-TK-0510-1050	Cutting, Bevelling & Rolling of Shell No.3	8h	04-Jan-14	05-Jan-14
CZA-TK-0510-1060	Cutting, Bevelling & Rolling of Shell No.4	8h	05-Jan-14	06-Jan-14
CZA-TK-0510-1070	Cutting, Bevelling & Rolling of Shell No.5	8h	06-Jan-14	06-Jan-14
CZA-TK-0510-1080	Cutting, Bevelling & Rolling of Shell No.6	8h	07-Jan-14	07-Jan-14
CZA-TK-0510-1090	Cutting, Bevelling & Rolling of Curb Angle	16h	07-Jan-14	09-Jan-14
CZA-TK-0510-1100	Cutting, Bevelling & Rolling of Roof Structure	40h	09-Jan-14	14-Jan-14
CZA-TK-0510-1110	Cutting of Roof Plates	10h	14-Jan-14	15-Jan-14
CZA-TK-0510-1120	Cutting,Fit-up and Welding of Roof Nozzles, Manholes & Other Appurtanances	56h	15-Jan-14	21-Jan-14
CZA-TK-0510-1130	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	80h	18-Jan-14	26-Jan-14
CZA-TK-0510-1140	Cutting, Fit-up and Welding of Stairway Platfrom, Gratings and Handrails	80h	18-Jan-14	26-Jan-14
CZA-14.3.1.2 Foundation Takeover		0h	30-Jan-14	30-Jan-14
CZA-TK-0510-1150	Foundation Takeover from Client	0h	30-Jan-14	
CZA-14.3.1.7 Mechanical Erection		1130h	30-Jan-14	10-Jun-14
CZA-14.3.1.7.1 Annular Plates		40h	30-Jan-14	03-Feb-14
CZA-TK-0510-1160	Laying and Fit-up	10h	30-Jan-14	30-Jan-14
CZA-TK-0510-1170	Welding	30h	01-Feb-14	03-Feb-14
CZA-TK-0510-1180	Inspection	40h	30-Jan-14	03-Feb-14

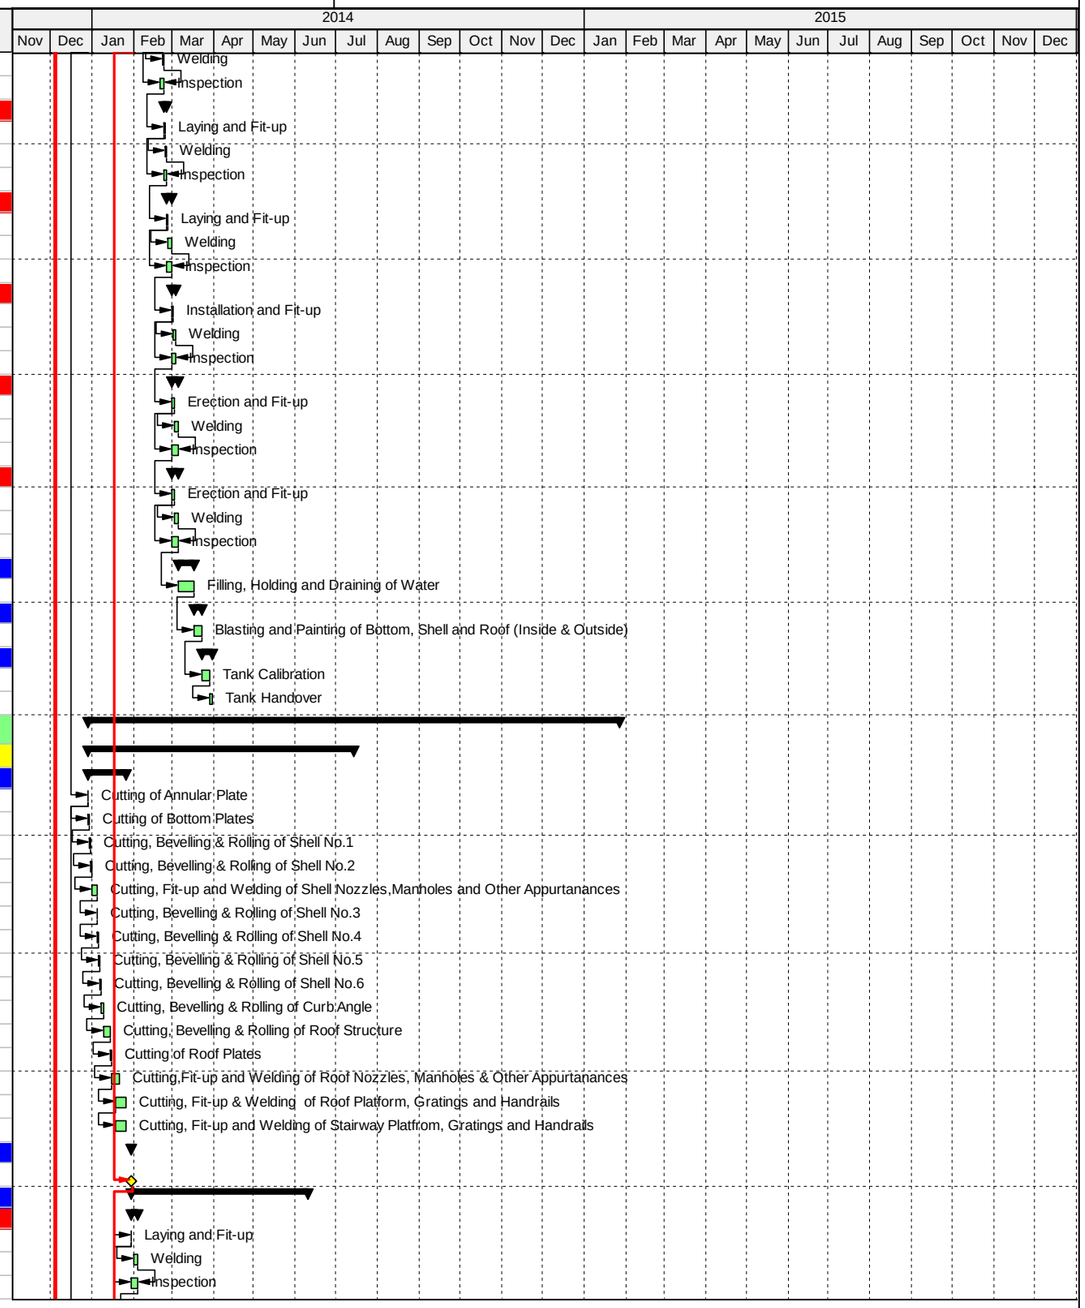

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

Petrofac

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.1.7.19 Bottom Plates		**50h**	**04-Feb-14**	**09-Feb-14**
CZA-TK-0510-1190	Erection and Fit-up	10h	04-Feb-14	04-Feb-14
CZA-TK-0510-1200	Welding	40h	05-Feb-14	09-Feb-14
CZA-TK-0510-1210	Inspection	50h	04-Feb-14	09-Feb-14
CZA-14.3.1.7.2 Shell No.1		**50h**	**10-Feb-14**	**15-Feb-14**
CZA-TK-0510-1220	Erection and Fit-up	10h	10-Feb-14	10-Feb-14
CZA-TK-0510-1230	Welding	40h	11-Feb-14	15-Feb-14
CZA-TK-0510-1240	Inspection	50h	10-Feb-14	15-Feb-14
CZA-14.3.1.7.3 Shell No.2		**50h**	**16-Feb-14**	**20-Feb-14**
CZA-TK-0510-1250	Erection and Fit-up	10h	16-Feb-14	16-Feb-14
CZA-TK-0510-1260	Welding	40h	17-Feb-14	20-Feb-14
CZA-TK-0510-1270	Inspection	50h	16-Feb-14	20-Feb-14
CZA-14.3.1.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**80h**	**22-Feb-14**	**02-Mar-14**
CZA-TK-0510-1280	Cutting, Installation and Fit-up	20h	22-Feb-14	23-Feb-14
CZA-TK-0510-1290	Welding	60h	24-Feb-14	02-Mar-14
CZA-TK-0510-1300	Inspection	80h	22-Feb-14	02-Mar-14
CZA-14.3.1.7.7 Shell No.3		**50h**	**03-Mar-14**	**08-Mar-14**
CZA-TK-0510-1310	Erection and Fit-up	10h	03-Mar-14	03-Mar-14
CZA-TK-0510-1320	Welding	40h	04-Mar-14	08-Mar-14
CZA-TK-0510-1330	Inspection	50h	03-Mar-14	08-Mar-14
CZA-14.3.1.7.8 Shell No.4		**50h**	**09-Mar-14**	**13-Mar-14**
CZA-TK-0510-1340	Erection and Fit-up	10h	09-Mar-14	09-Mar-14
CZA-TK-0510-1350	Welding	40h	10-Mar-14	13-Mar-14
CZA-TK-0510-1360	Inspection	50h	09-Mar-14	13-Mar-14
CZA-14.3.1.7.9 Shell No.5		**50h**	**15-Mar-14**	**19-Mar-14**
CZA-TK-0510-1370	Erection and Fit-up	10h	15-Mar-14	15-Mar-14
CZA-TK-0510-1380	Welding	40h	16-Mar-14	19-Mar-14
CZA-TK-0510-1390	Inspection	50h	15-Mar-14	19-Mar-14
CZA-14.3.1.7.10 Shell No.6		**50h**	**20-Mar-14**	**25-Mar-14**
CZA-TK-0510-1400	Erection and Fit-up	10h	20-Mar-14	20-Mar-14
CZA-TK-0510-1410	Welding	40h	22-Mar-14	25-Mar-14
CZA-TK-0510-1420	Inspection	50h	20-Mar-14	25-Mar-14
CZA-14.3.1.7.12 Shell Nozzles and attachements (Upper)		**70h**	**26-Mar-14**	**02-Apr-14**
CZA-TK-0510-1430	Cutting, Installation and Fit-up	20h	26-Mar-14	27-Mar-14
CZA-TK-0510-1440	Welding	50h	29-Mar-14	02-Apr-14
CZA-TK-0510-1450	Inspection	70h	26-Mar-14	02-Apr-14
CZA-14.3.1.7.13 Curb Angle		**30h**	**03-Apr-14**	**06-Apr-14**
CZA-TK-0510-1460	Erection and Fit-up	10h	03-Apr-14	03-Apr-14
CZA-TK-0510-1470	Welding	20h	05-Apr-14	06-Apr-14
CZA-TK-0510-1480	Inspection	30h	03-Apr-14	06-Apr-14
CZA-14.3.1.7.14 Roof Structure		**70h**	**07-Apr-14**	**14-Apr-14**
CZA-TK-0510-1490	Laying and Fit-up	20h	07-Apr-14	08-Apr-14
CZA-TK-0510-1500	Welding	50h	09-Apr-14	14-Apr-14
CZA-TK-0510-1510	Inspection	70h	07-Apr-14	14-Apr-14
CZA-14.3.1.7.15 Roof Plates		**70h**	**15-Apr-14**	**22-Apr-14**
CZA-TK-0510-1520	Laying and Fit-up	20h	15-Apr-14	16-Apr-14
CZA-TK-0510-1530	Welding	50h	17-Apr-14	22-Apr-14
CZA-TK-0510-1540	Inspection	70h	15-Apr-14	22-Apr-14
CZA-14.3.1.7.16 Roof Nozzles, Manholes and Other Appurtanances		**140h**	**23-Apr-14**	**08-May-14**
CZA-TK-0510-1550	Installation and Fit-up	40h	23-Apr-14	27-Apr-14
CZA-TK-0510-1560	Welding	100h	28-Apr-14	08-May-14
CZA-TK-0510-1570	Inspection	140h	23-Apr-14	08-May-14
CZA-14.3.1.7.18 Stairway Platform, Handrails and Gratings		**140h**	**10-May-14**	**25-May-14**
CZA-TK-0510-1580	Erection and Fit-up	40h	10-May-14	13-May-14

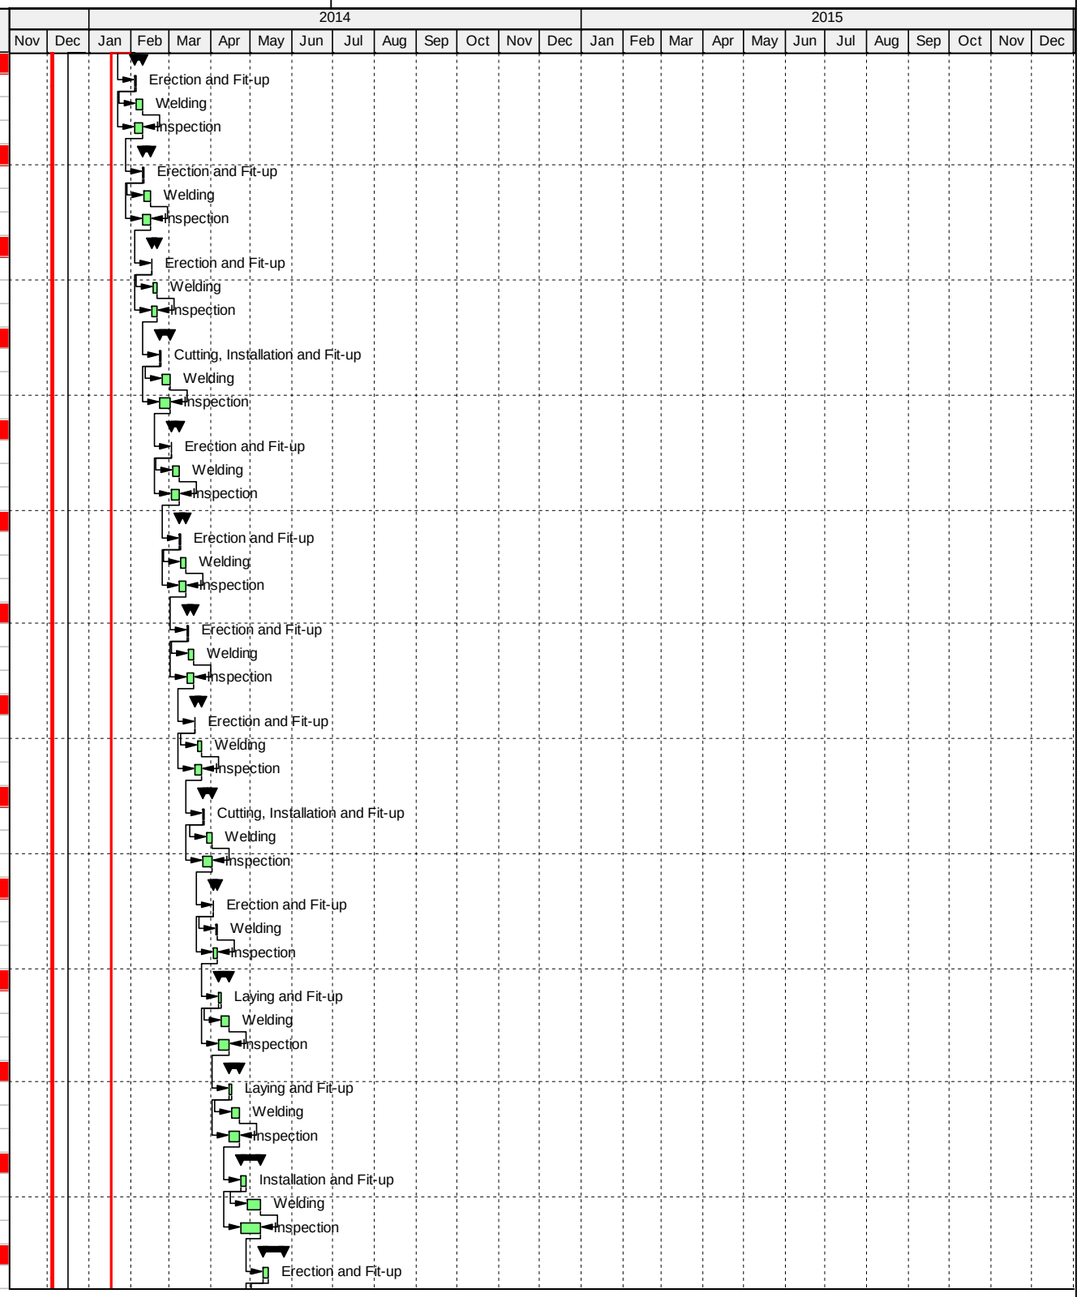

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0510-1590	Welding	100h	14-May-14	25-May-14
CZA-TK-0510-1600	Inspection	140h	10-May-14	25-May-14
CZA-14.3.1.7.17 Roof Platform, Handrails and Gratings		140h	26-May-14	10-Jun-14
CZA-TK-0510-1610	Erection and Fit-up	40h	26-May-14	29-May-14
CZA-TK-0510-1620	Welding	100h	31-May-14	10-Jun-14
CZA-TK-0510-1630	Inspection	140h	26-May-14	10-Jun-14
CZA-14.3.1.4 Hydotest		150h	11-Jun-14	28-Jun-14
CZA-TK-0510-1640	Filling, Holding and Draining of Water	150h	11-Jun-14	28-Jun-14
CZA-14.3.1.5 Blasting and Painting		70h	29-Jun-14	06-Jul-14
CZA-TK-0510-1650	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	70h	29-Jun-14	06-Jul-14
CZA-14.3.1.6 Tank Calibration and Handover		70h	07-Jul-14	14-Jul-14
CZA-TK-0510-1660	Tank Calibration	50h	07-Jul-14	12-Jul-14
CZA-TK-0510-1670	Tank Handover	20h	13-Jul-14	14-Jul-14
CZA-14.3.2 S210-TK-0511 (Extender Oil-1 Feed Tank Dia 11.61m x Ht 13.05m)		1680h	29-Dec-13	12-Jul-14
CZA-14.3.2.1 Fabrication Works		250h	29-Dec-13	26-Jan-14
CZA-TK-0511-1350	Cutting of Annular Plate	8h	29-Dec-13	29-Dec-13
CZA-TK-0511-1360	Cutting of Bottom Plates	8h	29-Dec-13	30-Dec-13
CZA-TK-0511-1370	Cutting, Bevelling & Rolling of Shell No.1	8h	30-Dec-13	31-Dec-13
CZA-TK-0511-1380	Cutting, Bevelling & Rolling of Shell No.2	8h	31-Dec-13	01-Jan-14
CZA-TK-0511-1390	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	24h	01-Jan-14	04-Jan-14
CZA-TK-0511-1400	Cutting, Bevelling & Rolling of Shell No.3	8h	04-Jan-14	05-Jan-14
CZA-TK-0511-1410	Cutting, Bevelling & Rolling of Shell No.4	8h	05-Jan-14	06-Jan-14
CZA-TK-0511-1420	Cutting, Bevelling & Rolling of Shell No.5	8h	06-Jan-14	06-Jan-14
CZA-TK-0511-1430	Cutting, Bevelling & Rolling of Shell No.6	8h	07-Jan-14	07-Jan-14
CZA-TK-0511-1440	Cutting, Bevelling & Rolling of Curb Angle	16h	07-Jan-14	09-Jan-14
CZA-TK-0511-1450	Cutting, Bevelling & Rolling of Roof Structure	40h	09-Jan-14	14-Jan-14
CZA-TK-0511-1460	Cutting of Roof Plates	10h	14-Jan-14	15-Jan-14
CZA-TK-0511-1470	Cutting,Fit-up and Welding of Roof Nozzles, Manholes & Other Appurtanances	56h	15-Jan-14	21-Jan-14
CZA-TK-0511-1480	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	80h	18-Jan-14	26-Jan-14
CZA-TK-0511-1490	Cutting, Fit-up and Welding of Stairway Platfrom, Gratings and Handrails	80h	18-Jan-14	26-Jan-14
CZA-14.3.2.2 Foundation Takeover		0h	30-Jan-14	30-Jan-14
CZA-TK-0511-1500	Foundation Takeover from Client	0h	30-Jan-14	
CZA-14.3.2.7 Mechanical Erection		1210h	30-Jan-14	19-Jun-14
CZA-14.3.2.7.1 Annular Plates		40h	30-Jan-14	03-Feb-14
CZA-TK-0511-1510	Laying and Fit-up	10h	30-Jan-14	30-Jan-14
CZA-TK-0511-1520	Welding	30h	01-Feb-14	03-Feb-14
CZA-TK-0511-1530	Inspection	40h	30-Jan-14	03-Feb-14
CZA-14.3.2.7.19 Bottom Plates		50h	04-Feb-14	09-Feb-14
CZA-TK-0511-1540	Erection and Fit-up	10h	04-Feb-14	04-Feb-14
CZA-TK-0511-1550	Welding	40h	05-Feb-14	09-Feb-14
CZA-TK-0511-1560	Inspection	50h	04-Feb-14	09-Feb-14
CZA-14.3.2.7.2 Shell No.1		50h	10-Feb-14	15-Feb-14
CZA-TK-0511-1570	Erection and Fit-up	10h	10-Feb-14	10-Feb-14
CZA-TK-0511-1580	Welding	40h	11-Feb-14	15-Feb-14
CZA-TK-0511-1590	Inspection	50h	10-Feb-14	15-Feb-14
CZA-14.3.2.7.3 Shell No.2		50h	16-Feb-14	20-Feb-14
CZA-TK-0511-1600	Erection and Fit-up	10h	16-Feb-14	16-Feb-14
CZA-TK-0511-1610	Welding	40h	17-Feb-14	20-Feb-14
CZA-TK-0511-1620	Inspection	50h	16-Feb-14	20-Feb-14
CZA-14.3.2.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		80h	22-Feb-14	02-Mar-14
CZA-TK-0511-1630	Cutting, Installation and Fit-up	20h	22-Feb-14	23-Feb-14
CZA-TK-0511-1640	Welding	60h	24-Feb-14	02-Mar-14
CZA-TK-0511-1650	Inspection	80h	22-Feb-14	02-Mar-14
CZA-14.3.2.7.7 Shell No.3		50h	03-Mar-14	08-Mar-14

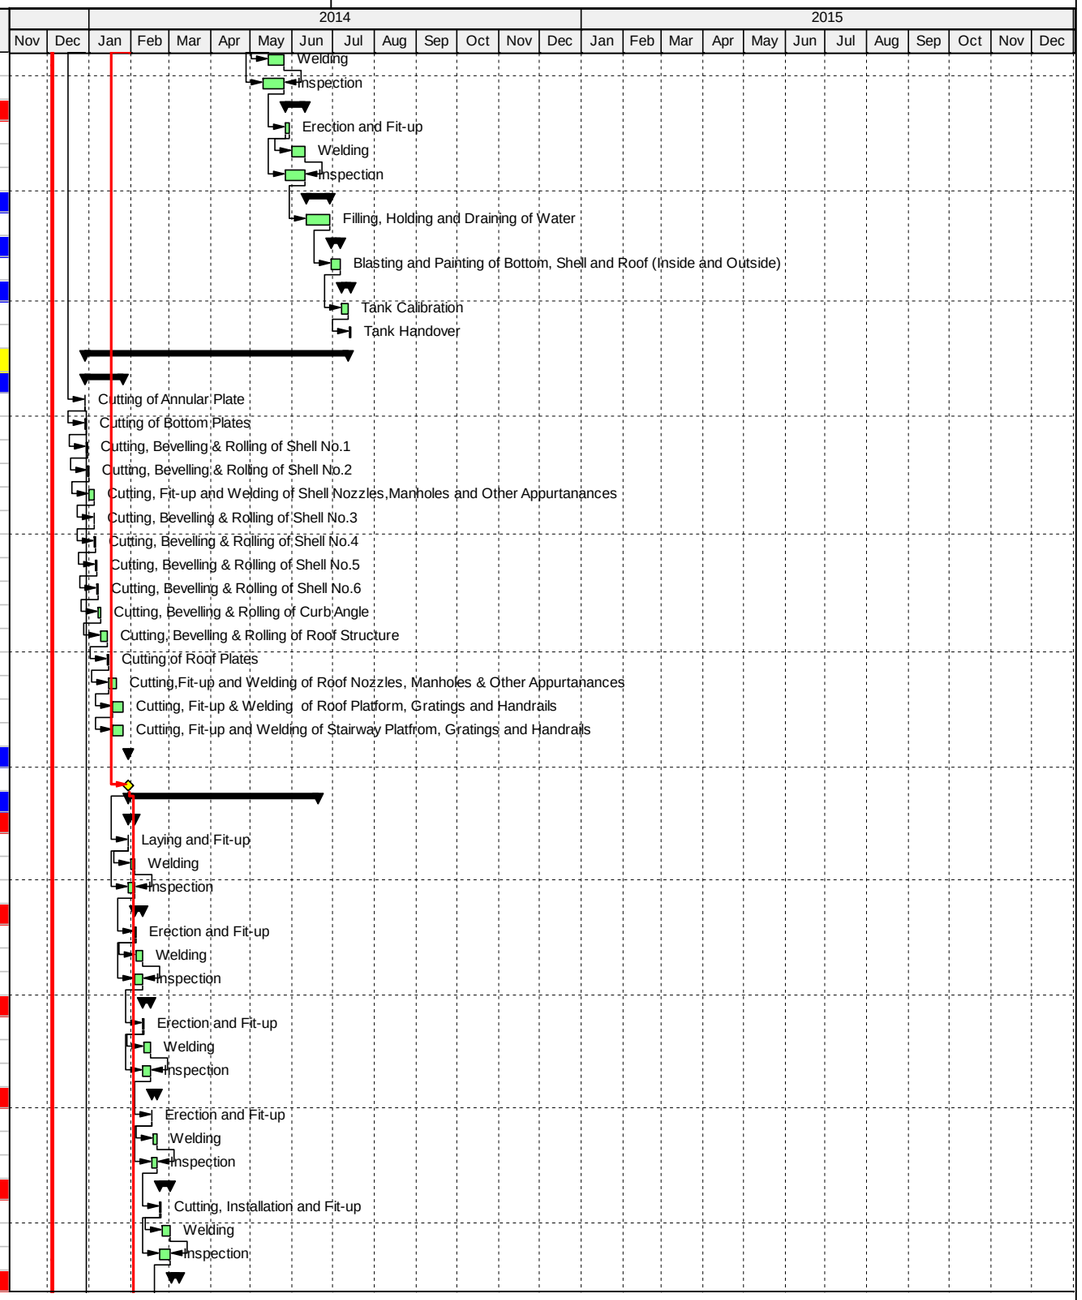

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0511-1660	Erection and Fit-up	10h	03-Mar-14	03-Mar-14
CZA-TK-0511-1670	Welding	40h	04-Mar-14	08-Mar-14
CZA-TK-0511-1680	Inspection	50h	03-Mar-14	08-Mar-14
CZA-14.3.2.7.8 Shell No.4		**50h**	**09-Mar-14**	**13-Mar-14**
CZA-TK-0511-1690	Erection and Fit-up	10h	09-Mar-14	09-Mar-14
CZA-TK-0511-1700	Welding	40h	10-Mar-14	13-Mar-14
CZA-TK-0511-1710	Inspection	50h	09-Mar-14	13-Mar-14
CZA-14.3.2.7.9 Shell No.5		**50h**	**15-Mar-14**	**19-Mar-14**
CZA-TK-0511-1720	Erection and Fit-up	10h	15-Mar-14	15-Mar-14
CZA-TK-0511-1730	Welding	40h	16-Mar-14	19-Mar-14
CZA-TK-0511-1740	Inspection	50h	15-Mar-14	19-Mar-14
CZA-14.3.2.7.10 Shell No.6		**50h**	**20-Mar-14**	**25-Mar-14**
CZA-TK-0511-1750	Erection and Fit-up	10h	20-Mar-14	20-Mar-14
CZA-TK-0511-1760	Welding	40h	22-Mar-14	25-Mar-14
CZA-TK-0511-1770	Inspection	50h	20-Mar-14	25-Mar-14
CZA-14.3.2.7.12 Shell Nozzles and attachements (Upper)		**70h**	**26-Mar-14**	**02-Apr-14**
CZA-TK-0511-1780	Cutting, Installation and Fit-up	20h	26-Mar-14	27-Mar-14
CZA-TK-0511-1790	Welding	50h	29-Mar-14	02-Apr-14
CZA-TK-0511-1800	Inspection	70h	26-Mar-14	02-Apr-14
CZA-14.3.2.7.13 Curb Angle		**30h**	**03-Apr-14**	**06-Apr-14**
CZA-TK-0511-1810	Erection and Fit-up	10h	03-Apr-14	03-Apr-14
CZA-TK-0511-1820	Welding	20h	05-Apr-14	06-Apr-14
CZA-TK-0511-1830	Inspection	30h	03-Apr-14	06-Apr-14
CZA-14.3.2.7.14 Roof Structure		**90h**	**07-Apr-14**	**16-Apr-14**
CZA-TK-0511-1840	Laying and Fit-up	20h	07-Apr-14	08-Apr-14
CZA-TK-0511-1850	Welding	70h	09-Apr-14	16-Apr-14
CZA-TK-0511-1860	Inspection	90h	07-Apr-14	16-Apr-14
CZA-14.3.2.7.15 Roof Plates		**70h**	**17-Apr-14**	**24-Apr-14**
CZA-TK-0511-1870	Laying and Fit-up	20h	17-Apr-14	19-Apr-14
CZA-TK-0511-1880	Welding	50h	20-Apr-14	24-Apr-14
CZA-TK-0511-1890	Inspection	70h	17-Apr-14	24-Apr-14
CZA-14.3.2.7.16 Roof Nozzles, Manholes and Other Appurtanances		**160h**	**26-Apr-14**	**13-May-14**
CZA-TK-0511-1900	Installation and Fit-up	40h	26-Apr-14	29-Apr-14
CZA-TK-0511-1910	Welding	120h	30-Apr-14	13-May-14
CZA-TK-0511-1920	Inspection	160h	26-Apr-14	13-May-14
CZA-14.3.2.7.18 Stairway Platform, Handrails and Gratings		**160h**	**14-May-14**	**01-Jun-14**
CZA-TK-0511-1930	Erection and Fit-up	40h	14-May-14	18-May-14
CZA-TK-0511-1940	Welding	120h	19-May-14	01-Jun-14
CZA-TK-0511-1950	Inspection	160h	14-May-14	01-Jun-14
CZA-14.3.2.7.17 Roof Platform, Handrails and Gratings		**160h**	**02-Jun-14**	**19-Jun-14**
CZA-TK-0511-1960	Erection and Fit-up	40h	02-Jun-14	05-Jun-14
CZA-TK-0511-1970	Welding	120h	07-Jun-14	19-Jun-14
CZA-TK-0511-1980	Inspection	160h	02-Jun-14	19-Jun-14
CZA-14.3.2.4 Hydotest		**80h**	**21-Jun-14**	**29-Jun-14**
CZA-TK-0511-1990	Filling, Holding and Draining of Water	80h	21-Jun-14	29-Jun-14
CZA-14.3.2.5 Blasting and Painting		**40h**	**30-Jun-14**	**03-Jul-14**
CZA-TK-0511-2000	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	40h	30-Jun-14	03-Jul-14
CZA-14.3.2.6 Tank Calibration and Handover		**70h**	**05-Jul-14**	**12-Jul-14**
CZA-TK-0511-2010	Tank Calibration	50h	05-Jul-14	09-Jul-14
CZA-TK-0511-2020	Tank Handover	20h	10-Jul-14	12-Jul-14
CZA-14.3.7 S210-TK-0600(P-Xylene Product Tank Dia 45.76m x Ht 20.55m with IFR)		**3142h**	**12-Jan-14**	**13-Jan-15**
CZA-14.3.7.1 Fabrication Works		**488h**	**12-Jan-14**	**09-Mar-14**
CZA-TK-0600-1000	Cutting of Annular Plates	40h	12-Jan-14	15-Jan-14
CZA-TK-0600-1010	Cutting of Bottom Plates	40h	12-Jan-14	15-Jan-14

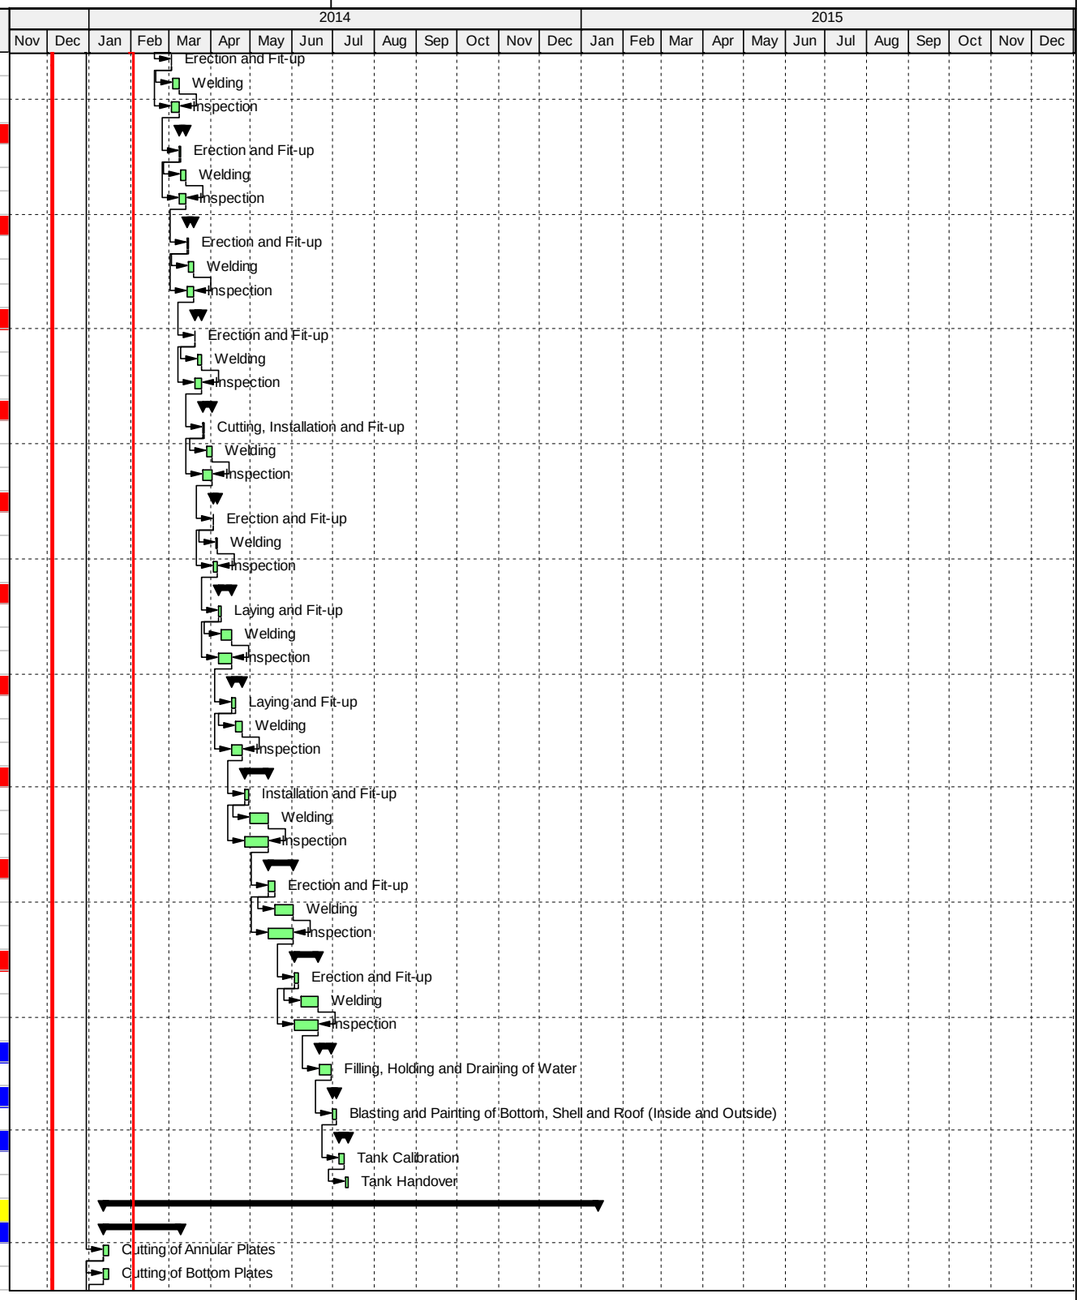

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0600-1020	Cutting,Bevelling & Rolling Shell No.8	16h	13-Jan-14	15-Jan-14
CZA-TK-0600-1030	Cutting,Bevelling & Rolling Shell No.9	16h	14-Jan-14	15-Jan-14
CZA-TK-0600-1040	Cutting of Floating Deck	56h	16-Jan-14	22-Jan-14
CZA-TK-0600-1050	Cutting of Pontoon	112h	16-Jan-14	29-Jan-14
CZA-TK-0600-1060	Cutting of Floating Legs and Manhole	56h	30-Jan-14	05-Feb-14
CZA-TK-0600-1070	Cutting, Fit-up and Welding of Roof Structure	56h	05-Feb-14	12-Feb-14
CZA-TK-0600-1080	Cutting of Compression Ring & Stairways	80h	08-Feb-14	17-Feb-14
CZA-TK-0600-1090	Cutting of Roof Plates	32h	08-Feb-14	11-Feb-14
CZA-TK-0600-1100	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	48h	10-Feb-14	16-Feb-14
CZA-TK-0600-1110	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	112h	10-Feb-14	23-Feb-14
CZA-TK-0600-1120	Cutting, Bevelling & Rolling of Shell No.7	16h	23-Feb-14	25-Feb-14
CZA-TK-0600-1130	Cutting, Bevelling & Rolling of Shell No.6	16h	23-Feb-14	25-Feb-14
CZA-TK-0600-1140	Cutting, Bevelling & Rolling of Shell No.5	16h	25-Feb-14	26-Feb-14
CZA-TK-0600-1150	Cutting, Bevelling & Rolling of Shell No.4	16h	27-Feb-14	01-Mar-14
CZA-TK-0600-1160	Cutting, Bevelling & Rolling of Shell No.3	16h	27-Feb-14	01-Mar-14
CZA-TK-0600-1170	Cutting, Bevelling & Rolling of Shell No.2	16h	01-Mar-14	03-Mar-14
CZA-TK-0600-1180	Cutting, Bevelling & Rolling of Shell No.1	16h	03-Mar-14	04-Mar-14
CZA-TK-0600-1190	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtances	56h	03-Mar-14	09-Mar-14
CZA-TK-0600-1200	Cutting, Fit-up & Welding of Stairway Platform, Gratings and Handrails	48h	03-Mar-14	08-Mar-14
CZA-14.3.7.2 FoundationTakeover		**0h**	**15-Feb-14**	**15-Feb-14**
CZA-TK-0600-1210	Foundation Takeover From Client	0h	15-Feb-14	
CZA-14.3.7.7 Mechanical Erection		**2016h**	**15-Feb-14**	**08-Oct-14**
CZA-14.3.7.7.1 Annular Plates		**50h**	**15-Feb-14**	**20-Feb-14**
CZA-TK-0600-1220	Laying and Fit-up	20h	15-Feb-14	17-Feb-14
CZA-TK-0600-1230	Welding	30h	17-Feb-14	20-Feb-14
CZA-TK-0600-1240	Inspection	50h	15-Feb-14	20-Feb-14
CZA-14.3.7.7.2 Bottom Plates		**190h**	**20-Feb-14**	**15-Mar-14**
CZA-TK-0600-1250	Laying and Fit-up	40h	20-Feb-14	25-Feb-14
CZA-TK-0600-1260	Welding	150h	25-Feb-14	15-Mar-14
CZA-TK-0600-1270	Inspection	160h	24-Feb-14	15-Mar-14
CZA-14.3.7.7.3 Shell No.8		**80h**	**15-Mar-14**	**24-Mar-14**
CZA-TK-0600-1280	Erection and Fit-up	20h	15-Mar-14	17-Mar-14
CZA-TK-0600-1290	Welding	60h	17-Mar-14	24-Mar-14
CZA-TK-0600-1300	Inspection	80h	15-Mar-14	24-Mar-14
CZA-14.3.7.7.4 Shell No.9		**80h**	**24-Mar-14**	**02-Apr-14**
CZA-TK-0600-1310	Erection and Fit-up	20h	24-Mar-14	26-Mar-14
CZA-TK-0600-1320	Welding	60h	26-Mar-14	02-Apr-14
CZA-TK-0600-1330	Inspection	80h	24-Mar-14	02-Apr-14
CZA-14.3.7.7.5 Shell Nozzles and Other Attachments		**70h**	**02-Apr-14**	**10-Apr-14**
CZA-TK-0600-1340	Cutting, Installation and Fit-up	20h	02-Apr-14	05-Apr-14
CZA-TK-0600-1350	Welding	50h	05-Apr-14	10-Apr-14
CZA-TK-0600-1360	Inspection	70h	02-Apr-14	10-Apr-14
CZA-14.3.7.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**40h**	**07-Apr-14**	**12-Apr-14**
CZA-TK-0600-1370	Erection and Fit-up	20h	07-Apr-14	09-Apr-14
CZA-TK-0600-1380	Welding	20h	09-Apr-14	12-Apr-14
CZA-TK-0600-1390	Inspection	40h	07-Apr-14	12-Apr-14
CZA-14.3.7.7.7 Deck Plate		**140h**	**12-Apr-14**	**28-Apr-14**
CZA-TK-0600-1400	Laying and Fit-up	40h	12-Apr-14	16-Apr-14
CZA-TK-0600-1410	Welding	100h	16-Apr-14	28-Apr-14
CZA-TK-0600-1420	Inspection	140h	12-Apr-14	28-Apr-14
CZA-14.3.7.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**150h**	**28-Apr-14**	**15-May-14**
CZA-TK-0600-1430	Laying, Cutting all Holes and Fit-up	40h	28-Apr-14	03-May-14
CZA-TK-0600-1440	Welding	110h	28-Apr-14	11-May-14
CZA-TK-0600-1450	Inspection	150h	28-Apr-14	15-May-14

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.7.7.9 Roof Structure		**140h**	**15-May-14**	**01-Jun-14**
CZA-TK-0600-1460	Erection and Fit-up	50h	15-May-14	21-May-14
CZA-TK-0600-1470	Welding	90h	21-May-14	01-Jun-14
CZA-TK-0600-1480	Inspection	140h	15-May-14	01-Jun-14
CZA-14.3.7.7.10 Roof Plates		**80h**	**01-Jun-14**	**10-Jun-14**
CZA-TK-0600-1490	Laying and Fit-up	20h	01-Jun-14	03-Jun-14
CZA-TK-0600-1500	Welding	60h	03-Jun-14	10-Jun-14
CZA-TK-0600-1510	Inspection	80h	01-Jun-14	10-Jun-14
CZA-14.3.7.7.11 Compression Ring		**100h**	**10-Jun-14**	**22-Jun-14**
CZA-TK-0600-1520	Laying and Fit-up	30h	10-Jun-14	14-Jun-14
CZA-TK-0600-1530	Welding	70h	14-Jun-14	22-Jun-14
CZA-TK-0600-1540	Inspection	100h	10-Jun-14	22-Jun-14
CZA-14.3.7.7.12 Roof Nozzles, Manholes and Other Appurtanances		**80h**	**22-Jun-14**	**01-Jul-14**
CZA-TK-0600-1550	Cutting,Installation and Fit-up	20h	22-Jun-14	24-Jun-14
CZA-TK-0600-1560	Welding	60h	24-Jun-14	01-Jul-14
CZA-TK-0600-1570	Inspection	80h	22-Jun-14	01-Jul-14
CZA-14.3.7.7.13 Roof Platform, Gratings and Handrails		**100h**	**01-Jul-14**	**13-Jul-14**
CZA-TK-0600-1580	Erection and Fit-up	30h	01-Jul-14	05-Jul-14
CZA-TK-0600-1590	Welding	70h	05-Jul-14	13-Jul-14
CZA-TK-0600-1600	Inspection	100h	01-Jul-14	13-Jul-14
CZA-14.3.7.7.14 Shell No.7		**80h**	**13-Jul-14**	**22-Jul-14**
CZA-TK-0600-1610	Jacking, Erection and Fit-up	20h	13-Jul-14	15-Jul-14
CZA-TK-0600-1620	Welding	60h	15-Jul-14	22-Jul-14
CZA-TK-0600-1630	Inspection	80h	13-Jul-14	22-Jul-14
CZA-14.3.7.7.15 Shell No.6		**80h**	**22-Jul-14**	**31-Jul-14**
CZA-TK-0600-1640	Jacking,Erection and Fit-up	20h	22-Jul-14	24-Jul-14
CZA-TK-0600-1650	Welding	60h	24-Jul-14	31-Jul-14
CZA-TK-0600-1660	Inspection	80h	22-Jul-14	31-Jul-14
CZA-14.3.7.7.16 Shell No.5		**80h**	**31-Jul-14**	**10-Aug-14**
CZA-TK-0600-1670	Jacking,Erection and Fit-up	20h	31-Jul-14	03-Aug-14
CZA-TK-0600-1680	Welding	60h	03-Aug-14	10-Aug-14
CZA-TK-0600-1690	Inspection	80h	31-Jul-14	10-Aug-14
CZA-14.3.7.7.17 Shell No.4		**80h**	**10-Aug-14**	**19-Aug-14**
CZA-TK-0600-1700	Jacking, Erection and Fit-up	20h	10-Aug-14	12-Aug-14
CZA-TK-0600-1710	Welding	60h	12-Aug-14	19-Aug-14
CZA-TK-0600-1720	Inspection	80h	10-Aug-14	19-Aug-14
CZA-14.3.7.7.18 Shell No.3		**80h**	**19-Aug-14**	**28-Aug-14**
CZA-TK-0600-1730	Jacking, Erection and Fit-up	20h	19-Aug-14	21-Aug-14
CZA-TK-0600-1740	Welding	60h	21-Aug-14	28-Aug-14
CZA-TK-0600-1750	Inspection	80h	19-Aug-14	28-Aug-14
CZA-14.3.7.7.19 Shell No.2		**80h**	**28-Aug-14**	**07-Sep-14**
CZA-TK-0600-1760	Jacking, Erection and Fit-up	20h	28-Aug-14	31-Aug-14
CZA-TK-0600-1770	Welding	60h	31-Aug-14	07-Sep-14
CZA-TK-0600-1780	Inspection	80h	28-Aug-14	07-Sep-14
CZA-14.3.7.7.20 Shell No.1		**80h**	**07-Sep-14**	**16-Sep-14**
CZA-TK-0600-1790	Jacking, Erection and Fit-up	20h	07-Sep-14	09-Sep-14
CZA-TK-0600-1800	Welding	60h	09-Sep-14	16-Sep-14
CZA-TK-0600-1810	Inspection	80h	07-Sep-14	16-Sep-14
CZA-14.3.7.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**70h**	**16-Sep-14**	**24-Sep-14**
CZA-TK-0600-1820	Lay-out, Cutting, and Fit-up	20h	16-Sep-14	18-Sep-14
CZA-TK-0600-1830	Welding	50h	18-Sep-14	24-Sep-14
CZA-TK-0600-1840	Inspection	70h	16-Sep-14	24-Sep-14
CZA-14.3.7.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		**100h**	**18-Sep-14**	**30-Sep-14**
CZA-TK-0600-1850	Erection and Fit-up	30h	18-Sep-14	22-Sep-14

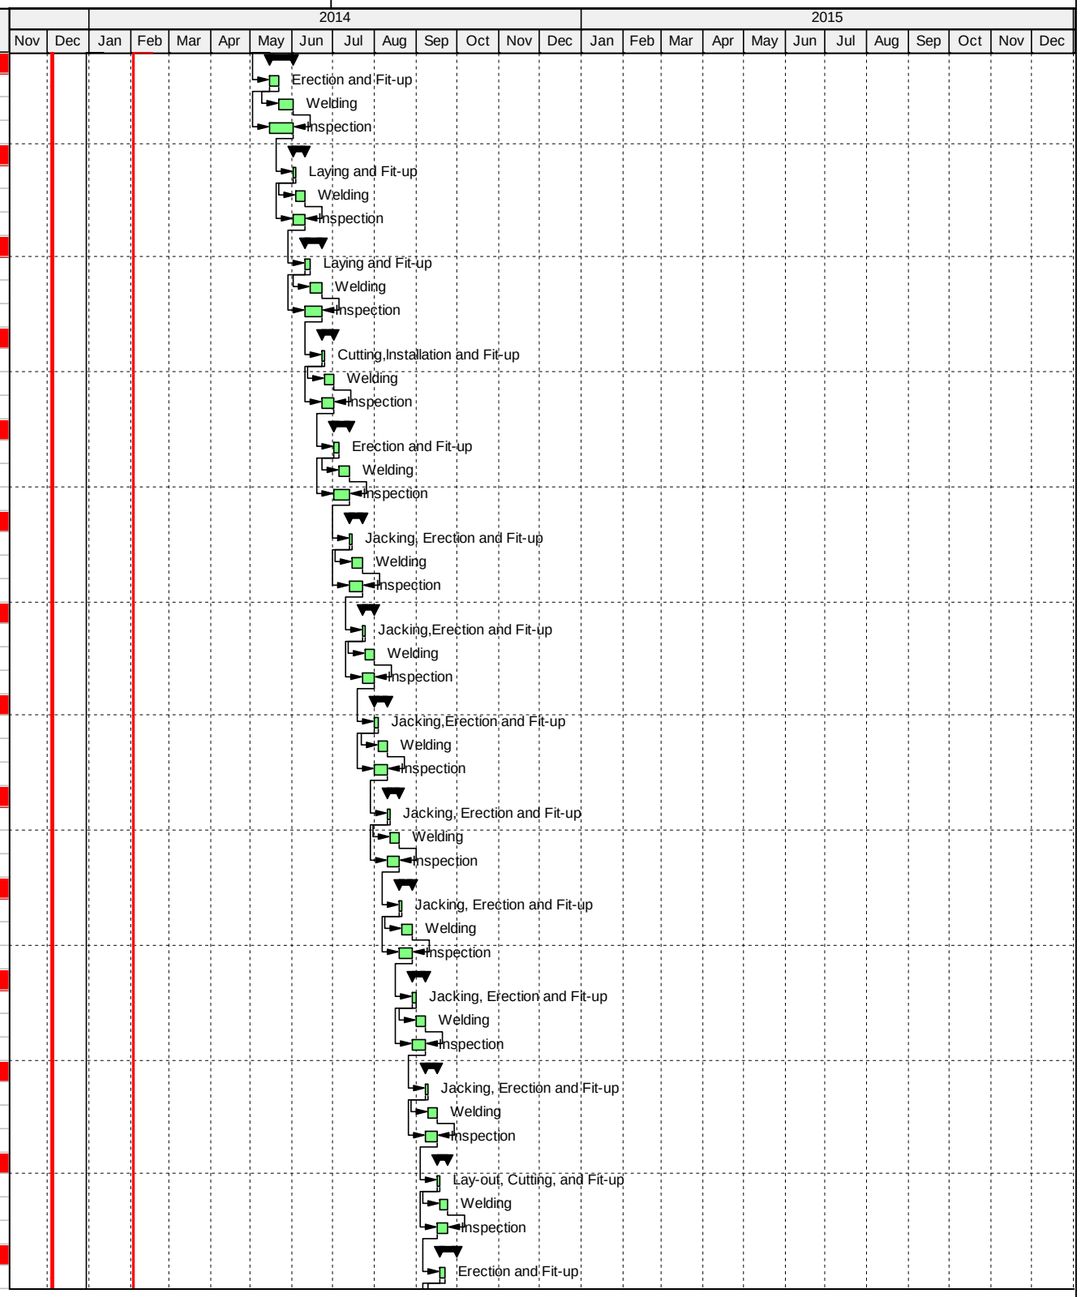

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0600-1860	Welding	70h	22-Sep-14	30-Sep-14
CZA-TK-0600-1870	Inspection	100h	18-Sep-14	30-Sep-14
CZA-14.3.7.7.24 Primary and Secondary Seal		**70h**	**30-Sep-14**	**08-Oct-14**
CZA-TK-0600-1880	Installation of Primary and Secondary Seal	60h	30-Sep-14	07-Oct-14
CZA-TK-0600-1890	Inspection	10h	07-Oct-14	08-Oct-14
CZA-14.3.7.4 Hydrotest		**510h**	**08-Oct-14**	**07-Dec-14**
CZA-TK-0600-1900	Filling, Holding and Draining	510h	08-Oct-14	07-Dec-14
CZA-14.3.7.5 Blasting and Painting		**250h**	**07-Dec-14**	**05-Jan-15**
CZA-TK-0600-1910	Blasting & Painting (Bottom, Shell & Roof) Inside and Outside	250h	07-Dec-14	05-Jan-15
CZA-14.3.7.6 Tank Calibration and Handover		**70h**	**05-Jan-15**	**13-Jan-15**
CZA-TK-0600-1920	Tank Calibration	50h	05-Jan-15	11-Jan-15
CZA-TK-0600-1930	Tank Handover	20h	11-Jan-15	13-Jan-15
CZA-14.3.3 S210-TK-0601(P-Xylene Product Tank Dia 45.76m x Ht 20.55m with IFR)		**3262h**	**12-Jan-14**	**27-Jan-15**
CZA-14.3.3.1 Fabrication Works		**488h**	**12-Jan-14**	**09-Mar-14**
CZA-TK-0601-1460	Cutting of Annular Plates	40h	12-Jan-14	15-Jan-14
CZA-TK-0601-1470	Cutting of Bottom Plates	40h	12-Jan-14	15-Jan-14
CZA-TK-0601-1480	Cutting,Bevelling & Rolling Shell No.8	16h	13-Jan-14	15-Jan-14
CZA-TK-0601-1490	Cutting,Bevelling & Rolling Shell No.9	16h	14-Jan-14	15-Jan-14
CZA-TK-0601-1500	Cutting of Floating Deck	56h	16-Jan-14	22-Jan-14
CZA-TK-0601-1510	Cutting of Pontoon	112h	16-Jan-14	29-Jan-14
CZA-TK-0601-1520	Cutting of Floating Legs and Manhole	56h	30-Jan-14	05-Feb-14
CZA-TK-0601-1530	Cutting, Fit-up and Welding of Roof Structure	56h	05-Feb-14	12-Feb-14
CZA-TK-0601-1540	Cutting of Compression Ring & Stairways	16h	08-Feb-14	09-Feb-14
CZA-TK-0601-1550	Cutting of Roof Plates	32h	08-Feb-14	11-Feb-14
CZA-TK-0601-1560	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	48h	10-Feb-14	16-Feb-14
CZA-TK-0601-1570	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	112h	10-Feb-14	23-Feb-14
CZA-TK-0601-1580	Cutting, Bevelling & Rolling of Shell No.7	16h	23-Feb-14	25-Feb-14
CZA-TK-0601-1590	Cutting, Bevelling & Rolling of Shell No.6	16h	23-Feb-14	25-Feb-14
CZA-TK-0601-1600	Cutting, Bevelling & Rolling of Shell No.5	16h	25-Feb-14	26-Feb-14
CZA-TK-0601-1610	Cutting, Bevelling & Rolling of Shell No.4	16h	27-Feb-14	01-Mar-14
CZA-TK-0601-1620	Cutting, Bevelling & Rolling of Shell No.3	16h	27-Feb-14	01-Mar-14
CZA-TK-0601-1630	Cutting, Bevelling & Rolling of Shell No.2	16h	01-Mar-14	03-Mar-14
CZA-TK-0601-1640	Cutting, Bevelling & Rolling of Shell No.1	16h	03-Mar-14	04-Mar-14
CZA-TK-0601-1650	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtances	56h	03-Mar-14	09-Mar-14
CZA-TK-0601-1660	Cutting, Fit-up & Welding of Stairway Platform, Gratings and Handrails	48h	03-Mar-14	08-Mar-14
CZA-14.3.3.2 FoundationTakeover		**0h**	**15-Feb-14**	**15-Feb-14**
CZA-TK-0601-1670	Foundation Takeover From Client	0h	15-Feb-14	
CZA-14.3.3.7 Mechanical Erection		**1976h**	**15-Feb-14**	**04-Oct-14**
CZA-14.3.3.7.1 Annular Plates		**50h**	**15-Feb-14**	**20-Feb-14**
CZA-TK-0601-1680	Laying and Fit-up	20h	15-Feb-14	17-Feb-14
CZA-TK-0601-1690	Welding	30h	17-Feb-14	20-Feb-14
CZA-TK-0601-1700	Inspection	50h	15-Feb-14	20-Feb-14
CZA-14.3.3.7.2 Bottom Plates		**160h**	**20-Feb-14**	**11-Mar-14**
CZA-TK-0601-1710	Laying and Fit-up	40h	20-Feb-14	25-Feb-14
CZA-TK-0601-1720	Welding	120h	25-Feb-14	11-Mar-14
CZA-TK-0601-1730	Inspection	160h	20-Feb-14	11-Mar-14
CZA-14.3.3.7.3 Shell No.8		**80h**	**11-Mar-14**	**20-Mar-14**
CZA-TK-0601-1740	Erection and Fit-up	20h	11-Mar-14	13-Mar-14
CZA-TK-0601-1750	Welding	60h	13-Mar-14	20-Mar-14
CZA-TK-0601-1760	Inspection	80h	11-Mar-14	20-Mar-14
CZA-14.3.3.7.4 Shell No.9		**80h**	**20-Mar-14**	**30-Mar-14**
CZA-TK-0601-1770	Erection and Fit-up	20h	20-Mar-14	23-Mar-14
CZA-TK-0601-1780	Welding	60h	23-Mar-14	30-Mar-14
CZA-TK-0601-1790	Inspection	80h	20-Mar-14	30-Mar-14

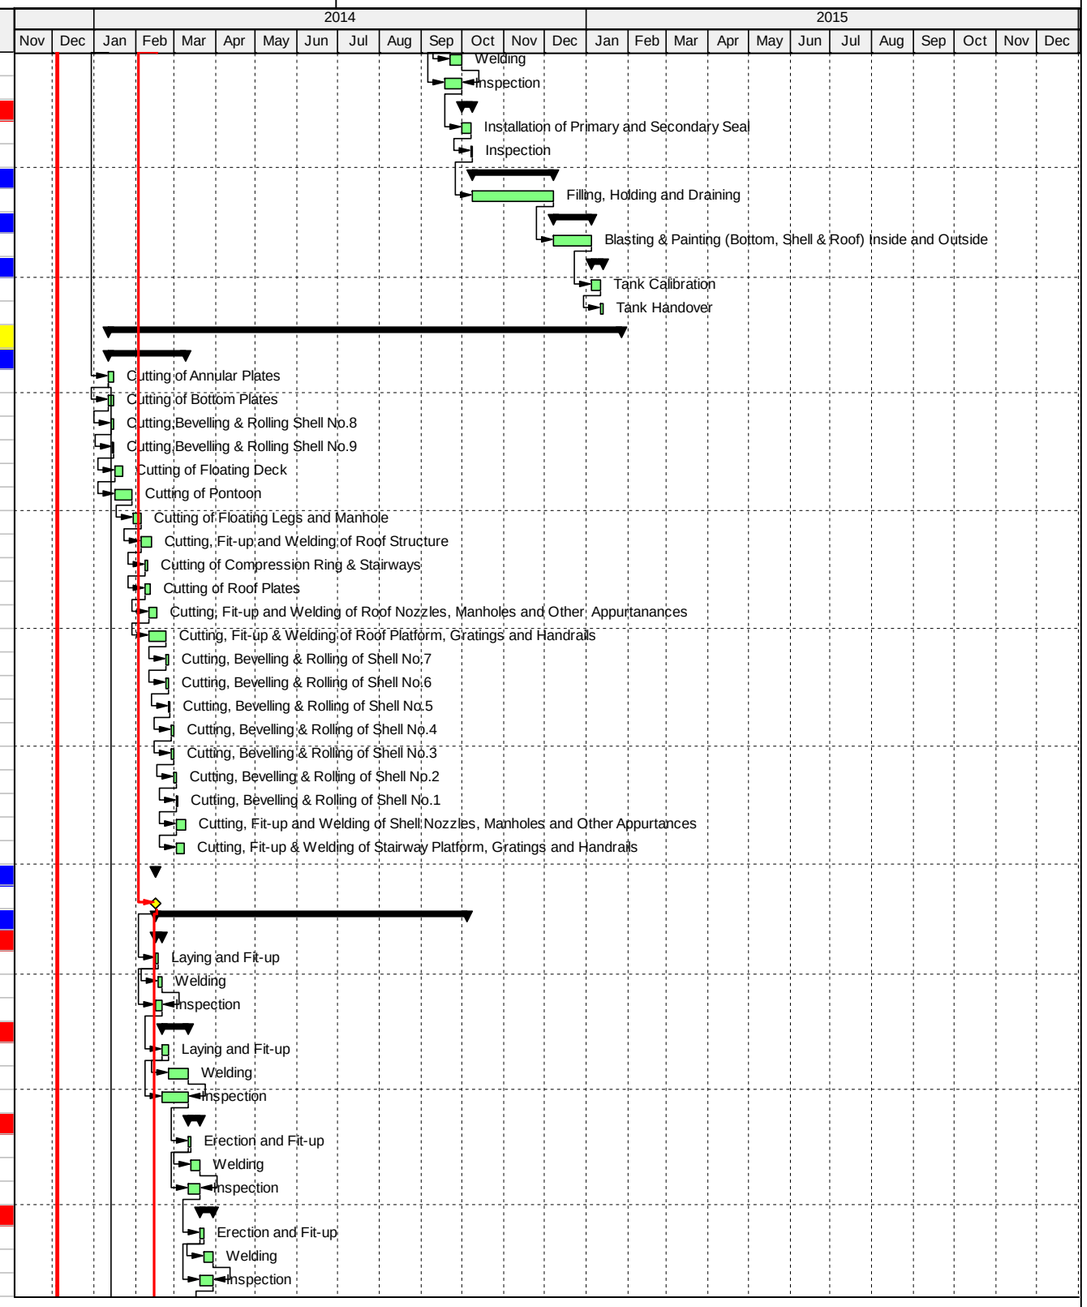

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.3.7.5 Shell Nozzles and Other Attachments		**70h**	**30-Mar-14**	**07-Apr-14**
CZA-TK-0601-1800	Cutting, Installation and Fit-up	20h	30-Mar-14	01-Apr-14
CZA-TK-0601-1810	Welding	50h	01-Apr-14	07-Apr-14
CZA-TK-0601-1820	Inspection	70h	30-Mar-14	07-Apr-14
CZA-14.3.3.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**40h**	**03-Apr-14**	**08-Apr-14**
CZA-TK-0601-1830	Erection and Fit-up	20h	03-Apr-14	06-Apr-14
CZA-TK-0601-1840	Welding	20h	06-Apr-14	08-Apr-14
CZA-TK-0601-1850	Inspection	40h	03-Apr-14	08-Apr-14
CZA-14.3.3.7.7 Deck Plate		**140h**	**08-Apr-14**	**24-Apr-14**
CZA-TK-0601-1860	Laying and Fit-up	40h	08-Apr-14	13-Apr-14
CZA-TK-0601-1870	Welding	100h	13-Apr-14	24-Apr-14
CZA-TK-0601-1880	Inspection	140h	08-Apr-14	24-Apr-14
CZA-14.3.3.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**150h**	**24-Apr-14**	**12-May-14**
CZA-TK-0601-1890	Laying, Cutting all Holes and Fit-up	40h	24-Apr-14	29-Apr-14
CZA-TK-0601-1900	Welding	110h	24-Apr-14	07-May-14
CZA-TK-0601-1910	Inspection	150h	24-Apr-14	12-May-14
CZA-14.3.3.7.9 Roof Structure		**140h**	**12-May-14**	**28-May-14**
CZA-TK-0601-1920	Erection and Fit-up	50h	12-May-14	18-May-14
CZA-TK-0601-1930	Welding	90h	18-May-14	28-May-14
CZA-TK-0601-1940	Inspection	140h	12-May-14	28-May-14
CZA-14.3.3.7.10 Roof Plates		**80h**	**28-May-14**	**07-Jun-14**
CZA-TK-0601-1950	Laying and Fit-up	20h	28-May-14	31-May-14
CZA-TK-0601-1960	Welding	60h	31-May-14	07-Jun-14
CZA-TK-0601-1970	Inspection	80h	28-May-14	07-Jun-14
CZA-14.3.3.7.11 Compression Ring		**100h**	**07-Jun-14**	**18-Jun-14**
CZA-TK-0601-1980	Laying and Fit-up	30h	07-Jun-14	10-Jun-14
CZA-TK-0601-1990	Welding	70h	10-Jun-14	18-Jun-14
CZA-TK-0601-2000	Inspection	100h	07-Jun-14	18-Jun-14
CZA-14.3.3.7.12 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**18-Jun-14**	**26-Jun-14**
CZA-TK-0601-2010	Cutting,Installation and Fit-up	20h	18-Jun-14	21-Jun-14
CZA-TK-0601-2020	Welding	50h	21-Jun-14	26-Jun-14
CZA-TK-0601-2030	Inspection	70h	18-Jun-14	26-Jun-14
CZA-14.3.3.7.13 Roof Platform, Gratings and Handrails		**100h**	**26-Jun-14**	**08-Jul-14**
CZA-TK-0601-2040	Erection and Fit-up	30h	26-Jun-14	30-Jun-14
CZA-TK-0601-2050	Welding	70h	30-Jun-14	08-Jul-14
CZA-TK-0601-2060	Inspection	100h	26-Jun-14	08-Jul-14
CZA-14.3.3.7.14 Shell No.7		**80h**	**08-Jul-14**	**17-Jul-14**
CZA-TK-0601-2070	Jacking, Erection and Fit-up	20h	08-Jul-14	10-Jul-14
CZA-TK-0601-2080	Welding	60h	10-Jul-14	17-Jul-14
CZA-TK-0601-2090	Inspection	80h	08-Jul-14	17-Jul-14
CZA-14.3.3.7.15 Shell No.6		**80h**	**17-Jul-14**	**27-Jul-14**
CZA-TK-0601-2100	Jacking,Erection and Fit-up	20h	17-Jul-14	20-Jul-14
CZA-TK-0601-2110	Welding	60h	20-Jul-14	27-Jul-14
CZA-TK-0601-2120	Inspection	80h	17-Jul-14	27-Jul-14
CZA-14.3.3.7.16 Shell No.5		**80h**	**27-Jul-14**	**05-Aug-14**
CZA-TK-0601-2130	Jacking,Erection and Fit-up	20h	27-Jul-14	29-Jul-14
CZA-TK-0601-2140	Welding	60h	29-Jul-14	05-Aug-14
CZA-TK-0601-2150	Inspection	80h	27-Jul-14	05-Aug-14
CZA-14.3.3.7.17 Shell No.4		**80h**	**05-Aug-14**	**14-Aug-14**
CZA-TK-0601-2160	Jacking, Erection and Fit-up	20h	05-Aug-14	07-Aug-14
CZA-TK-0601-2170	Welding	60h	07-Aug-14	14-Aug-14
CZA-TK-0601-2180	Inspection	80h	05-Aug-14	14-Aug-14
CZA-14.3.3.7.18 Shell No.3		**80h**	**14-Aug-14**	**24-Aug-14**
CZA-TK-0601-2190	Jacking, Erection and Fit-up	20h	14-Aug-14	17-Aug-14

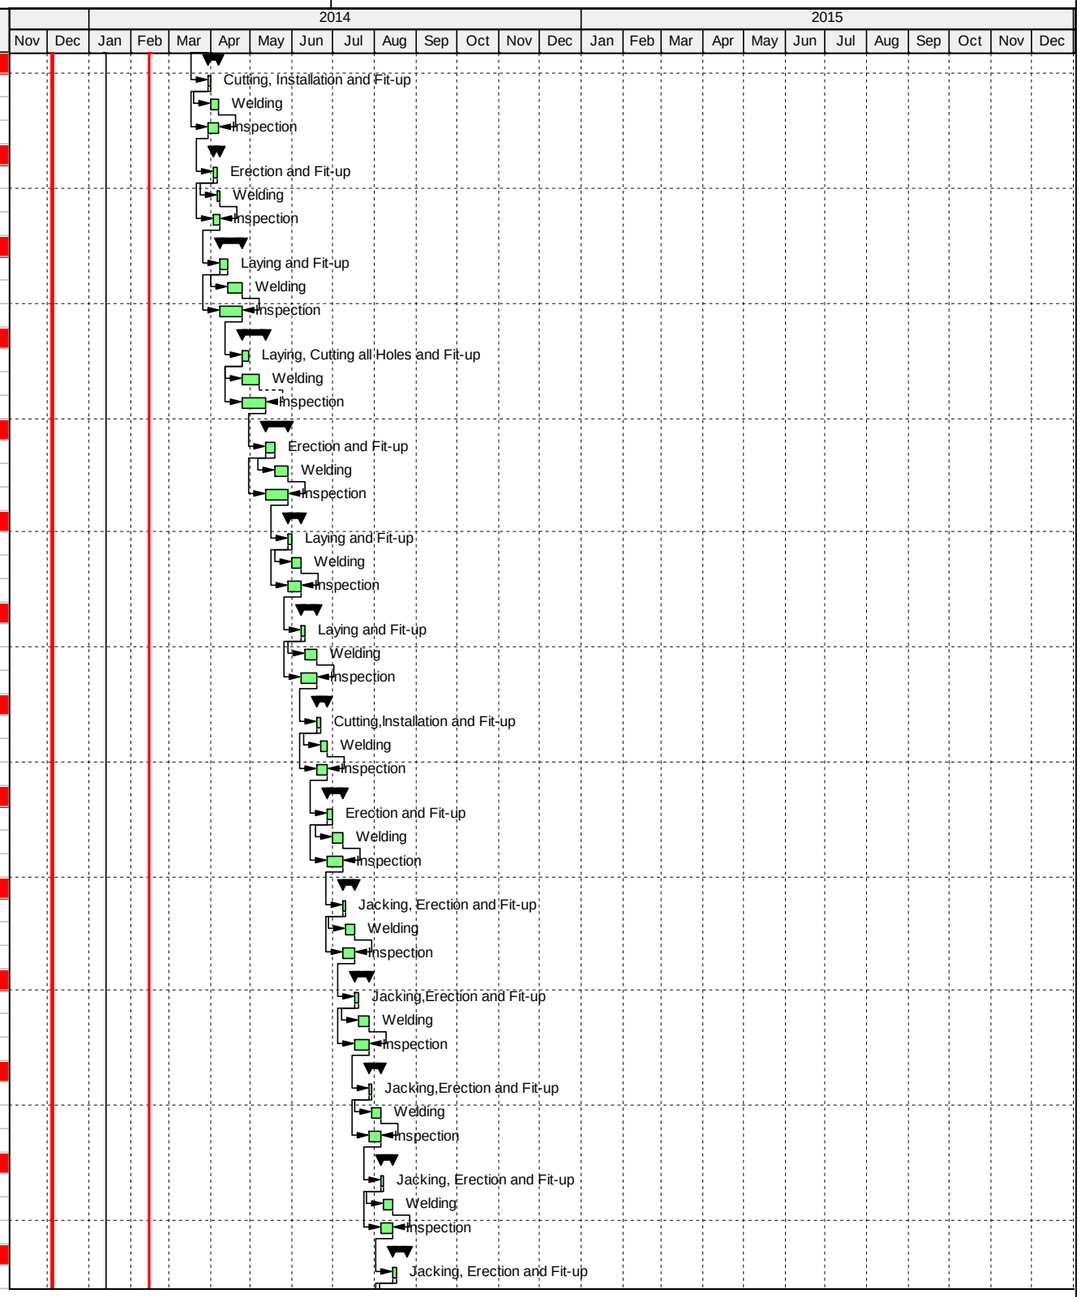

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0601-2200	Welding	60h	17-Aug-14	24-Aug-14
CZA-TK-0601-2210	Inspection	80h	14-Aug-14	24-Aug-14
CZA-14.3.3.7.19 Shell No.2		80h	24-Aug-14	02-Sep-14
CZA-TK-0601-2220	Jacking, Erection and Fit-up	20h	24-Aug-14	26-Aug-14
CZA-TK-0601-2230	Welding	60h	26-Aug-14	02-Sep-14
CZA-TK-0601-2240	Inspection	80h	24-Aug-14	02-Sep-14
CZA-14.3.3.7.20 Shell No.1		80h	02-Sep-14	11-Sep-14
CZA-TK-0601-2250	Jacking, Erection and Fit-up	20h	02-Sep-14	04-Sep-14
CZA-TK-0601-2260	Welding	60h	04-Sep-14	11-Sep-14
CZA-TK-0601-2270	Inspection	80h	02-Sep-14	11-Sep-14
CZA-14.3.3.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		80h	11-Sep-14	21-Sep-14
CZA-TK-0601-2280	Lay-out, Cutting, and Fit-up	20h	11-Sep-14	14-Sep-14
CZA-TK-0601-2290	Welding	60h	14-Sep-14	21-Sep-14
CZA-TK-0601-2300	Inspection	80h	11-Sep-14	21-Sep-14
CZA-14.3.3.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		100h	14-Sep-14	25-Sep-14
CZA-TK-0601-2310	Erection and Fit-up	30h	14-Sep-14	17-Sep-14
CZA-TK-0601-2320	Welding	70h	17-Sep-14	25-Sep-14
CZA-TK-0601-2330	Inspection	100h	14-Sep-14	25-Sep-14
CZA-14.3.3.7.24 Primary and Secondary Seal		70h	25-Sep-14	04-Oct-14
CZA-TK-0601-2340	Installation of Primary and Secondary Seal	60h	25-Sep-14	02-Oct-14
CZA-TK-0601-2350	Inspection	10h	02-Oct-14	04-Oct-14
CZA-14.3.3.4 Hydrotest		610h	04-Oct-14	14-Dec-14
CZA-TK-0601-2360	Filling, Holding and Draining	610h	04-Oct-14	14-Dec-14
CZA-14.3.3.5 Blasting and Painting		310h	14-Dec-14	19-Jan-15
CZA-TK-0601-2370	Blasting & Painting (Bottom, Shell & Roof) Inside and Outside	310h	14-Dec-14	19-Jan-15
CZA-14.3.3.6 Tank Calibration and Handover		70h	19-Jan-15	27-Jan-15
CZA-TK-0601-2380	Tank Calibration	50h	19-Jan-15	25-Jan-15
CZA-TK-0601-2390	Tank Handover	20h	25-Jan-15	27-Jan-15
CZA-14.3.4 S210-TK-0602(P-Xylene Product Tank Dia 45.76m x Ht 20.55m with IFR)		2864h	26-Jan-14	25-Dec-14
CZA-14.3.4.1 Fabrication Works		488h	26-Jan-14	23-Mar-14
CZA-TK-0602-1920	Cutting of Annular Plates	40h	26-Jan-14	29-Jan-14
CZA-TK-0602-1930	Cutting of Bottom Plates	40h	26-Jan-14	29-Jan-14
CZA-TK-0602-1940	Cutting,Bevelling & Rolling Shell No.8	16h	27-Jan-14	29-Jan-14
CZA-TK-0602-1950	Cutting,Bevelling & Rolling Shell No.9	16h	28-Jan-14	29-Jan-14
CZA-TK-0602-1960	Cutting of Floating Deck	56h	30-Jan-14	05-Feb-14
CZA-TK-0602-1970	Cutting of Pontoon	112h	30-Jan-14	12-Feb-14
CZA-TK-0602-1980	Cutting of Floating Legs and Manhole	56h	13-Feb-14	19-Feb-14
CZA-TK-0602-1990	Cutting, Fit-up and Welding of Roof Structure	56h	19-Feb-14	26-Feb-14
CZA-TK-0602-2000	Cutting of Compression Ring & Stairways	80h	22-Feb-14	03-Mar-14
CZA-TK-0602-2010	Cutting of Roof Plates	32h	22-Feb-14	25-Feb-14
CZA-TK-0602-2020	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	48h	24-Feb-14	02-Mar-14
CZA-TK-0602-2030	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	112h	24-Feb-14	09-Mar-14
CZA-TK-0602-2040	Cutting, Bevelling & Rolling of Shell No.7	16h	09-Mar-14	11-Mar-14
CZA-TK-0602-2050	Cutting, Bevelling & Rolling of Shell No.6	16h	09-Mar-14	11-Mar-14
CZA-TK-0602-2060	Cutting, Bevelling & Rolling of Shell No.5	16h	11-Mar-14	12-Mar-14
CZA-TK-0602-2070	Cutting, Bevelling & Rolling of Shell No.4	16h	13-Mar-14	15-Mar-14
CZA-TK-0602-2080	Cutting, Bevelling & Rolling of Shell No.3	16h	13-Mar-14	15-Mar-14
CZA-TK-0602-2090	Cutting, Bevelling & Rolling of Shell No.2	16h	15-Mar-14	17-Mar-14
CZA-TK-0602-2100	Cutting, Bevelling & Rolling of Shell No.1	16h	17-Mar-14	18-Mar-14
CZA-TK-0602-2110	Cutting, Fit-up and Welding of Shell Nozzles, Manholes and Other Appurtances	56h	17-Mar-14	23-Mar-14
CZA-TK-0602-2120	Cutting, Fit-up & Welding of Stairway Platform, Gratings and Handrails	48h	17-Mar-14	22-Mar-14
CZA-14.3.4.2 FoundationTakeover		0h	27-Feb-14	27-Feb-14
CZA-TK-0602-2130	Foundation Takeover From Client	0h	27-Feb-14	
CZA-14.3.4.7 Mechanical Erection		1906h	27-Feb-14	08-Oct-14

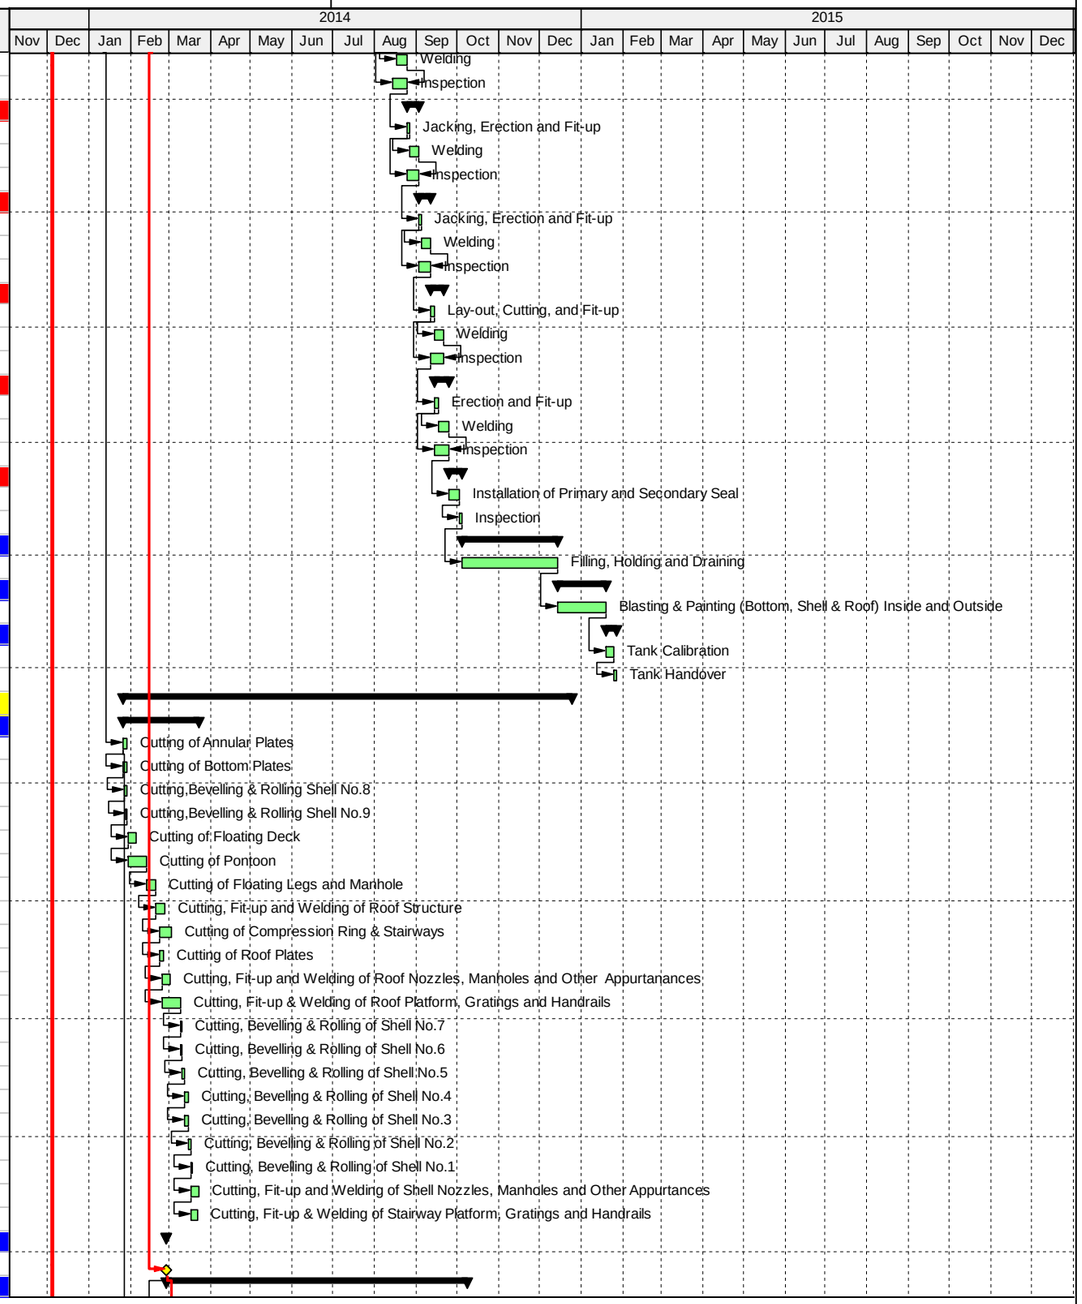

- Actual Level of Effort
- summary
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.4.7.1 Annular Plates		**50h**	**27-Feb-14**	**05-Mar-14**
CZA-TK-0602-2140	Laying and Fit-up	20h	27-Feb-14	02-Mar-14
CZA-TK-0602-2150	Welding	30h	02-Mar-14	05-Mar-14
CZA-TK-0602-2160	Inspection	50h	27-Feb-14	05-Mar-14
CZA-14.3.4.7.2 Bottom Plates		**180h**	**05-Mar-14**	**26-Mar-14**
CZA-TK-0602-2170	Laying and Fit-up	40h	05-Mar-14	10-Mar-14
CZA-TK-0602-2180	Welding	140h	10-Mar-14	26-Mar-14
CZA-TK-0602-2190	Inspection	180h	05-Mar-14	26-Mar-14
CZA-14.3.4.7.3 Shell No.8		**80h**	**26-Mar-14**	**05-Apr-14**
CZA-TK-0602-2200	Erection and Fit-up	20h	26-Mar-14	29-Mar-14
CZA-TK-0602-2210	Welding	60h	29-Mar-14	05-Apr-14
CZA-TK-0602-2220	Inspection	80h	26-Mar-14	05-Apr-14
CZA-14.3.4.7.4 Shell No.9		**80h**	**05-Apr-14**	**14-Apr-14**
CZA-TK-0602-2230	Erection and Fit-up	20h	05-Apr-14	07-Apr-14
CZA-TK-0602-2240	Welding	60h	07-Apr-14	14-Apr-14
CZA-TK-0602-2250	Inspection	80h	05-Apr-14	14-Apr-14
CZA-14.3.4.7.5 Shell Nozzles and Other Attachments		**70h**	**14-Apr-14**	**22-Apr-14**
CZA-TK-0602-2260	Cutting, Installation and Fit-up	20h	14-Apr-14	16-Apr-14
CZA-TK-0602-2270	Welding	50h	16-Apr-14	22-Apr-14
CZA-TK-0602-2280	Inspection	70h	14-Apr-14	22-Apr-14
CZA-14.3.4.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**40h**	**19-Apr-14**	**23-Apr-14**
CZA-TK-0602-2290	Erection and Fit-up	20h	19-Apr-14	21-Apr-14
CZA-TK-0602-2300	Welding	20h	21-Apr-14	23-Apr-14
CZA-TK-0602-2310	Inspection	40h	19-Apr-14	23-Apr-14
CZA-14.3.4.7.7 Deck Plate		**120h**	**23-Apr-14**	**07-May-14**
CZA-TK-0602-2320	Laying and Fit-up	30h	23-Apr-14	27-Apr-14
CZA-TK-0602-2330	Welding	90h	27-Apr-14	07-May-14
CZA-TK-0602-2340	Inspection	120h	23-Apr-14	07-May-14
CZA-14.3.4.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**140h**	**07-May-14**	**24-May-14**
CZA-TK-0602-2350	Laying, Cutting all Holes and Fit-up	40h	07-May-14	12-May-14
CZA-TK-0602-2360	Welding	100h	07-May-14	19-May-14
CZA-TK-0602-2370	Inspection	140h	07-May-14	24-May-14
CZA-14.3.4.7.9 Roof Structure		**110h**	**24-May-14**	**05-Jun-14**
CZA-TK-0602-2380	Erection and Fit-up	30h	24-May-14	27-May-14
CZA-TK-0602-2390	Welding	80h	27-May-14	05-Jun-14
CZA-TK-0602-2400	Inspection	110h	24-May-14	05-Jun-14
CZA-14.3.4.7.10 Roof Plates		**80h**	**05-Jun-14**	**15-Jun-14**
CZA-TK-0602-2410	Laying and Fit-up	20h	05-Jun-14	08-Jun-14
CZA-TK-0602-2420	Welding	60h	08-Jun-14	15-Jun-14
CZA-TK-0602-2430	Inspection	80h	05-Jun-14	15-Jun-14
CZA-14.3.4.7.11 Compression Ring		**90h**	**15-Jun-14**	**25-Jun-14**
CZA-TK-0602-2440	Laying and Fit-up	20h	15-Jun-14	17-Jun-14
CZA-TK-0602-2450	Welding	70h	17-Jun-14	25-Jun-14
CZA-TK-0602-2460	Inspection	90h	15-Jun-14	25-Jun-14
CZA-14.3.4.7.12 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**25-Jun-14**	**03-Jul-14**
CZA-TK-0602-2470	Cutting,Installation and Fit-up	20h	25-Jun-14	28-Jun-14
CZA-TK-0602-2480	Welding	50h	28-Jun-14	03-Jul-14
CZA-TK-0602-2490	Inspection	70h	25-Jun-14	03-Jul-14
CZA-14.3.4.7.13 Roof Platform, Gratings and Handrails		**100h**	**03-Jul-14**	**15-Jul-14**
CZA-TK-0602-2500	Erection and Fit-up	30h	03-Jul-14	07-Jul-14
CZA-TK-0602-2510	Welding	70h	07-Jul-14	15-Jul-14
CZA-TK-0602-2520	Inspection	100h	03-Jul-14	15-Jul-14
CZA-14.3.4.7.14 Shell No.7		**80h**	**15-Jul-14**	**24-Jul-14**
CZA-TK-0602-2530	Jacking, Erection and Fit-up	20h	15-Jul-14	17-Jul-14

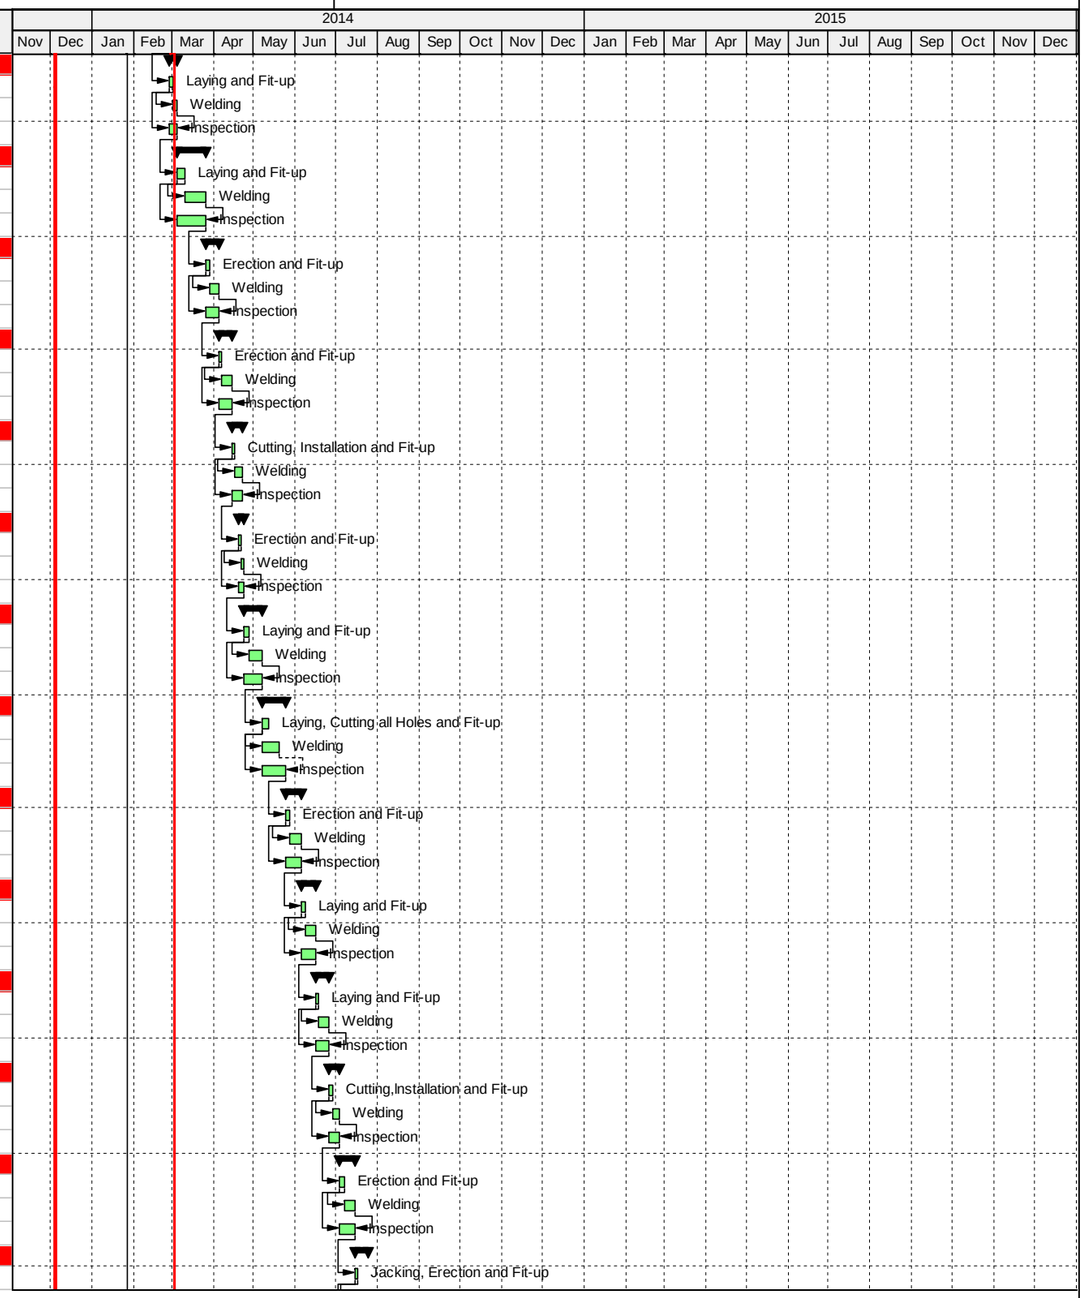

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0602-2540	Welding	60h	17-Jul-14	24-Jul-14
CZA-TK-0602-2550	Inspection	80h	15-Jul-14	24-Jul-14
CZA-14.3.4.7.15 Shell No.6		80h	24-Jul-14	03-Aug-14
CZA-TK-0602-2560	Jacking,Erection and Fit-up	20h	24-Jul-14	27-Jul-14
CZA-TK-0602-2570	Welding	60h	27-Jul-14	03-Aug-14
CZA-TK-0602-2580	Inspection	80h	24-Jul-14	03-Aug-14
CZA-14.3.4.7.16 Shell No.5		80h	03-Aug-14	12-Aug-14
CZA-TK-0602-2590	Jacking,Erection and Fit-up	20h	03-Aug-14	05-Aug-14
CZA-TK-0602-2600	Welding	60h	05-Aug-14	12-Aug-14
CZA-TK-0602-2610	Inspection	80h	03-Aug-14	12-Aug-14
CZA-14.3.4.7.17 Shell No.4		80h	12-Aug-14	21-Aug-14
CZA-TK-0602-2620	Jacking, Erection and Fit-up	20h	12-Aug-14	14-Aug-14
CZA-TK-0602-2630	Welding	60h	14-Aug-14	21-Aug-14
CZA-TK-0602-2640	Inspection	80h	12-Aug-14	21-Aug-14
CZA-14.3.4.7.18 Shell No.3		80h	21-Aug-14	31-Aug-14
CZA-TK-0602-2650	Jacking, Erection and Fit-up	20h	21-Aug-14	24-Aug-14
CZA-TK-0602-2660	Welding	60h	24-Aug-14	31-Aug-14
CZA-TK-0602-2670	Inspection	80h	21-Aug-14	31-Aug-14
CZA-14.3.4.7.19 Shell No.2		80h	31-Aug-14	09-Sep-14
CZA-TK-0602-2680	Jacking, Erection and Fit-up	20h	31-Aug-14	02-Sep-14
CZA-TK-0602-2690	Welding	60h	02-Sep-14	09-Sep-14
CZA-TK-0602-2700	Inspection	80h	31-Aug-14	09-Sep-14
CZA-14.3.4.7.20 Shell No.1		80h	09-Sep-14	18-Sep-14
CZA-TK-0602-2710	Jacking, Erection and Fit-up	20h	09-Sep-14	11-Sep-14
CZA-TK-0602-2720	Welding	60h	11-Sep-14	18-Sep-14
CZA-TK-0602-2730	Inspection	80h	09-Sep-14	18-Sep-14
CZA-14.3.4.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		70h	18-Sep-14	27-Sep-14
CZA-TK-0602-2740	Lay-out, Cutting, and Fit-up	20h	18-Sep-14	21-Sep-14
CZA-TK-0602-2750	Welding	50h	21-Sep-14	27-Sep-14
CZA-TK-0602-2760	Inspection	70h	18-Sep-14	27-Sep-14
CZA-14.3.4.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		80h	21-Sep-14	30-Sep-14
CZA-TK-0602-2770	Erection and Fit-up	20h	21-Sep-14	23-Sep-14
CZA-TK-0602-2780	Welding	60h	23-Sep-14	30-Sep-14
CZA-TK-0602-2790	Inspection	80h	21-Sep-14	30-Sep-14
CZA-14.3.4.7.24 Primary and Secondary Seal		70h	30-Sep-14	08-Oct-14
CZA-TK-0602-2800	Installation of Primary and Secondary Seal	60h	30-Sep-14	07-Oct-14
CZA-TK-0602-2810	Inspection	10h	07-Oct-14	08-Oct-14
CZA-14.3.4.4 Hydrotest		400h	08-Oct-14	24-Nov-14
CZA-TK-0602-2820	Filling, Holding and Draining	400h	08-Oct-14	24-Nov-14
CZA-14.3.4.5 Blasting and Painting		200h	24-Nov-14	17-Dec-14
CZA-TK-0602-2830	Blasting & Painting (Bottom, Shell & Roof) Inside and Outside	200h	24-Nov-14	17-Dec-14
CZA-14.3.4.6 Tank Calibration and Handover		70h	17-Dec-14	25-Dec-14
CZA-TK-0602-2840	Tank Calibration	50h	17-Dec-14	23-Dec-14
CZA-TK-0602-2850	Tank Handover	20h	23-Dec-14	25-Dec-14
CZA-14.3.5 S210-TK-0505 (Vam Feed Tank Dia 19.35m x Ht 12.10m)		1962h	09-Feb-14	25-Sep-14
CZA-14.3.5.1 Fabrication Works		322h	09-Feb-14	18-Mar-14
CZA-TK-0505-1350	Cutting of Annular Plate	8h	09-Feb-14	09-Feb-14
CZA-TK-0505-1360	Cutting of Bottom Plates	8h	09-Feb-14	10-Feb-14
CZA-TK-0505-1370	Cutting, Bevelling & Rolling of Shell No.1	8h	10-Feb-14	11-Feb-14
CZA-TK-0505-1380	Cutting, Bevelling & Rolling of Shell No.2	8h	11-Feb-14	12-Feb-14
CZA-TK-0505-1390	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	56h	12-Feb-14	18-Feb-14
CZA-TK-0505-1400	Cutting, Bevelling & Rolling of Shell No.3	8h	18-Feb-14	19-Feb-14
CZA-TK-0505-1410	Cutting, Bevelling & Rolling of Shell No.4	8h	19-Feb-14	20-Feb-14
CZA-TK-0505-1420	Cutting, Bevelling & Rolling of Shell No.5	8h	20-Feb-14	22-Feb-14

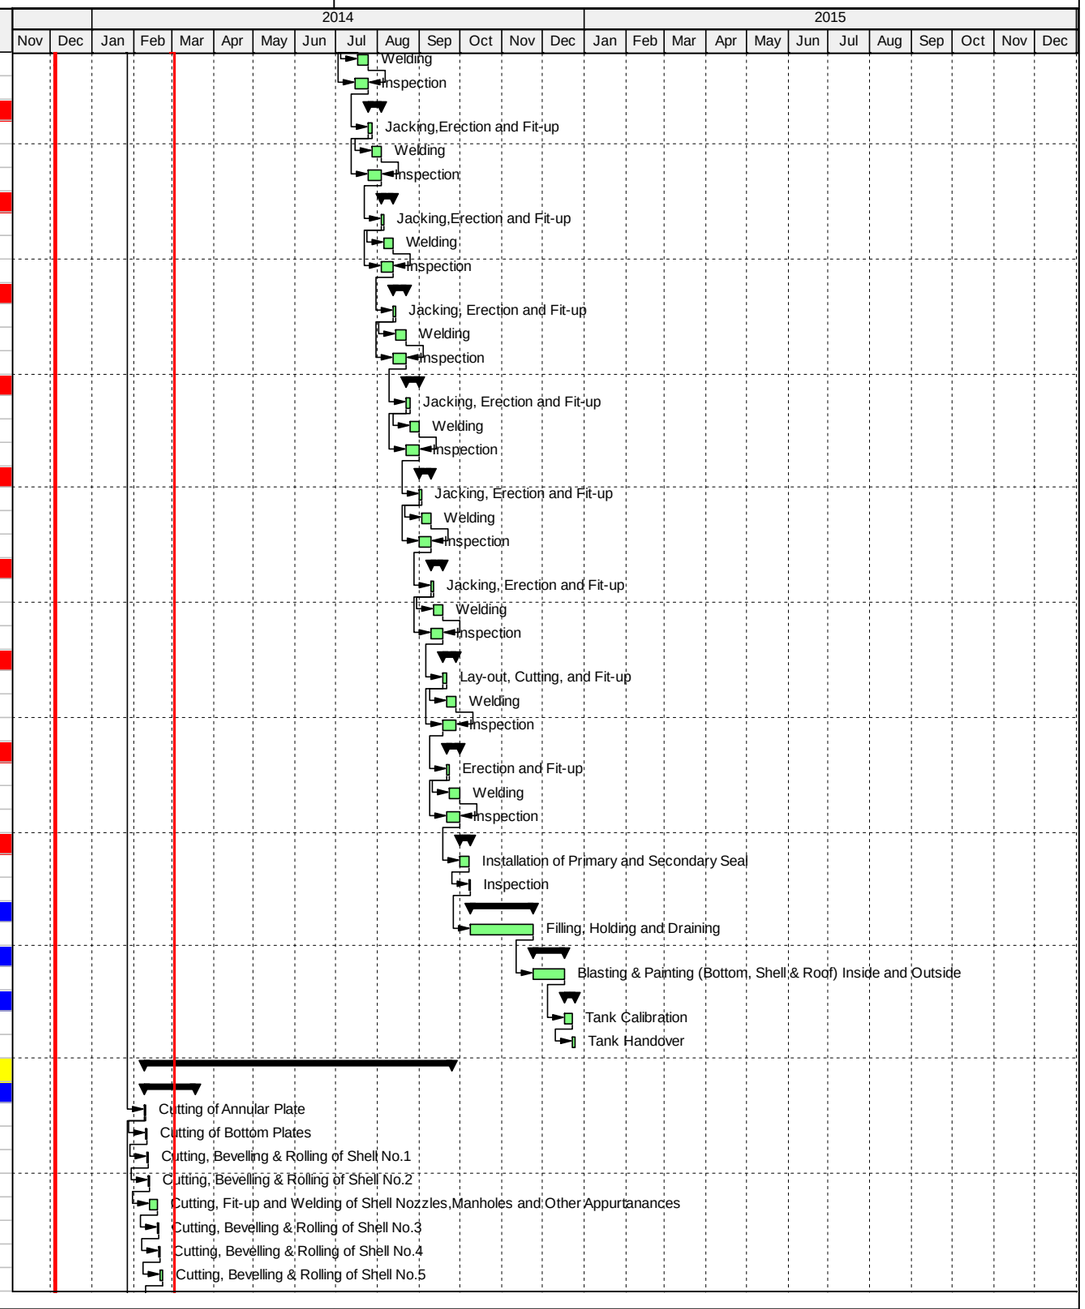

- Actual Level of Effort
- summary
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0505-1430	Cutting, Bevelling & Rolling of Shell No.6	8h	22-Feb-14	22-Feb-14
CZA-TK-0505-1440	Cutting, Bevelling & Rolling of Curb Angle	16h	23-Feb-14	24-Feb-14
CZA-TK-0505-1450	Cutting, Bevelling & Rolling of Roof Structure	40h	24-Feb-14	01-Mar-14
CZA-TK-0505-1460	Cutting of Roof Plates	10h	01-Mar-14	02-Mar-14
CZA-TK-0505-1470	Cutting,Fit-up and Welding of Roof Nozzles, Manholes & Other Appurtanances	56h	02-Mar-14	09-Mar-14
CZA-TK-0505-1480	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	96h	04-Mar-14	15-Mar-14
CZA-TK-0505-1490	Cutting, Fit-up and Welding of Stairway Platfrom, Gratings and Handrails	96h	06-Mar-14	18-Mar-14
CZA-14.3.5.2 Foundation Takeover		**0h**	**15-Mar-14**	**15-Mar-14**
CZA-TK-0505-1500	Foundation Takeover from Client	0h	15-Mar-14	
CZA-14.3.5.7 Mechanical Erection		**1066h**	**15-Mar-14**	**17-Jul-14**
CZA-14.3.5.7.1 Annular Plates		**40h**	**15-Mar-14**	**19-Mar-14**
CZA-TK-0505-1510	Laying and Fit-up	10h	15-Mar-14	16-Mar-14
CZA-TK-0505-1520	Welding	30h	16-Mar-14	19-Mar-14
CZA-TK-0505-1530	Inspection	40h	15-Mar-14	19-Mar-14
CZA-14.3.5.7.19 Bottom Plates		**40h**	**19-Mar-14**	**24-Mar-14**
CZA-TK-0505-1540	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-0505-1550	Welding	30h	20-Mar-14	24-Mar-14
CZA-TK-0505-1560	Inspection	40h	19-Mar-14	24-Mar-14
CZA-14.3.5.7.2 Shell No.1		**50h**	**24-Mar-14**	**30-Mar-14**
CZA-TK-0505-1570	Erection and Fit-up	10h	24-Mar-14	25-Mar-14
CZA-TK-0505-1580	Welding	40h	25-Mar-14	30-Mar-14
CZA-TK-0505-1590	Inspection	50h	24-Mar-14	30-Mar-14
CZA-14.3.5.7.3 Shell No.2		**50h**	**30-Mar-14**	**05-Apr-14**
CZA-TK-0505-1600	Erection and Fit-up	10h	30-Mar-14	31-Mar-14
CZA-TK-0505-1610	Welding	40h	31-Mar-14	05-Apr-14
CZA-TK-0505-1620	Inspection	50h	30-Mar-14	05-Apr-14
CZA-14.3.5.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**40h**	**05-Apr-14**	**09-Apr-14**
CZA-TK-0505-1630	Cutting, Installation and Fit-up	20h	05-Apr-14	07-Apr-14
CZA-TK-0505-1640	Welding	20h	07-Apr-14	09-Apr-14
CZA-TK-0505-1650	Inspection	40h	05-Apr-14	09-Apr-14
CZA-14.3.5.7.7 Shell No.3		**50h**	**09-Apr-14**	**15-Apr-14**
CZA-TK-0505-1660	Erection and Fit-up	10h	09-Apr-14	10-Apr-14
CZA-TK-0505-1670	Welding	40h	10-Apr-14	15-Apr-14
CZA-TK-0505-1680	Inspection	50h	09-Apr-14	15-Apr-14
CZA-14.3.5.7.8 Shell No.4		**50h**	**15-Apr-14**	**21-Apr-14**
CZA-TK-0505-1690	Erection and Fit-up	10h	15-Apr-14	16-Apr-14
CZA-TK-0505-1700	Welding	40h	16-Apr-14	21-Apr-14
CZA-TK-0505-1710	Inspection	50h	15-Apr-14	21-Apr-14
CZA-14.3.5.7.9 Shell No.5		**50h**	**21-Apr-14**	**27-Apr-14**
CZA-TK-0505-1720	Erection and Fit-up	10h	21-Apr-14	22-Apr-14
CZA-TK-0505-1730	Welding	40h	22-Apr-14	27-Apr-14
CZA-TK-0505-1740	Inspection	50h	21-Apr-14	27-Apr-14
CZA-14.3.5.7.10 Shell No.6		**50h**	**27-Apr-14**	**03-May-14**
CZA-TK-0505-1750	Erection and Fit-up	10h	27-Apr-14	28-Apr-14
CZA-TK-0505-1760	Welding	40h	28-Apr-14	03-May-14
CZA-TK-0505-1770	Inspection	50h	27-Apr-14	03-May-14
CZA-14.3.5.7.12 Shell Nozzles and attachements (Upper)		**60h**	**03-May-14**	**10-May-14**
CZA-TK-0505-1780	Cutting, Installation and Fit-up	20h	03-May-14	05-May-14
CZA-TK-0505-1790	Welding	40h	05-May-14	10-May-14
CZA-TK-0505-1800	Inspection	60h	03-May-14	10-May-14
CZA-14.3.5.7.13 Curb Angle		**40h**	**10-May-14**	**14-May-14**
CZA-TK-0505-1810	Erection and Fit-up	10h	10-May-14	11-May-14
CZA-TK-0505-1820	Welding	30h	11-May-14	14-May-14
CZA-TK-0505-1830	Inspection	40h	10-May-14	14-May-14

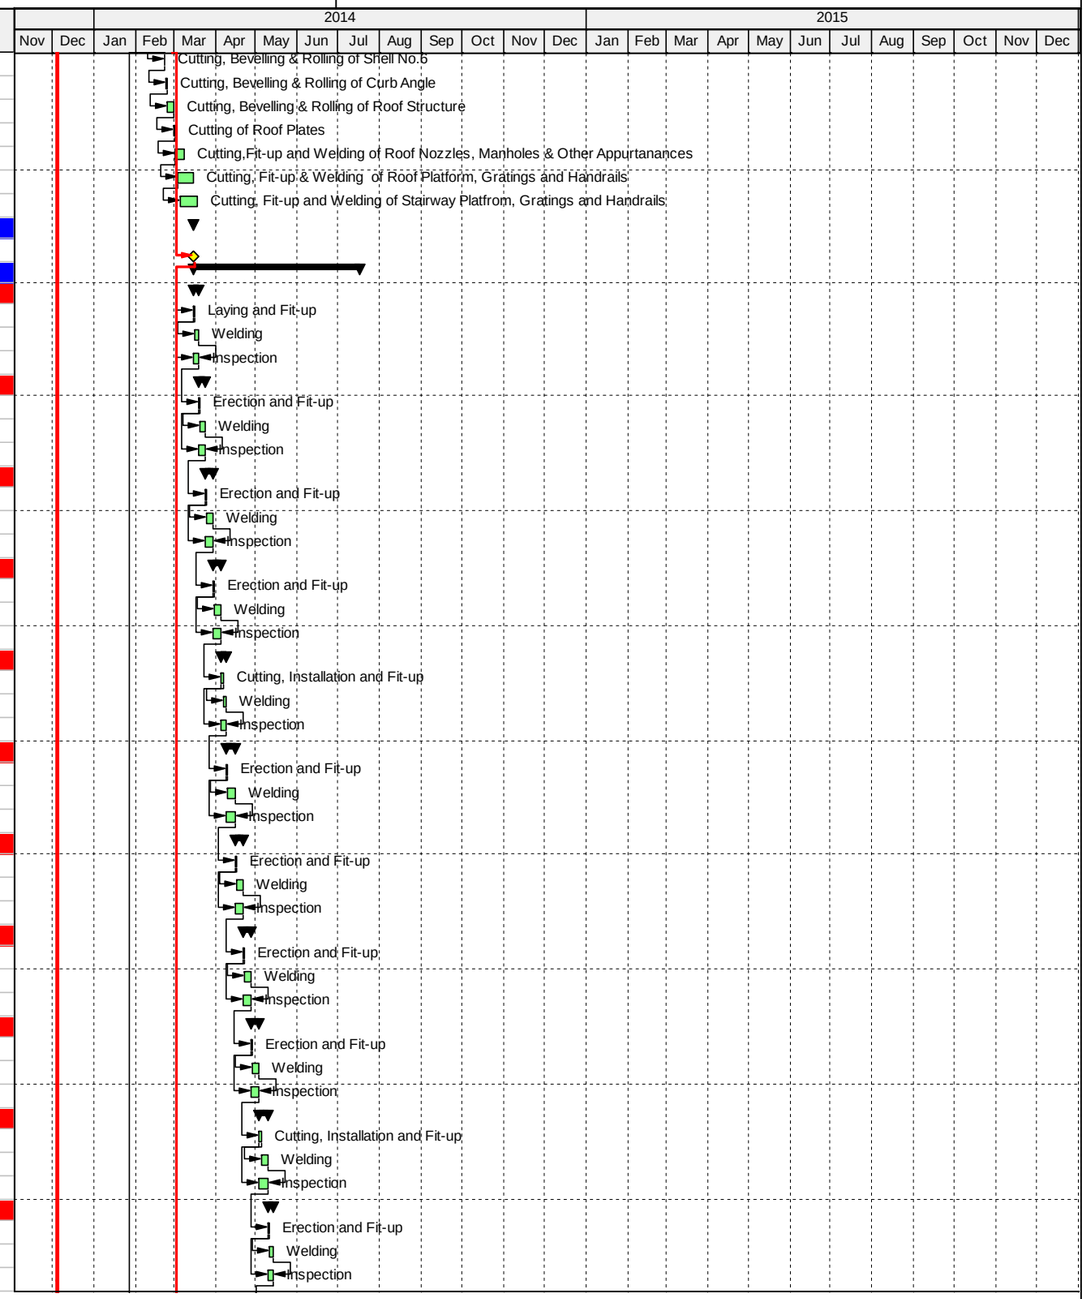

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.5.7.14 Roof Structure		**70h**	**14-May-14**	**22-May-14**
CZA-TK-0505-1840	Laying and Fit-up	30h	14-May-14	18-May-14
CZA-TK-0505-1850	Welding	40h	18-May-14	22-May-14
CZA-TK-0505-1860	Inspection	70h	14-May-14	22-May-14
CZA-14.3.5.7.15 Roof Plates		**70h**	**22-May-14**	**31-May-14**
CZA-TK-0505-1870	Laying and Fit-up	20h	22-May-14	25-May-14
CZA-TK-0505-1880	Welding	50h	25-May-14	31-May-14
CZA-TK-0505-1890	Inspection	70h	22-May-14	31-May-14
CZA-14.3.5.7.16 Roof Nozzles, Manholes and Other Appurtanances		**50h**	**31-May-14**	**05-Jun-14**
CZA-TK-0505-1900	Installation and Fit-up	20h	31-May-14	02-Jun-14
CZA-TK-0505-1910	Welding	30h	02-Jun-14	05-Jun-14
CZA-TK-0505-1920	Inspection	50h	31-May-14	05-Jun-14
CZA-14.3.5.7.18 Stairway Platform, Handrails and Gratings		**120h**	**05-Jun-14**	**19-Jun-14**
CZA-TK-0505-1930	Erection and Fit-up	30h	05-Jun-14	09-Jun-14
CZA-TK-0505-1940	Welding	90h	09-Jun-14	19-Jun-14
CZA-TK-0505-1950	Inspection	120h	05-Jun-14	19-Jun-14
CZA-14.3.5.7.17 Roof Platform, Handrails and Gratings		**120h**	**12-Jun-14**	**26-Jun-14**
CZA-TK-0505-1960	Erection and Fit-up	30h	12-Jun-14	16-Jun-14
CZA-TK-0505-1970	Welding	90h	16-Jun-14	26-Jun-14
CZA-TK-0505-1980	Inspection	120h	12-Jun-14	26-Jun-14
CZA-14.3.5.7.20 Primary and Secondary Seal		**40h**	**26-Jun-14**	**01-Jul-14**
CZA-TK-0505-1990	Installation of Primary and Secondary Seal	30h	26-Jun-14	30-Jun-14
CZA-TK-0505-2000	Inspection	10h	30-Jun-14	01-Jul-14
CZA-14.3.5.7.11 Insulation		**140h**	**01-Jul-14**	**17-Jul-14**
CZA-TK-0505-2010	Insulation Works	130h	01-Jul-14	16-Jul-14
CZA-TK-0505-2020	Inspection	10h	16-Jul-14	17-Jul-14
CZA-14.3.5.4 Hydotest		**350h**	**17-Jul-14**	**27-Aug-14**
CZA-TK-0505-2030	Filling, Holding and Draining of Water	350h	17-Jul-14	27-Aug-14
CZA-14.3.5.5 Blasting and Painting		**180h**	**27-Aug-14**	**17-Sep-14**
CZA-TK-0505-2040	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	180h	27-Aug-14	17-Sep-14
CZA-14.3.5.6 Tank Calibration and Handover		**70h**	**17-Sep-14**	**25-Sep-14**
CZA-TK-0505-2050	Tank Calibration	50h	17-Sep-14	23-Sep-14
CZA-TK-0505-2060	Tank Handover	20h	23-Sep-14	25-Sep-14
CZA-14.3.8 S210-TK-0516 (ENB Feed Tank Dia 13.54m x Ht 12.40m with IFR)		**1518h**	**09-Feb-14**	**04-Aug-14**
CZA-14.3.8.1 Fabrication Works		**240h**	**09-Feb-14**	**08-Mar-14**
CZA-TK-0516-1710	Cutting of Annular Plate	8h	09-Feb-14	09-Feb-14
CZA-TK-0516-1720	Cutting of Bottom Plates	8h	09-Feb-14	10-Feb-14
CZA-TK-0516-1730	Cutting, Bevelling & Rolling of Shell No.1	8h	10-Feb-14	11-Feb-14
CZA-TK-0516-1740	Cutting, Bevelling & Rolling of Shell No.2	8h	10-Feb-14	11-Feb-14
CZA-TK-0516-1750	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	40h	10-Feb-14	15-Feb-14
CZA-TK-0516-1760	Cutting of Floating Deck Plate	8h	15-Feb-14	16-Feb-14
CZA-TK-0516-1770	Cutting,Fit up and Welding of Pontoon	8h	16-Feb-14	17-Feb-14
CZA-TK-0516-1780	Cutting of Floating Legs and Manholes	8h	17-Feb-14	17-Feb-14
CZA-TK-0516-1790	Cutting, Bevelling & Rolling of Shell No.3	8h	18-Feb-14	18-Feb-14
CZA-TK-0516-1800	Cutting, Bevelling & Rolling of Shell No.4	8h	18-Feb-14	18-Feb-14
CZA-TK-0516-1810	Cutting, Bevelling & Rolling of Shell No.5	8h	18-Feb-14	19-Feb-14
CZA-TK-0516-1820	Cutting, Bevelling & Rolling of Shell No.6	10h	19-Feb-14	20-Feb-14
CZA-TK-0516-1830	Cutting, Bevelling & Rolling of Shell No.7	8h	19-Feb-14	20-Feb-14
CZA-TK-0516-1840	Cutting, Bevelling & Rolling of Curb Angle	16h	22-Feb-14	23-Feb-14
CZA-TK-0516-1850	Cutting, Fit-up and Welding of Roof Structure	32h	24-Feb-14	27-Feb-14
CZA-TK-0516-1860	Cutting of Roof Plates	8h	27-Feb-14	01-Mar-14
CZA-TK-0516-1870	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	01-Mar-14	05-Mar-14
CZA-TK-0516-1880	Cutting, Fit-up and Welding of Roof Platform,Gratings and Stairway	56h	02-Mar-14	08-Mar-14
CZA-TK-0516-1890	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	02-Mar-14	08-Mar-14

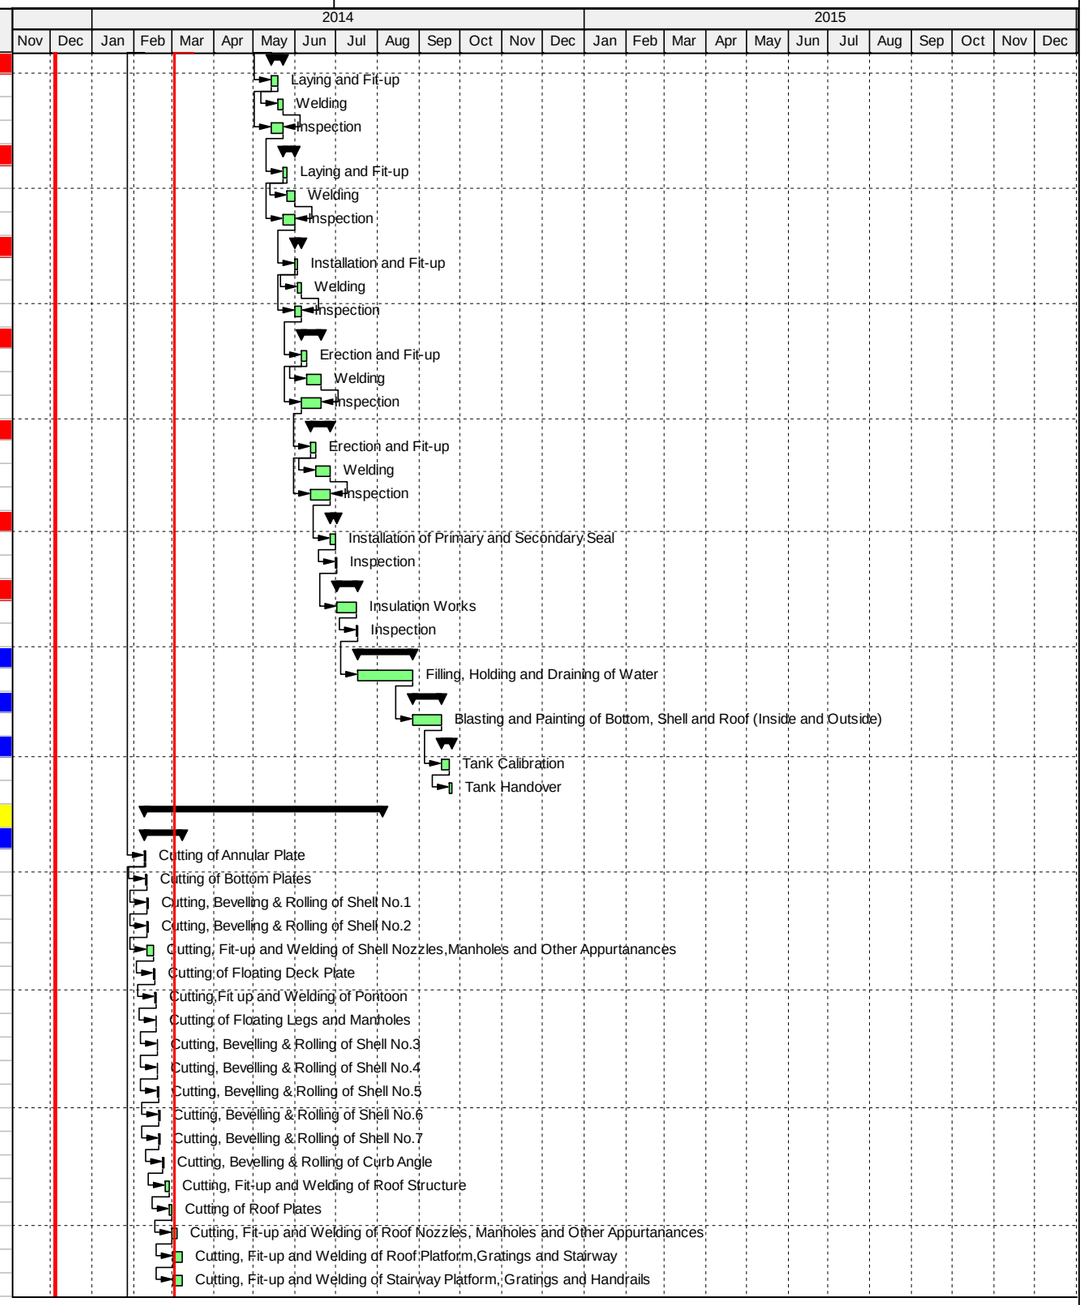

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.8.2 Foundation Takeover		0h	15-Mar-14	15-Mar-14
CZA-TK-0516-1900	Foundation Takeover from Client	0h	15-Mar-14	
CZA-14.3.8.7 Mechanical Erection		972h	15-Mar-14	06-Jul-14
CZA-14.3.8.7.1 Annular Plates		40h	15-Mar-14	19-Mar-14
CZA-TK-0516-1910	Laying and Fit-up	10h	15-Mar-14	16-Mar-14
CZA-TK-0516-1920	Welding	30h	16-Mar-14	19-Mar-14
CZA-TK-0516-1930	Inspection	40h	15-Mar-14	19-Mar-14
CZA-14.3.8.7.19 Bottom Plates		40h	19-Mar-14	24-Mar-14
CZA-TK-0516-1940	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-0516-1950	Welding	30h	20-Mar-14	24-Mar-14
CZA-TK-0516-1960	Inspection	40h	19-Mar-14	24-Mar-14
CZA-14.3.8.7.2 Shell No.1		40h	24-Mar-14	29-Mar-14
CZA-TK-0516-1970	Erection and Fit-up	10h	24-Mar-14	25-Mar-14
CZA-TK-0516-1980	Welding	30h	25-Mar-14	29-Mar-14
CZA-TK-0516-1990	Inspection	40h	24-Mar-14	29-Mar-14
CZA-14.3.8.7.3 Shell No.2		40h	29-Mar-14	02-Apr-14
CZA-TK-0516-2000	Erection and Fit-up	10h	29-Mar-14	30-Mar-14
CZA-TK-0516-2010	Welding	30h	30-Mar-14	02-Apr-14
CZA-TK-0516-2020	Inspection	40h	29-Mar-14	02-Apr-14
CZA-14.3.8.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		60h	02-Apr-14	09-Apr-14
CZA-TK-0516-2030	Cutting, Installation and Fit-up	20h	02-Apr-14	05-Apr-14
CZA-TK-0516-2040	Welding	40h	05-Apr-14	09-Apr-14
CZA-TK-0516-2050	Inspection	60h	02-Apr-14	09-Apr-14
CZA-14.3.8.7.5 Deck Plates		80h	02-Apr-14	12-Apr-14
CZA-TK-0516-2060	Laying & Fit-up	20h	02-Apr-14	05-Apr-14
CZA-TK-0516-2070	Welding	60h	05-Apr-14	12-Apr-14
CZA-TK-0516-2080	Inspection	80h	02-Apr-14	12-Apr-14
CZA-14.3.8.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		100h	12-Apr-14	23-Apr-14
CZA-TK-0516-2090	Cutting of All Holes, Laying and Fit-up	20h	12-Apr-14	14-Apr-14
CZA-TK-0516-2100	Welding of Sleeves and Plates	60h	14-Apr-14	21-Apr-14
CZA-TK-0516-2110	Installation of Leg Support	20h	21-Apr-14	23-Apr-14
CZA-TK-0516-2120	Inspection	100h	12-Apr-14	23-Apr-14
CZA-14.3.8.7.7 Shell No.3		40h	05-Apr-14	09-Apr-14
CZA-TK-0516-2130	Erection and Fit-up	10h	05-Apr-14	06-Apr-14
CZA-TK-0516-2140	Welding	30h	06-Apr-14	09-Apr-14
CZA-TK-0516-2150	Inspection	40h	05-Apr-14	09-Apr-14
CZA-14.3.8.7.8 Shell No.4		40h	09-Apr-14	14-Apr-14
CZA-TK-0516-2160	Erection and Fit-up	10h	09-Apr-14	10-Apr-14
CZA-TK-0516-2170	Welding	30h	10-Apr-14	14-Apr-14
CZA-TK-0516-2180	Inspection	40h	09-Apr-14	14-Apr-14
CZA-14.3.8.7.9 Shell No.5		40h	14-Apr-14	19-Apr-14
CZA-TK-0516-2190	Erection and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0516-2200	Welding	30h	15-Apr-14	19-Apr-14
CZA-TK-0516-2210	Inspection	40h	14-Apr-14	19-Apr-14
CZA-14.3.8.7.10 Shell No.6		40h	19-Apr-14	23-Apr-14
CZA-TK-0516-2220	Erection and Fit-up	10h	19-Apr-14	20-Apr-14
CZA-TK-0516-2230	Welding	30h	20-Apr-14	23-Apr-14
CZA-TK-0516-2240	Inspection	40h	19-Apr-14	23-Apr-14
CZA-14.3.8.7.11 Shell No.7		40h	23-Apr-14	28-Apr-14
CZA-TK-0516-2250	Erection and Fit-up	10h	23-Apr-14	24-Apr-14
CZA-TK-0516-2260	Welding	30h	24-Apr-14	28-Apr-14
CZA-TK-0516-2270	Inspection	40h	23-Apr-14	28-Apr-14
CZA-14.3.8.7.12 Shell Nozzles and attachements (Upper)		50h	28-Apr-14	04-May-14
CZA-TK-0516-2280	Cutting, Installation and Fit-up	20h	28-Apr-14	30-Apr-14

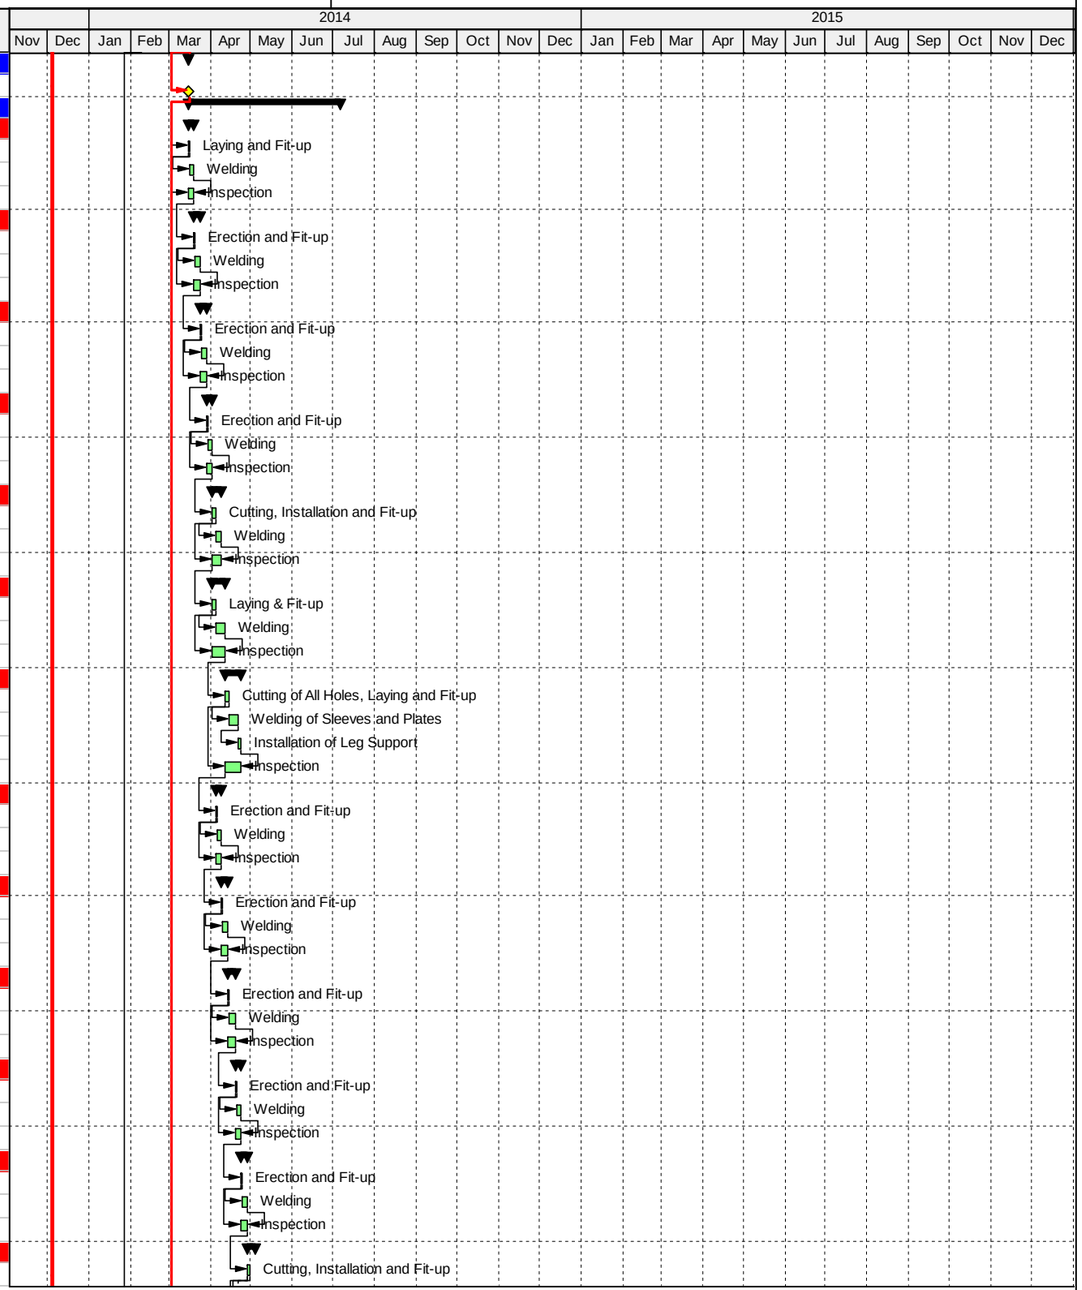

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0516-2290	Welding	30h	30-Apr-14	04-May-14
CZA-TK-0516-2300	Inspection	50h	28-Apr-14	04-May-14
CZA-14.3.8.7.13 Curb Angle		**40h**	**04-May-14**	**08-May-14**
CZA-TK-0516-2310	Erection and Fit-up	10h	04-May-14	05-May-14
CZA-TK-0516-2320	Welding	30h	05-May-14	08-May-14
CZA-TK-0516-2330	Inspection	40h	04-May-14	08-May-14
CZA-14.3.8.7.14 Roof Structure		**60h**	**08-May-14**	**15-May-14**
CZA-TK-0516-2340	Laying and Fit-up	20h	08-May-14	11-May-14
CZA-TK-0516-2350	Welding	40h	11-May-14	15-May-14
CZA-TK-0516-2360	Inspection	60h	08-May-14	15-May-14
CZA-14.3.8.7.15 Roof Plates		**40h**	**15-May-14**	**20-May-14**
CZA-TK-0516-2370	Laying and Fit-up	10h	15-May-14	17-May-14
CZA-TK-0516-2380	Welding	30h	17-May-14	20-May-14
CZA-TK-0516-2390	Inspection	40h	15-May-14	20-May-14
CZA-14.3.8.7.16 Roof Nozzles, Manholes and Other Appurtanances		**60h**	**20-May-14**	**27-May-14**
CZA-TK-0516-2400	Installation and Fit-up	20h	20-May-14	22-May-14
CZA-TK-0516-2410	Welding	40h	22-May-14	27-May-14
CZA-TK-0516-2420	Inspection	60h	20-May-14	27-May-14
CZA-14.3.8.7.18 Stairway Platform, Handrails and Gratings		**140h**	**21-May-14**	**07-Jun-14**
CZA-TK-0516-2430	Erection and Fit-up	30h	21-May-14	25-May-14
CZA-TK-0516-2440	Welding	110h	25-May-14	07-Jun-14
CZA-TK-0516-2450	Inspection	140h	21-May-14	07-Jun-14
CZA-14.3.8.7.17 Roof Platform, Handrails and Gratings		**140h**	**21-May-14**	**07-Jun-14**
CZA-TK-0516-2460	Erection and Fit-up	30h	21-May-14	25-May-14
CZA-TK-0516-2470	Welding	110h	25-May-14	07-Jun-14
CZA-TK-0516-2480	Inspection	140h	21-May-14	07-Jun-14
CZA-14.3.8.7.20 Installation of Primary and Secondary Seal		**40h**	**07-Jun-14**	**11-Jun-14**
CZA-TK-0516-2490	Installation of Primary and Secondary Seal	40h	07-Jun-14	11-Jun-14
CZA-TK-0516-2500	Inspection	40h	07-Jun-14	11-Jun-14
CZA-14.3.8.7.21 Insulation		**210h**	**11-Jun-14**	**06-Jul-14**
CZA-TK-0516-2510	Insulation Works	200h	11-Jun-14	05-Jul-14
CZA-TK-0516-2520	Inspection	10h	05-Jul-14	06-Jul-14
CZA-14.3.8.4 Hydotest		**120h**	**06-Jul-14**	**20-Jul-14**
CZA-TK-0516-2530	Filling, Holding and Draining of Water	120h	06-Jul-14	20-Jul-14
CZA-14.3.8.5 Blasting and Painting		**60h**	**20-Jul-14**	**27-Jul-14**
CZA-TK-0516-2540	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	60h	20-Jul-14	27-Jul-14
CZA-14.3.8.6 Tank Calibration and Handover		**70h**	**27-Jul-14**	**04-Aug-14**
CZA-TK-0516-2550	Tank Calibration	50h	27-Jul-14	02-Aug-14
CZA-TK-0516-2560	Tank Handover	20h	02-Aug-14	04-Aug-14
CZA-14.3.9 S210-TK-0520 (Hexane Feed Tank Dia 15.48m x Ht 13.60m with IFR)		**1756h**	**09-Feb-14**	**01-Sep-14**
CZA-14.3.9.1 Fabrication Works		**290h**	**09-Feb-14**	**13-Mar-14**
CZA-TK-0520-2150	Cutting of Annular Plate	8h	09-Feb-14	09-Feb-14
CZA-TK-0520-2160	Cutting of Bottom Plates	8h	09-Feb-14	10-Feb-14
CZA-TK-0520-2170	Cutting, Bevelling & Rolling of Shell No.1	8h	10-Feb-14	11-Feb-14
CZA-TK-0520-2180	Cutting, Bevelling & Rolling of Shell No.2	8h	10-Feb-14	11-Feb-14
CZA-TK-0520-2190	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	40h	10-Feb-14	15-Feb-14
CZA-TK-0520-2200	Cutting of Floating Deck Plate	8h	15-Feb-14	16-Feb-14
CZA-TK-0520-2210	Cutting,Fit up and Welding of Pontoon	8h	16-Feb-14	17-Feb-14
CZA-TK-0520-2220	Cutting of Floating Legs and Manholes	8h	17-Feb-14	17-Feb-14
CZA-TK-0520-2230	Cutting, Bevelling & Rolling of Shell No.3	8h	18-Feb-14	18-Feb-14
CZA-TK-0520-2240	Cutting, Bevelling & Rolling of Shell No.4	8h	18-Feb-14	18-Feb-14
CZA-TK-0520-2250	Cutting, Bevelling & Rolling of Shell No.5	8h	18-Feb-14	19-Feb-14
CZA-TK-0520-2260	Cutting, Bevelling & Rolling of Shell No.6	10h	19-Feb-14	20-Feb-14
CZA-TK-0520-2280	Cutting, Bevelling & Rolling of Curb Angle	16h	20-Feb-14	23-Feb-14

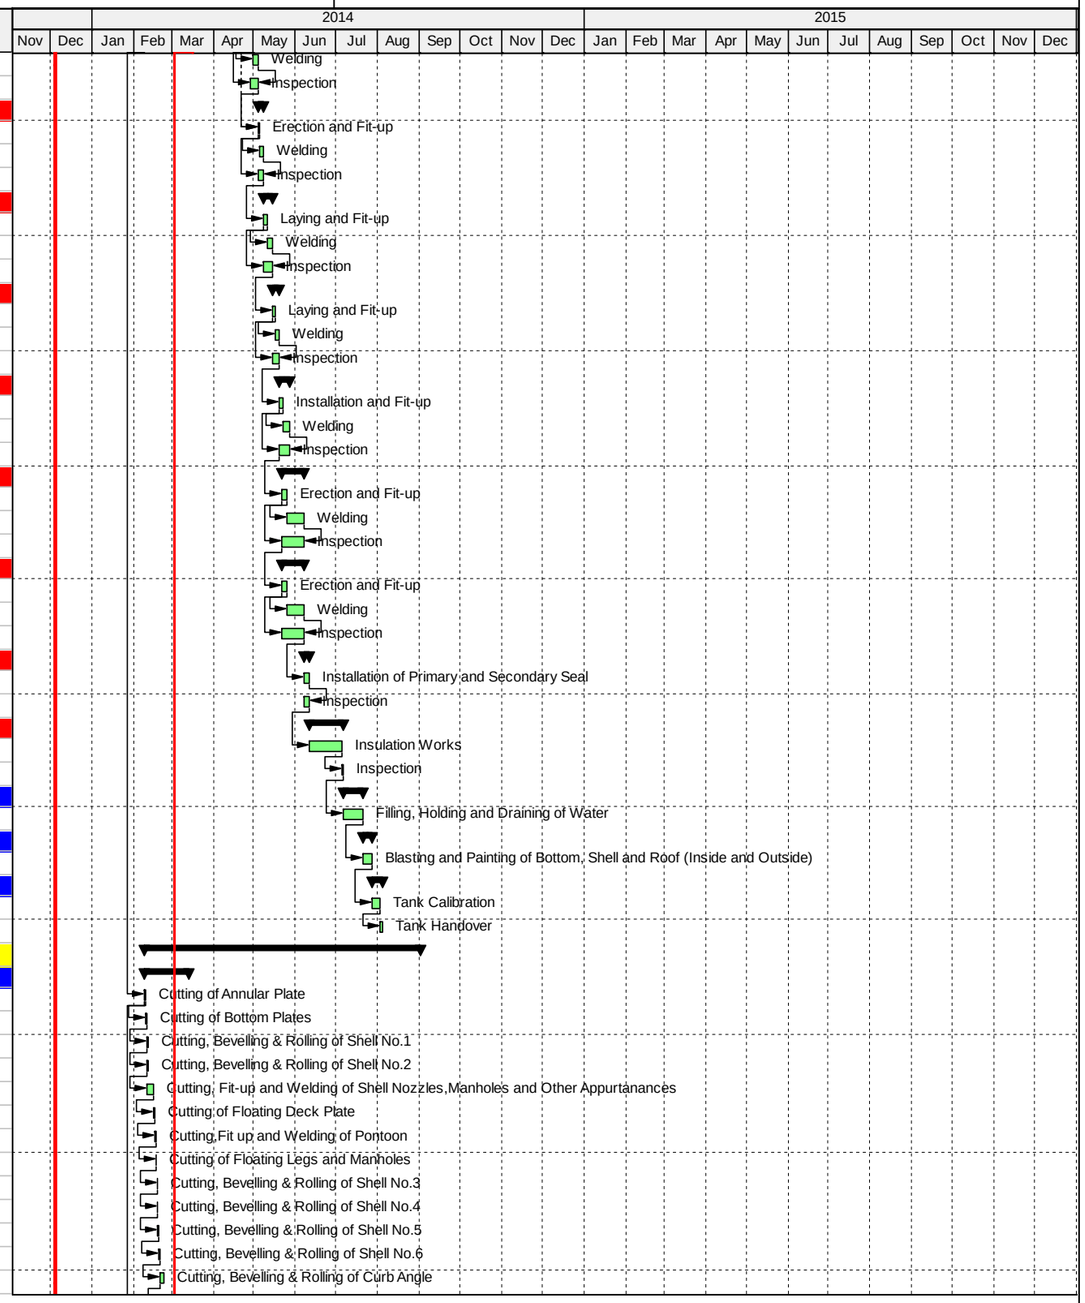

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone
- summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0520-2290	Cutting, Fit-up and Welding of Roof Structure	32h	24-Feb-14	27-Feb-14
CZA-TK-0520-2510	Cutting of Roof Plates	16h	27-Feb-14	01-Mar-14
CZA-TK-0520-2520	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	01-Mar-14	05-Mar-14
CZA-TK-0520-2530	Cutting, Fit-up and Welding of Roof Platform,Gratings and Stairway	56h	05-Mar-14	11-Mar-14
CZA-TK-0520-2540	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	08-Mar-14	13-Mar-14
CZA-14.3.9.2 Foundation Takeover		**0h**	**15-Mar-14**	**15-Mar-14**
CZA-TK-0520-2300	Foundation Takeover from Client	0h	15-Mar-14	
CZA-14.3.9.7 Mechanical Erection		**1190h**	**15-Mar-14**	**31-Jul-14**
CZA-14.3.9.7.1 Annular Plates		**40h**	**15-Mar-14**	**19-Mar-14**
CZA-TK-0520-2310	Laying and Fit-up	10h	15-Mar-14	16-Mar-14
CZA-TK-0520-2320	Welding	30h	16-Mar-14	19-Mar-14
CZA-TK-0520-2330	Inspection	40h	15-Mar-14	19-Mar-14
CZA-14.3.9.7.19 Bottom Plates		**50h**	**19-Mar-14**	**25-Mar-14**
CZA-TK-0520-2340	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-0520-2350	Welding	40h	20-Mar-14	25-Mar-14
CZA-TK-0520-2360	Inspection	50h	19-Mar-14	25-Mar-14
CZA-14.3.9.7.2 Shell No.1		**40h**	**25-Mar-14**	**30-Mar-14**
CZA-TK-0520-2370	Erection and Fit-up	10h	25-Mar-14	26-Mar-14
CZA-TK-0520-2380	Welding	30h	26-Mar-14	30-Mar-14
CZA-TK-0520-2390	Inspection	40h	25-Mar-14	30-Mar-14
CZA-14.3.9.7.3 Shell No.2		**40h**	**30-Mar-14**	**03-Apr-14**
CZA-TK-0520-2400	Erection and Fit-up	10h	30-Mar-14	31-Mar-14
CZA-TK-0520-2410	Welding	30h	31-Mar-14	03-Apr-14
CZA-TK-0520-2420	Inspection	40h	30-Mar-14	03-Apr-14
CZA-14.3.9.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**50h**	**03-Apr-14**	**09-Apr-14**
CZA-TK-0520-2430	Cutting, Installation and Fit-up	20h	03-Apr-14	06-Apr-14
CZA-TK-0520-2440	Welding	30h	06-Apr-14	09-Apr-14
CZA-TK-0520-2450	Inspection	50h	03-Apr-14	09-Apr-14
CZA-14.3.9.7.5 Deck Plates		**90h**	**09-Apr-14**	**20-Apr-14**
CZA-TK-0520-2460	Laying & Fit-up	20h	09-Apr-14	12-Apr-14
CZA-TK-0520-2470	Welding	70h	12-Apr-14	20-Apr-14
CZA-TK-0520-2480	Inspection	90h	09-Apr-14	20-Apr-14
CZA-14.3.9.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		**140h**	**20-Apr-14**	**06-May-14**
CZA-TK-0520-2490	Cutting of All Holes, Laying & Fit-up	30h	20-Apr-14	23-Apr-14
CZA-TK-0520-2500	Welding of Sleeves and Plates	100h	23-Apr-14	05-May-14
CZA-TK-0520-2550	Installation of Leg Support	10h	05-May-14	06-May-14
CZA-TK-0520-2560	Inspection	140h	20-Apr-14	06-May-14
CZA-14.3.9.7.7 Shell No.3		**40h**	**06-May-14**	**11-May-14**
CZA-TK-0520-2570	Erection and Fit-up	10h	06-May-14	07-May-14
CZA-TK-0520-2580	Welding	30h	07-May-14	11-May-14
CZA-TK-0520-2590	Inspection	40h	06-May-14	11-May-14
CZA-14.3.9.7.8 Shell No.4		**40h**	**11-May-14**	**15-May-14**
CZA-TK-0520-2600	Erection and Fit-up	10h	11-May-14	12-May-14
CZA-TK-0520-2610	Welding	30h	12-May-14	15-May-14
CZA-TK-0520-2620	Inspection	40h	11-May-14	15-May-14
CZA-14.3.9.7.9 Shell No.5		**40h**	**15-May-14**	**20-May-14**
CZA-TK-0520-2630	Erection and Fit-up	10h	15-May-14	17-May-14
CZA-TK-0520-2640	Welding	30h	17-May-14	20-May-14
CZA-TK-0520-2650	Inspection	40h	15-May-14	20-May-14
CZA-14.3.9.7.10 Shell No.6		**40h**	**20-May-14**	**25-May-14**
CZA-TK-0520-2660	Erection and Fit-up	10h	20-May-14	21-May-14
CZA-TK-0520-2670	Welding	30h	21-May-14	25-May-14
CZA-TK-0520-2680	Inspection	40h	20-May-14	25-May-14
CZA-14.3.9.7.12 Shell Nozzles and attachements (Upper)		**60h**	**25-May-14**	**01-Jun-14**

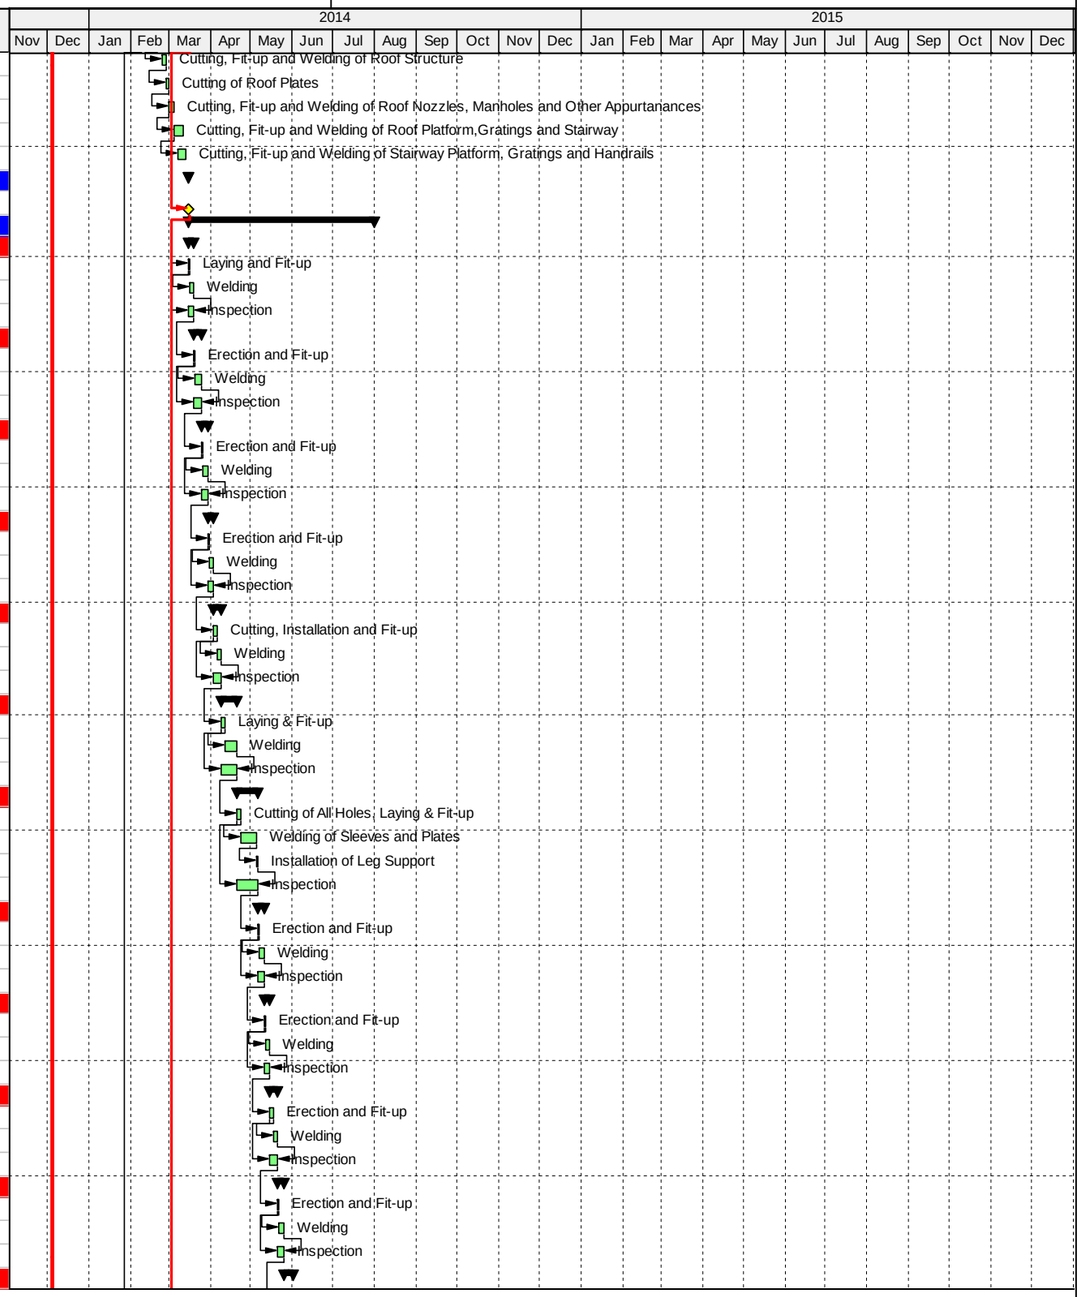

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0520-2690	Cutting, Installation and Fit-up	20h	25-May-14	27-May-14
CZA-TK-0520-2700	Welding	40h	27-May-14	01-Jun-14
CZA-TK-0520-2710	Inspection	60h	25-May-14	01-Jun-14
CZA-14.3.9.7.13 Curb Angle		**40h**	**01-Jun-14**	**05-Jun-14**
CZA-TK-0520-2720	Erection and Fit-up	10h	01-Jun-14	02-Jun-14
CZA-TK-0520-2730	Welding	30h	02-Jun-14	05-Jun-14
CZA-TK-0520-2740	Inspection	40h	01-Jun-14	05-Jun-14
CZA-14.3.9.7.14 Roof Structure		**50h**	**05-Jun-14**	**11-Jun-14**
CZA-TK-0520-2750	Laying and Fit-up	20h	05-Jun-14	08-Jun-14
CZA-TK-0520-2760	Welding	30h	08-Jun-14	11-Jun-14
CZA-TK-0520-2770	Inspection	50h	05-Jun-14	11-Jun-14
CZA-14.3.9.7.15 Roof Plates		**40h**	**11-Jun-14**	**16-Jun-14**
CZA-TK-0520-2780	Laying and Fit-up	10h	11-Jun-14	12-Jun-14
CZA-TK-0520-2790	Welding	30h	12-Jun-14	16-Jun-14
CZA-TK-0520-2800	Inspection	40h	11-Jun-14	16-Jun-14
CZA-14.3.9.7.16 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**16-Jun-14**	**24-Jun-14**
CZA-TK-0520-2810	Installation and Fit-up	20h	16-Jun-14	18-Jun-14
CZA-TK-0520-2820	Welding	50h	18-Jun-14	24-Jun-14
CZA-TK-0520-2830	Inspection	70h	16-Jun-14	24-Jun-14
CZA-14.3.9.7.18 Stairway Platform, Handrails and Gratings		**140h**	**24-Jun-14**	**10-Jul-14**
CZA-TK-0520-2840	Erection and Fit-up	40h	24-Jun-14	29-Jun-14
CZA-TK-0520-2850	Welding	100h	29-Jun-14	10-Jul-14
CZA-TK-0520-2860	Inspection	140h	24-Jun-14	10-Jul-14
CZA-14.3.9.7.17 Roof Platform, Handrails and Gratings		**140h**	**10-Jul-14**	**27-Jul-14**
CZA-TK-0520-2870	Erection and Fit-up	40h	10-Jul-14	15-Jul-14
CZA-TK-0520-2880	Welding	100h	15-Jul-14	27-Jul-14
CZA-TK-0520-2890	Inspection	140h	10-Jul-14	27-Jul-14
CZA-14.3.9.7.20 Primary and Secondary Seal		**40h**	**27-Jul-14**	**31-Jul-14**
CZA-TK-0520-2900	Installation of Primary and Secondary Seal	30h	27-Jul-14	30-Jul-14
CZA-TK-0520-2910	Inspection	10h	30-Jul-14	31-Jul-14
CZA-14.3.9.4 Hydotest		**130h**	**31-Jul-14**	**16-Aug-14**
CZA-TK-0520-2920	Filling, Holding and Draining of Water	130h	31-Jul-14	16-Aug-14
CZA-14.3.9.5 Blasting and Painting		**70h**	**16-Aug-14**	**24-Aug-14**
CZA-TK-0520-2930	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	70h	16-Aug-14	24-Aug-14
CZA-14.3.9.6 Tank Calibration and Handover		**70h**	**24-Aug-14**	**01-Sep-14**
CZA-TK-0520-2940	Tank Calibration	50h	24-Aug-14	30-Aug-14
CZA-TK-0520-2950	Tank Handover	20h	30-Aug-14	01-Sep-14
CZA-14.3.10 S210-TK-0515(ENB Feed Tank Dia 13.54m x Ht 12.40m with IFR)		**1988h**	**09-Feb-14**	**28-Sep-14**
CZA-14.3.10.1 Fabrication Works		**264h**	**09-Feb-14**	**11-Mar-14**
CZA-TK-0515-2150	Cutting of Annular Plate	8h	09-Feb-14	09-Feb-14
CZA-TK-0515-2160	Cutting of Bottom Plates	8h	09-Feb-14	10-Feb-14
CZA-TK-0515-2170	Cutting, Bevelling & Rolling of Shell No.1	8h	10-Feb-14	11-Feb-14
CZA-TK-0515-2180	Cutting, Bevelling & Rolling of Shell No.2	8h	10-Feb-14	11-Feb-14
CZA-TK-0515-2190	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	40h	10-Feb-14	15-Feb-14
CZA-TK-0515-2200	Cutting of Floating Deck Plate	8h	15-Feb-14	16-Feb-14
CZA-TK-0515-2210	Cutting,Fit up and Welding of Pontoon	8h	16-Feb-14	17-Feb-14
CZA-TK-0515-2220	Cutting of Floating Legs and Manholes	8h	17-Feb-14	17-Feb-14
CZA-TK-0515-2230	Cutting, Bevelling & Rolling of Shell No.3	8h	18-Feb-14	18-Feb-14
CZA-TK-0515-2240	Cutting, Bevelling & Rolling of Shell No.4	8h	18-Feb-14	18-Feb-14
CZA-TK-0515-2250	Cutting, Bevelling & Rolling of Shell No.5	8h	18-Feb-14	19-Feb-14
CZA-TK-0515-2260	Cutting, Bevelling & Rolling of Shell No.6	10h	19-Feb-14	20-Feb-14
CZA-TK-0515-2270	Cutting, Bevelling & Rolling of Shell No.7	8h	19-Feb-14	20-Feb-14
CZA-TK-0515-2280	Cutting, Bevelling & Rolling of Curb Angle	16h	22-Feb-14	23-Feb-14
CZA-TK-0515-2290	Cutting, Fit-up and Welding of Roof Structure	32h	24-Feb-14	27-Feb-14

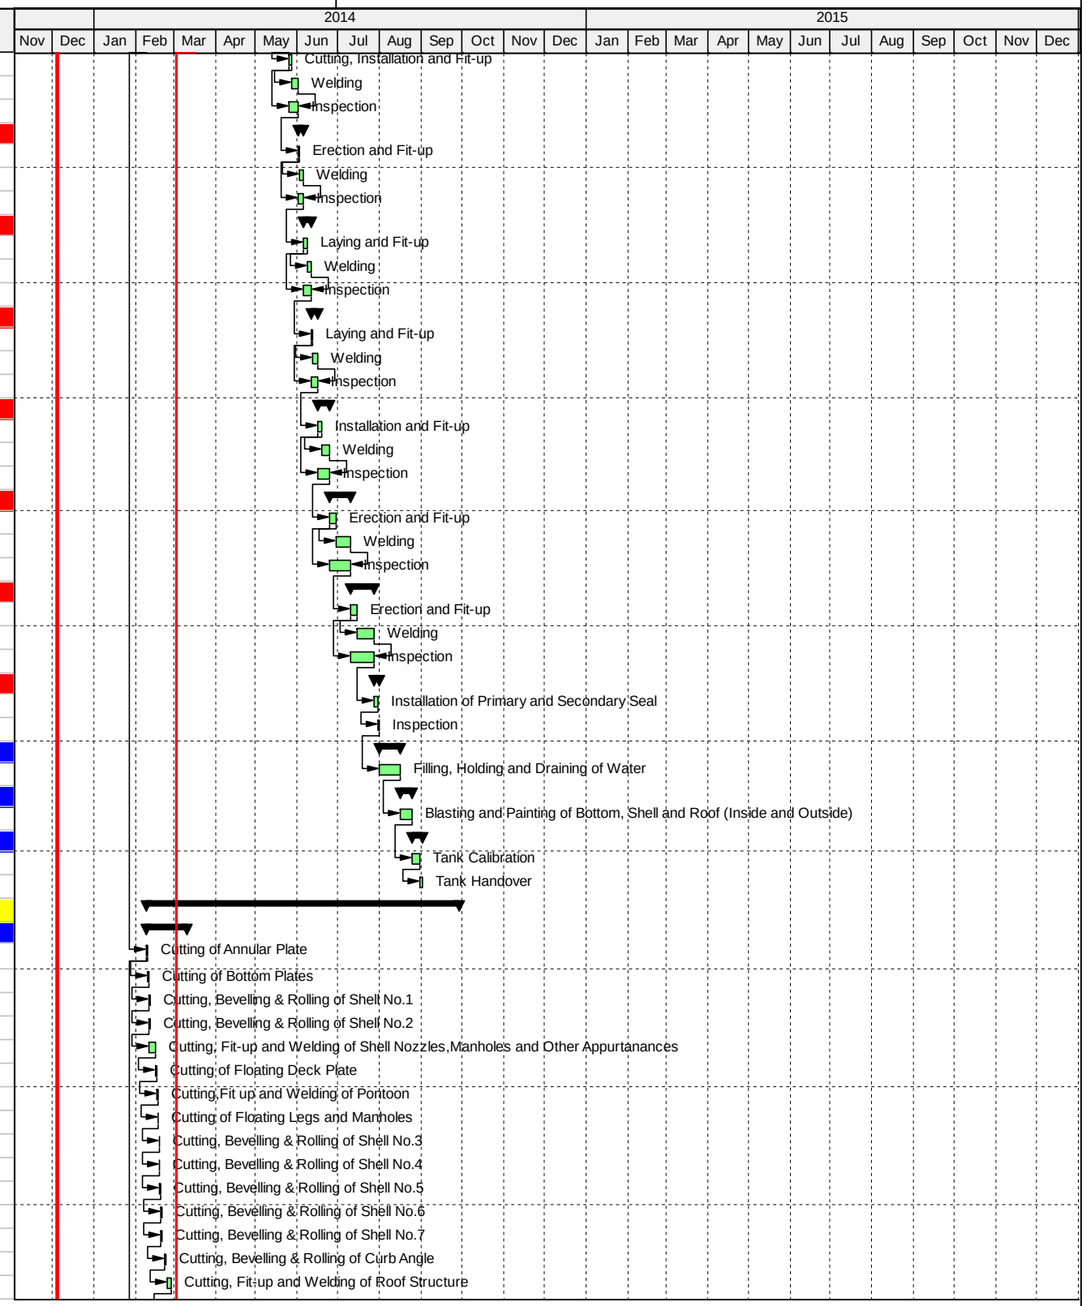

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0515-2510	Cutting of Roof Plates	8h	27-Feb-14	01-Mar-14
CZA-TK-0515-2520	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	01-Mar-14	05-Mar-14
CZA-TK-0515-2530	Cutting, Fit-up and Welding of Roof Platform,Gratings and Stairway	56h	04-Mar-14	10-Mar-14
CZA-TK-0515-2540	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	04-Mar-14	11-Mar-14
CZA-14.3.10.2 Foundation Takeover		**0h**	**15-Mar-14**	**15-Mar-14**
CZA-TK-0515-2300	Foundation Takeover from Client	0h	15-Mar-14	
CZA-14.3.10.7 Mechanical Erection		**1012h**	**15-Mar-14**	**10-Jul-14**
CZA-14.3.10.7.1 Annular Plates		**40h**	**15-Mar-14**	**19-Mar-14**
CZA-TK-0515-2310	Laying and Fit-up	10h	15-Mar-14	16-Mar-14
CZA-TK-0515-2320	Welding	30h	16-Mar-14	19-Mar-14
CZA-TK-0515-2330	Inspection	40h	15-Mar-14	19-Mar-14
CZA-14.3.10.7.19 Bottom Plates		**40h**	**19-Mar-14**	**24-Mar-14**
CZA-TK-0515-2340	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-0515-2350	Welding	30h	20-Mar-14	24-Mar-14
CZA-TK-0515-2360	Inspection	40h	19-Mar-14	24-Mar-14
CZA-14.3.10.7.2 Shell No.1		**40h**	**24-Mar-14**	**29-Mar-14**
CZA-TK-0515-2370	Erection and Fit-up	10h	24-Mar-14	25-Mar-14
CZA-TK-0515-2380	Welding	30h	25-Mar-14	29-Mar-14
CZA-TK-0515-2390	Inspection	40h	24-Mar-14	29-Mar-14
CZA-14.3.10.7.3 Shell No.2		**40h**	**29-Mar-14**	**02-Apr-14**
CZA-TK-0515-2400	Erection and Fit-up	10h	29-Mar-14	30-Mar-14
CZA-TK-0515-2410	Welding	30h	30-Mar-14	02-Apr-14
CZA-TK-0515-2420	Inspection	40h	29-Mar-14	02-Apr-14
CZA-14.3.10.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**60h**	**02-Apr-14**	**09-Apr-14**
CZA-TK-0515-2430	Cutting, Installation and Fit-up	20h	02-Apr-14	05-Apr-14
CZA-TK-0515-2440	Welding	40h	05-Apr-14	09-Apr-14
CZA-TK-0515-2450	Inspection	60h	02-Apr-14	09-Apr-14
CZA-14.3.10.7.5 Deck Plates		**80h**	**02-Apr-14**	**12-Apr-14**
CZA-TK-0515-2460	Laying & Fit-up	20h	02-Apr-14	05-Apr-14
CZA-TK-0515-2470	Welding	60h	05-Apr-14	12-Apr-14
CZA-TK-0515-2480	Inspection	80h	02-Apr-14	12-Apr-14
CZA-14.3.10.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		**100h**	**12-Apr-14**	**23-Apr-14**
CZA-TK-0515-2490	Cutting of All Holes, Laying and Fit-up	20h	12-Apr-14	14-Apr-14
CZA-TK-0515-2500	Welding of Sleeves and Plates	60h	14-Apr-14	21-Apr-14
CZA-TK-0515-2560	Installation of Leg Support	20h	21-Apr-14	23-Apr-14
CZA-TK-0515-2570	Inspection	100h	12-Apr-14	23-Apr-14
CZA-14.3.10.7.7 Shell No.3		**40h**	**05-Apr-14**	**09-Apr-14**
CZA-TK-0515-2580	Erection and Fit-up	10h	05-Apr-14	06-Apr-14
CZA-TK-0515-2590	Welding	30h	06-Apr-14	09-Apr-14
CZA-TK-0515-2600	Inspection	40h	05-Apr-14	09-Apr-14
CZA-14.3.10.7.8 Shell No.4		**40h**	**09-Apr-14**	**14-Apr-14**
CZA-TK-0515-2610	Erection and Fit-up	10h	09-Apr-14	10-Apr-14
CZA-TK-0515-2620	Welding	30h	10-Apr-14	14-Apr-14
CZA-TK-0515-2630	Inspection	40h	09-Apr-14	14-Apr-14
CZA-14.3.10.7.9 Shell No.5		**40h**	**14-Apr-14**	**19-Apr-14**
CZA-TK-0515-2640	Erection and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0515-2650	Welding	30h	15-Apr-14	19-Apr-14
CZA-TK-0515-2660	Inspection	40h	14-Apr-14	19-Apr-14
CZA-14.3.10.7.10 Shell No.6		**40h**	**19-Apr-14**	**23-Apr-14**
CZA-TK-0515-2670	Erection and Fit-up	10h	19-Apr-14	20-Apr-14
CZA-TK-0515-2680	Welding	30h	20-Apr-14	23-Apr-14
CZA-TK-0515-2690	Inspection	40h	19-Apr-14	23-Apr-14
CZA-14.3.10.7.11 Shell No.7		**40h**	**23-Apr-14**	**28-Apr-14**
CZA-TK-0515-2700	Erection and Fit-up	10h	23-Apr-14	24-Apr-14

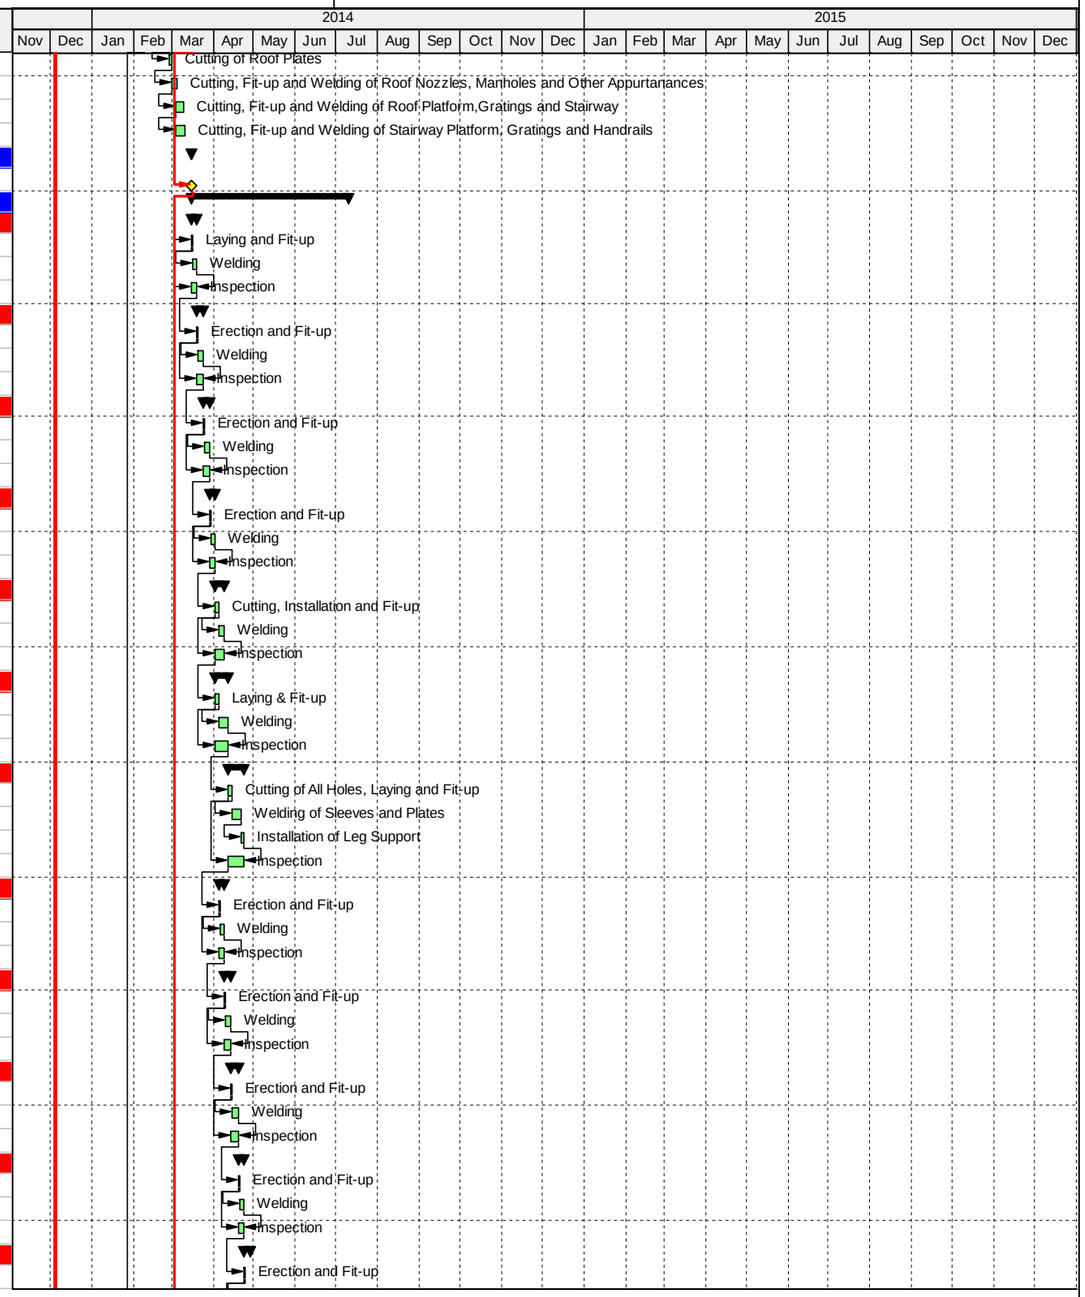

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0515-2710	Welding	30h	24-Apr-14	28-Apr-14
CZA-TK-0515-2720	Inspection	40h	23-Apr-14	28-Apr-14
CZA-14.3.10.7.12	**Shell Nozzles and attachements (Upper)**	70h	28-Apr-14	06-May-14
CZA-TK-0515-2730	Cutting, Installation and Fit-up	20h	28-Apr-14	30-Apr-14
CZA-TK-0515-2740	Welding	50h	30-Apr-14	06-May-14
CZA-TK-0515-2750	Inspection	70h	28-Apr-14	06-May-14
CZA-14.3.10.7.13	**Curb Angle**	40h	06-May-14	11-May-14
CZA-TK-0515-2760	Erection and Fit-up	10h	06-May-14	07-May-14
CZA-TK-0515-2770	Welding	30h	07-May-14	11-May-14
CZA-TK-0515-2780	Inspection	40h	06-May-14	11-May-14
CZA-14.3.10.7.14	**Roof Structure**	70h	11-May-14	19-May-14
CZA-TK-0515-2790	Laying and Fit-up	20h	11-May-14	13-May-14
CZA-TK-0515-2800	Welding	50h	13-May-14	19-May-14
CZA-TK-0515-2810	Inspection	70h	11-May-14	19-May-14
CZA-14.3.10.7.15	**Roof Plates**	50h	19-May-14	25-May-14
CZA-TK-0515-2820	Laying and Fit-up	10h	19-May-14	20-May-14
CZA-TK-0515-2830	Welding	40h	20-May-14	25-May-14
CZA-TK-0515-2840	Inspection	50h	19-May-14	25-May-14
CZA-14.3.10.7.16	**Roof Nozzles, Manholes and Other Appurtanances**	60h	25-May-14	01-Jun-14
CZA-TK-0515-2850	Installation and Fit-up	20h	25-May-14	27-May-14
CZA-TK-0515-2860	Welding	40h	27-May-14	01-Jun-14
CZA-TK-0515-2870	Inspection	60h	25-May-14	01-Jun-14
CZA-14.3.10.7.18	**Stairway Platform, Handrails and Gratings**	140h	26-May-14	11-Jun-14
CZA-TK-0515-2880	Erection and Fit-up	30h	26-May-14	29-May-14
CZA-TK-0515-2890	Welding	110h	29-May-14	11-Jun-14
CZA-TK-0515-2900	Inspection	140h	26-May-14	11-Jun-14
CZA-14.3.10.7.17	**Roof Platform, Handrails and Gratings**	140h	26-May-14	11-Jun-14
CZA-TK-0515-2910	Erection and Fit-up	30h	26-May-14	29-May-14
CZA-TK-0515-2920	Welding	110h	29-May-14	11-Jun-14
CZA-TK-0515-2930	Inspection	140h	26-May-14	11-Jun-14
CZA-14.3.10.7.20	**Installation of Primary and Secondary Seal**	40h	11-Jun-14	16-Jun-14
CZA-TK-0515-2940	Installation of Primary and Secondary Seal	40h	11-Jun-14	16-Jun-14
CZA-TK-0515-2950	Inspection	40h	11-Jun-14	16-Jun-14
CZA-14.3.10.7.21	**Insulation**	210h	16-Jun-14	10-Jul-14
CZA-TK-0515-2970	Insulation Works	200h	16-Jun-14	09-Jul-14
CZA-TK-0515-2980	Inspection	10h	09-Jul-14	10-Jul-14
CZA-14.3.10.4	**Hydotest**	410h	10-Jul-14	27-Aug-14
CZA-TK-0515-2990	Filling, Holding and Draining of Water	410h	10-Jul-14	27-Aug-14
CZA-14.3.10.5	**Blasting and Painting**	200h	27-Aug-14	20-Sep-14
CZA-TK-0515-3000	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	200h	27-Aug-14	20-Sep-14
CZA-14.3.10.6	**Tank Calibration and Handover**	70h	20-Sep-14	28-Sep-14
CZA-TK-0515-3010	Tank Calibration	50h	20-Sep-14	25-Sep-14
CZA-TK-0515-3020	Tank Handover	20h	25-Sep-14	28-Sep-14
CZA-14.3.11	**S210-TK-0521(Hexane Feed Tank Dia 15.48m x Ht 13.60m with IFR)**	3016h	09-Feb-14	26-Jan-15
CZA-14.3.11.1	**Fabrication Works**	290h	09-Feb-14	13-Mar-14
CZA-TK-0521-2580	Cutting of Annular Plate	8h	09-Feb-14	09-Feb-14
CZA-TK-0521-2590	Cutting of Bottom Plates	8h	09-Feb-14	10-Feb-14
CZA-TK-0521-2600	Cutting, Bevelling & Rolling of Shell No.1	8h	10-Feb-14	11-Feb-14
CZA-TK-0521-2610	Cutting, Bevelling & Rolling of Shell No.2	8h	10-Feb-14	11-Feb-14
CZA-TK-0521-2620	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	40h	10-Feb-14	15-Feb-14
CZA-TK-0521-2630	Cutting of Floating Deck Plate	8h	15-Feb-14	16-Feb-14
CZA-TK-0521-2640	Cutting,Fit up and Welding of Pontoon	8h	16-Feb-14	17-Feb-14
CZA-TK-0521-2650	Cutting of Floating Legs and Manholes	8h	17-Feb-14	17-Feb-14
CZA-TK-0521-2660	Cutting, Bevelling & Rolling of Shell No.3	8h	18-Feb-14	18-Feb-14

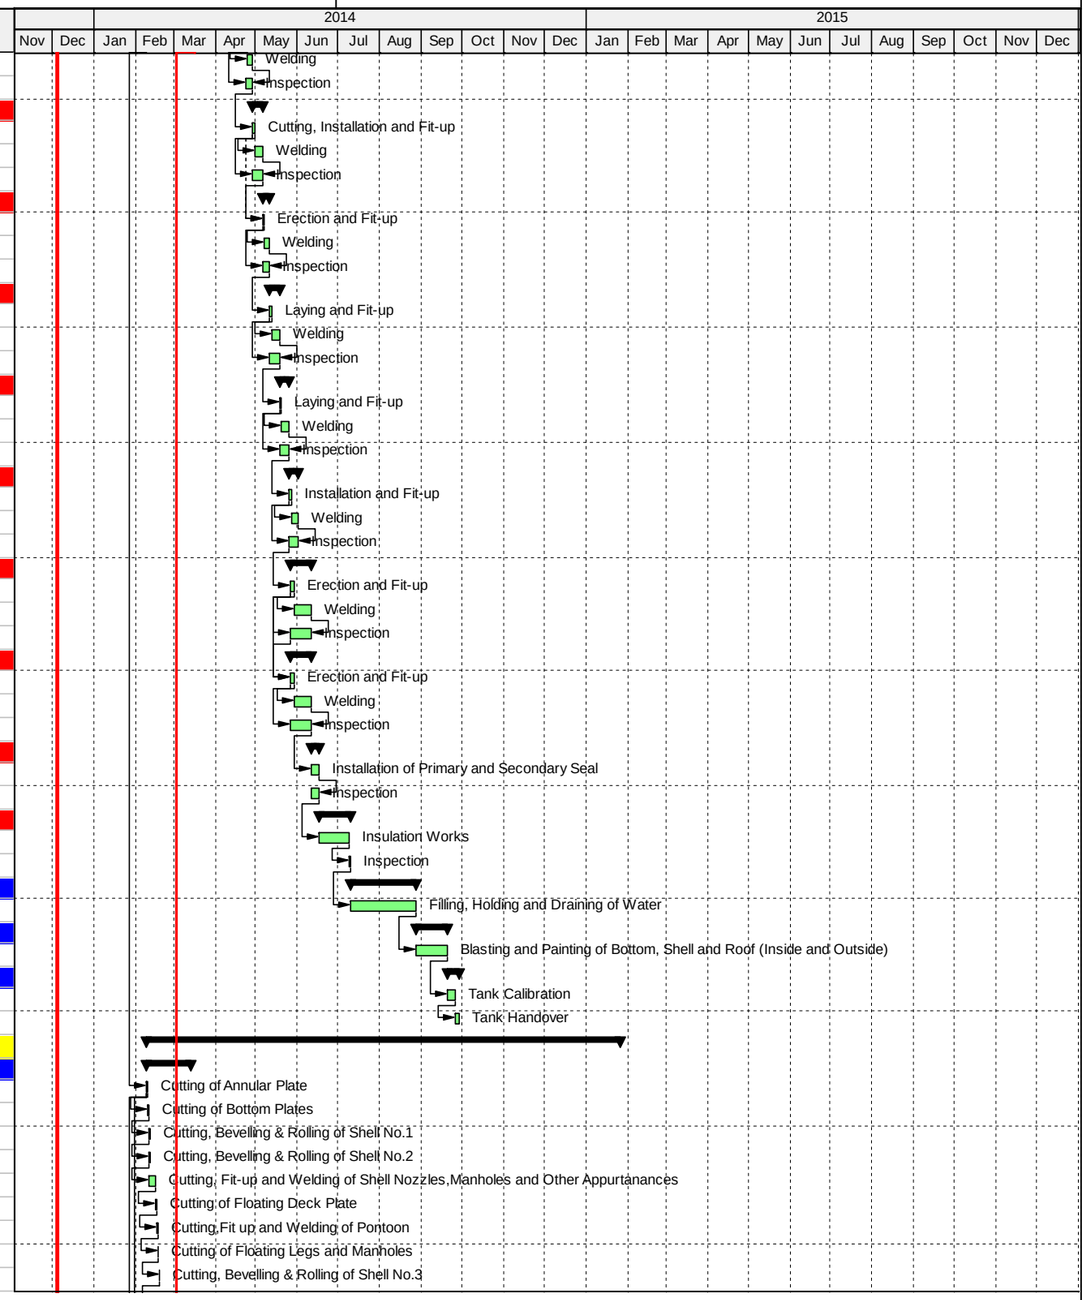

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0521-2670	Cutting, Bevelling & Rolling of Shell No.4	8h	18-Feb-14	18-Feb-14
CZA-TK-0521-2680	Cutting, Bevelling & Rolling of Shell No.5	8h	18-Feb-14	19-Feb-14
CZA-TK-0521-2690	Cutting, Bevelling & Rolling of Shell No.6	10h	19-Feb-14	20-Feb-14
CZA-TK-0521-2700	Cutting, Bevelling & Rolling of Curb Angle	16h	20-Feb-14	23-Feb-14
CZA-TK-0521-2710	Cutting, Fit-up and Welding of Roof Structure	32h	24-Feb-14	27-Feb-14
CZA-TK-0521-2920	Cutting of Roof Plates	16h	27-Feb-14	01-Mar-14
CZA-TK-0521-2930	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	01-Mar-14	05-Mar-14
CZA-TK-0521-2940	Cutting, Fit-up and Welding of Roof Platform,Gratings and Stairway	56h	05-Mar-14	11-Mar-14
CZA-TK-0521-2950	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails	56h	08-Mar-14	13-Mar-14
CZA-14.3.11.2 Foundation Takeover		**0h**	**15-Mar-14**	**15-Mar-14**
CZA-TK-0521-2720	Foundation Takeover from Client	0h	15-Mar-14	
CZA-14.3.11.7 Mechanical Erection		**2470h**	**15-Mar-14**	**28-Dec-14**
CZA-14.3.11.7.1 Annular Plates		**40h**	**15-Mar-14**	**19-Mar-14**
CZA-TK-0521-2960	Laying and Fit-up	10h	15-Mar-14	16-Mar-14
CZA-TK-0521-2970	Welding	30h	16-Mar-14	19-Mar-14
CZA-TK-0521-2980	Inspection	40h	15-Mar-14	19-Mar-14
CZA-14.3.11.7.19 Bottom Plates		**50h**	**19-Mar-14**	**25-Mar-14**
CZA-TK-0521-2990	Erection and Fit-up	10h	19-Mar-14	20-Mar-14
CZA-TK-0521-3000	Welding	40h	20-Mar-14	25-Mar-14
CZA-TK-0521-3010	Inspection	50h	19-Mar-14	25-Mar-14
CZA-14.3.11.7.2 Shell No.1		**40h**	**25-Mar-14**	**30-Mar-14**
CZA-TK-0521-3020	Erection and Fit-up	10h	25-Mar-14	26-Mar-14
CZA-TK-0521-3030	Welding	30h	26-Mar-14	30-Mar-14
CZA-TK-0521-3040	Inspection	40h	25-Mar-14	30-Mar-14
CZA-14.3.11.7.3 Shell No.2		**40h**	**30-Mar-14**	**03-Apr-14**
CZA-TK-0521-3050	Erection and Fit-up	10h	30-Mar-14	31-Mar-14
CZA-TK-0521-3060	Welding	30h	31-Mar-14	03-Apr-14
CZA-TK-0521-3070	Inspection	40h	30-Mar-14	03-Apr-14
CZA-14.3.11.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**50h**	**03-Apr-14**	**09-Apr-14**
CZA-TK-0521-3080	Cutting, Installation and Fit-up	20h	03-Apr-14	06-Apr-14
CZA-TK-0521-3090	Welding	30h	06-Apr-14	09-Apr-14
CZA-TK-0521-3100	Inspection	50h	03-Apr-14	09-Apr-14
CZA-14.3.11.7.5 Deck Plates		**90h**	**09-Apr-14**	**20-Apr-14**
CZA-TK-0521-3110	Laying & Fit-up	20h	09-Apr-14	12-Apr-14
CZA-TK-0521-3120	Welding	70h	12-Apr-14	20-Apr-14
CZA-TK-0521-3130	Inspection	90h	09-Apr-14	20-Apr-14
CZA-14.3.11.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		**1400h**	**20-Apr-14**	**30-Sep-14**
CZA-TK-0521-3140	Cutting of All Holes, Laying & Fit-up	30h	20-Apr-14	23-Apr-14
CZA-TK-0521-3150	Welding of Sleeves and Plates	100h	23-Apr-14	05-May-14
CZA-TK-0521-3160	Installation of Leg Support	10h	05-May-14	06-May-14
CZA-TK-0521-3170	Inspection	1400h	20-Apr-14	30-Sep-14
CZA-14.3.11.7.7 Shell No.3		**40h**	**30-Sep-14**	**05-Oct-14**
CZA-TK-0521-3180	Erection and Fit-up	10h	30-Sep-14	01-Oct-14
CZA-TK-0521-3190	Welding	30h	01-Oct-14	05-Oct-14
CZA-TK-0521-3200	Inspection	40h	30-Sep-14	05-Oct-14
CZA-14.3.11.7.8 Shell No.4		**40h**	**05-Oct-14**	**09-Oct-14**
CZA-TK-0521-3210	Erection and Fit-up	10h	05-Oct-14	06-Oct-14
CZA-TK-0521-3220	Welding	30h	06-Oct-14	09-Oct-14
CZA-TK-0521-3230	Inspection	40h	05-Oct-14	09-Oct-14
CZA-14.3.11.7.9 Shell No.5		**40h**	**09-Oct-14**	**14-Oct-14**
CZA-TK-0521-3240	Erection and Fit-up	10h	09-Oct-14	11-Oct-14
CZA-TK-0521-3250	Welding	30h	11-Oct-14	14-Oct-14
CZA-TK-0521-3260	Inspection	40h	09-Oct-14	14-Oct-14
CZA-14.3.11.7.10 Shell No.6		**40h**	**14-Oct-14**	**19-Oct-14**

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0521-3270	Erection and Fit-up	10h	14-Oct-14	15-Oct-14
CZA-TK-0521-3280	Welding	30h	15-Oct-14	19-Oct-14
CZA-TK-0521-3290	Inspection	40h	14-Oct-14	19-Oct-14
CZA-14.3.11.7.12 Shell Nozzles and attachements (Upper)		70h	19-Oct-14	27-Oct-14
CZA-TK-0521-3300	Cutting, Installation and Fit-up	20h	19-Oct-14	21-Oct-14
CZA-TK-0521-3310	Welding	50h	21-Oct-14	27-Oct-14
CZA-TK-0521-3320	Inspection	70h	19-Oct-14	27-Oct-14
CZA-14.3.11.7.13 Curb Angle		40h	27-Oct-14	01-Nov-14
CZA-TK-0521-3330	Erection and Fit-up	10h	27-Oct-14	28-Oct-14
CZA-TK-0521-3340	Welding	30h	28-Oct-14	01-Nov-14
CZA-TK-0521-3350	Inspection	40h	27-Oct-14	01-Nov-14
CZA-14.3.11.7.14 Roof Structure		60h	01-Nov-14	08-Nov-14
CZA-TK-0521-3360	Laying and Fit-up	20h	01-Nov-14	03-Nov-14
CZA-TK-0521-3370	Welding	40h	03-Nov-14	08-Nov-14
CZA-TK-0521-3380	Inspection	60h	01-Nov-14	08-Nov-14
CZA-14.3.11.7.15 Roof Plates		40h	08-Nov-14	12-Nov-14
CZA-TK-0521-3390	Laying and Fit-up	10h	08-Nov-14	09-Nov-14
CZA-TK-0521-3400	Welding	30h	09-Nov-14	12-Nov-14
CZA-TK-0521-3410	Inspection	40h	08-Nov-14	12-Nov-14
CZA-14.3.11.7.16 Roof Nozzles, Manholes and Other Appurtanances		70h	12-Nov-14	20-Nov-14
CZA-TK-0521-3420	Installation and Fit-up	20h	12-Nov-14	15-Nov-14
CZA-TK-0521-3430	Welding	50h	15-Nov-14	20-Nov-14
CZA-TK-0521-3440	Inspection	70h	12-Nov-14	20-Nov-14
CZA-14.3.11.7.18 Stairway Platform, Handrails and Gratings		140h	20-Nov-14	07-Dec-14
CZA-TK-0521-3480	Erection and Fit-up	40h	20-Nov-14	25-Nov-14
CZA-TK-0521-3490	Welding	100h	25-Nov-14	07-Dec-14
CZA-TK-0521-3500	Inspection	140h	20-Nov-14	07-Dec-14
CZA-14.3.11.7.17 Roof Platform, Handrails and Gratings		140h	07-Dec-14	23-Dec-14
CZA-TK-0521-3450	Erection and Fit-up	40h	07-Dec-14	11-Dec-14
CZA-TK-0521-3460	Welding	100h	11-Dec-14	23-Dec-14
CZA-TK-0521-3470	Inspection	140h	07-Dec-14	23-Dec-14
CZA-14.3.11.7.20 Primary and Secondary Seal		40h	23-Dec-14	28-Dec-14
CZA-TK-0521-3510	Installation of Primary and Secondary Seal	30h	23-Dec-14	27-Dec-14
CZA-TK-0521-3520	Inspection	10h	27-Dec-14	28-Dec-14
CZA-14.3.11.4 Hydotest		120h	28-Dec-14	11-Jan-15
CZA-TK-0521-3530	Filling, Holding and Draining of Water	120h	28-Dec-14	11-Jan-15
CZA-14.3.11.5 Blasting and Painting		60h	11-Jan-15	18-Jan-15
CZA-TK-0521-3540	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	60h	11-Jan-15	18-Jan-15
CZA-14.3.11.6 Tank Calibration and Handover		70h	18-Jan-15	26-Jan-15
CZA-TK-0521-3550	Tank Calibration	50h	18-Jan-15	24-Jan-15
CZA-TK-0521-3560	Tank Handover	20h	24-Jan-15	26-Jan-15
CZA-14.3.12 S210-TK-0605(Benzene Product Tank Dia 29.02m x Ht 19.2m with IFR)		2460h	13-Feb-14	26-Nov-14
CZA-14.3.12.1 Fabrication Works		368h	13-Feb-14	27-Mar-14
CZA-TK-0605-1480	Cutting of Annular Plates and Bottom Plates	8h	13-Feb-14	13-Feb-14
CZA-TK-0605-1490	Cutting,Bevelling & Rolling Shell No. 7	8h	13-Feb-14	15-Feb-14
CZA-TK-0605-1500	Cutting , Beveling & Rolling Shell No.8	8h	15-Feb-14	16-Feb-14
CZA-TK-0605-1510	Cutting, Fit-up and Weld of Stairway Platform, gratings Handrails (Upper Part)	40h	16-Feb-14	20-Feb-14
CZA-TK-0605-1520	Cutting of Floating Roof Plates	32h	18-Feb-14	22-Feb-14
CZA-TK-0605-1530	Cutting, Fit-up and Welding of Pontoon	56h	19-Feb-14	26-Feb-14
CZA-TK-0605-1540	Cutting of Floating Roof Legs and Manholes	80h	19-Feb-14	01-Mar-14
CZA-TK-0605-1550	Cutting, Fit-up and Welding of Roof Structure	40h	01-Mar-14	05-Mar-14
CZA-TK-0605-1560	Cutting of Compression Ring	16h	05-Mar-14	08-Mar-14
CZA-TK-0605-1570	Cutting of Roof Plates	8h	08-Mar-14	08-Mar-14
CZA-TK-0605-1580	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	56h	09-Mar-14	15-Mar-14

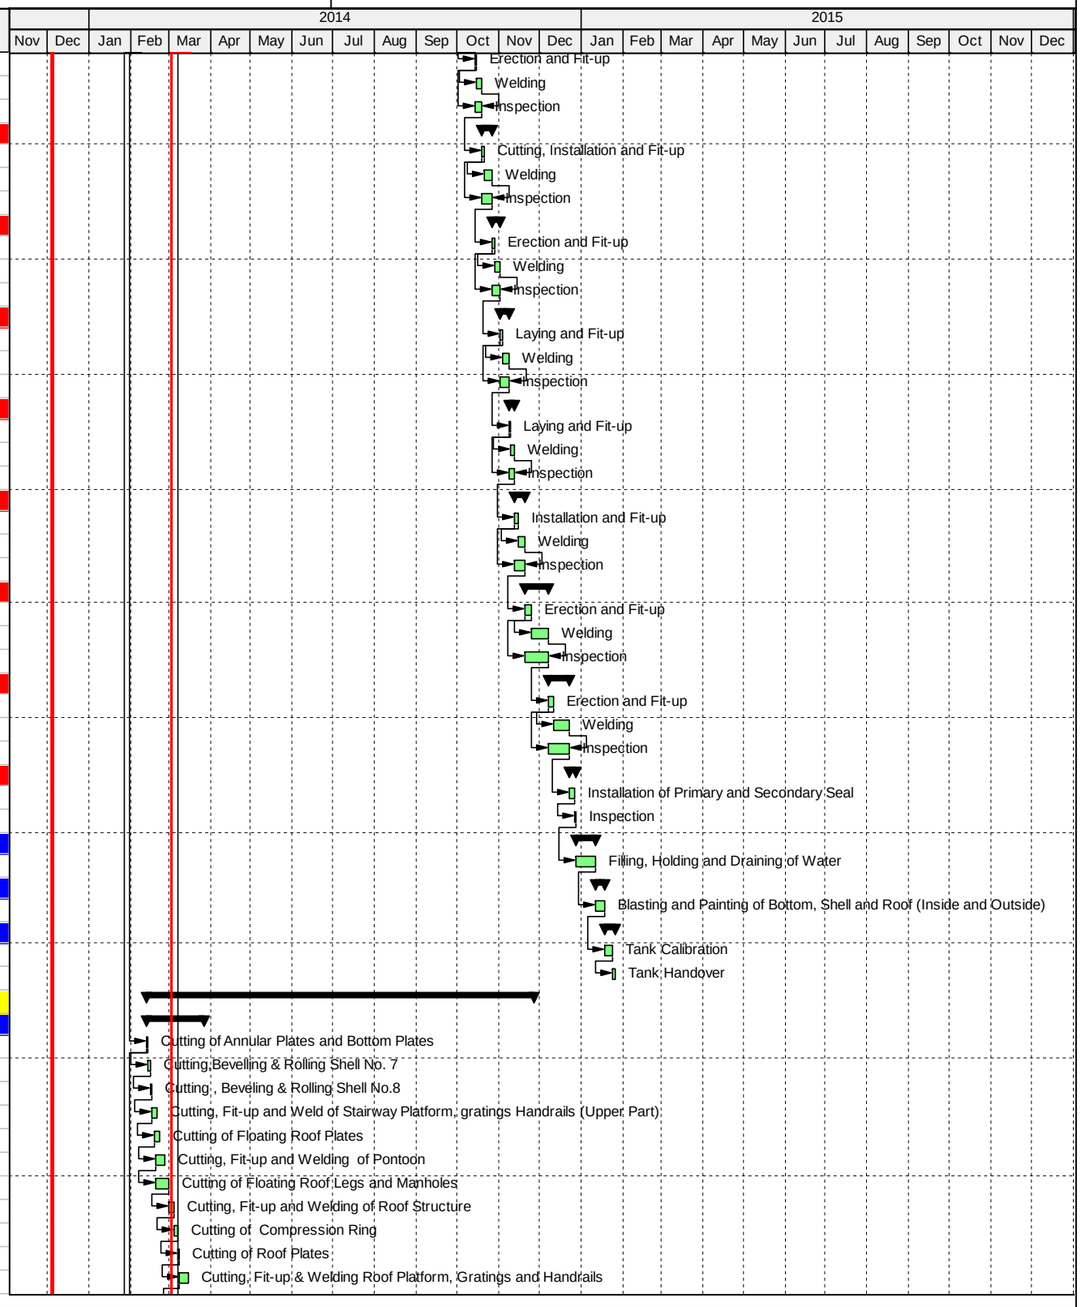

- Actual Level of Effort
- summary
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0605-1590	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	56h	10-Mar-14	17-Mar-14
CZA-TK-0605-1600	Cutting , Beveling & Rolling Shell No.6	8h	17-Mar-14	17-Mar-14
CZA-TK-0605-1610	Cutting , Beveling & Rolling Shell No.5	8h	17-Mar-14	17-Mar-14
CZA-TK-0605-1620	Cutting , Beveling & Rolling Shell No.4	8h	18-Mar-14	18-Mar-14
CZA-TK-0605-1630	Cutting , Beveling & Rolling Shell No.3	8h	19-Mar-14	20-Mar-14
CZA-TK-0605-1640	Cutting , Beveling & Rolling Shell No.2	8h	19-Mar-14	20-Mar-14
CZA-TK-0605-1900	Cutting , Beveling & Rolling Shell No.1	8h	20-Mar-14	22-Mar-14
CZA-TK-0605-1910	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	56h	22-Mar-14	27-Mar-14
CZA-TK-0605-1920	Cutting, Fit-up and Weld of Stairway Platform, gratings Handrails (Upper Part)	40h	22-Mar-14	26-Mar-14
CZA-14.3.12.2 FoundationTakeover		**0h**	**20-Mar-14**	**20-Mar-14**
CZA-TK-0605-1650	Foundation Takeover From Client	0h	20-Mar-14	
CZA-14.3.12.7 Mechanical Erection		**1496h**	**20-Mar-14**	**10-Sep-14**
CZA-14.3.12.7.1 Annular Plates		**50h**	**20-Mar-14**	**26-Mar-14**
CZA-TK-0605-1930	Laying and Fit-up	10h	20-Mar-14	22-Mar-14
CZA-TK-0605-1940	Welding	40h	22-Mar-14	26-Mar-14
CZA-TK-0605-1950	Inspection	50h	20-Mar-14	26-Mar-14
CZA-14.3.12.7.2 Bottom Plates		**100h**	**26-Mar-14**	**07-Apr-14**
CZA-TK-0605-1960	Laying and Fit-up	30h	26-Mar-14	30-Mar-14
CZA-TK-0605-1970	Welding	70h	30-Mar-14	07-Apr-14
CZA-TK-0605-1980	Inspection	100h	26-Mar-14	07-Apr-14
CZA-14.3.12.7.3 Shell No.7		**60h**	**07-Apr-14**	**14-Apr-14**
CZA-TK-0605-1990	Erection and Fit-up	10h	07-Apr-14	08-Apr-14
CZA-TK-0605-2000	Welding	50h	08-Apr-14	14-Apr-14
CZA-TK-0605-2010	Inspection	60h	07-Apr-14	14-Apr-14
CZA-14.3.12.7.4 Shell No.8		**60h**	**14-Apr-14**	**21-Apr-14**
CZA-TK-0605-2020	Erection and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0605-2030	Welding	50h	15-Apr-14	21-Apr-14
CZA-TK-0605-2040	Inspection	60h	14-Apr-14	21-Apr-14
CZA-14.3.12.7.5 Shell Nozzles and Other Attachments		**70h**	**21-Apr-14**	**29-Apr-14**
CZA-TK-0605-2050	Cutting, Installation and Fit-up	20h	21-Apr-14	23-Apr-14
CZA-TK-0605-2060	Welding	50h	23-Apr-14	29-Apr-14
CZA-TK-0605-2070	Inspection	70h	21-Apr-14	29-Apr-14
CZA-14.3.12.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**50h**	**21-Apr-14**	**27-Apr-14**
CZA-TK-0605-2080	Erection and Fit-up	20h	21-Apr-14	23-Apr-14
CZA-TK-0605-2090	Welding	30h	23-Apr-14	27-Apr-14
CZA-TK-0605-2100	Inspection	50h	21-Apr-14	27-Apr-14
CZA-14.3.12.7.7 Deck Plate		**100h**	**27-Apr-14**	**08-May-14**
CZA-TK-0605-2110	Laying and Fit-up	20h	27-Apr-14	29-Apr-14
CZA-TK-0605-2120	Welding	80h	29-Apr-14	08-May-14
CZA-TK-0605-2130	Inspection	100h	27-Apr-14	08-May-14
CZA-14.3.12.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**140h**	**08-May-14**	**25-May-14**
CZA-TK-0605-2140	Laying, Cutting all Holes and Fit-up	40h	08-May-14	13-May-14
CZA-TK-0605-2150	Welding	100h	08-May-14	20-May-14
CZA-TK-0605-2160	Inspection	140h	08-May-14	25-May-14
CZA-14.3.12.7.9 Roof Structure		**70h**	**25-May-14**	**02-Jun-14**
CZA-TK-0605-2170	Erection and Fit-up	20h	25-May-14	27-May-14
CZA-TK-0605-2180	Welding	50h	27-May-14	02-Jun-14
CZA-TK-0605-2190	Inspection	70h	25-May-14	02-Jun-14
CZA-14.3.12.7.10 Roof Plates		**70h**	**02-Jun-14**	**10-Jun-14**
CZA-TK-0605-2200	Laying and Fit-up	20h	02-Jun-14	04-Jun-14
CZA-TK-0605-2210	Welding	50h	04-Jun-14	10-Jun-14
CZA-TK-0605-2220	Inspection	70h	02-Jun-14	10-Jun-14
CZA-14.3.12.7.11 Compression Ring		**50h**	**10-Jun-14**	**16-Jun-14**
CZA-TK-0605-2230	Laying and Fit-up	10h	10-Jun-14	11-Jun-14

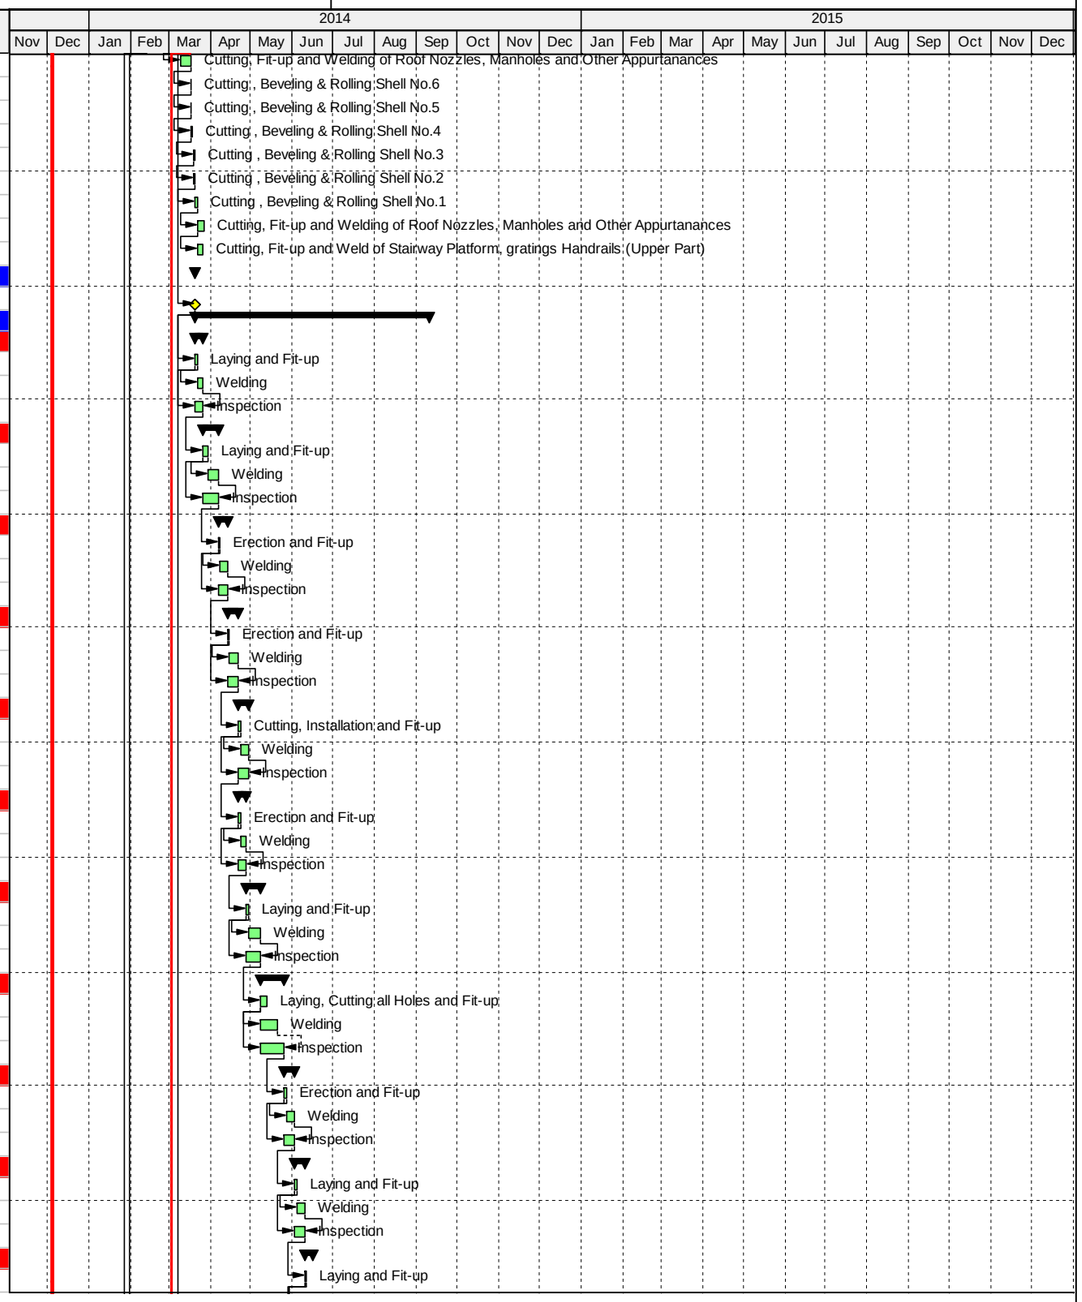

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0605-2240	Welding	40h	11-Jun-14	16-Jun-14
CZA-TK-0605-2250	Inspection	50h	10-Jun-14	16-Jun-14
CZA-14.3.12.7.12 Roof Nozzles, Manholes and Other Appurtanances		70h	16-Jun-14	24-Jun-14
CZA-TK-0605-2260	Cutting,Installation and Fit-up	20h	16-Jun-14	18-Jun-14
CZA-TK-0605-2270	Welding	50h	18-Jun-14	24-Jun-14
CZA-TK-0605-2280	Inspection	70h	16-Jun-14	24-Jun-14
CZA-14.3.12.7.13 Roof Platform, Gratings and Handrails		140h	16-Jun-14	02-Jul-14
CZA-TK-0605-2290	Erection and Fit-up	40h	16-Jun-14	21-Jun-14
CZA-TK-0605-2300	Welding	100h	21-Jun-14	02-Jul-14
CZA-TK-0605-2310	Inspection	140h	16-Jun-14	02-Jul-14
CZA-14.3.12.7.14 Shell No.6		60h	02-Jul-14	09-Jul-14
CZA-TK-0605-2320	Jacking, Erection and Fit-up	10h	02-Jul-14	03-Jul-14
CZA-TK-0605-2330	Welding	50h	03-Jul-14	09-Jul-14
CZA-TK-0605-2340	Inspection	60h	02-Jul-14	09-Jul-14
CZA-14.3.12.7.15 Shell No.5		60h	09-Jul-14	16-Jul-14
CZA-TK-0605-2350	Jacking,Erection and Fit-up	10h	09-Jul-14	10-Jul-14
CZA-TK-0605-2360	Welding	50h	10-Jul-14	16-Jul-14
CZA-TK-0605-2370	Inspection	60h	09-Jul-14	16-Jul-14
CZA-14.3.12.7.16 Shell No.4		60h	16-Jul-14	23-Jul-14
CZA-TK-0605-2380	Jacking,Erection and Fit-up	10h	16-Jul-14	17-Jul-14
CZA-TK-0605-2390	Welding	50h	17-Jul-14	23-Jul-14
CZA-TK-0605-2400	Inspection	60h	16-Jul-14	23-Jul-14
CZA-14.3.12.7.17 Shell No.3		60h	23-Jul-14	30-Jul-14
CZA-TK-0605-2410	Jacking, Erection and Fit-up	10h	23-Jul-14	24-Jul-14
CZA-TK-0605-2420	Welding	50h	24-Jul-14	30-Jul-14
CZA-TK-0605-2430	Inspection	60h	23-Jul-14	30-Jul-14
CZA-14.3.12.7.18 Shell No.2		60h	30-Jul-14	06-Aug-14
CZA-TK-0605-2440	Jacking, Erection and Fit-up	10h	30-Jul-14	31-Jul-14
CZA-TK-0605-2450	Welding	50h	31-Jul-14	06-Aug-14
CZA-TK-0605-2560	Inspection	60h	30-Jul-14	06-Aug-14
CZA-14.3.12.7.19 Shell No.1		60h	06-Aug-14	13-Aug-14
CZA-TK-0605-2570	Jacking, Erection and Fit-up	10h	06-Aug-14	07-Aug-14
CZA-TK-0605-2580	Welding	50h	07-Aug-14	13-Aug-14
CZA-TK-0605-2590	Inspection	60h	06-Aug-14	13-Aug-14
CZA-14.3.12.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		80h	13-Aug-14	23-Aug-14
CZA-TK-0605-2600	Lay-out, Cutting, and Fit-up	30h	13-Aug-14	17-Aug-14
CZA-TK-0605-2610	Welding	50h	17-Aug-14	23-Aug-14
CZA-TK-0605-2620	Inspection	80h	13-Aug-14	23-Aug-14
CZA-14.3.12.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		140h	20-Aug-14	04-Sep-14
CZA-TK-0605-2630	Erection and Fit-up	40h	20-Aug-14	24-Aug-14
CZA-TK-0605-2640	Welding	100h	25-Aug-14	04-Sep-14
CZA-TK-0605-2650	Inspection	140h	20-Aug-14	04-Sep-14
CZA-14.3.12.7.24 Primary and Secondary Seal		50h	06-Sep-14	10-Sep-14
CZA-TK-0605-2660	Installation of Primary and Secondary Seal	40h	06-Sep-14	09-Sep-14
CZA-TK-0605-2670	Inspection	10h	10-Sep-14	10-Sep-14
CZA-14.3.12.4 Hydrotest		400h	11-Sep-14	27-Oct-14
CZA-TK-0605-2680	Filling, Holding and Draining of Water	400h	11-Sep-14	27-Oct-14
CZA-14.3.12.5 Blasting and Painting		200h	28-Oct-14	19-Nov-14
CZA-TK-0605-2690	Blasting and Painting Inside, Outside and Bottom Plates	200h	28-Oct-14	19-Nov-14
CZA-14.3.12.6 Tank Calibration and Handover		60h	20-Nov-14	26-Nov-14
CZA-TK-0605-2700	Tank Calibration	50h	20-Nov-14	25-Nov-14
CZA-TK-0605-2710	Tank Handover	10h	26-Nov-14	26-Nov-14
CZA-14.3.13 S210-TK-0606(Benzene Product Tank Dia 29.02m x Ht 19.2m with IFR)		2394h	13-Feb-14	19-Nov-14
CZA-14.3.13.1 Fabrication Works		368h	13-Feb-14	27-Mar-14

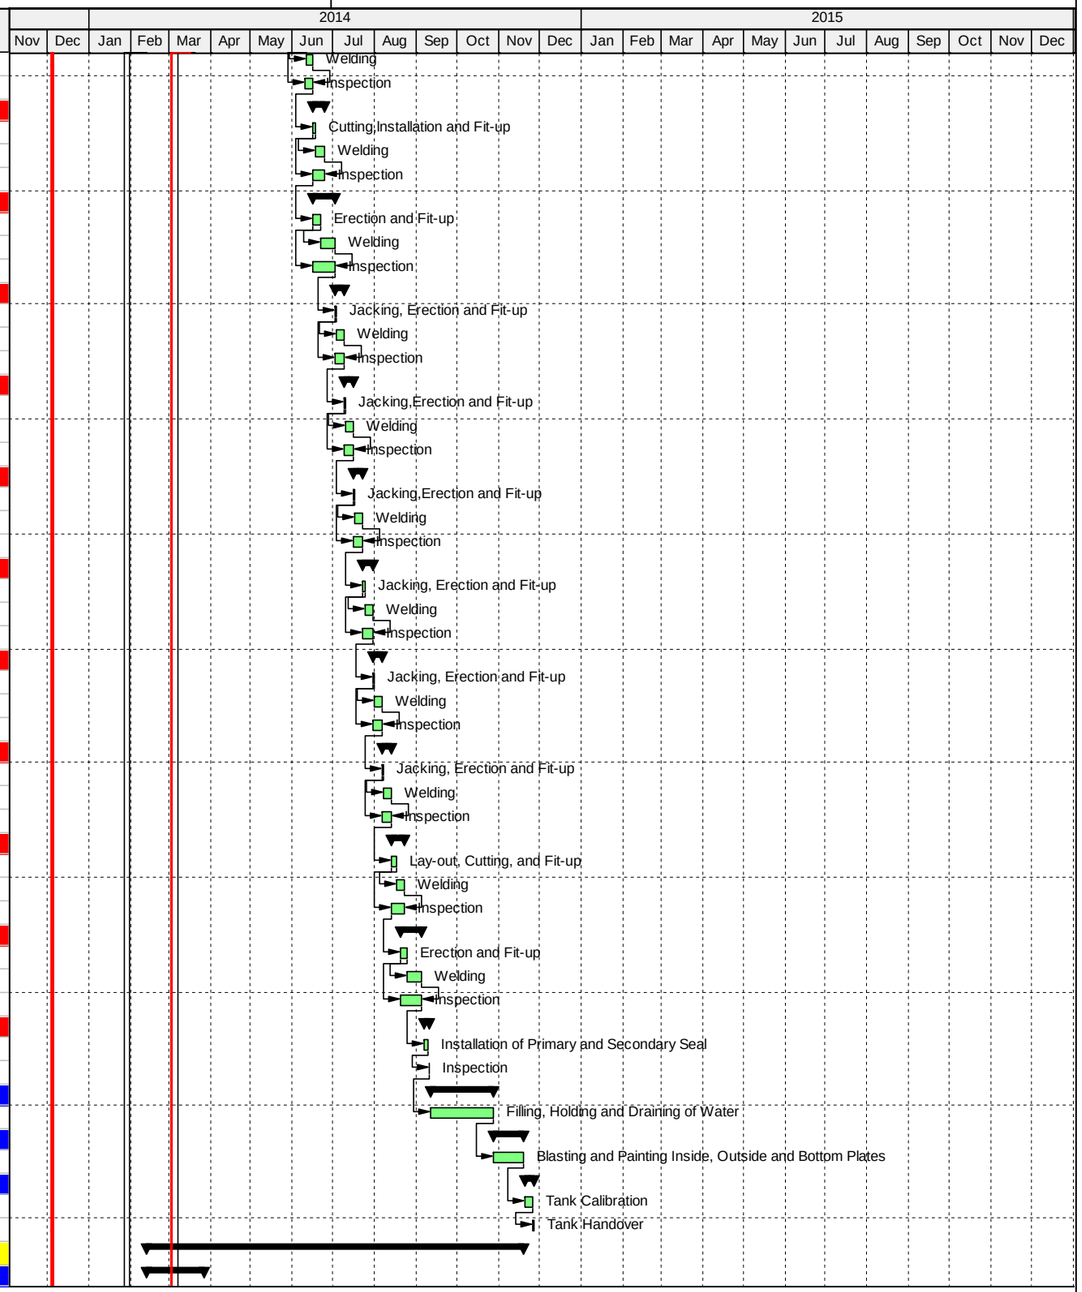

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0606-1880	Cutting of Annular Plates and Bottom Plates	8h	13-Feb-14	13-Feb-14
CZA-TK-0606-1890	Cutting,Bevelling & Rolling Shell No. 7	8h	13-Feb-14	15-Feb-14
CZA-TK-0606-1900	Cutting , Beveling & Rolling Shell No.8	8h	15-Feb-14	16-Feb-14
CZA-TK-0606-1910	Cutting, Fit-up and Weld of Stairway Platform, gratings Handrails (Upper Part)	48h	16-Feb-14	22-Feb-14
CZA-TK-0606-1920	Cutting of Floating Roof Plates	32h	18-Feb-14	22-Feb-14
CZA-TK-0606-1930	Cutting, Fit-up and Welding of Pontoon	56h	23-Feb-14	01-Mar-14
CZA-TK-0606-1940	Cutting of Floating Roof Legs and Manholes	80h	23-Feb-14	03-Mar-14
CZA-TK-0606-1950	Cutting, Fit-up and Welding of Roof Structure	40h	23-Feb-14	27-Feb-14
CZA-TK-0606-1960	Cutting of Roof Plates	16h	27-Feb-14	02-Mar-14
CZA-TK-0606-1970	Cutting of Compression Ring	8h	02-Mar-14	03-Mar-14
CZA-TK-0606-1980	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	56h	03-Mar-14	09-Mar-14
CZA-TK-0606-1990	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	56h	09-Mar-14	16-Mar-14
CZA-TK-0606-2000	Cutting , Beveling & Rolling Shell No.6	8h	16-Mar-14	17-Mar-14
CZA-TK-0606-2010	Cutting , Beveling & Rolling Shell No.5	8h	17-Mar-14	17-Mar-14
CZA-TK-0606-2020	Cutting , Beveling & Rolling Shell No.4	8h	18-Mar-14	18-Mar-14
CZA-TK-0606-2030	Cutting , Beveling & Rolling Shell No.3	8h	19-Mar-14	20-Mar-14
CZA-TK-0606-2040	Cutting , Beveling & Rolling Shell No.2 & 1	8h	20-Mar-14	22-Mar-14
CZA-TK-0606-2290	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	56h	22-Mar-14	27-Mar-14
CZA-TK-0606-2300	Cutting, Fit-up and Weld of Stairway Platform, gratings Handrails (Upper Part)	40h	23-Mar-14	27-Mar-14
CZA-14.3.13.2 FoundationTakeover		**0h**	**20-Mar-14**	**20-Mar-14**
CZA-TK-0606-2050	Foundation Takeover From Client	0h	20-Mar-14	
CZA-14.3.13.7 Mechanical Erection		**1520h**	**20-Mar-14**	**14-Sep-14**
CZA-14.3.13.7.1 Annular Plates		**50h**	**20-Mar-14**	**26-Mar-14**
CZA-TK-0606-2310	Laying and Fit-up	10h	20-Mar-14	22-Mar-14
CZA-TK-0606-2320	Welding	40h	22-Mar-14	26-Mar-14
CZA-TK-0606-2330	Inspection	50h	20-Mar-14	26-Mar-14
CZA-14.3.13.7.2 Bottom Plates		**100h**	**26-Mar-14**	**07-Apr-14**
CZA-TK-0606-2340	Laying and Fit-up	30h	26-Mar-14	30-Mar-14
CZA-TK-0606-2350	Welding	70h	30-Mar-14	07-Apr-14
CZA-TK-0606-2360	Inspection	100h	26-Mar-14	07-Apr-14
CZA-14.3.13.7.3 Shell No.7		**60h**	**07-Apr-14**	**14-Apr-14**
CZA-TK-0606-2370	Erection and Fit-up	10h	07-Apr-14	08-Apr-14
CZA-TK-0606-2380	Welding	50h	08-Apr-14	14-Apr-14
CZA-TK-0606-2390	Inspection	60h	07-Apr-14	14-Apr-14
CZA-14.3.13.7.4 Shell No.8		**60h**	**14-Apr-14**	**21-Apr-14**
CZA-TK-0606-2400	Erection and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0606-2410	Welding	50h	15-Apr-14	21-Apr-14
CZA-TK-0606-2420	Inspection	60h	14-Apr-14	21-Apr-14
CZA-14.3.13.7.5 Shell Nozzles and Other Attachments		**70h**	**21-Apr-14**	**29-Apr-14**
CZA-TK-0606-2430	Cutting, Installation and Fit-up	20h	21-Apr-14	23-Apr-14
CZA-TK-0606-2440	Welding	50h	23-Apr-14	29-Apr-14
CZA-TK-0606-2450	Inspection	70h	21-Apr-14	29-Apr-14
CZA-14.3.13.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**60h**	**21-Apr-14**	**28-Apr-14**
CZA-TK-0606-2460	Erection and Fit-up	20h	21-Apr-14	23-Apr-14
CZA-TK-0606-2470	Welding	40h	23-Apr-14	28-Apr-14
CZA-TK-0606-2480	Inspection	60h	21-Apr-14	28-Apr-14
CZA-14.3.13.7.7 Deck Plate		**100h**	**28-Apr-14**	**10-May-14**
CZA-TK-0606-2490	Laying and Fit-up	20h	28-Apr-14	30-Apr-14
CZA-TK-0606-2500	Welding	80h	30-Apr-14	10-May-14
CZA-TK-0606-2510	Inspection	100h	28-Apr-14	10-May-14
CZA-14.3.13.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**140h**	**10-May-14**	**26-May-14**
CZA-TK-0606-2520	Laying, Cutting all Holes and Fit-up	40h	10-May-14	14-May-14
CZA-TK-0606-2530	Welding	100h	10-May-14	21-May-14
CZA-TK-0606-2540	Inspection	140h	10-May-14	26-May-14

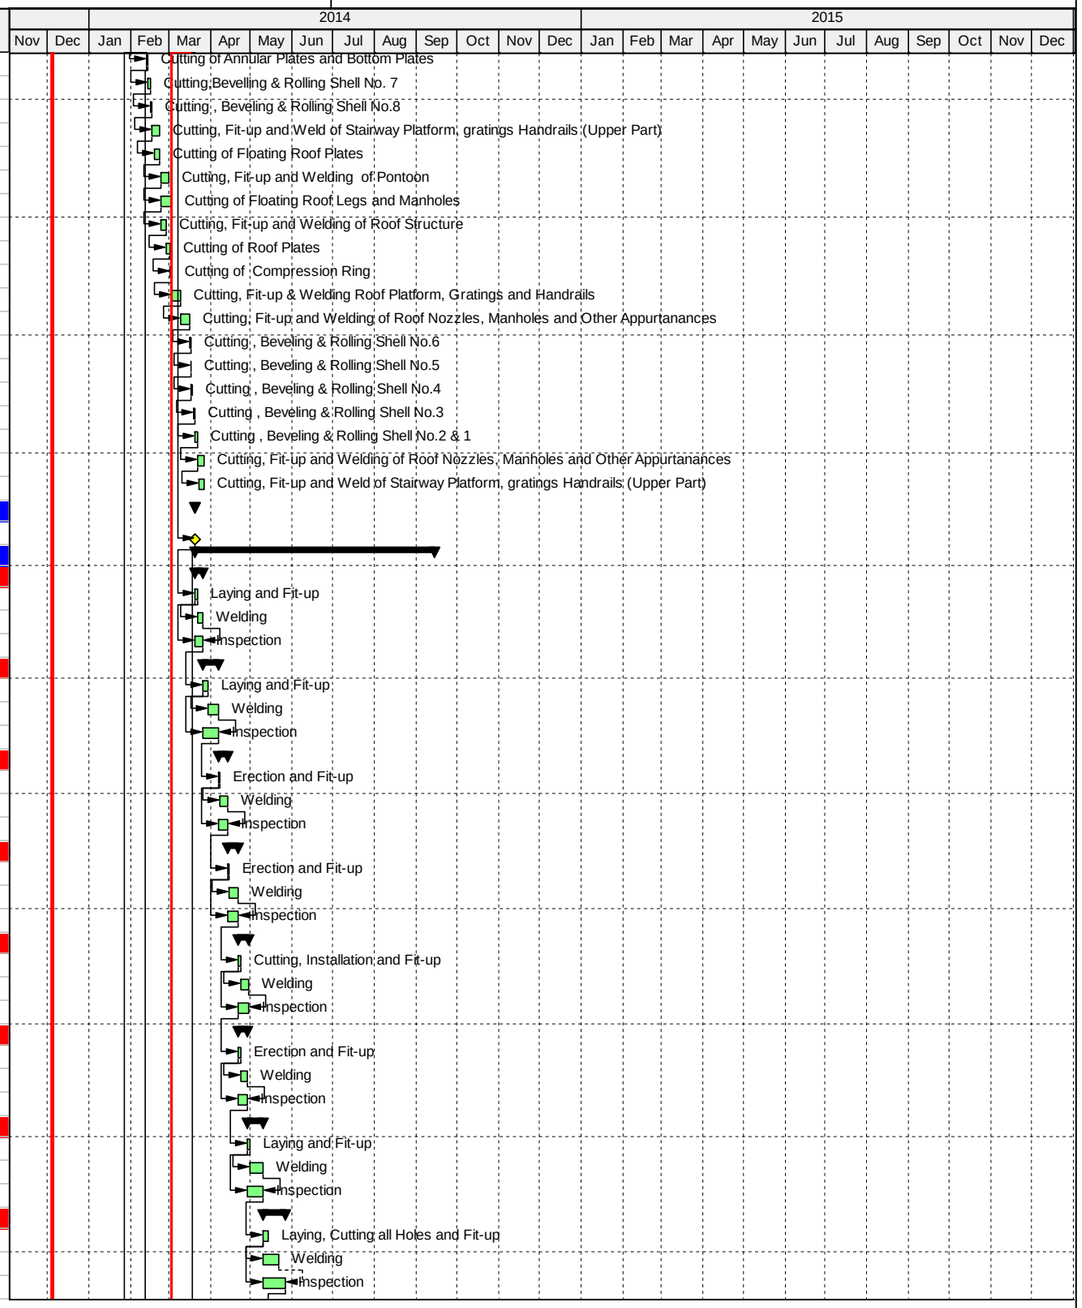

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.13.7.9 Roof Structure		**70h**	**26-May-14**	**03-Jun-14**
CZA-TK-0606-2550	Erection and Fit-up	20h	26-May-14	28-May-14
CZA-TK-0606-2560	Welding	50h	28-May-14	03-Jun-14
CZA-TK-0606-2570	Inspection	70h	26-May-14	03-Jun-14
CZA-14.3.13.7.10 Roof Plates		**70h**	**03-Jun-14**	**11-Jun-14**
CZA-TK-0606-2580	Laying and Fit-up	20h	03-Jun-14	05-Jun-14
CZA-TK-0606-2590	Welding	50h	05-Jun-14	11-Jun-14
CZA-TK-0606-2600	Inspection	70h	03-Jun-14	11-Jun-14
CZA-14.3.13.7.11 Compression Ring		**50h**	**11-Jun-14**	**17-Jun-14**
CZA-TK-0606-2610	Laying and Fit-up	10h	11-Jun-14	12-Jun-14
CZA-TK-0606-2620	Welding	40h	12-Jun-14	17-Jun-14
CZA-TK-0606-2630	Inspection	50h	11-Jun-14	17-Jun-14
CZA-14.3.13.7.12 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**17-Jun-14**	**25-Jun-14**
CZA-TK-0606-2640	Cutting,Installation and Fit-up	20h	17-Jun-14	19-Jun-14
CZA-TK-0606-2650	Welding	50h	19-Jun-14	25-Jun-14
CZA-TK-0606-2660	Inspection	70h	17-Jun-14	25-Jun-14
CZA-14.3.13.7.13 Roof Platform, Gratings and Handrails		**140h**	**17-Jun-14**	**03-Jul-14**
CZA-TK-0606-2670	Erection and Fit-up	40h	17-Jun-14	22-Jun-14
CZA-TK-0606-2680	Welding	100h	22-Jun-14	03-Jul-14
CZA-TK-0606-2690	Inspection	140h	17-Jun-14	03-Jul-14
CZA-14.3.13.7.14 Shell No.6		**60h**	**03-Jul-14**	**10-Jul-14**
CZA-TK-0606-2700	Jacking, Erection and Fit-up	10h	03-Jul-14	05-Jul-14
CZA-TK-0606-2710	Welding	50h	05-Jul-14	10-Jul-14
CZA-TK-0606-2720	Inspection	60h	03-Jul-14	10-Jul-14
CZA-14.3.13.7.15 Shell No.5		**60h**	**10-Jul-14**	**17-Jul-14**
CZA-TK-0606-2730	Jacking,Erection and Fit-up	10h	10-Jul-14	12-Jul-14
CZA-TK-0606-2740	Welding	50h	12-Jul-14	17-Jul-14
CZA-TK-0606-2750	Inspection	60h	10-Jul-14	17-Jul-14
CZA-14.3.13.7.16 Shell No.4		**60h**	**17-Jul-14**	**24-Jul-14**
CZA-TK-0606-2760	Jacking,Erection and Fit-up	10h	17-Jul-14	19-Jul-14
CZA-TK-0606-2770	Welding	50h	19-Jul-14	24-Jul-14
CZA-TK-0606-2780	Inspection	60h	17-Jul-14	24-Jul-14
CZA-14.3.13.7.17 Shell No.3		**60h**	**24-Jul-14**	**31-Jul-14**
CZA-TK-0606-2790	Jacking, Erection and Fit-up	10h	24-Jul-14	26-Jul-14
CZA-TK-0606-2800	Welding	50h	26-Jul-14	31-Jul-14
CZA-TK-0606-2810	Inspection	60h	24-Jul-14	31-Jul-14
CZA-14.3.13.7.18 Shell No.2		**60h**	**31-Jul-14**	**07-Aug-14**
CZA-TK-0606-2820	Jacking, Erection and Fit-up	10h	31-Jul-14	02-Aug-14
CZA-TK-0606-2830	Welding	50h	02-Aug-14	07-Aug-14
CZA-TK-0606-2840	Inspection	60h	31-Jul-14	07-Aug-14
CZA-14.3.13.7.19 Shell No.1		**60h**	**07-Aug-14**	**14-Aug-14**
CZA-TK-0606-2850	Jacking, Erection and Fit-up	10h	07-Aug-14	09-Aug-14
CZA-TK-0606-2860	Welding	50h	09-Aug-14	14-Aug-14
CZA-TK-0606-2870	Inspection	60h	07-Aug-14	14-Aug-14
CZA-14.3.13.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**70h**	**14-Aug-14**	**23-Aug-14**
CZA-TK-0606-2880	Lay-out, Cutting, and Fit-up	30h	14-Aug-14	18-Aug-14
CZA-TK-0606-2890	Welding	40h	18-Aug-14	23-Aug-14
CZA-TK-0606-2900	Inspection	70h	14-Aug-14	23-Aug-14
CZA-14.3.13.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		**140h**	**23-Aug-14**	**08-Sep-14**
CZA-TK-0606-2910	Erection and Fit-up	40h	23-Aug-14	27-Aug-14
CZA-TK-0606-2920	Welding	100h	27-Aug-14	08-Sep-14
CZA-TK-0606-2930	Inspection	140h	23-Aug-14	08-Sep-14
CZA-14.3.13.7.24 Primary and Secondary Seal		**50h**	**08-Sep-14**	**14-Sep-14**
CZA-TK-0606-2940	Installation of Primary and Secondary Seal	40h	08-Sep-14	13-Sep-14

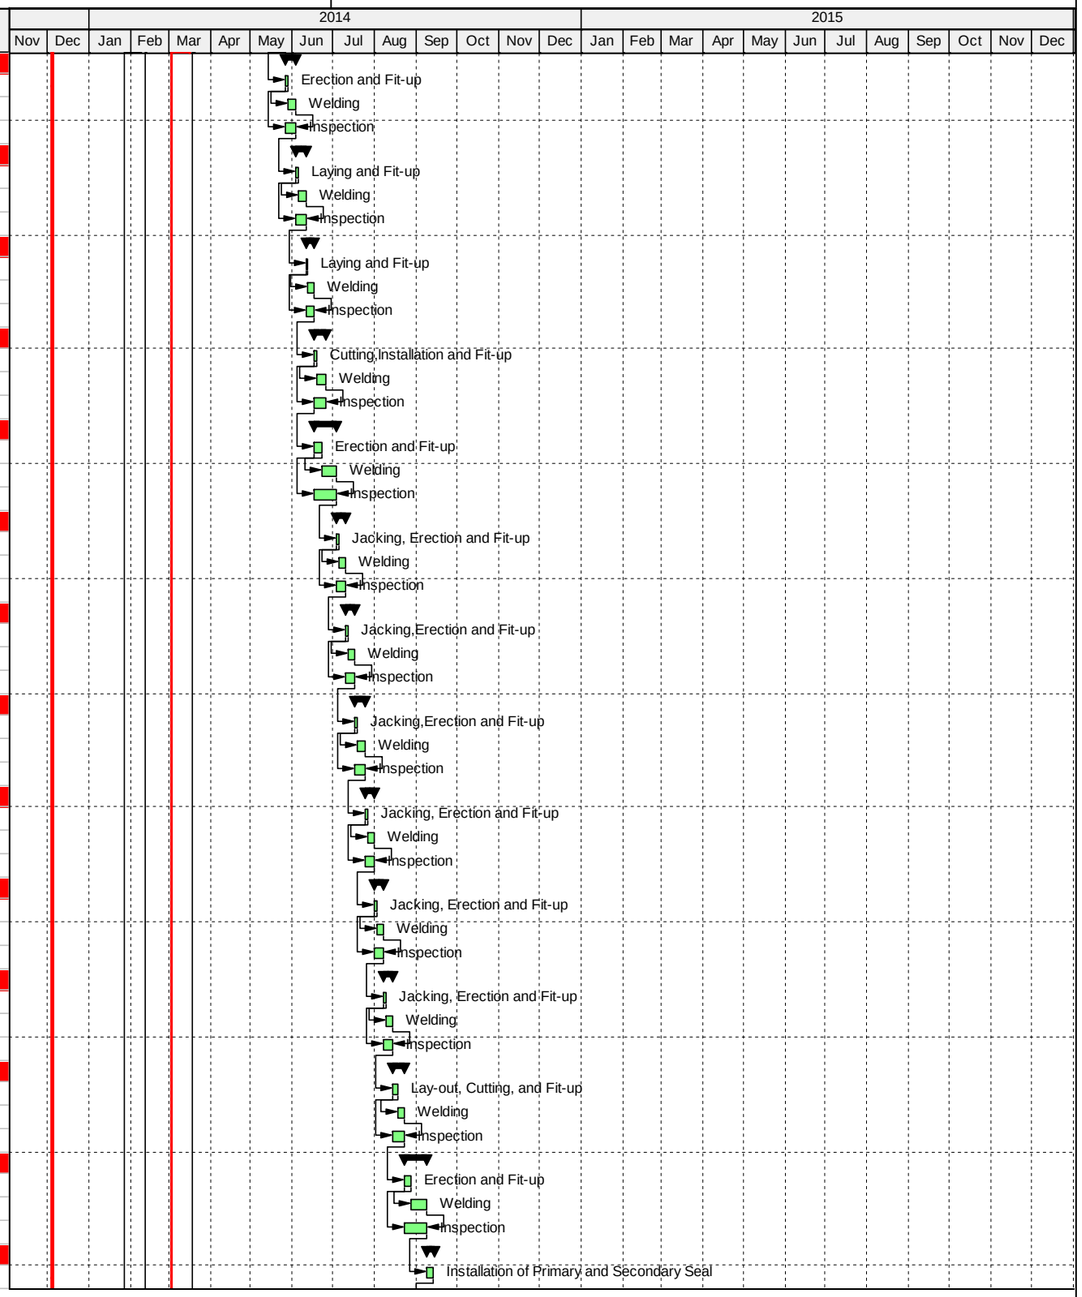

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0606-2950	Inspection	10h	13-Sep-14	14-Sep-14
CZA-14.3.13.4 Hydrotest		330h	14-Sep-14	22-Oct-14
CZA-TK-0606-2960	Filling, Holding and Draining of Water	330h	14-Sep-14	22-Oct-14
CZA-14.3.13.5 Blasting and Painting		170h	22-Oct-14	11-Nov-14
CZA-TK-0606-2970	Blasting and Painting Inside, Outside and Bottom Plates	170h	22-Oct-14	11-Nov-14
CZA-14.3.13.6 Tank Calibration and Handover		70h	11-Nov-14	19-Nov-14
CZA-TK-0606-2980	Tank Calibration	50h	11-Nov-14	17-Nov-14
CZA-TK-0606-2990	Tank Handover	20h	17-Nov-14	19-Nov-14
CZA-14.3.14 S210-TK-0535(MTBE Import Tank Dia 34.83m x Ht 19.8m with IFR)		2278h	24-Feb-14	17-Nov-14
CZA-14.3.14.1 Fabrication Works		368h	24-Feb-14	08-Apr-14
CZA-TK-0535-1940	Cutting of Annular Plates	32h	24-Feb-14	27-Feb-14
CZA-TK-0535-1950	Cutting of Bottom Plates & Compression Ring	32h	24-Feb-14	27-Feb-14
CZA-TK-0535-1960	Cutting, Bevelling & Rolling Shell No.8	16h	26-Feb-14	27-Feb-14
CZA-TK-0535-1970	Cutting, Bevelling and Rolling Shell No.9	16h	26-Feb-14	27-Feb-14
CZA-TK-0535-1980	Cutting of Floating Deck Plate & Stairway (Upper Part)	56h	27-Feb-14	06-Mar-14
CZA-TK-0535-1990	Cutting of Pontoon	80h	02-Mar-14	11-Mar-14
CZA-TK-0535-2000	Cutting, Fit-up, Roof legs and Manholes	56h	04-Mar-14	10-Mar-14
CZA-TK-0535-2010	Cutting, Fit-up, and Welding of Roof Structure	56h	10-Mar-14	17-Mar-14
CZA-TK-0535-2020	Cutting of Roof Plates	16h	17-Mar-14	18-Mar-14
CZA-TK-0535-2030	Cutting, Fit-up, & Welding of Roof Nozzles, Manholes & other Appurtanances	56h	18-Mar-14	25-Mar-14
CZA-TK-0535-2040	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	120h	22-Mar-14	05-Apr-14
CZA-TK-0535-2050	Cutting, Bevelling and Rolling Shell No.7	16h	27-Mar-14	30-Mar-14
CZA-TK-0535-2060	Cutting, Bevelling and Rolling Shell No.6	16h	27-Mar-14	30-Mar-14
CZA-TK-0535-2070	Cutting, Bevelling and Rolling Shell No.5	16h	30-Mar-14	31-Mar-14
CZA-TK-0535-2080	Cutting, Bevelling and Rolling Shell No.4	16h	30-Mar-14	31-Mar-14
CZA-TK-0535-2090	Cutting, Bevelling and Rolling Shell No.3	16h	01-Apr-14	02-Apr-14
CZA-TK-0535-2100	Cutting, Bevelling and Rolling Shell No.2	16h	01-Apr-14	02-Apr-14
CZA-TK-0535-2110	Cutting, Bevelling and Rolling Shell No.1	16h	01-Apr-14	02-Apr-14
CZA-TK-0535-2130	Cutting, Fit-up & Welding of Shell Nozzles, Manholes and Other Appurtanances	64h	01-Apr-14	08-Apr-14
CZA-TK-0535-2140	Cutting, Fit-up and Welding of Stairway Platform, Gratings and Handrails (Lower Part)	48h	01-Apr-14	06-Apr-14
CZA-14.3.14.2 FoundationTakeover		0h	31-Mar-14	31-Mar-14
CZA-TK-0535-2150	Foundation Takeover From Client	0h	31-Mar-14	
CZA-14.3.14.7 Mechanical Erection		1302h	31-Mar-14	30-Aug-14
CZA-14.3.14.7.1 Annular Plates		40h	31-Mar-14	05-Apr-14
CZA-TK-0535-2160	Laying and Fit-up	10h	31-Mar-14	01-Apr-14
CZA-TK-0535-2170	Welding	30h	01-Apr-14	05-Apr-14
CZA-TK-0535-2180	Inspection	40h	31-Mar-14	05-Apr-14
CZA-14.3.14.7.2 Bottom Plates		80h	05-Apr-14	14-Apr-14
CZA-TK-0535-2190	Laying and Fit-up	20h	05-Apr-14	07-Apr-14
CZA-TK-0535-2200	Welding	60h	07-Apr-14	14-Apr-14
CZA-TK-0535-2210	Inspection	80h	05-Apr-14	14-Apr-14
CZA-14.3.14.7.3 Shell No.8		60h	14-Apr-14	21-Apr-14
CZA-TK-0535-2220	Erection and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0535-2230	Welding	50h	15-Apr-14	21-Apr-14
CZA-TK-0535-2240	Inspection	60h	14-Apr-14	21-Apr-14
CZA-14.3.14.7.4 Shell No.9		60h	21-Apr-14	28-Apr-14
CZA-TK-0535-2250	Erection and Fit-up	10h	21-Apr-14	22-Apr-14
CZA-TK-0535-2260	Welding	50h	22-Apr-14	28-Apr-14
CZA-TK-0535-2270	Inspection	60h	21-Apr-14	28-Apr-14
CZA-14.3.14.7.5 Shell Nozzles and Other Attachments		50h	28-Apr-14	04-May-14
CZA-TK-0535-2280	Cutting, Installation and Fit-up	20h	28-Apr-14	30-Apr-14
CZA-TK-0535-2290	Welding	30h	30-Apr-14	04-May-14
CZA-TK-0535-2300	Inspection	50h	28-Apr-14	04-May-14
CZA-14.3.14.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		50h	28-Apr-14	04-May-14

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0535-2310	Erection and Fit-up	20h	28-Apr-14	30-Apr-14
CZA-TK-0535-2320	Welding	30h	30-Apr-14	04-May-14
CZA-TK-0535-2330	Inspection	50h	28-Apr-14	04-May-14
CZA-14.3.14.7.7 Deck Plate		**100h**	**04-May-14**	**15-May-14**
CZA-TK-0535-2340	Laying and Fit-up	30h	04-May-14	07-May-14
CZA-TK-0535-2350	Welding	70h	07-May-14	15-May-14
CZA-TK-0535-2360	Inspection	100h	04-May-14	15-May-14
CZA-14.3.14.7.8 Pontoons, Floating Legs, Manholes, and other Appurtanances		**80h**	**15-May-14**	**25-May-14**
CZA-TK-0535-2370	Laying, Cutting all Holes and Fit-up	20h	15-May-14	18-May-14
CZA-TK-0535-2380	Welding	60h	15-May-14	22-May-14
CZA-TK-0535-2390	Inspection	80h	15-May-14	25-May-14
CZA-14.3.14.7.9 Roof Structure		**100h**	**25-May-14**	**05-Jun-14**
CZA-TK-0535-2400	Erection and Fit-up	30h	25-May-14	28-May-14
CZA-TK-0535-2410	Welding	70h	28-May-14	05-Jun-14
CZA-TK-0535-2420	Inspection	100h	25-May-14	05-Jun-14
CZA-14.3.14.7.10 Roof Plates		**80h**	**05-Jun-14**	**15-Jun-14**
CZA-TK-0535-2430	Laying and Fit-up	20h	05-Jun-14	08-Jun-14
CZA-TK-0535-2440	Welding	60h	08-Jun-14	15-Jun-14
CZA-TK-0535-2450	Inspection	80h	05-Jun-14	15-Jun-14
CZA-14.3.14.7.11 Compression Ring		**70h**	**15-Jun-14**	**23-Jun-14**
CZA-TK-0535-2460	Laying and Fit-up	20h	15-Jun-14	17-Jun-14
CZA-TK-0535-2470	Welding	50h	17-Jun-14	23-Jun-14
CZA-TK-0535-2480	Inspection	70h	15-Jun-14	23-Jun-14
CZA-14.3.14.7.12 Roof Nozzles, Manholes and Other Appurtanances		**80h**	**23-Jun-14**	**02-Jul-14**
CZA-TK-0535-2490	Cutting,Installation and Fit-up	30h	23-Jun-14	26-Jun-14
CZA-TK-0535-2500	Welding	50h	26-Jun-14	02-Jul-14
CZA-TK-0535-2510	Inspection	80h	23-Jun-14	02-Jul-14
CZA-14.3.14.7.13 Roof Platform, Gratings and Handrails		**80h**	**23-Jun-14**	**02-Jul-14**
CZA-TK-0535-2520	Erection and Fit-up	30h	23-Jun-14	26-Jun-14
CZA-TK-0535-2530	Welding	50h	26-Jun-14	02-Jul-14
CZA-TK-0535-2540	Inspection	80h	23-Jun-14	02-Jul-14
CZA-14.3.14.7.14 Shell No.7		**60h**	**02-Jul-14**	**09-Jul-14**
CZA-TK-0535-2550	Jacking, Erection and Fit-up	10h	02-Jul-14	03-Jul-14
CZA-TK-0535-2560	Welding	50h	03-Jul-14	09-Jul-14
CZA-TK-0535-2570	Inspection	60h	02-Jul-14	09-Jul-14
CZA-14.3.14.7.15 Shell No.6		**60h**	**09-Jul-14**	**16-Jul-14**
CZA-TK-0535-2580	Jacking,Erection and Fit-up	10h	09-Jul-14	10-Jul-14
CZA-TK-0535-2590	Welding	50h	10-Jul-14	16-Jul-14
CZA-TK-0535-2600	Inspection	60h	09-Jul-14	16-Jul-14
CZA-14.3.14.7.16 Shell No.5		**60h**	**16-Jul-14**	**23-Jul-14**
CZA-TK-0535-2610	Jacking,Erection and Fit-up	10h	16-Jul-14	17-Jul-14
CZA-TK-0535-2620	Welding	50h	17-Jul-14	23-Jul-14
CZA-TK-0535-2630	Inspection	60h	16-Jul-14	23-Jul-14
CZA-14.3.14.7.17 Shell No.4		**60h**	**23-Jul-14**	**30-Jul-14**
CZA-TK-0535-2640	Jacking, Erection and Fit-up	10h	23-Jul-14	24-Jul-14
CZA-TK-0535-2650	Welding	50h	24-Jul-14	30-Jul-14
CZA-TK-0535-2660	Inspection	60h	23-Jul-14	30-Jul-14
CZA-14.3.14.7.18 Shell No.3		**60h**	**30-Jul-14**	**06-Aug-14**
CZA-TK-0535-2670	Jacking, Erection and Fit-up	10h	30-Jul-14	31-Jul-14
CZA-TK-0535-2680	Welding	50h	31-Jul-14	06-Aug-14
CZA-TK-0535-2690	Inspection	60h	30-Jul-14	06-Aug-14
CZA-14.3.14.7.19 Shell No.2		**60h**	**06-Aug-14**	**13-Aug-14**
CZA-TK-0535-2700	Jacking, Erection and Fit-up	10h	06-Aug-14	07-Aug-14
CZA-TK-0535-2710	Welding	50h	07-Aug-14	13-Aug-14

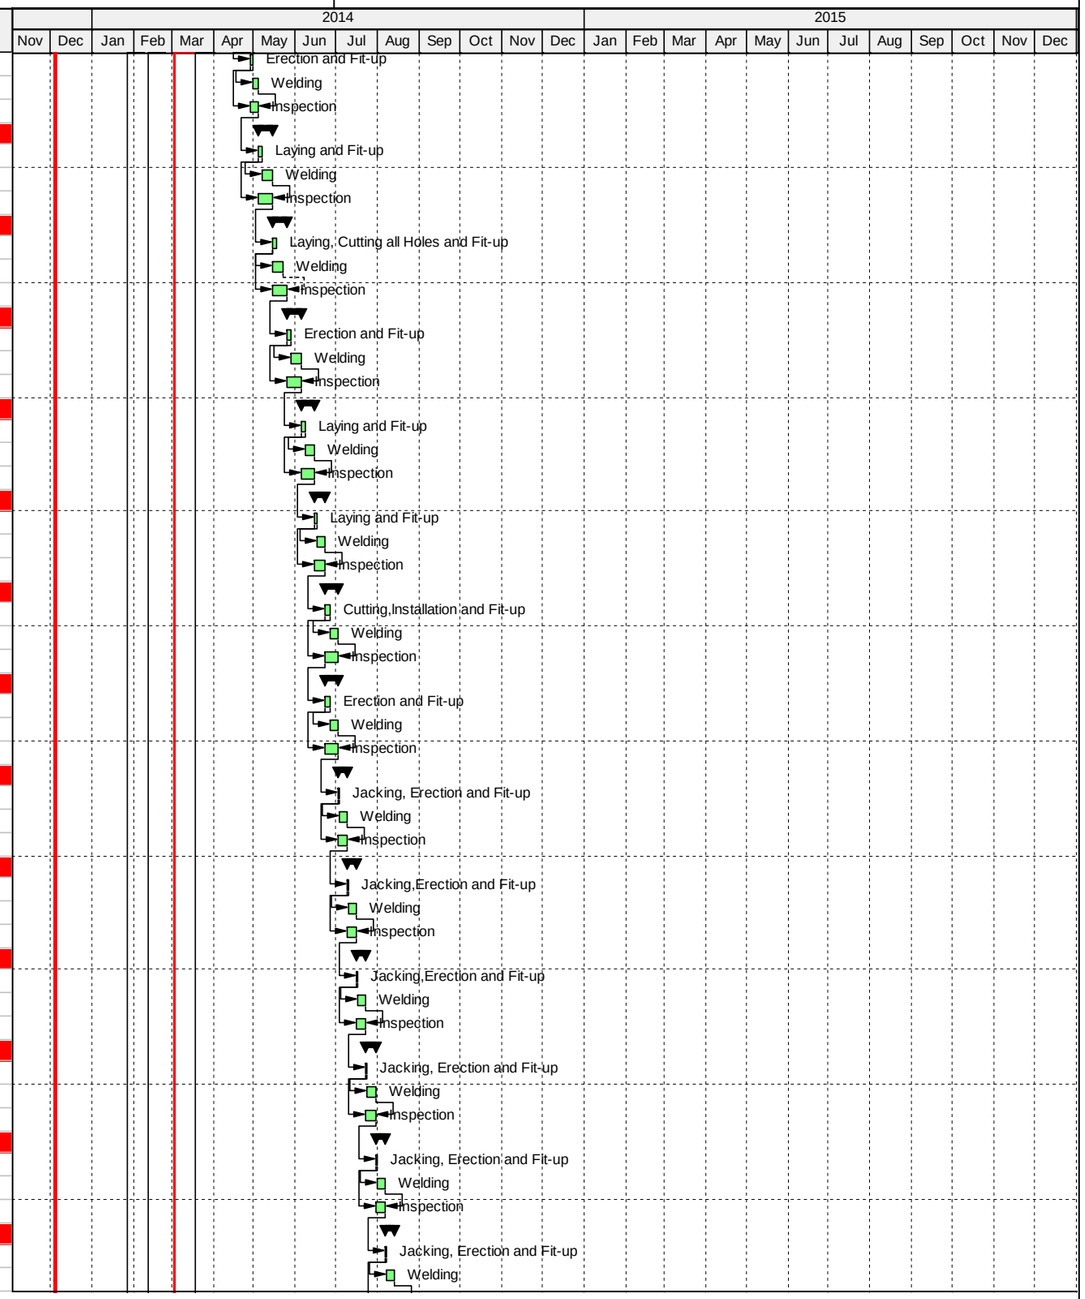

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0535-2720	Inspection	60h	06-Aug-14	13-Aug-14
CZA-14.3.14.7.20 Shell No.1		**60h**	**13-Aug-14**	**20-Aug-14**
CZA-TK-0535-2730	Jacking, Erection and Fit-up	10h	13-Aug-14	14-Aug-14
CZA-TK-0535-2740	Welding	50h	14-Aug-14	20-Aug-14
CZA-TK-0535-2750	Inspection	60h	13-Aug-14	20-Aug-14
CZA-14.3.14.7.22 Shell Nozzles, Manholes , Attachments and Other Appurtanances		**80h**	**20-Aug-14**	**30-Aug-14**
CZA-TK-0535-2760	Lay-out, Cutting, and Fit-up	30h	20-Aug-14	24-Aug-14
CZA-TK-0535-2770	Welding	50h	24-Aug-14	30-Aug-14
CZA-TK-0535-2780	Inspection	80h	20-Aug-14	30-Aug-14
CZA-14.3.14.7.23 Stairway Platform, Handrails and Gratings (Lower Part)		**70h**	**20-Aug-14**	**28-Aug-14**
CZA-TK-0535-2790	Erection and Fit-up	20h	20-Aug-14	23-Aug-14
CZA-TK-0535-2800	Welding	50h	23-Aug-14	28-Aug-14
CZA-TK-0535-2810	Inspection	70h	20-Aug-14	28-Aug-14
CZA-14.3.14.7.24 Primary and Secondary Seal		**50h**	**24-Aug-14**	**30-Aug-14**
CZA-TK-0535-2820	Installation of Primary and Secondary Seal	40h	24-Aug-14	28-Aug-14
CZA-TK-0535-2830	Inspection	10h	28-Aug-14	30-Aug-14
CZA-14.3.14.4 Hydrotest		**410h**	**30-Aug-14**	**16-Oct-14**
CZA-TK-0535-2840	Filling, Holding and Draining of Water	410h	30-Aug-14	16-Oct-14
CZA-14.3.14.5 Blasting and Painting		**200h**	**16-Oct-14**	**09-Nov-14**
CZA-TK-0535-2850	Blasting and Painting (Shell, Roof & Bottom)-Outside & Inside	200h	16-Oct-14	09-Nov-14
CZA-14.3.14.6 Tank Calibration and Handover		**70h**	**09-Nov-14**	**17-Nov-14**
CZA-TK-0535-2860	Tank Calibration	50h	09-Nov-14	15-Nov-14
CZA-TK-0535-2870	Tank Handover	20h	15-Nov-14	17-Nov-14
CZA-14.3.6 S210-TK-0506 (Vam Feed Tank Dia 19.35m x Ht 12.10m)		**1676h**	**24-Feb-14**	**08-Sep-14**
CZA-14.3.6.1 Fabrication Works		**322h**	**24-Feb-14**	**02-Apr-14**
CZA-TK-0506-1710	Cutting of Annular Plate	8h	24-Feb-14	25-Feb-14
CZA-TK-0506-1720	Cutting of Bottom Plates	8h	25-Feb-14	26-Feb-14
CZA-TK-0506-1730	Cutting, Bevelling & Rolling of Shell No.1	8h	26-Feb-14	26-Feb-14
CZA-TK-0506-1740	Cutting, Bevelling & Rolling of Shell No.2	8h	27-Feb-14	27-Feb-14
CZA-TK-0506-1750	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	56h	27-Feb-14	06-Mar-14
CZA-TK-0506-1760	Cutting, Bevelling & Rolling of Shell No.3	8h	06-Mar-14	08-Mar-14
CZA-TK-0506-1770	Cutting, Bevelling & Rolling of Shell No.4	8h	08-Mar-14	08-Mar-14
CZA-TK-0506-1780	Cutting, Bevelling & Rolling of Shell No.5	8h	09-Mar-14	09-Mar-14
CZA-TK-0506-1790	Cutting, Bevelling & Rolling of Shell No.6	8h	09-Mar-14	10-Mar-14
CZA-TK-0506-1800	Cutting, Bevelling & Rolling of Curb Angle	16h	10-Mar-14	12-Mar-14
CZA-TK-0506-1810	Cutting, Bevelling & Rolling of Roof Structure	40h	12-Mar-14	17-Mar-14
CZA-TK-0506-1820	Cutting of Roof Plates	10h	17-Mar-14	18-Mar-14
CZA-TK-0506-1830	Cutting,Fit-up and Welding of Roof Nozzles, Manholes & Other Appurtanances	56h	18-Mar-14	24-Mar-14
CZA-TK-0506-1840	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	96h	19-Mar-14	31-Mar-14
CZA-TK-0506-1850	Cutting, Fit-up and Welding of Stairway Platfrom, Gratings and Handrails	96h	23-Mar-14	02-Apr-14
CZA-14.3.6.2 Foundation Takeover		**0h**	**31-Mar-14**	**31-Mar-14**
CZA-TK-0506-1860	Foundation Takeover from Client	0h	31-Mar-14	
CZA-14.3.6.7 Mechanical Erection		**1040h**	**31-Mar-14**	**30-Jul-14**
CZA-14.3.6.7.1 Annular Plates		**40h**	**31-Mar-14**	**05-Apr-14**
CZA-TK-0506-1870	Laying and Fit-up	10h	31-Mar-14	01-Apr-14
CZA-TK-0506-1880	Welding	30h	01-Apr-14	05-Apr-14
CZA-TK-0506-1890	Inspection	40h	31-Mar-14	05-Apr-14
CZA-14.3.6.7.19 Bottom Plates		**40h**	**05-Apr-14**	**09-Apr-14**
CZA-TK-0506-1900	Erection and Fit-up	10h	05-Apr-14	06-Apr-14
CZA-TK-0506-1910	Welding	30h	06-Apr-14	09-Apr-14
CZA-TK-0506-1920	Inspection	40h	05-Apr-14	09-Apr-14
CZA-14.3.6.7.2 Shell No.1		**50h**	**09-Apr-14**	**15-Apr-14**
CZA-TK-0506-1930	Erection and Fit-up	10h	09-Apr-14	10-Apr-14
CZA-TK-0506-1940	Welding	40h	10-Apr-14	15-Apr-14

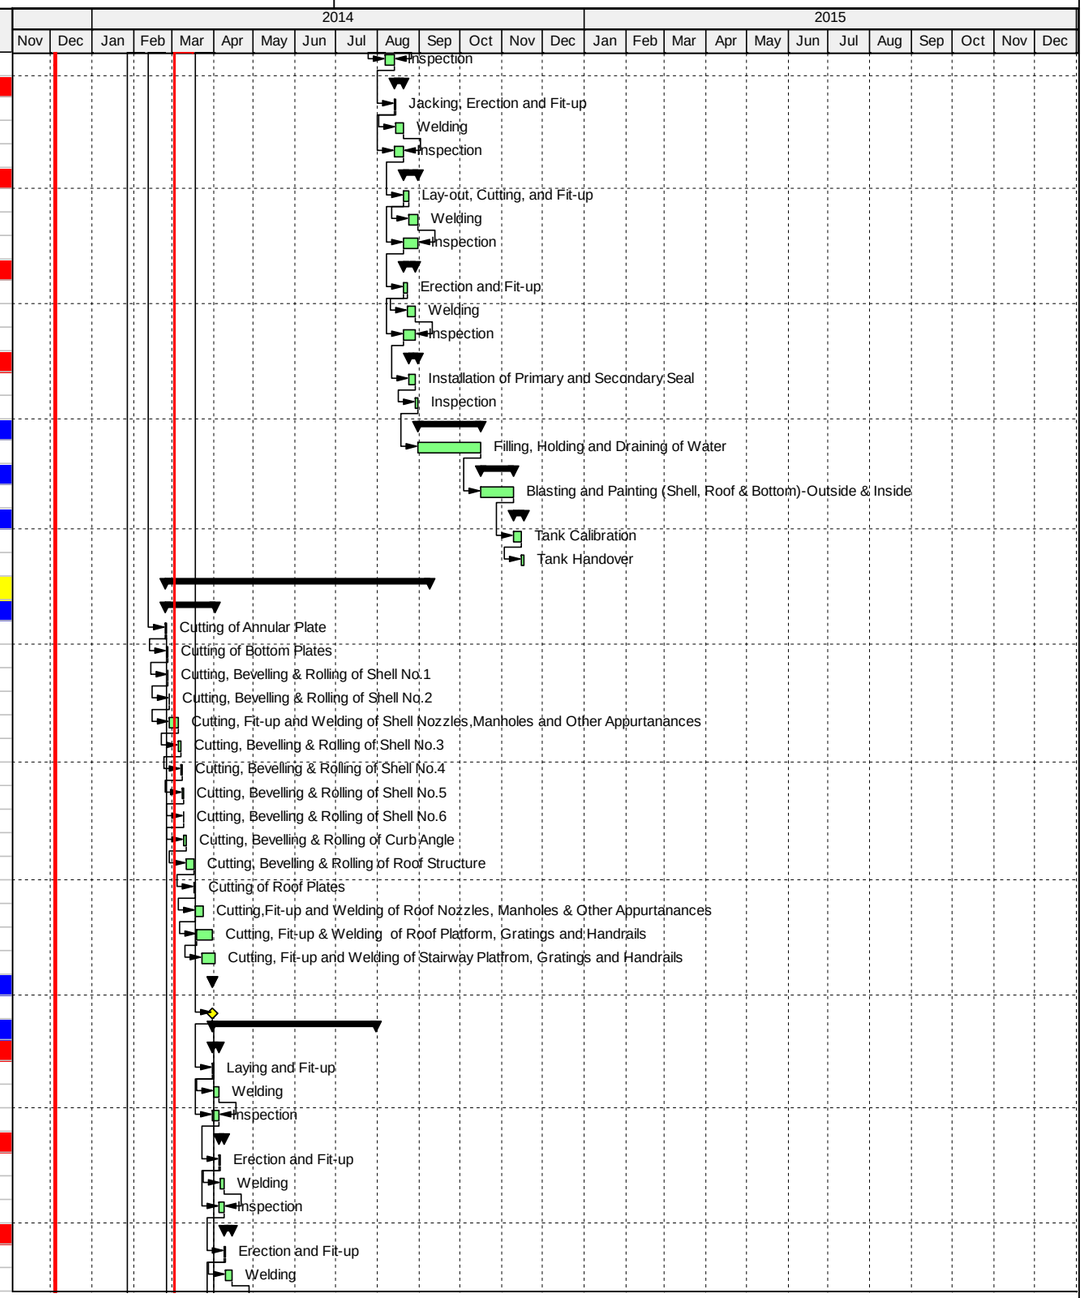

- Actual Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone
- summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0506-1950	Inspection	50h	09-Apr-14	15-Apr-14
CZA-14.3.6.7.3 Shell No.2		**50h**	**15-Apr-14**	**21-Apr-14**
CZA-TK-0506-1960	Erection and Fit-up	10h	15-Apr-14	16-Apr-14
CZA-TK-0506-1970	Welding	40h	16-Apr-14	21-Apr-14
CZA-TK-0506-1980	Inspection	50h	15-Apr-14	21-Apr-14
CZA-14.3.6.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**40h**	**21-Apr-14**	**26-Apr-14**
CZA-TK-0506-1990	Cutting, Installation and Fit-up	20h	21-Apr-14	23-Apr-14
CZA-TK-0506-2000	Welding	20h	23-Apr-14	26-Apr-14
CZA-TK-0506-2010	Inspection	40h	21-Apr-14	26-Apr-14
CZA-14.3.6.7.7 Shell No.3		**50h**	**26-Apr-14**	**01-May-14**
CZA-TK-0506-2020	Erection and Fit-up	10h	26-Apr-14	27-Apr-14
CZA-TK-0506-2030	Welding	40h	27-Apr-14	01-May-14
CZA-TK-0506-2040	Inspection	50h	26-Apr-14	01-May-14
CZA-14.3.6.7.8 Shell No.4		**50h**	**01-May-14**	**07-May-14**
CZA-TK-0506-2050	Erection and Fit-up	10h	01-May-14	03-May-14
CZA-TK-0506-2060	Welding	40h	03-May-14	07-May-14
CZA-TK-0506-2070	Inspection	50h	01-May-14	07-May-14
CZA-14.3.6.7.9 Shell No.5		**50h**	**07-May-14**	**13-May-14**
CZA-TK-0506-2080	Erection and Fit-up	10h	07-May-14	08-May-14
CZA-TK-0506-2090	Welding	40h	08-May-14	13-May-14
CZA-TK-0506-2100	Inspection	50h	07-May-14	13-May-14
CZA-14.3.6.7.10 Shell No.6		**50h**	**13-May-14**	**19-May-14**
CZA-TK-0506-2110	Erection and Fit-up	10h	13-May-14	14-May-14
CZA-TK-0506-2120	Welding	40h	14-May-14	19-May-14
CZA-TK-0506-2130	Inspection	50h	13-May-14	19-May-14
CZA-14.3.6.7.12 Shell Nozzles and attachements (Upper)		**60h**	**19-May-14**	**26-May-14**
CZA-TK-0506-2140	Cutting, Installation and Fit-up	20h	19-May-14	21-May-14
CZA-TK-0506-2150	Welding	40h	21-May-14	26-May-14
CZA-TK-0506-2160	Inspection	60h	19-May-14	26-May-14
CZA-14.3.6.7.13 Curb Angle		**40h**	**26-May-14**	**31-May-14**
CZA-TK-0506-2170	Erection and Fit-up	10h	26-May-14	27-May-14
CZA-TK-0506-2180	Welding	30h	27-May-14	31-May-14
CZA-TK-0506-2190	Inspection	40h	26-May-14	31-May-14
CZA-14.3.6.7.14 Roof Structure		**70h**	**31-May-14**	**08-Jun-14**
CZA-TK-0506-2200	Laying and Fit-up	30h	31-May-14	03-Jun-14
CZA-TK-0506-2210	Welding	40h	03-Jun-14	08-Jun-14
CZA-TK-0506-2220	Inspection	70h	31-May-14	08-Jun-14
CZA-14.3.6.7.15 Roof Plates		**70h**	**08-Jun-14**	**16-Jun-14**
CZA-TK-0506-2230	Laying and Fit-up	20h	08-Jun-14	10-Jun-14
CZA-TK-0506-2240	Welding	50h	10-Jun-14	16-Jun-14
CZA-TK-0506-2250	Inspection	70h	08-Jun-14	16-Jun-14
CZA-14.3.6.7.16 Roof Nozzles, Manholes and Other Appurtanances		**50h**	**16-Jun-14**	**22-Jun-14**
CZA-TK-0506-2260	Installation and Fit-up	20h	16-Jun-14	18-Jun-14
CZA-TK-0506-2270	Welding	30h	18-Jun-14	22-Jun-14
CZA-TK-0506-2280	Inspection	50h	16-Jun-14	22-Jun-14
CZA-14.3.6.7.18 Stairway Platform, Handrails and Gratings		**100h**	**22-Jun-14**	**03-Jul-14**
CZA-TK-0506-2290	Erection and Fit-up	30h	22-Jun-14	25-Jun-14
CZA-TK-0506-2300	Welding	70h	25-Jun-14	03-Jul-14
CZA-TK-0506-2310	Inspection	100h	22-Jun-14	03-Jul-14
CZA-14.3.6.7.17 Roof Platform, Handrails and Gratings		**110h**	**26-Jun-14**	**09-Jul-14**
CZA-TK-0506-2320	Erection and Fit-up	30h	26-Jun-14	30-Jun-14
CZA-TK-0506-2330	Welding	80h	30-Jun-14	09-Jul-14
CZA-TK-0506-2340	Inspection	110h	26-Jun-14	09-Jul-14
CZA-14.3.6.7.20 Primary and Secondary Seal		**40h**	**09-Jul-14**	**14-Jul-14**

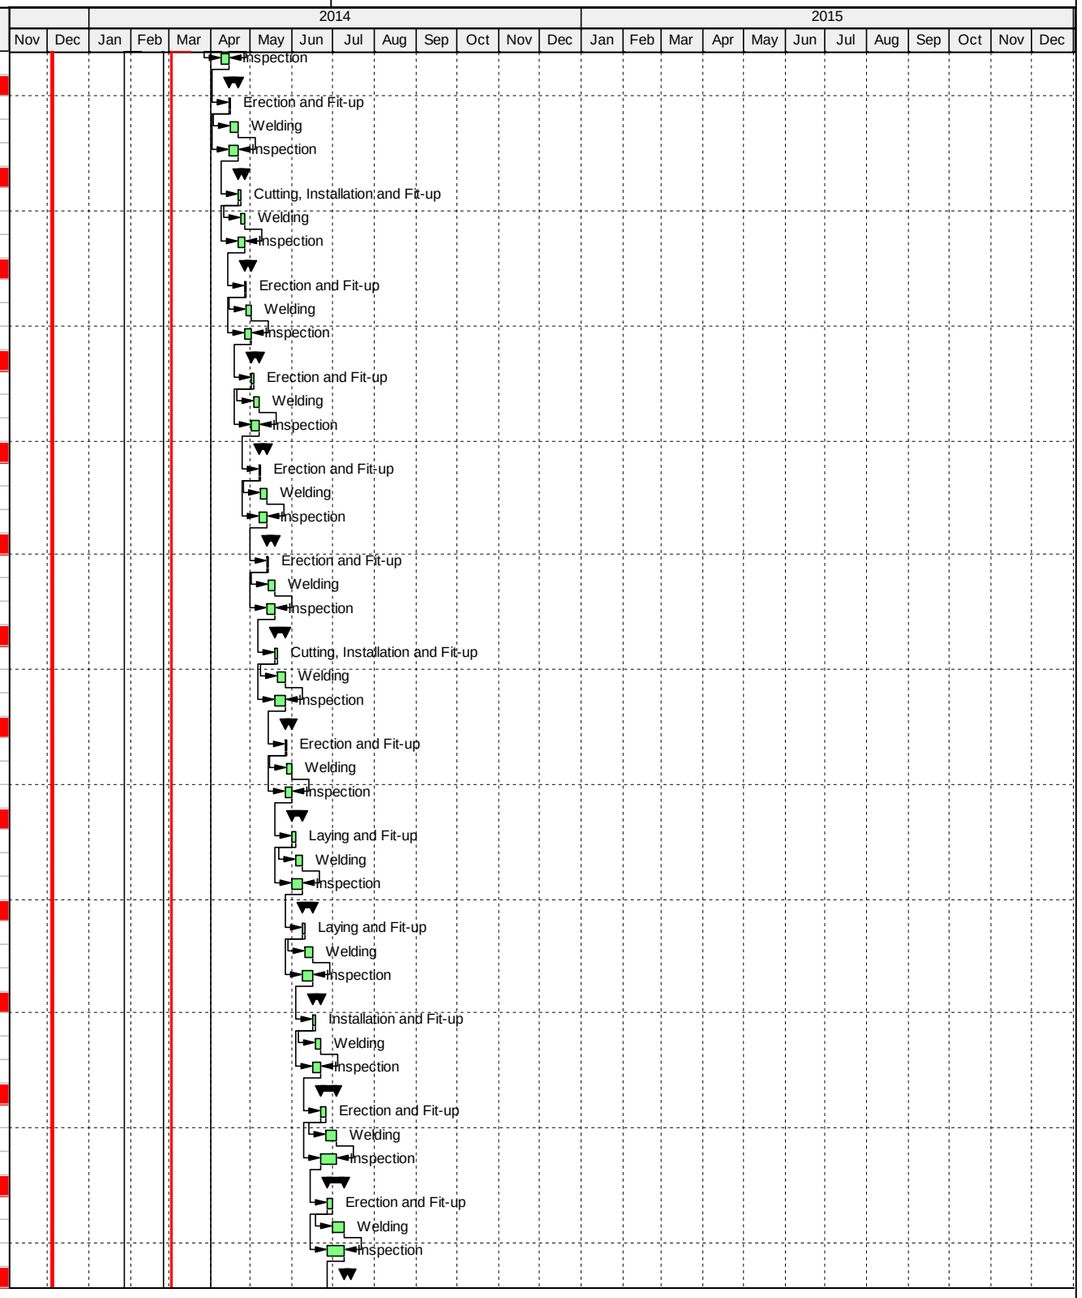

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0506-2350	Installation of Primary and Secondary Seal	30h	09-Jul-14	13-Jul-14
CZA-TK-0506-2360	Inspection	10h	13-Jul-14	14-Jul-14
CZA-14.3.6.7.11 Insulation		140h	14-Jul-14	30-Jul-14
CZA-TK-0506-2370	Insulation Works	130h	14-Jul-14	29-Jul-14
CZA-TK-0506-2380	Inspection	10h	29-Jul-14	30-Jul-14
CZA-14.3.6.4 Hydotest		180h	30-Jul-14	20-Aug-14
CZA-TK-0506-2390	Filling, Holding and Draining of Water	180h	30-Jul-14	20-Aug-14
CZA-14.3.6.5 Blasting and Painting		90h	20-Aug-14	31-Aug-14
CZA-TK-0506-2400	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	90h	20-Aug-14	31-Aug-14
CZA-14.3.6.6 Tank Calibration and Handover		70h	31-Aug-14	08-Sep-14
CZA-TK-0506-2410	Tank Calibration	50h	31-Aug-14	06-Sep-14
CZA-TK-0506-2420	Tank Handover	20h	06-Sep-14	08-Sep-14
CZA-14.3.15 S210-TK-0525(Methanol Feed Tank Dia 21.28m x Ht 16.40m with IFR)		1974h	10-Mar-14	26-Oct-14
CZA-14.3.15.1 Fabrication Works		368h	10-Mar-14	22-Apr-14
CZA-TK-0525-2280	Cutting of Annular Plates and Bottom Plates	8h	10-Mar-14	11-Mar-14
CZA-TK-0525-2290	Cutting,Bevelling & Rolling Shell No. 1	8h	11-Mar-14	12-Mar-14
CZA-TK-0525-2300	Cutting , Beveling & Rolling Shell No.2	8h	12-Mar-14	12-Mar-14
CZA-TK-0525-2310	Cutting, Fit-up and Weld of Shell Nozzles, Manholes & Other Appurtanances	40h	13-Mar-14	17-Mar-14
CZA-TK-0525-2320	Cutting, Bevelling & Rolling Shell No.3	8h	15-Mar-14	16-Mar-14
CZA-TK-0525-2330	Cutting of Floating Roof Plates	16h	16-Mar-14	17-Mar-14
CZA-TK-0525-2340	Cutting, Fit-up and Welding of Pontoon	80h	16-Mar-14	25-Mar-14
CZA-TK-0525-2350	Cutting of Floating Roof Legs and Manholes	32h	25-Mar-14	29-Mar-14
CZA-TK-0525-2360	Cutting, Bevelling & Rolling Shell No.4	8h	29-Mar-14	30-Mar-14
CZA-TK-0525-2370	Cutting, Bevelling & Rolling Shell No.5	8h	30-Mar-14	31-Mar-14
CZA-TK-0525-2380	Cutting, Bevelling & Rolling Shell No.6	8h	31-Mar-14	31-Mar-14
CZA-TK-0525-2390	Cutting, Bevelling & Rolling Shell no.7	8h	01-Apr-14	01-Apr-14
CZA-TK-0525-2400	Cutting, Fit-up & Welding Roof Structures & Compression Ring	48h	01-Apr-14	07-Apr-14
CZA-TK-0525-2410	Cutting of Roof Plates	16h	07-Apr-14	09-Apr-14
CZA-TK-0525-2420	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	80h	09-Apr-14	19-Apr-14
CZA-TK-0525-2430	Cutting, Fit-up and Welding of Stairways	56h	10-Apr-14	17-Apr-14
CZA-TK-0525-2440	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	17-Apr-14	22-Apr-14
CZA-14.3.15.2 FoundationTakeover		0h	14-Apr-14	14-Apr-14
CZA-TK-0525-2450	Foundation Takeover From Client	0h	14-Apr-14	
CZA-14.3.15.7 Mechanical Erection		1258h	14-Apr-14	07-Sep-14
CZA-14.3.15.7.1 Annular Plates		40h	14-Apr-14	19-Apr-14
CZA-TK-0525-2460	Laying and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0525-2470	Welding	30h	15-Apr-14	19-Apr-14
CZA-TK-0525-2480	Inspection	40h	14-Apr-14	19-Apr-14
CZA-14.3.15.7.19 Bottom Plates		50h	19-Apr-14	24-Apr-14
CZA-TK-0525-2490	Erection and Fit-up	10h	19-Apr-14	20-Apr-14
CZA-TK-0525-2500	Welding	40h	20-Apr-14	24-Apr-14
CZA-TK-0525-2510	Inspection	50h	19-Apr-14	24-Apr-14
CZA-14.3.15.7.2 Shell No.1		50h	24-Apr-14	30-Apr-14
CZA-TK-0525-2520	Erection and Fit-up	10h	24-Apr-14	26-Apr-14
CZA-TK-0525-2530	Welding	40h	26-Apr-14	30-Apr-14
CZA-TK-0525-2540	Inspection	50h	24-Apr-14	30-Apr-14
CZA-14.3.15.7.3 Shell No.2		50h	30-Apr-14	06-May-14
CZA-TK-0525-2550	Erection and Fit-up	10h	30-Apr-14	01-May-14
CZA-TK-0525-2560	Welding	40h	01-May-14	06-May-14
CZA-TK-0525-2570	Inspection	50h	30-Apr-14	06-May-14
CZA-14.3.15.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		50h	06-May-14	12-May-14
CZA-TK-0525-2580	Cutting, Installation and Fit-up	20h	06-May-14	08-May-14
CZA-TK-0525-2590	Welding	30h	08-May-14	12-May-14
CZA-TK-0525-2600	Inspection	50h	06-May-14	12-May-14

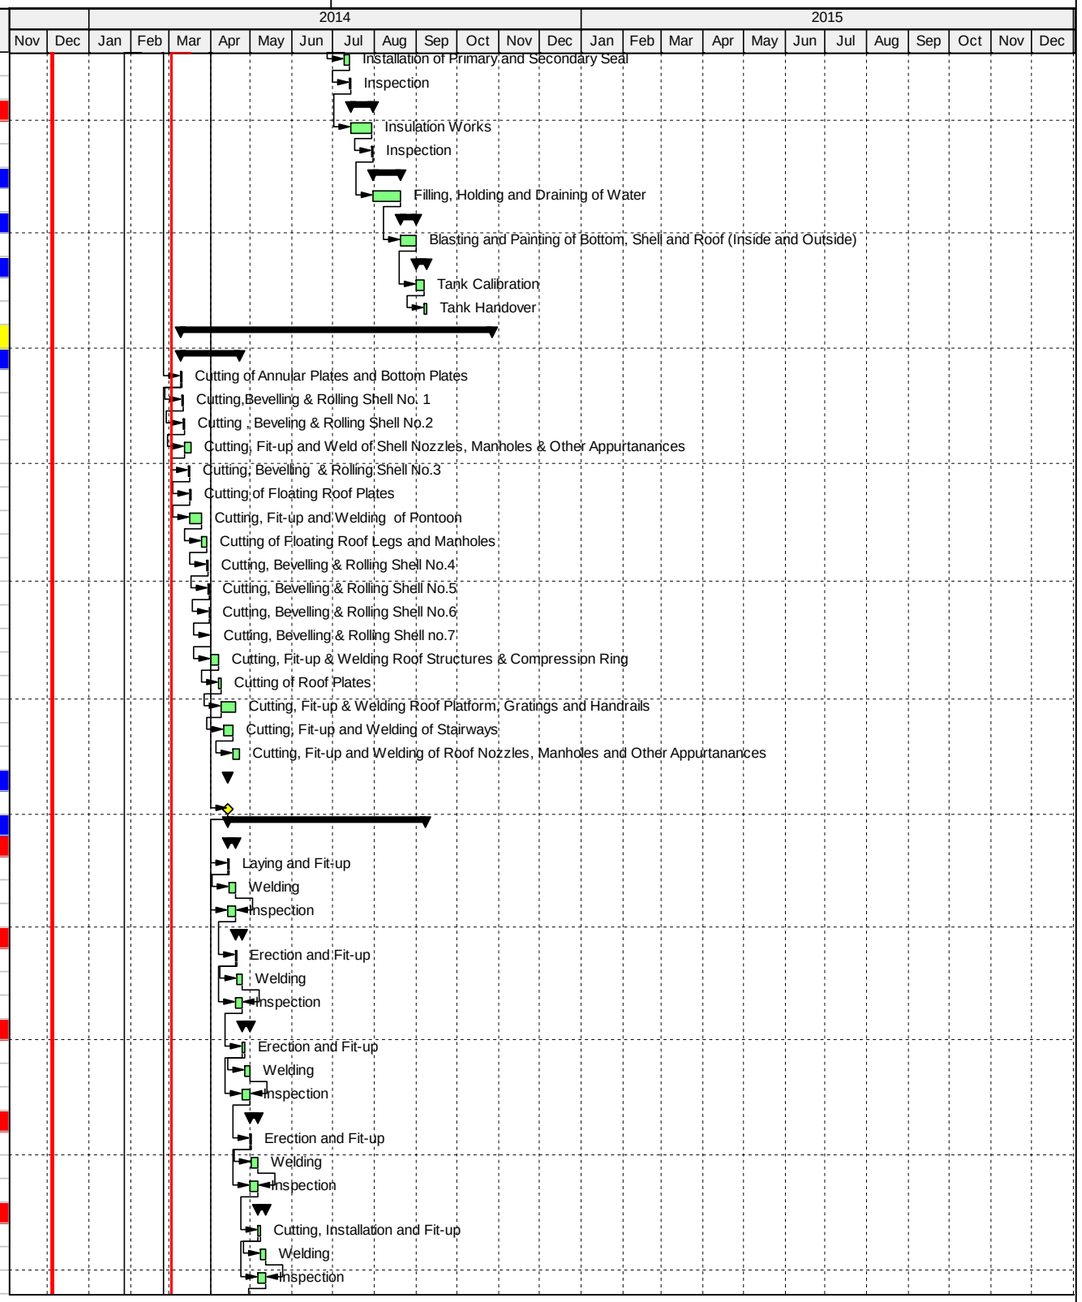

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.15.7.5 Deck Plates		**100h**	**12-May-14**	**24-May-14**
CZA-TK-0525-2610	Laying & Fit-up	30h	12-May-14	15-May-14
CZA-TK-0525-2620	Welding	70h	15-May-14	24-May-14
CZA-TK-0525-2630	Inspection	100h	12-May-14	24-May-14
CZA-14.3.15.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		**150h**	**24-May-14**	**10-Jun-14**
CZA-TK-0525-2640	Cutting of All Holes, Laying and Fit-up	40h	24-May-14	28-May-14
CZA-TK-0525-2650	Welding of Sleeves and Plates	100h	28-May-14	09-Jun-14
CZA-TK-0525-2660	Installation of Leg Support	10h	09-Jun-14	10-Jun-14
CZA-TK-0525-2670	Inspection	150h	24-May-14	10-Jun-14
CZA-14.3.15.7.7 Shell No.3		**50h**	**10-Jun-14**	**16-Jun-14**
CZA-TK-0525-2680	Erection and Fit-up	10h	10-Jun-14	11-Jun-14
CZA-TK-0525-2690	Welding	40h	11-Jun-14	16-Jun-14
CZA-TK-0525-2700	Inspection	50h	10-Jun-14	16-Jun-14
CZA-14.3.15.7.8 Shell No.4		**50h**	**16-Jun-14**	**22-Jun-14**
CZA-TK-0525-2710	Erection and Fit-up	10h	16-Jun-14	17-Jun-14
CZA-TK-0525-2720	Welding	40h	17-Jun-14	22-Jun-14
CZA-TK-0525-2730	Inspection	50h	16-Jun-14	22-Jun-14
CZA-14.3.15.7.9 Shell No.5		**50h**	**22-Jun-14**	**28-Jun-14**
CZA-TK-0525-2740	Erection and Fit-up	10h	22-Jun-14	23-Jun-14
CZA-TK-0525-2750	Welding	40h	23-Jun-14	28-Jun-14
CZA-TK-0525-2760	Inspection	50h	22-Jun-14	28-Jun-14
CZA-14.3.15.7.10 Shell No.6		**50h**	**28-Jun-14**	**03-Jul-14**
CZA-TK-0525-2770	Erection and Fit-up	10h	28-Jun-14	29-Jun-14
CZA-TK-0525-2780	Welding	40h	29-Jun-14	03-Jul-14
CZA-TK-0525-2790	Inspection	50h	28-Jun-14	03-Jul-14
CZA-14.3.15.7.11 Shell No.7		**60h**	**03-Jul-14**	**10-Jul-14**
CZA-TK-0525-2800	Erection and Fit-up	10h	03-Jul-14	05-Jul-14
CZA-TK-0525-2810	Welding	40h	05-Jul-14	09-Jul-14
CZA-TK-0525-2820	Inspection	50h	05-Jul-14	10-Jul-14
CZA-14.3.15.7.12 Shell Nozzles and attachements (Upper)		**50h**	**10-Jul-14**	**16-Jul-14**
CZA-TK-0525-2830	Cutting, Installation and Fit-up	20h	10-Jul-14	13-Jul-14
CZA-TK-0525-2840	Welding	30h	13-Jul-14	16-Jul-14
CZA-TK-0525-2850	Inspection	50h	10-Jul-14	16-Jul-14
CZA-14.3.15.7.13 Roof Structure		**70h**	**16-Jul-14**	**24-Jul-14**
CZA-TK-0525-2860	Erection and Fit-up	20h	16-Jul-14	19-Jul-14
CZA-TK-0525-2870	Welding	50h	19-Jul-14	24-Jul-14
CZA-TK-0525-2880	Inspection	70h	16-Jul-14	24-Jul-14
CZA-14.3.15.7.14 Roof Plates		**70h**	**24-Jul-14**	**02-Aug-14**
CZA-TK-0525-2890	Laying and Fit-up	20h	24-Jul-14	27-Jul-14
CZA-TK-0525-2900	Welding	50h	27-Jul-14	02-Aug-14
CZA-TK-0525-2910	Inspection	70h	24-Jul-14	02-Aug-14
CZA-14.3.15.7.15 Compression Ring		**40h**	**02-Aug-14**	**06-Aug-14**
CZA-TK-0525-2920	Laying and Fit-up	10h	02-Aug-14	03-Aug-14
CZA-TK-0525-2930	Welding	30h	03-Aug-14	06-Aug-14
CZA-TK-0525-2940	Inspection	40h	02-Aug-14	06-Aug-14
CZA-14.3.15.7.16 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**06-Aug-14**	**14-Aug-14**
CZA-TK-0525-2950	Installation and Fit-up	20h	06-Aug-14	09-Aug-14
CZA-TK-0525-2960	Welding	50h	09-Aug-14	14-Aug-14
CZA-TK-0525-2970	Inspection	70h	06-Aug-14	14-Aug-14
CZA-14.3.15.7.18 Stairway Platform, Handrails and Gratings		**130h**	**14-Aug-14**	**30-Aug-14**
CZA-TK-0525-2980	Erection and Fit-up	30h	14-Aug-14	18-Aug-14
CZA-TK-0525-2990	Welding	100h	18-Aug-14	30-Aug-14
CZA-TK-0525-3000	Inspection	130h	14-Aug-14	30-Aug-14
CZA-14.3.15.7.17 Roof Platform, Handrails and Gratings		**130h**	**20-Aug-14**	**03-Sep-14**

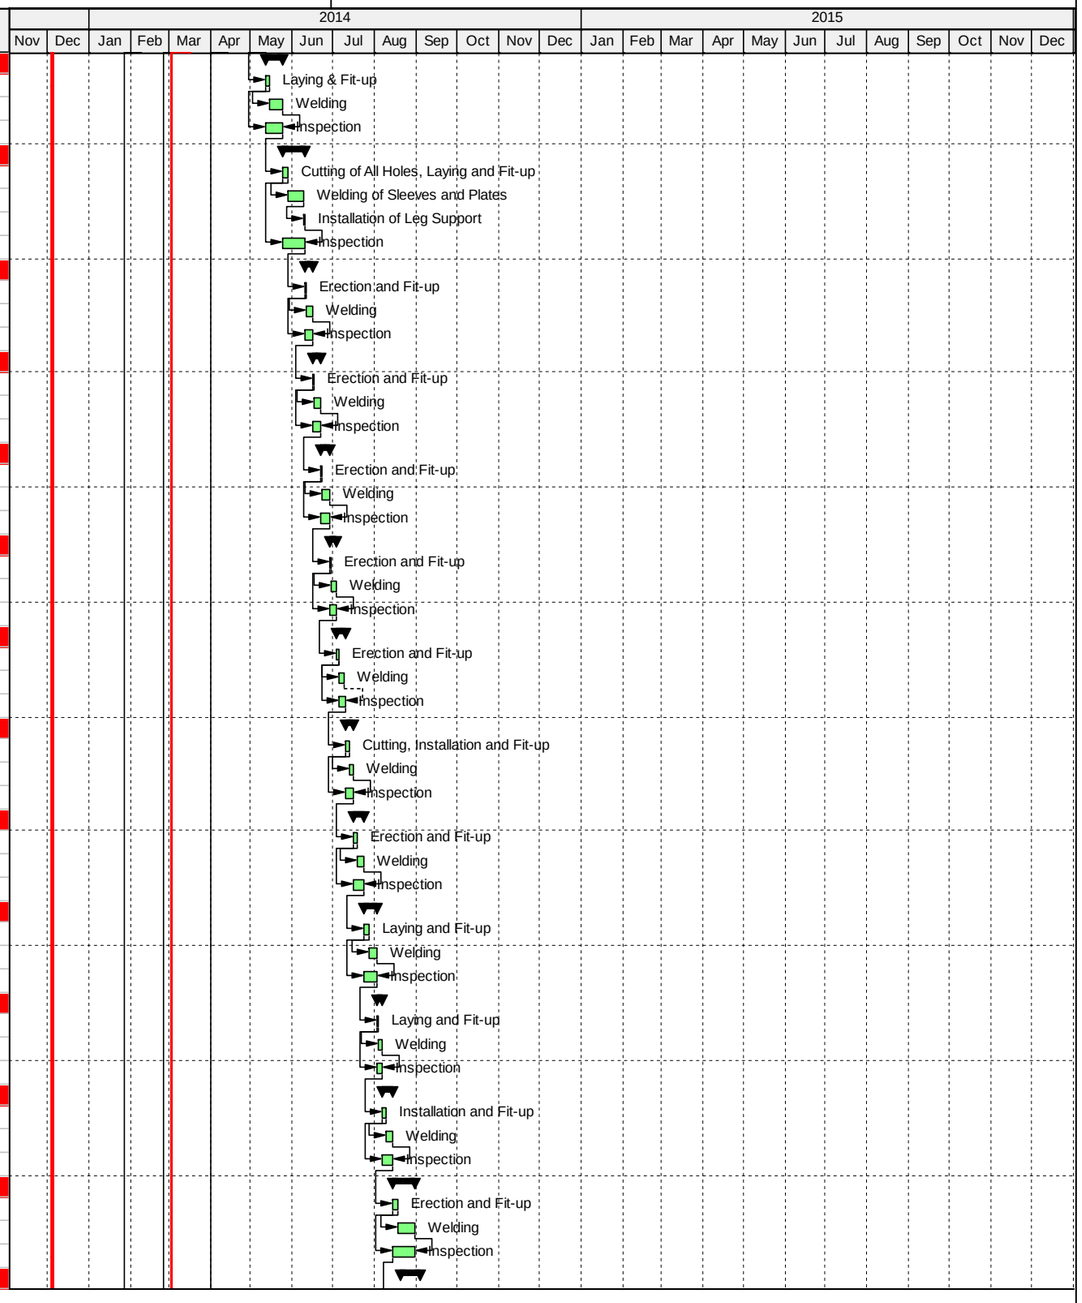

- Actual Level of Effort
- summary
- Actual Work
- Remaining Work
- Critical Remaining Work
- Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0525-3010	Erection and Fit-up	30h	20-Aug-14	23-Aug-14
CZA-TK-0525-3020	Welding	100h	24-Aug-14	03-Sep-14
CZA-TK-0525-3030	Inspection	130h	20-Aug-14	03-Sep-14
CZA-14.3.15.7.20 Installation of Primary and Secondary Seal		30h	04-Sep-14	07-Sep-14
CZA-TK-0525-3040	Installation of Primary and Secondary Seal	30h	04-Sep-14	07-Sep-14
CZA-TK-0525-3050	Inspection	30h	04-Sep-14	07-Sep-14
CZA-14.3.15.4 Hydrotest		230h	08-Sep-14	04-Oct-14
CZA-TK-0525-3060	Filling, Holding and Draining of Water	230h	08-Sep-14	04-Oct-14
CZA-14.3.15.5 Blasting and Painting		120h	05-Oct-14	18-Oct-14
CZA-TK-0525-3070	Blasting and Painting Inside, Outside and Bottom Plates	120h	05-Oct-14	18-Oct-14
CZA-14.3.15.6 Tank Calibration and Handover		70h	19-Oct-14	26-Oct-14
CZA-TK-0525-3080	Tank Calibration	50h	19-Oct-14	23-Oct-14
CZA-TK-0525-3090	Tank Handover	20h	25-Oct-14	26-Oct-14
CZA-14.3.16 S210-TK-0526(Methanol Feed Tank Dia 21.28m x Ht 16.40m with IFR)		1890h	10-Mar-14	16-Oct-14
CZA-14.3.16.1 Fabrication Works		360h	10-Mar-14	21-Apr-14
CZA-TK-0526-2680	Cutting of Annular Plates and Bottom Plates	8h	10-Mar-14	11-Mar-14
CZA-TK-0526-2690	Cutting,Bevelling & Rolling Shell No. 1	8h	11-Mar-14	12-Mar-14
CZA-TK-0526-2700	Cutting, Fit-up and Weld of Shell Nozzles, Manholes & Other Appurtanances	40h	12-Mar-14	17-Mar-14
CZA-TK-0526-2710	Cutting, Bevelling & Rolling Shell No.3	8h	13-Mar-14	15-Mar-14
CZA-TK-0526-2720	Cutting of Floating Roof Plates	16h	15-Mar-14	17-Mar-14
CZA-TK-0526-2730	Cutting, Fit-up and Welding of Pontoon	80h	15-Mar-14	24-Mar-14
CZA-TK-0526-2740	Cutting of Floating Roof Legs and Manholes	32h	24-Mar-14	27-Mar-14
CZA-TK-0526-2750	Cutting, Bevelling & Rolling Shell No.4	8h	27-Mar-14	29-Mar-14
CZA-TK-0526-2760	Cutting, Bevelling & Rolling Shell No.5	8h	29-Mar-14	30-Mar-14
CZA-TK-0526-2770	Cutting, Bevelling & Rolling Shell No.6	8h	30-Mar-14	31-Mar-14
CZA-TK-0526-2780	Cutting, Bevelling & Rolling Shell no.7	8h	31-Mar-14	31-Mar-14
CZA-TK-0526-2790	Cutting, Fit-up & Welding Roof Structures & Compression Ring	48h	01-Apr-14	06-Apr-14
CZA-TK-0526-2800	Cutting of Roof Plates	16h	06-Apr-14	08-Apr-14
CZA-TK-0526-2810	Cutting, Fit-up & Welding Roof Platform, Gratings and Handrails	80h	08-Apr-14	17-Apr-14
CZA-TK-0526-2820	Cutting, Fit-up and Welding of Stairways	56h	10-Apr-14	16-Apr-14
CZA-TK-0526-2830	Cutting, Fit-up and Welding of Roof Nozzles, Manholes and Other Appurtanances	40h	16-Apr-14	21-Apr-14
CZA-14.3.16.2 FoundationTakeover		0h	14-Apr-14	14-Apr-14
CZA-TK-0526-2840	Foundation Takeover From Client	0h	14-Apr-14	
CZA-14.3.16.7 Mechanical Erection		1184h	14-Apr-14	30-Aug-14
CZA-14.3.16.7.1 Annular Plates		40h	14-Apr-14	19-Apr-14
CZA-TK-0526-2850	Laying and Fit-up	10h	14-Apr-14	15-Apr-14
CZA-TK-0526-2860	Welding	30h	15-Apr-14	19-Apr-14
CZA-TK-0526-2870	Inspection	40h	14-Apr-14	19-Apr-14
CZA-14.3.16.7.19 Bottom Plates		50h	19-Apr-14	24-Apr-14
CZA-TK-0526-2880	Erection and Fit-up	10h	19-Apr-14	20-Apr-14
CZA-TK-0526-2890	Welding	40h	20-Apr-14	24-Apr-14
CZA-TK-0526-2900	Inspection	50h	19-Apr-14	24-Apr-14
CZA-14.3.16.7.2 Shell No.1		50h	24-Apr-14	30-Apr-14
CZA-TK-0526-2910	Erection and Fit-up	10h	24-Apr-14	26-Apr-14
CZA-TK-0526-2920	Welding	40h	26-Apr-14	30-Apr-14
CZA-TK-0526-2930	Inspection	50h	24-Apr-14	30-Apr-14
CZA-14.3.16.7.3 Shell No.2		50h	30-Apr-14	06-May-14
CZA-TK-0526-2940	Erection and Fit-up	10h	30-Apr-14	01-May-14
CZA-TK-0526-2950	Welding	40h	01-May-14	06-May-14
CZA-TK-0526-2960	Inspection	50h	30-Apr-14	06-May-14
CZA-14.3.16.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		50h	06-May-14	12-May-14
CZA-TK-0526-2970	Cutting, Installation and Fit-up	20h	06-May-14	08-May-14
CZA-TK-0526-2980	Welding	30h	08-May-14	12-May-14
CZA-TK-0526-2990	Inspection	50h	06-May-14	12-May-14

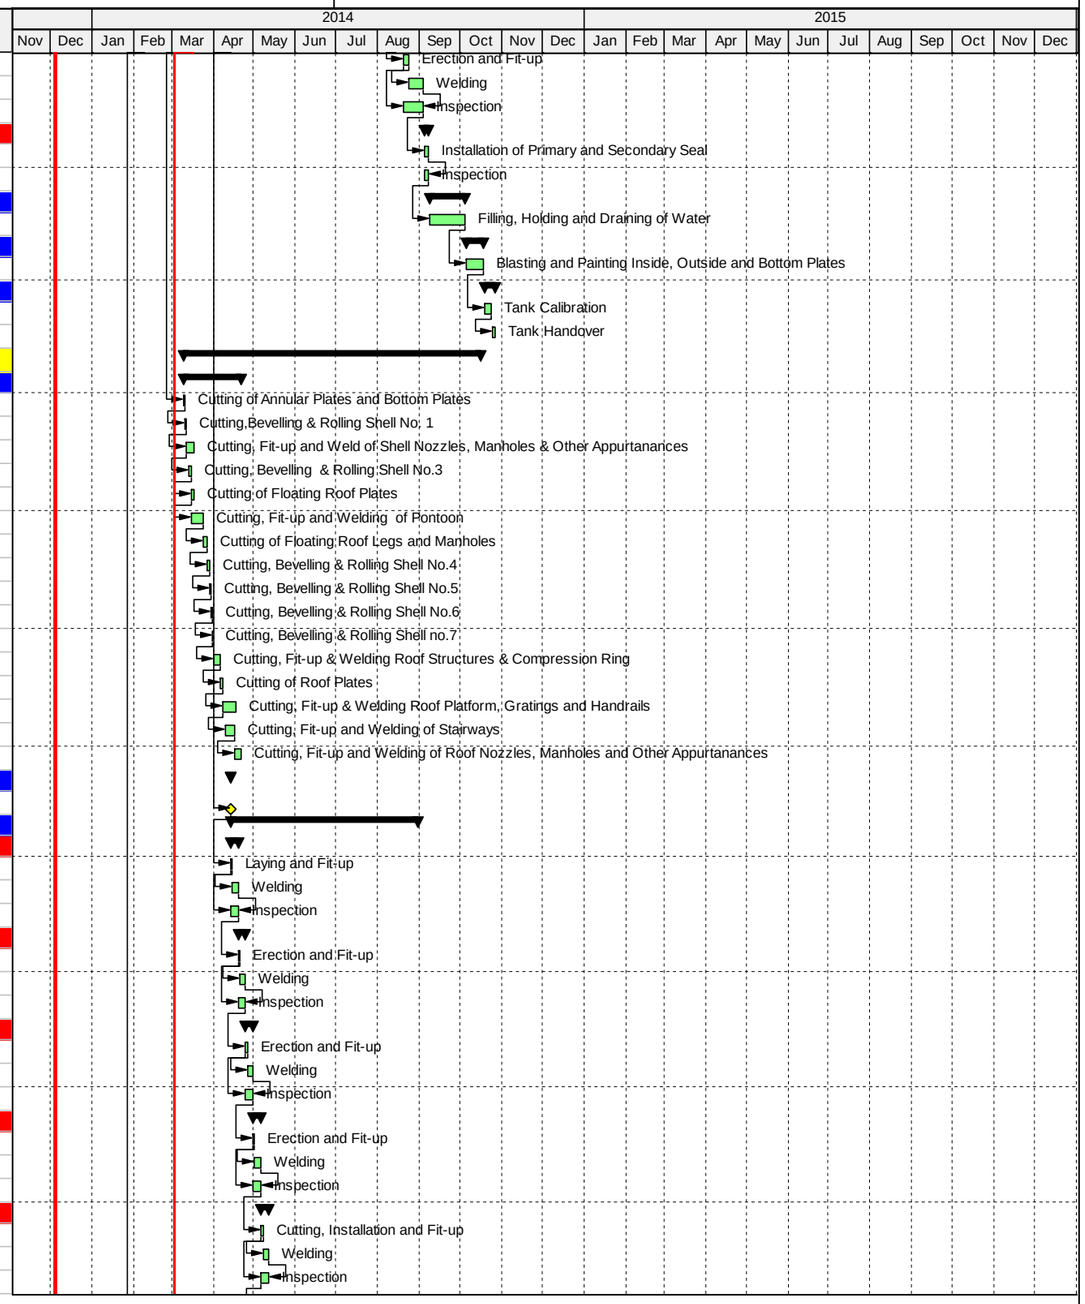

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.3.16.7.5 Deck Plates		**100h**	**08-May-14**	**20-May-14**
CZA-TK-0526-3000	Laying & Fit-up	30h	08-May-14	12-May-14
CZA-TK-0526-3010	Welding	70h	12-May-14	20-May-14
CZA-TK-0526-3020	Inspection	100h	08-May-14	20-May-14
CZA-14.3.16.7.6 Pontoons, Floating Legs, Manholes, and other Appurtanances		**150h**	**20-May-14**	**07-Jun-14**
CZA-TK-0526-3030	Cutting of All Holes, Laying and Fit-up	40h	20-May-14	25-May-14
CZA-TK-0526-3040	Welding of Sleeves and Plates	100h	25-May-14	05-Jun-14
CZA-TK-0526-3050	Installation of Leg Support	10h	05-Jun-14	07-Jun-14
CZA-TK-0526-3060	Inspection	150h	20-May-14	07-Jun-14
CZA-14.3.16.7.7 Shell No.3		**50h**	**07-Jun-14**	**12-Jun-14**
CZA-TK-0526-3070	Erection and Fit-up	10h	07-Jun-14	08-Jun-14
CZA-TK-0526-3080	Welding	40h	08-Jun-14	12-Jun-14
CZA-TK-0526-3090	Inspection	50h	07-Jun-14	12-Jun-14
CZA-14.3.16.7.8 Shell No.4		**50h**	**12-Jun-14**	**18-Jun-14**
CZA-TK-0526-3100	Erection and Fit-up	10h	12-Jun-14	14-Jun-14
CZA-TK-0526-3110	Welding	40h	14-Jun-14	18-Jun-14
CZA-TK-0526-3120	Inspection	50h	12-Jun-14	18-Jun-14
CZA-14.3.16.7.9 Shell No.5		**50h**	**18-Jun-14**	**24-Jun-14**
CZA-TK-0526-3130	Erection and Fit-up	10h	18-Jun-14	19-Jun-14
CZA-TK-0526-3140	Welding	40h	19-Jun-14	24-Jun-14
CZA-TK-0526-3150	Inspection	50h	18-Jun-14	24-Jun-14
CZA-14.3.16.7.10 Shell No.6		**50h**	**24-Jun-14**	**30-Jun-14**
CZA-TK-0526-3160	Erection and Fit-up	10h	24-Jun-14	25-Jun-14
CZA-TK-0526-3170	Welding	40h	25-Jun-14	30-Jun-14
CZA-TK-0526-3180	Inspection	50h	24-Jun-14	30-Jun-14
CZA-14.3.16.7.11 Shell No.7		**60h**	**30-Jun-14**	**07-Jul-14**
CZA-TK-0526-3190	Erection and Fit-up	10h	30-Jun-14	01-Jul-14
CZA-TK-0526-3200	Welding	40h	01-Jul-14	06-Jul-14
CZA-TK-0526-3210	Inspection	50h	01-Jul-14	07-Jul-14
CZA-14.3.16.7.12 Shell Nozzles and attachements (Upper)		**50h**	**07-Jul-14**	**13-Jul-14**
CZA-TK-0526-3220	Cutting, Installation and Fit-up	20h	07-Jul-14	09-Jul-14
CZA-TK-0526-3230	Welding	30h	09-Jul-14	13-Jul-14
CZA-TK-0526-3240	Inspection	50h	07-Jul-14	13-Jul-14
CZA-14.3.16.7.13 Roof Structure		**70h**	**13-Jul-14**	**21-Jul-14**
CZA-TK-0526-3250	Erection and Fit-up	20h	13-Jul-14	15-Jul-14
CZA-TK-0526-3260	Welding	50h	15-Jul-14	21-Jul-14
CZA-TK-0526-3270	Inspection	70h	13-Jul-14	21-Jul-14
CZA-14.3.16.7.14 Roof Plates		**70h**	**21-Jul-14**	**29-Jul-14**
CZA-TK-0526-3280	Laying and Fit-up	20h	21-Jul-14	23-Jul-14
CZA-TK-0526-3290	Welding	50h	23-Jul-14	29-Jul-14
CZA-TK-0526-3300	Inspection	70h	21-Jul-14	29-Jul-14
CZA-14.3.16.7.15 Compression Ring		**40h**	**29-Jul-14**	**03-Aug-14**
CZA-TK-0526-3310	Laying and Fit-up	10h	29-Jul-14	30-Jul-14
CZA-TK-0526-3320	Welding	30h	30-Jul-14	03-Aug-14
CZA-TK-0526-3330	Inspection	40h	29-Jul-14	03-Aug-14
CZA-14.3.16.7.16 Roof Nozzles, Manholes and Other Appurtanances		**70h**	**03-Aug-14**	**11-Aug-14**
CZA-TK-0526-3340	Installation and Fit-up	20h	03-Aug-14	05-Aug-14
CZA-TK-0526-3350	Welding	50h	05-Aug-14	11-Aug-14
CZA-TK-0526-3360	Inspection	70h	03-Aug-14	11-Aug-14
CZA-14.3.16.7.18 Stairway Platform, Handrails and Gratings		**130h**	**11-Aug-14**	**26-Aug-14**
CZA-TK-0526-3370	Erection and Fit-up	30h	11-Aug-14	14-Aug-14
CZA-TK-0526-3380	Welding	100h	14-Aug-14	26-Aug-14
CZA-TK-0526-3390	Inspection	130h	11-Aug-14	26-Aug-14
CZA-14.3.16.7.17 Roof Platform, Handrails and Gratings		**130h**	**11-Aug-14**	**26-Aug-14**

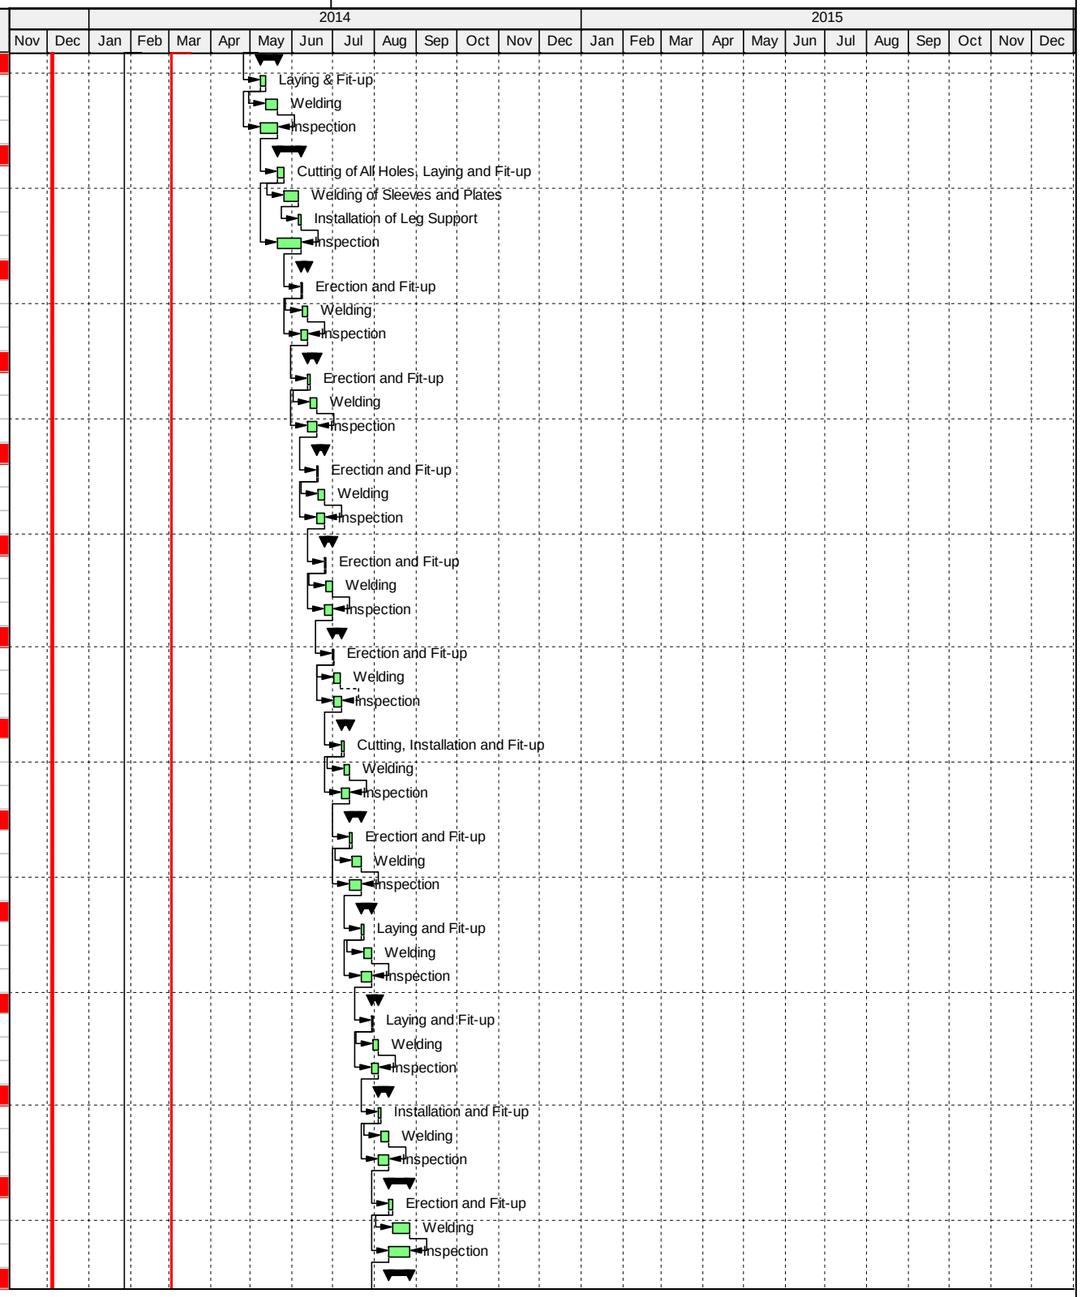

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-0526-3400	Erection and Fit-up	30h	11-Aug-14	14-Aug-14
CZA-TK-0526-3410	Welding	100h	14-Aug-14	26-Aug-14
CZA-TK-0526-3420	Inspection	130h	11-Aug-14	26-Aug-14
CZA-14.3.16.7.20 Installation of Primary and Secondary Seal		**30h**	**26-Aug-14**	**30-Aug-14**
CZA-TK-0526-3430	Installation of Primary and Secondary Seal	30h	26-Aug-14	30-Aug-14
CZA-TK-0526-3440	Inspection	30h	26-Aug-14	30-Aug-14
CZA-14.3.16.4 Hydrotest		**230h**	**30-Aug-14**	**25-Sep-14**
CZA-TK-0526-3450	Filling, Holding and Draining of Water	230h	30-Aug-14	25-Sep-14
CZA-14.3.16.5 Blasting and Painting		**110h**	**25-Sep-14**	**08-Oct-14**
CZA-TK-0526-3460	Blasting and Painting Inside, Outside and Bottom Plates	110h	25-Sep-14	08-Oct-14
CZA-14.3.16.6 Tank Calibration and Handover		**70h**	**08-Oct-14**	**16-Oct-14**
CZA-TK-0526-3470	Tank Calibration	50h	08-Oct-14	14-Oct-14
CZA-TK-0526-3480	Tank Handover	20h	14-Oct-14	16-Oct-14
CZA-14.4 WASTE WATER TREATMENT PLANT(WWTP)		**3436h**	**09-Feb-14**	**16-Mar-15**
CZA-14.4.6 C340-TK-3490(Wash Down Utility Water Tank Dia 19.35m x Ht 12.80m)		**2074h**	**09-Feb-14**	**08-Oct-14**
CZA-14.4.6.1 Fabrication Works		**242h**	**09-Feb-14**	**09-Mar-14**
CZA-TK-3490-2070	Cutting of Annular Plate	8h	09-Feb-14	09-Feb-14
CZA-TK-3490-2080	Cutting of Bottom Plates	8h	09-Feb-14	10-Feb-14
CZA-TK-3490-2090	Cutting, Bevelling & Rolling of Shell No.1	8h	10-Feb-14	11-Feb-14
CZA-TK-3490-2100	Cutting, Bevelling & Rolling of Shell No.2	8h	11-Feb-14	12-Feb-14
CZA-TK-3490-2110	Cutting, Fit-up and Welding of Shell Nozzles,Manholes and Other Appurtanances	40h	12-Feb-14	17-Feb-14
CZA-TK-3490-2120	Cutting, Bevelling & Rolling of Shell No.3	8h	17-Feb-14	17-Feb-14
CZA-TK-3490-2130	Cutting, Bevelling & Rolling of Shell No.4	8h	18-Feb-14	18-Feb-14
CZA-TK-3490-2140	Cutting, Bevelling & Rolling of Shell No.5	8h	18-Feb-14	19-Feb-14
CZA-TK-3490-2150	Cutting, Bevelling & Rolling of Shell No.6	8h	19-Feb-14	20-Feb-14
CZA-TK-3490-2160	Cutting, Bevelling & Rolling of Curb Angle	16h	20-Feb-14	22-Feb-14
CZA-TK-3490-2170	Cutting, Bevelling & Rolling of Roof Structure	40h	23-Feb-14	26-Feb-14
CZA-TK-3490-2180	Cutting of Roof Plates	10h	26-Feb-14	27-Feb-14
CZA-TK-3490-2190	Cutting,Fit-up and Welding of Roof Nozzles, Manholes & Other Appurtanances	40h	27-Feb-14	04-Mar-14
CZA-TK-3490-2200	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	80h	27-Feb-14	09-Mar-14
CZA-TK-3490-2210	Cutting, Fit-up and Welding of Stairway Platfrom, Gratings and Handrails	80h	27-Feb-14	09-Mar-14
CZA-14.4.6.2 Foundation Takeover		**0h**	**15-Mar-14**	**15-Mar-14**
CZA-TK-3490-2220	Foundation Takeover from Client	0h	15-Mar-14	
CZA-14.4.6.7 Mechanical Erection		**1400h**	**16-Mar-14**	**26-Aug-14**
CZA-14.4.6.7.1 Annular Plates		**50h**	**16-Mar-14**	**22-Mar-14**
CZA-TK-3490-2230	Laying and Fit-up	10h	16-Mar-14	17-Mar-14
CZA-TK-3490-2240	Welding	40h	17-Mar-14	22-Mar-14
CZA-TK-3490-2250	Inspection	50h	16-Mar-14	22-Mar-14
CZA-14.4.6.7.19 Bottom Plates		**100h**	**22-Mar-14**	**02-Apr-14**
CZA-TK-3490-2260	Erection and Fit-up	30h	22-Mar-14	25-Mar-14
CZA-TK-3490-2270	Welding	70h	25-Mar-14	02-Apr-14
CZA-TK-3490-2280	Inspection	100h	22-Mar-14	02-Apr-14
CZA-14.4.6.7.2 Shell No.1		**80h**	**02-Apr-14**	**12-Apr-14**
CZA-TK-3490-2290	Erection and Fit-up	10h	02-Apr-14	03-Apr-14
CZA-TK-3490-2300	Welding	70h	03-Apr-14	12-Apr-14
CZA-TK-3490-2310	Inspection	80h	02-Apr-14	12-Apr-14
CZA-14.4.6.7.3 Shell No.2		**80h**	**12-Apr-14**	**21-Apr-14**
CZA-TK-3490-2320	Erection and Fit-up	10h	12-Apr-14	13-Apr-14
CZA-TK-3490-2330	Welding	70h	13-Apr-14	21-Apr-14
CZA-TK-3490-2340	Inspection	80h	12-Apr-14	21-Apr-14
CZA-14.4.6.7.4 Shell Nozzles, Manholes , Attachements and Other Appurtanances (Lower)		**100h**	**21-Apr-14**	**03-May-14**
CZA-TK-3490-2350	Cutting, Installation and Fit-up	20h	21-Apr-14	23-Apr-14
CZA-TK-3490-2360	Welding	80h	23-Apr-14	03-May-14
CZA-TK-3490-2370	Inspection	100h	21-Apr-14	03-May-14

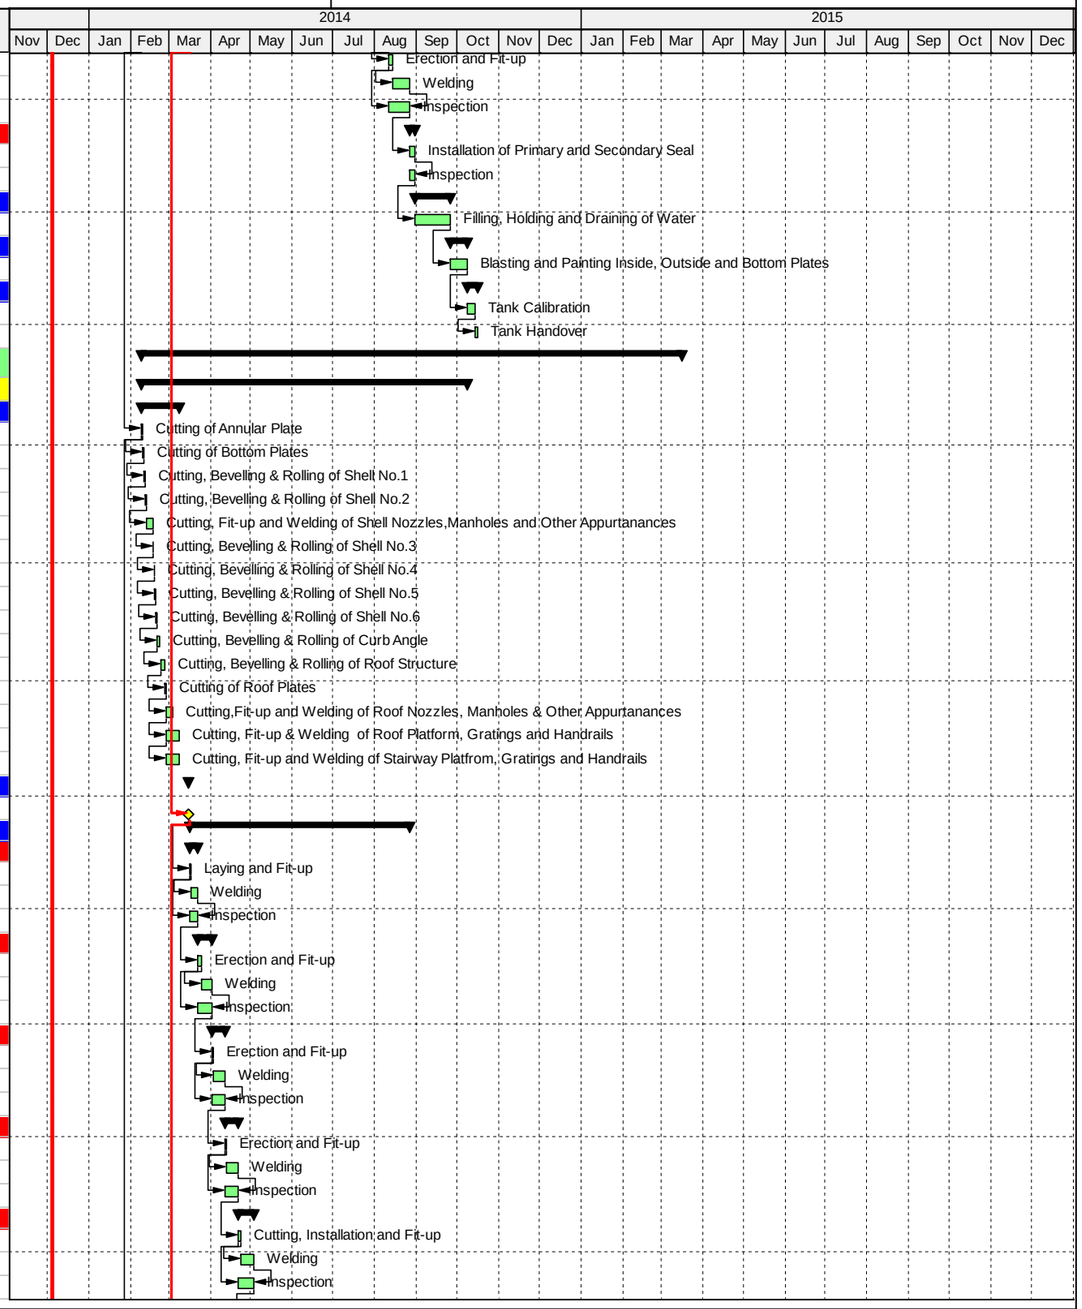

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS			
Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-14.4.6.7.7 Shell No.3		**80h**	**03-May-14**	**12-May-14**
CZA-TK-3490-2380	Erection and Fit-up	10h	03-May-14	04-May-14
CZA-TK-3490-2390	Welding	70h	04-May-14	12-May-14
CZA-TK-3490-2400	Inspection	80h	03-May-14	12-May-14
CZA-14.4.6.7.8 Shell No.4		**80h**	**12-May-14**	**21-May-14**
CZA-TK-3490-2410	Erection and Fit-up	10h	12-May-14	13-May-14
CZA-TK-3490-2420	Welding	70h	13-May-14	21-May-14
CZA-TK-3490-2430	Inspection	80h	12-May-14	21-May-14
CZA-14.4.6.7.9 Shell No.5		**80h**	**21-May-14**	**31-May-14**
CZA-TK-3490-2440	Erection and Fit-up	10h	21-May-14	22-May-14
CZA-TK-3490-2450	Welding	70h	22-May-14	31-May-14
CZA-TK-3490-2460	Inspection	80h	21-May-14	31-May-14
CZA-14.4.6.7.10 Shell No.6		**80h**	**31-May-14**	**09-Jun-14**
CZA-TK-3490-2470	Erection and Fit-up	10h	31-May-14	01-Jun-14
CZA-TK-3490-2480	Welding	70h	01-Jun-14	09-Jun-14
CZA-TK-3490-2490	Inspection	80h	31-May-14	09-Jun-14
CZA-14.4.6.7.12 Shell Nozzles and attachements (Upper)		**80h**	**09-Jun-14**	**18-Jun-14**
CZA-TK-3490-2500	Cutting, Installation and Fit-up	20h	09-Jun-14	11-Jun-14
CZA-TK-3490-2510	Welding	60h	11-Jun-14	18-Jun-14
CZA-TK-3490-2520	Inspection	80h	09-Jun-14	18-Jun-14
CZA-14.4.6.7.13 Roof Structure		**100h**	**18-Jun-14**	**30-Jun-14**
CZA-TK-3490-2530	Erection and Fit-up	30h	18-Jun-14	22-Jun-14
CZA-TK-3490-2540	Welding	70h	22-Jun-14	30-Jun-14
CZA-TK-3490-2550	Inspection	100h	18-Jun-14	30-Jun-14
CZA-14.4.6.7.14 Roof Plates		**70h**	**30-Jun-14**	**08-Jul-14**
CZA-TK-3490-2560	Laying and Fit-up	20h	30-Jun-14	02-Jul-14
CZA-TK-3490-2570	Welding	50h	02-Jul-14	08-Jul-14
CZA-TK-3490-2580	Inspection	70h	30-Jun-14	08-Jul-14
CZA-14.4.6.7.15 Compression Ring		**70h**	**08-Jul-14**	**16-Jul-14**
CZA-TK-3490-2590	Laying and Fit-up	20h	08-Jul-14	10-Jul-14
CZA-TK-3490-2600	Welding	50h	10-Jul-14	16-Jul-14
CZA-TK-3490-2610	Inspection	70h	08-Jul-14	16-Jul-14
CZA-14.4.6.7.16 Roof Nozzles, Manholes and Other Appurtanances		**100h**	**16-Jul-14**	**28-Jul-14**
CZA-TK-3490-2620	Installation and Fit-up	40h	16-Jul-14	21-Jul-14
CZA-TK-3490-2630	Welding	60h	21-Jul-14	28-Jul-14
CZA-TK-3490-2640	Inspection	100h	16-Jul-14	28-Jul-14
CZA-14.4.6.7.18 Stairway Platform, Handrails and Gratings		**170h**	**28-Jul-14**	**17-Aug-14**
CZA-TK-3490-2650	Erection and Fit-up	50h	28-Jul-14	03-Aug-14
CZA-TK-3490-2660	Welding	120h	03-Aug-14	17-Aug-14
CZA-TK-3490-2670	Inspection	170h	28-Jul-14	17-Aug-14
CZA-14.4.6.7.17 Roof Platform, Handrails and Gratings		**170h**	**06-Aug-14**	**26-Aug-14**
CZA-TK-3490-2680	Erection and Fit-up	50h	06-Aug-14	12-Aug-14
CZA-TK-3490-2690	Welding	120h	12-Aug-14	26-Aug-14
CZA-TK-3490-2700	Inspection	170h	06-Aug-14	26-Aug-14
CZA-14.4.6.4 Hydotest		**200h**	**26-Aug-14**	**18-Sep-14**
CZA-TK-3490-2710	Filling, Holding and Draining of Water	200h	26-Aug-14	18-Sep-14
CZA-14.4.6.5 Blasting and Painting		**100h**	**18-Sep-14**	**30-Sep-14**
CZA-TK-3490-2720	Blasting and Painting of Bottom, Shell and Roof (Inside and Outside)	100h	18-Sep-14	30-Sep-14
CZA-14.4.6.6 Tank Calibration and Handover		**70h**	**30-Sep-14**	**08-Oct-14**
CZA-TK-3490-2730	Tank Calibration	50h	30-Sep-14	06-Oct-14
CZA-TK-3490-2740	Tank Handover	20h	06-Oct-14	08-Oct-14
CZA-14.4.9 C340-TK-3491(Contaminated Surface Water Tank Dia 41.94m x Ht 20.75m)		**3436h**	**09-Feb-14**	**16-Mar-15**
CZA-14.4.9.1 Fabrication Works		**360h**	**09-Feb-14**	**22-Mar-14**
CZA-TK-3491-1680	Cutting of Annular Plates	24h	09-Feb-14	11-Feb-14

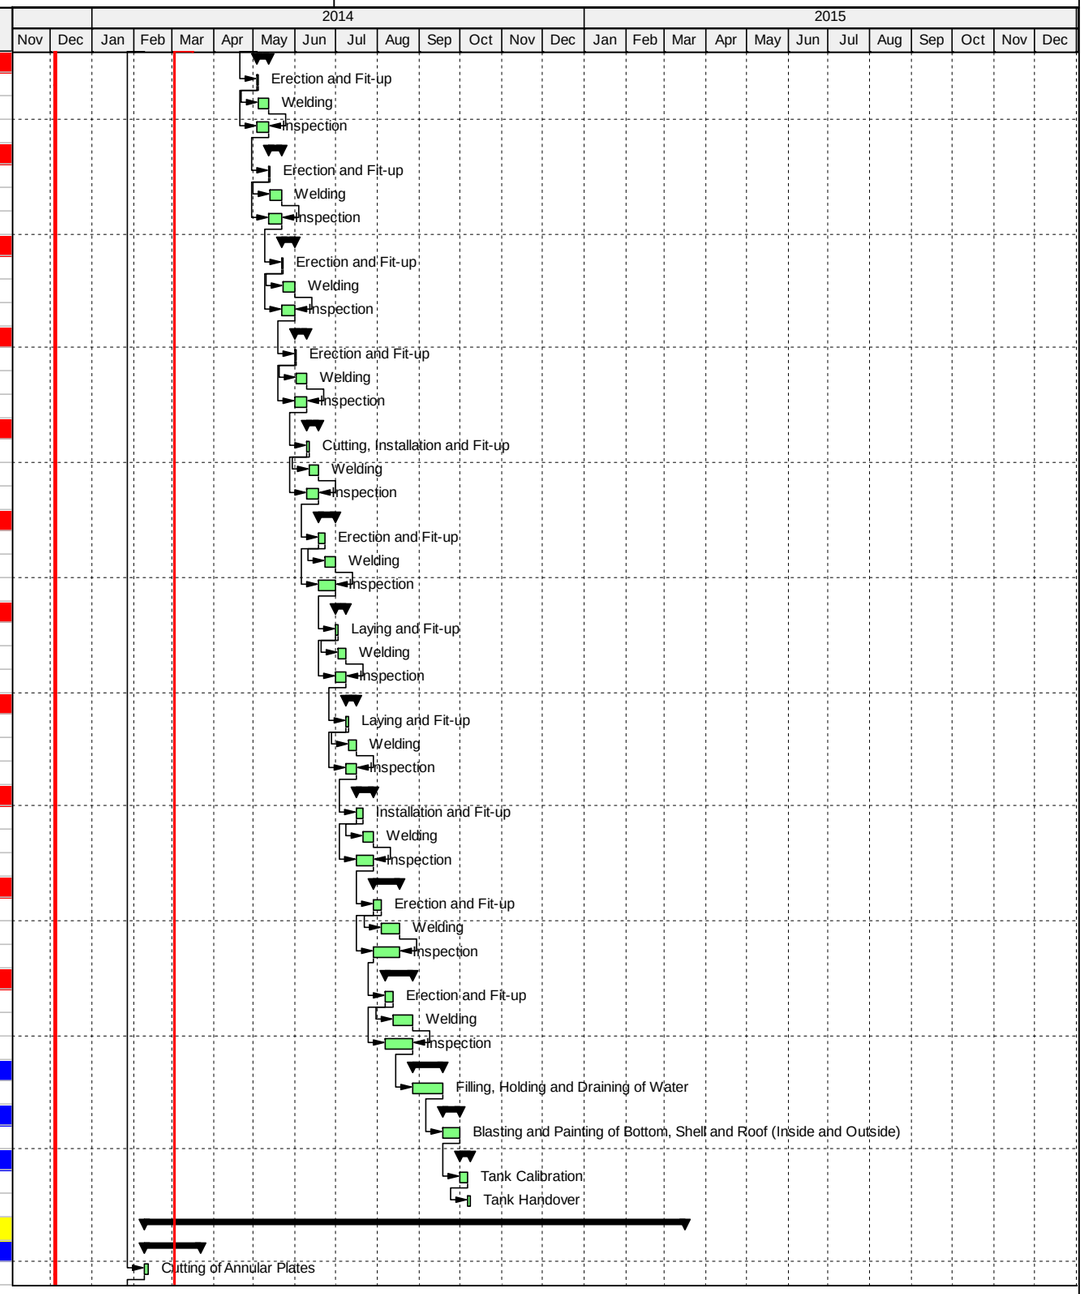

Actual Level of Effort
summary
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-3491-1690	Cutting of Bottom Plates & Compression Ring	24h	09-Feb-14	11-Feb-14
CZA-TK-3491-1700	Cutting, Bevelling & Rolling Shell No.8	16h	11-Feb-14	12-Feb-14
CZA-TK-3491-1710	Cutting, Bevelling and Rolling Shell No.9	16h	11-Feb-14	12-Feb-14
CZA-TK-3491-1750	Cutting, Fit-up, and Welding of Roof Structure & Stairways	112h	13-Feb-14	26-Feb-14
CZA-TK-3491-1760	Cutting of Roof Plates	16h	15-Feb-14	17-Feb-14
CZA-TK-3491-1770	Cutting, Fit-up, & Welding of Roof Nozzles, Manholes & other Appurtanances	48h	17-Feb-14	22-Feb-14
CZA-TK-3491-1780	Cutting, Fit-up & Welding of Roof Platform, Gratings and Handrails	96h	23-Feb-14	05-Mar-14
CZA-TK-3491-1790	Cutting, Bevelling and Rolling Shell No.7	16h	01-Mar-14	03-Mar-14
CZA-TK-3491-1800	Cutting, Bevelling and Rolling Shell No.6	16h	01-Mar-14	03-Mar-14
CZA-TK-3491-1810	Cutting, Bevelling and Rolling Shell No.5	16h	03-Mar-14	04-Mar-14
CZA-TK-3491-1820	Cutting, Bevelling and Rolling Shell No.4	16h	03-Mar-14	04-Mar-14
CZA-TK-3491-1830	Cutting, Bevelling and Rolling Shell No.3	16h	04-Mar-14	06-Mar-14
CZA-TK-3491-1840	Cutting, Bevelling and Rolling Shell No.2	16h	04-Mar-14	06-Mar-14
CZA-TK-3491-1850	Cutting, Bevelling and Rolling Shell No.1	16h	06-Mar-14	08-Mar-14
CZA-TK-3491-1870	Cutting, Fit-up & Welding of Shell Nozzles, Manholes and Other Appurtanances	56h	09-Mar-14	15-Mar-14
CZA-TK-3491-1880	Cutting, Fit-up & Welding of Stairway Platform, Gratings and Handrails	80h	13-Mar-14	22-Mar-14
CZA-14.4.9.2 FoundationTakeover		**0h**	**15-Mar-14**	**15-Mar-14**
CZA-TK-3491-1890	Foundation Takeover From Client	0h	15-Mar-14	
CZA-14.4.9.7 Mechanical Erection		**2150h**	**15-Mar-14**	**20-Nov-14**
CZA-14.4.9.7.1 Annular Plates		**60h**	**15-Mar-14**	**22-Mar-14**
CZA-TK-3491-1900	Laying and Fit-up	20h	15-Mar-14	17-Mar-14
CZA-TK-3491-1910	Welding	40h	17-Mar-14	22-Mar-14
CZA-TK-3491-1920	Inspection	60h	15-Mar-14	22-Mar-14
CZA-14.4.9.7.2 Bottom Plates		**190h**	**22-Mar-14**	**13-Apr-14**
CZA-TK-3491-1930	Laying and Fit-up	40h	22-Mar-14	26-Mar-14
CZA-TK-3491-1940	Welding	150h	26-Mar-14	13-Apr-14
CZA-TK-3491-1950	Inspection	190h	22-Mar-14	13-Apr-14
CZA-14.4.9.7.3 Shell No.8		**100h**	**13-Apr-14**	**24-Apr-14**
CZA-TK-3491-1960	Erection and Fit-up	20h	13-Apr-14	15-Apr-14
CZA-TK-3491-1970	Welding	80h	15-Apr-14	24-Apr-14
CZA-TK-3491-1980	Inspection	100h	13-Apr-14	24-Apr-14
CZA-14.4.9.7.4 Shell No.9		**100h**	**24-Apr-14**	**06-May-14**
CZA-TK-3491-1990	Erection and Fit-up	20h	24-Apr-14	27-Apr-14
CZA-TK-3491-2000	Welding	80h	27-Apr-14	06-May-14
CZA-TK-3491-2010	Inspection	100h	24-Apr-14	06-May-14
CZA-14.4.9.7.5 Shell Nozzles and Other Attachments		**90h**	**06-May-14**	**17-May-14**
CZA-TK-3491-2020	Cutting, Installation and Fit-up	30h	06-May-14	10-May-14
CZA-TK-3491-2030	Welding	60h	10-May-14	17-May-14
CZA-TK-3491-2040	Inspection	90h	06-May-14	17-May-14
CZA-14.4.9.7.6 Stairway Platform, Handrails and Gratings (Upper Part)		**100h**	**17-May-14**	**28-May-14**
CZA-TK-3491-2050	Erection and Fit-up	40h	17-May-14	21-May-14
CZA-TK-3491-2060	Welding	60h	21-May-14	28-May-14
CZA-TK-3491-2070	Inspection	100h	17-May-14	28-May-14
CZA-14.4.9.7.9 Roof Structure		**80h**	**28-May-14**	**07-Jun-14**
CZA-TK-3491-2080	Erection and Fit-up	30h	28-May-14	01-Jun-14
CZA-TK-3491-2090	Welding	50h	01-Jun-14	07-Jun-14
CZA-TK-3491-2100	Inspection	80h	28-May-14	07-Jun-14
CZA-14.4.9.7.10 Roof Plates		**120h**	**07-Jun-14**	**21-Jun-14**
CZA-TK-3491-2110	Laying and Fit-up	40h	07-Jun-14	11-Jun-14
CZA-TK-3491-2120	Welding	80h	11-Jun-14	21-Jun-14
CZA-TK-3491-2130	Inspection	120h	07-Jun-14	21-Jun-14
CZA-14.4.9.7.11 Compression Ring		**100h**	**21-Jun-14**	**02-Jul-14**
CZA-TK-3491-2140	Laying and Fit-up	20h	21-Jun-14	23-Jun-14
CZA-TK-3491-2150	Welding	80h	23-Jun-14	02-Jul-14

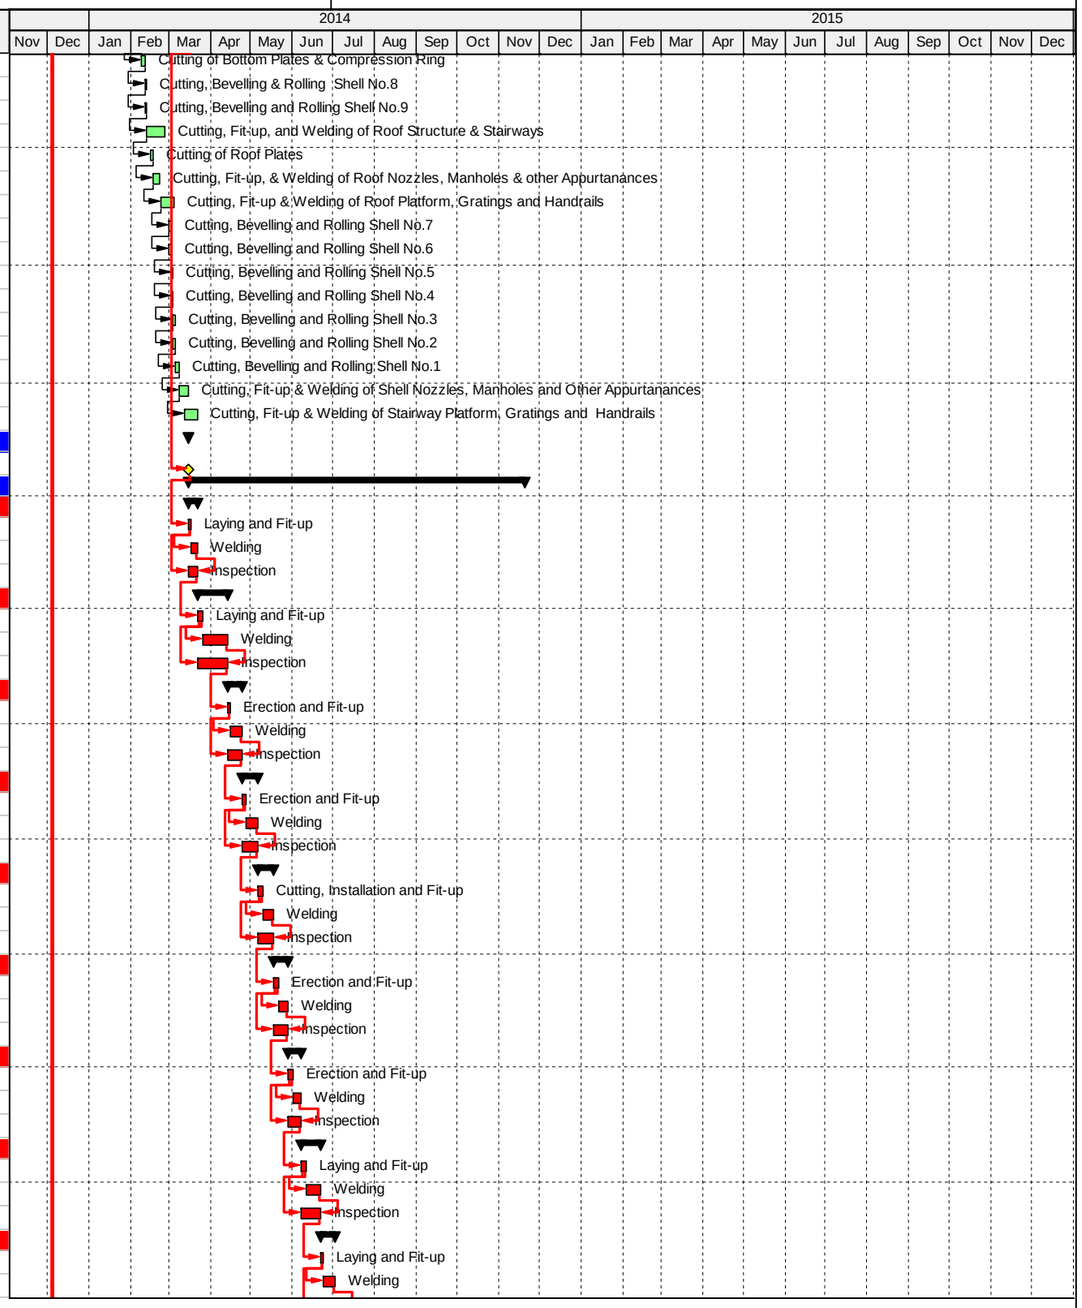

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects

AL ZAMIL METAL WORKS FACTORY

CS CARBON STEEL STORAGE TANKS NO.OF 33 - FABRICATION

PETROFAC SAUDI ARABIA LTD.

Activity ID	Activity Name	Original Duration	Start	Finish
CZA-TK-3491-2160	Inspection	100h	21-Jun-14	02-Jul-14
CZA-14.4.9.7.12	**Roof Nozzles, Manholes and Other Appurtanances**	100h	02-Jul-14	14-Jul-14
CZA-TK-3491-2170	Cutting,Installation and Fit-up	40h	02-Jul-14	07-Jul-14
CZA-TK-3491-2180	Welding	60h	07-Jul-14	14-Jul-14
CZA-TK-3491-2190	Inspection	80h	05-Jul-14	14-Jul-14
CZA-14.4.9.7.13	**Roof Platform, Gratings and Handrails**	140h	14-Jul-14	30-Jul-14
CZA-TK-3491-2200	Erection and Fit-up	40h	14-Jul-14	19-Jul-14
CZA-TK-3491-2210	Welding	100h	19-Jul-14	30-Jul-14
CZA-TK-3491-2220	Inspection	140h	14-Jul-14	30-Jul-14
CZA-14.4.9.7.14	**Shell No.7**	100h	30-Jul-14	11-Aug-14
CZA-TK-3491-2230	Jacking, Erection and Fit-up	20h	30-Jul-14	02-Aug-14
CZA-TK-3491-2240	Welding	80h	02-Aug-14	11-Aug-14
CZA-TK-3491-2250	Inspection	100h	30-Jul-14	11-Aug-14
CZA-14.4.9.7.15	**Shell No.6**	100h	11-Aug-14	23-Aug-14
CZA-TK-3491-2260	Jacking,Erection and Fit-up	20h	11-Aug-14	13-Aug-14
CZA-TK-3491-2270	Welding	80h	13-Aug-14	23-Aug-14
CZA-TK-3491-2280	Inspection	100h	11-Aug-14	23-Aug-14
CZA-14.4.9.7.16	**Shell No.5**	100h	23-Aug-14	03-Sep-14
CZA-TK-3491-2290	Jacking,Erection and Fit-up	20h	23-Aug-14	25-Aug-14
CZA-TK-3491-2300	Welding	80h	25-Aug-14	03-Sep-14
CZA-TK-3491-2310	Inspection	100h	23-Aug-14	03-Sep-14
CZA-14.4.9.7.17	**Shell No.4**	100h	03-Sep-14	15-Sep-14
CZA-TK-3491-2320	Jacking, Erection and Fit-up	20h	03-Sep-14	06-Sep-14
CZA-TK-3491-2330	Welding	80h	06-Sep-14	15-Sep-14
CZA-TK-3491-2340	Inspection	100h	03-Sep-14	15-Sep-14
CZA-14.4.9.7.18	**Shell No.3**	100h	15-Sep-14	27-Sep-14
CZA-TK-3491-2350	Jacking, Erection and Fit-up	20h	15-Sep-14	17-Sep-14
CZA-TK-3491-2360	Welding	80h	17-Sep-14	27-Sep-14
CZA-TK-3491-2370	Inspection	100h	15-Sep-14	27-Sep-14
CZA-14.4.9.7.19	**Shell No.2**	100h	27-Sep-14	08-Oct-14
CZA-TK-3491-2380	Jacking, Erection and Fit-up	20h	27-Sep-14	29-Sep-14
CZA-TK-3491-2390	Welding	80h	29-Sep-14	08-Oct-14
CZA-TK-3491-2400	Inspection	100h	27-Sep-14	08-Oct-14
CZA-14.4.9.7.20	**Shell No.1**	100h	08-Oct-14	20-Oct-14
CZA-TK-3491-2410	Jacking, Erection and Fit-up	20h	08-Oct-14	11-Oct-14
CZA-TK-3491-2420	Welding	80h	11-Oct-14	20-Oct-14
CZA-TK-3491-2430	Inspection	100h	08-Oct-14	20-Oct-14
CZA-14.4.9.7.22	**Shell Nozzles, Manholes , Attachments and Other Appurtanances**	120h	20-Oct-14	03-Nov-14
CZA-TK-3491-2440	Lay-out, Cutting, and Fit-up	40h	20-Oct-14	25-Oct-14
CZA-TK-3491-2450	Welding	80h	25-Oct-14	03-Nov-14
CZA-TK-3491-2460	Inspection	120h	20-Oct-14	03-Nov-14
CZA-14.4.9.7.23	**Stairway Platform, Handrails and Gratings (Lower Part)**	150h	03-Nov-14	20-Nov-14
CZA-TK-3491-2470	Erection and Fit-up	30h	03-Nov-14	06-Nov-14
CZA-TK-3491-2480	Welding	120h	06-Nov-14	20-Nov-14
CZA-TK-3491-2490	Inspection	150h	03-Nov-14	20-Nov-14
CZA-14.4.9.4	**Hydrotest**	610h	20-Nov-14	31-Jan-15
CZA-TK-3491-2500	Filling, Holding and Draining of Water	610h	20-Nov-14	31-Jan-15
CZA-14.4.9.5	**Blasting and Painting**	310h	31-Jan-15	08-Mar-15
CZA-TK-3491-2510	Blasting and Painting (Shell, Roof & Bottom)-Outside & Inside	310h	31-Jan-15	08-Mar-15
CZA-14.4.9.6	**Tank Calibration and Handover**	70h	08-Mar-15	16-Mar-15
CZA-TK-3491-2520	Tank Calibration	50h	08-Mar-15	14-Mar-15
CZA-TK-3491-2530	Tank Handover	20h	14-Mar-15	16-Mar-15

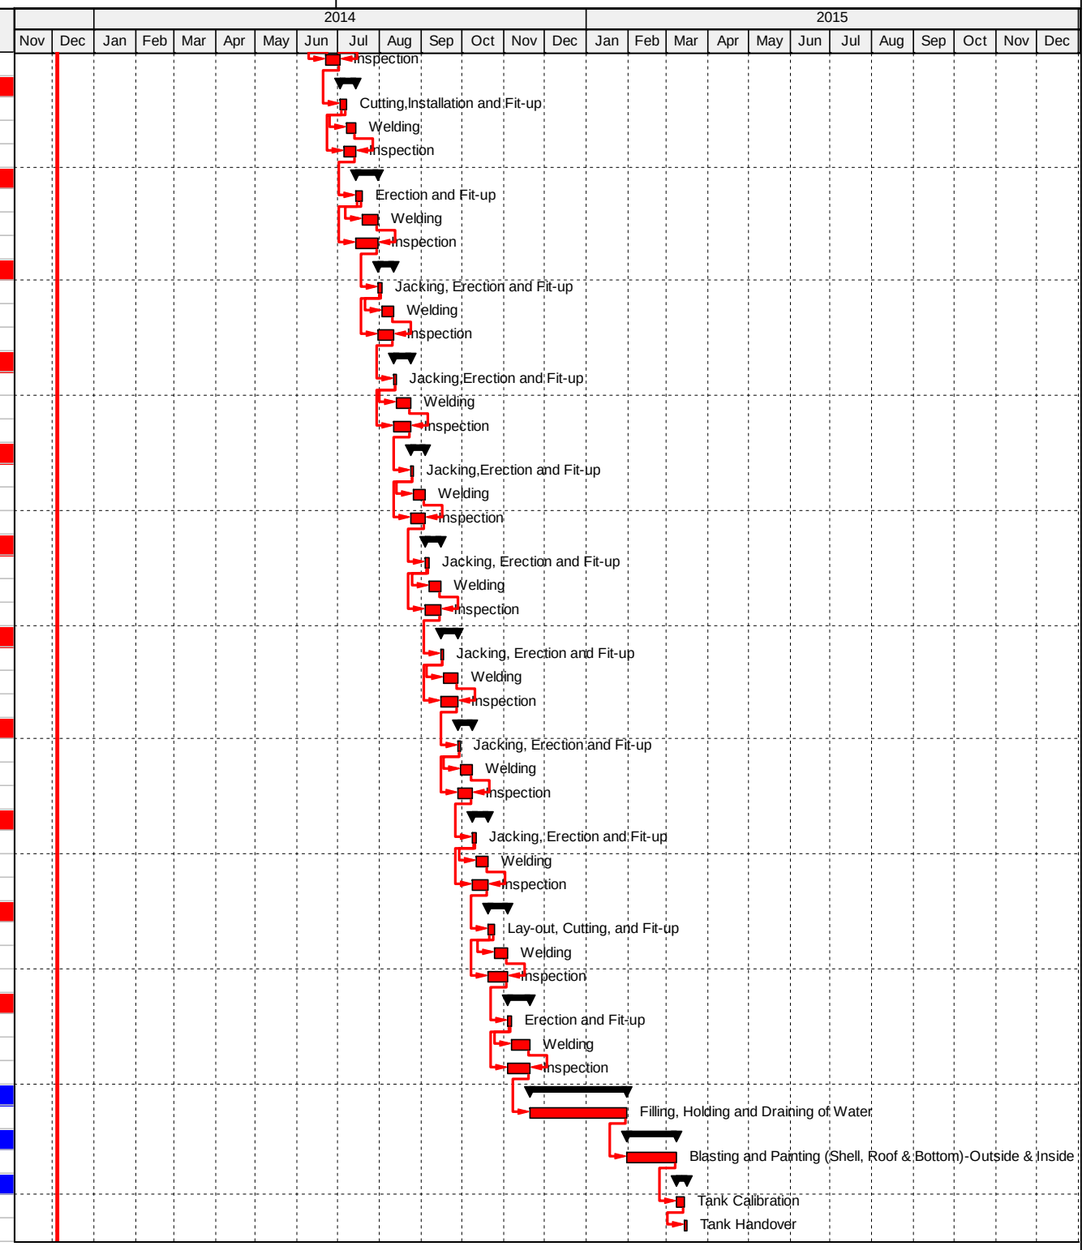

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Baseline Milestone
summary

CS CARBON STEEL STORAGE TANKS

Date	Revision	Checked	Approved
11-Dec-13	Rev.0	Planning	Projects
01-Jan-14	Rev.01	Planning	Projects
19-Jan-14	Rev.02 with last Comments Recieved by client	Planning	Projects
