Medor Adminstration Building

Consultant : Prof.Dr : Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Medor Adminstration Building		226	07-Jul-10 A	31-Mar-11	07-Jul-10	03-Apr-11	
general		226	07-Jul-10 A	31-Mar-11	07-Jul-10	03-Apr-11	
engineering		72	07-Jul-10 A	29-Sep-10	07-Jul-10	12-Aug-10	
skeleton		218	10-Jul-10 A	31-Mar-11	17-Jul-10	03-Apr-11	
ground floor		22	10-Jul-10 A	07-Aug-1...	17-Jul-10	10-Aug-10	
A1350	Slab Formwork & Rft. Part1	10	10-Jul-10 A	16-Jul-10 A	17-Jul-10	27-Jul-10	100%
A1330	columns Formwork & Rft. Part 2	8	17-Jul-10 A	27-Jul-10 A	17-Jul-10	25-Jul-10	100%
A1340	Columns Pouring Part2	1	28-Jul-10 A	28-Jul-10 A	26-Jul-10	26-Jul-10	100%
A1370	Slab Formwork & Rft. Part2	10	29-Jul-10 A	05-Aug-1...	29-Jul-10	09-Aug-10	100%
A1380	Slab Pouring	1	07-Aug-1...	07-Aug-1...	10-Aug-10	10-Aug-10	100%
1st floor		29	08-Aug-1...	14-Sep-10	12-Aug-10	16-Sep-10	
A1390	columns Formwork & Rft. Part1	8	08-Aug-1...	24-Aug-1...	12-Aug-10	21-Aug-10	100%
A1410	columns Formwork & Rft. Part 2	8	22-Aug-1...	29-Aug-1...	22-Aug-10	30-Aug-10	100%
A1400	Columns Pouring Part1	1	25-Aug-1...	25-Aug-1...	22-Aug-10	22-Aug-10	100%
A1420	Slab Formwork & Rft. Part1	10	26-Aug-1...	13-Sep-10	24-Aug-10	04-Sep-10	60%
A1440	Columns Pouring Part2	1	30-Aug-1...	30-Aug-1...	31-Aug-10	31-Aug-10	100%
A1460	Slab Formwork & Rft. Part2	10	31-Aug-1...	11-Sep-10	04-Sep-10	15-Sep-10	20%
A1480	Slab Pouring	1	14-Sep-10	14-Sep-10	16-Sep-10	16-Sep-10	0%
2nd floor		30	16-Sep-10	20-Oct-10	19-Sep-10	23-Oct-10	
A1490	columns Formwork & Rft. Part1	8	16-Sep-10	25-Sep-10	19-Sep-10	27-Sep-10	0%
A1500	Columns Pouring Part1	1	26-Sep-10	26-Sep-10	28-Sep-10	28-Sep-10	0%
A1510	columns Formwork & Rft. Part 2	8	26-Sep-10	04-Oct-10	28-Sep-10	06-Oct-10	0%

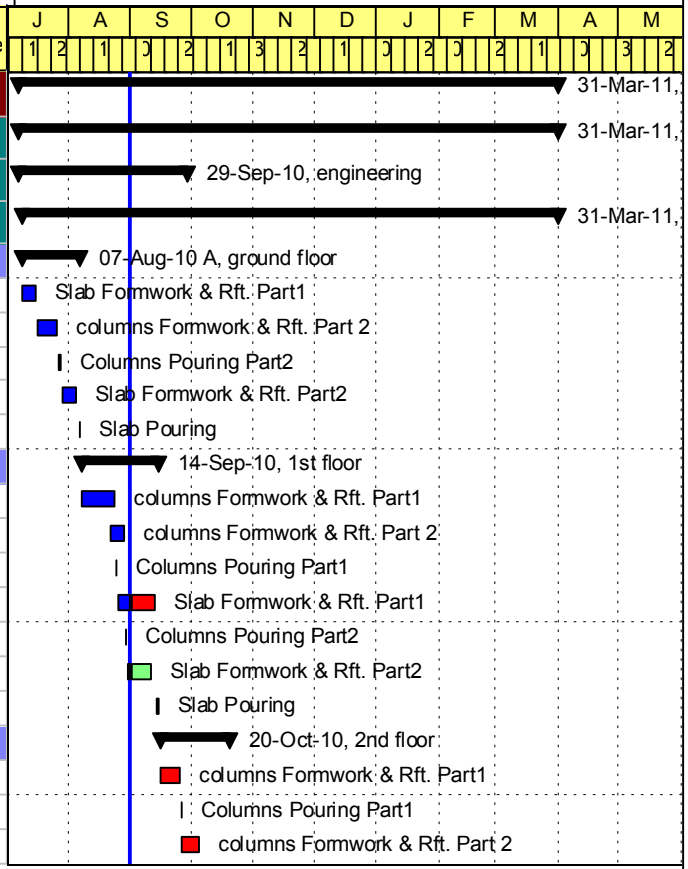

- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

B.L Project Start : 07-Jul-2010

B.L Project Finish: 03-Apr-2011

Start Project : 07-Jul-10

Finish Project : 31-Mar-11

Update 01-09-2010

TASK filter: All Activities

1 of 3

Date	Revision	Checked	Approved
24-Aug-10	Revision 2		

Medor Adminstration Building

Consultant : Prof.Dr : Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
A1520	Slab Formwork & Rft. Part1	10	28-Sep-10	09-Oct-10	30-Sep-10	11-Oct-10	0%
A1540	Columns Pouring Part2	1	05-Oct-10	05-Oct-10	07-Oct-10	07-Oct-10	0%
A1560	Slab Formwork & Rft. Part2	10	09-Oct-10	19-Oct-10	11-Oct-10	21-Oct-10	0%
A1580	Slab Pouring	1	20-Oct-10	20-Oct-10	23-Oct-10	23-Oct-10	0%
3rd floor		29	23-Oct-10	28-Nov-10	25-Oct-10	30-Nov-10	
A1590	columns Formwork & Rft. Part1	8	23-Oct-10	31-Oct-10	25-Oct-10	02-Nov-10	0%
A1610	columns Formwork & Rft. Part 2	8	31-Oct-10	08-Nov-10	02-Nov-10	10-Nov-10	0%
A1600	Columns Pouring Part1	1	01-Nov-10	01-Nov-10	03-Nov-10	03-Nov-10	0%
A1620	Slab Formwork & Rft. Part1	10	03-Nov-10	14-Nov-10	06-Nov-10	20-Nov-10	0%
A1640	Columns Pouring Part2	1	09-Nov-10	09-Nov-10	11-Nov-10	11-Nov-10	0%
A1660	Slab Formwork & Rft. Part2	10	13-Nov-10	27-Nov-10	15-Nov-10	29-Nov-10	0%
A1680	Slab Pouring	1	28-Nov-10	28-Nov-10	30-Nov-10	30-Nov-10	0%
4th floor		29	30-Nov-10	02-Jan-11	02-Dec-10	04-Jan-11	
A1690	columns Formwork & Rft. Part1	8	30-Nov-10	08-Dec-10	02-Dec-10	11-Dec-10	0%
A1710	columns Formwork & Rft. Part 2	8	08-Dec-10	16-Dec-10	11-Dec-10	19-Dec-10	0%
A1700	Columns Pouring Part1	1	09-Dec-10	09-Dec-10	12-Dec-10	12-Dec-10	0%
A1720	Slab Formwork & Rft. Part1	10	12-Dec-10	22-Dec-10	14-Dec-10	25-Dec-10	0%
A1740	Columns Pouring Part2	1	18-Dec-10	18-Dec-10	20-Dec-10	20-Dec-10	0%
A1760	Slab Formwork & Rft. Part2	10	21-Dec-10	01-Jan-11	23-Dec-10	03-Jan-11	0%
A1780	Slab Pouring	1	02-Jan-11	02-Jan-11	04-Jan-11	04-Jan-11	0%
5th floor		29	04-Jan-11	06-Feb-11	06-Jan-11	08-Feb-11	
A1790	columns Formwork & Rft. Part1	8	04-Jan-11	12-Jan-11	06-Jan-11	15-Jan-11	0%
A1810	columns Formwork & Rft. Part 2	8	12-Jan-11	20-Jan-11	15-Jan-11	23-Jan-11	0%

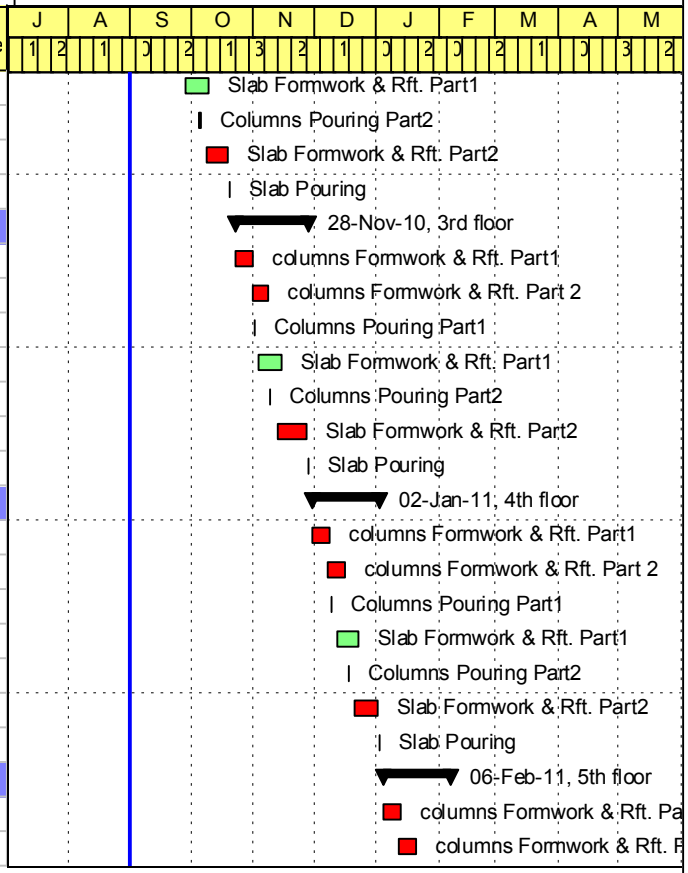

- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

B.L Project Start : 07-Jul-2010

B.L Project Finish: 03-Apr-2011

Start Project : 07-Jul-10

Finish Project : 31-Mar-11

Update 01-09-2010

TASK filter: All Activities

2 of 3

Date	Revision	Checked	Approved
24-Aug-10	Revision 2		

Medor Adminstration Building

Consultant : Prof.Dr : Kamal Hassan

Activity ID	Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
A1800	Columns Pouring Part1	1	13-Jan-11	13-Jan-11	16-Jan-11	16-Jan-11	0%
A1820	Slab Formwork & Rft. Part1	10	16-Jan-11	26-Jan-11	18-Jan-11	29-Jan-11	0%
A1840	Columns Pouring Part2	1	22-Jan-11	22-Jan-11	24-Jan-11	24-Jan-11	0%
A1860	Slab Formwork & Rft. Part2	10	25-Jan-11	05-Feb-11	27-Jan-11	07-Feb-11	0%
A1880	Slab Pouring	1	06-Feb-11	06-Feb-11	08-Feb-11	08-Feb-11	0%
6th floor		29	08-Feb-11	13-Mar-11	10-Feb-11	15-Mar-11	
A1890	columns Formwork & Rft. Part1	8	08-Feb-11	16-Feb-11	10-Feb-11	19-Feb-11	0%
A1910	columns Formwork & Rft. Part 2	8	16-Feb-11	24-Feb-11	19-Feb-11	27-Feb-11	0%
A1900	Columns Pouring Part1	1	17-Feb-11	17-Feb-11	20-Feb-11	20-Feb-11	0%
A1920	Slab Formwork & Rft. Part1	10	20-Feb-11	02-Mar-11	22-Feb-11	05-Mar-11	0%
A1940	Columns Pouring Part2	1	26-Feb-11	26-Feb-11	28-Feb-11	28-Feb-11	0%
A1960	Slab Formwork & Rft. Part2	10	01-Mar-11	12-Mar-11	03-Mar-11	14-Mar-11	0%
A1980	Slab Pouring	1	13-Mar-11	13-Mar-11	15-Mar-11	15-Mar-11	0%
Roof floor		14	16-Mar-11	31-Mar-11	19-Mar-11	03-Apr-11	
A2130	columns Formwork & Rft.	5	16-Mar-11	21-Mar-11	19-Mar-11	23-Mar-11	0%
A2140	Columns Pouring	1	22-Mar-11	22-Mar-11	24-Mar-11	24-Mar-11	0%
A2150	Slab Formwork & Rft.	7	23-Mar-11	30-Mar-11	26-Mar-11	02-Apr-11	0%
A2160	Slab Pouring	1	31-Mar-11	31-Mar-11	03-Apr-11	03-Apr-11	0%

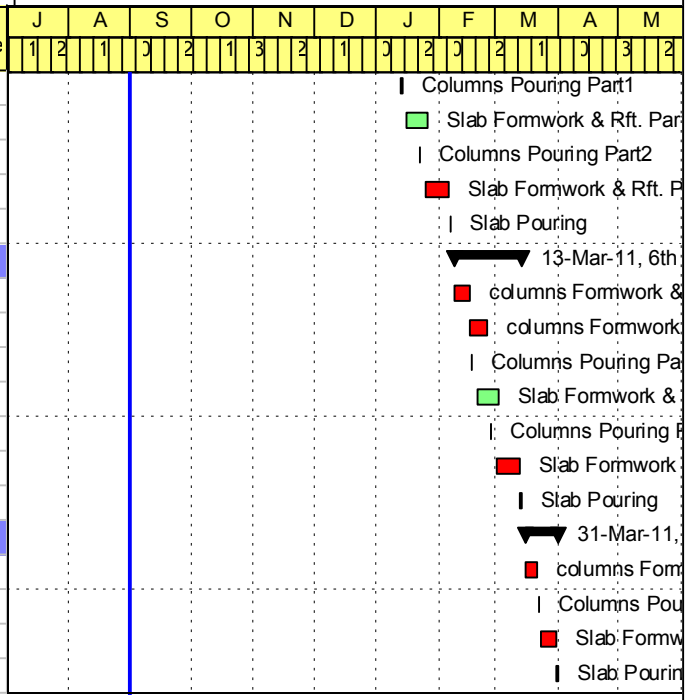

- Remaining Level of Effort
- Actual Work
- Remaining Work
- Critical Remaining Work
- Milestone
- Summary

B.L Project Start : 07-Jul-2010

B.L Project Finish: 03-Apr-2011

Start Project : 07-Jul-10

Finish Project : 31-Mar-11

Update 01-09-2010

TASK filter: All Activities

3 of 3

Date	Revision	Checked	Approved
24-Aug-10	Revision 2		
