Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
Office Building 14B01 Substructure Package		94	01-Jul-10 A	18-Oct-10
General		94	01-Jul-10	18-Oct-10
A1000	Start project	0	01-Jul-10	
A1010	Finish project	0		18-Oct-10
A1020	Mobilization	20	01-Jul-10	24-Jul-10
A1320	Receive issue for construction drawings	0	01-Jul-10	
Engineering		42	01-Jul-10	18-Aug-10
Part 1		33	01-Jul-10	08-Aug-10
A1140	Submittal of basement slab concrete	0	01-Jul-10	
A1141	Approval of basement slab concrete	0		04-Jul-10
A1150	Submittal of column layout	0	01-Jul-10	
A1151	Approval of column layout	0		04-Jul-10
A1160	Submittal of basement slab RFT&starters	0	12-Jul-10	
A1161	Approval of basement slab RFT&starters	0		14-Jul-10
A1170	Submittal of vertical element RFT	0	22-Jul-10	
A1171	Approval of vertical element RFT	0		25-Jul-10
A1180	Submittal of ground floor slab concrete	0	29-Jul-10	
A1181	Approval of ground floor slab concrete	0		01-Aug-10
A1190	Submittal of ground floor slab RFT	0	05-Aug-10	
A1191	Approval of ground floor slab RFT	0		08-Aug-10
Part 2		33	12-Jul-10	18-Aug-10
A1200	Submittal of basement slab concrete	0	12-Jul-10	
A1201	Approval of basement slab concrete	0		14-Jul-10
A1210	Submittal of column layout	0	12-Jul-10	
A1211	Approval of column layout	0		14-Jul-10
A1220	Submittal of basement slab RFT&starters	0	22-Jul-10	
A1221	Approval of basement slab RFT&starters	0		25-Jul-10
A1230	Submittal of vertical element RFT	0	29-Jul-10	

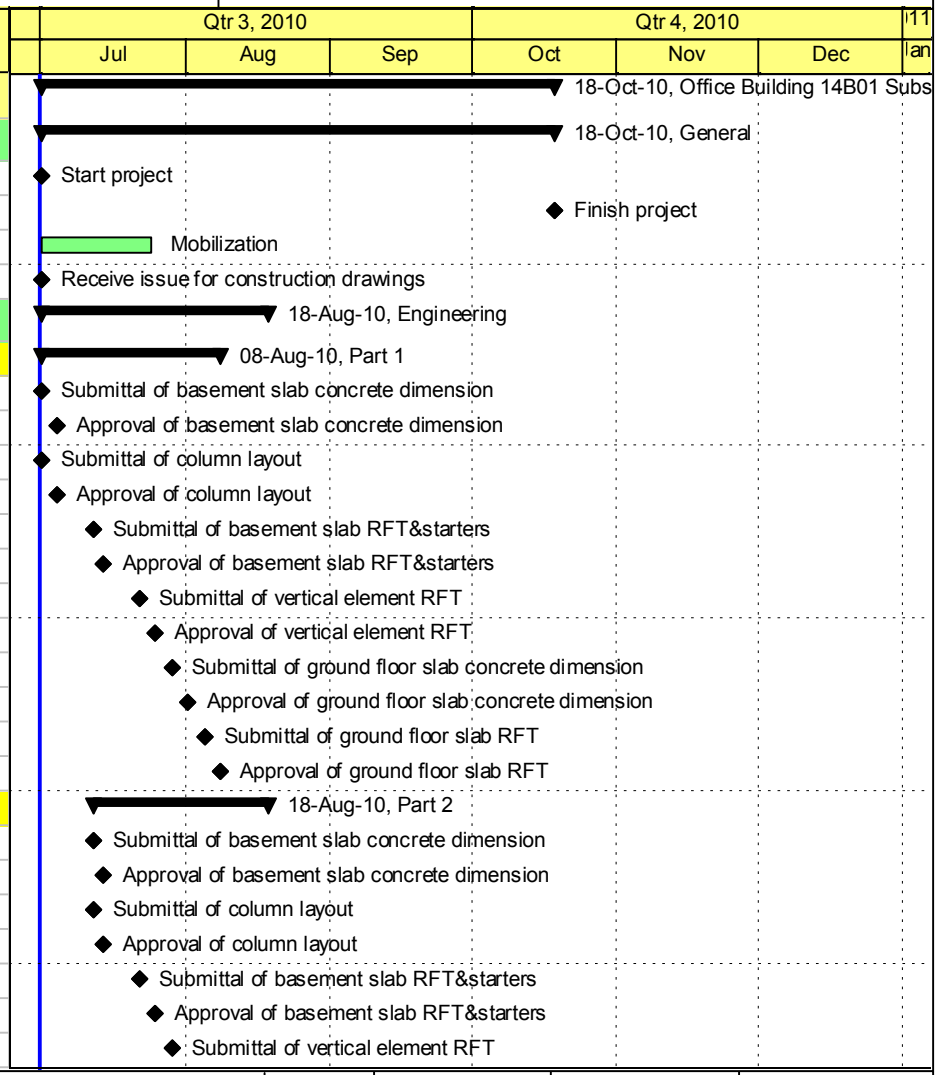

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		

Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
A1231	Approval of vertical element RFT	0		01-Aug-10
A1240	Submittal of ground floor slab concrete	0	05-Aug-10	
A1241	Approval of ground floor slab concrete	0		08-Aug-10
A1250	Submittal of ground floor slab RFT	0	16-Aug-10	
A1251	Approval of ground floor slab RFT	0		18-Aug-10
Tank		3	08-Jul-10	11-Jul-10
A1260	submittals of tank's shop drawings	0	08-Jul-10	
A2170	Approval of tank's shop drawings	0		11-Jul-10
construction		85	12-Jul-10	18-Oct-10
A1580	Start construction	0	12-Jul-10	
A1590	Finish construction	0		18-Oct-10
Office building		81	17-Jul-10	18-Oct-10
Part1		79	17-Jul-10	16-Oct-10
Area 1		69	25-Jul-10	12-Oct-10
A1268	Plain concrete foundation	6	27-Jul-10	02-Aug-10
A1269	Cable ducts fixing	2	25-Jul-10	26-Jul-10
A1270	Formwork For R.C raft	6	05-Aug-10	11-Aug-10
A1279	hammock for raft	12	05-Aug-10	18-Aug-10
A1280	Rebar For R.C raft	4	12-Aug-10	16-Aug-10
A1289	hammock for basement columns & walls	10	19-Aug-10	30-Aug-10
A1290	M&E conduits For R.C raft (by others)	0		14-Aug-10
A1299	hammock for ground floorslab	16	08-Sep-10	26-Sep-10
A1300	Pouring For R.C raft	1	17-Aug-10	17-Aug-10
A1310	Isolation For Foundation	4	01-Sep-10	05-Sep-10
A1330	Masonry works	7	05-Oct-10	12-Oct-10
A1340	Water proofing membrane	4	31-Aug-10	04-Sep-10
A1350	Water proofing protection layer	4	05-Sep-10	08-Sep-10
A1360	Formwork For basement walls & col.	8	19-Aug-10	28-Aug-10

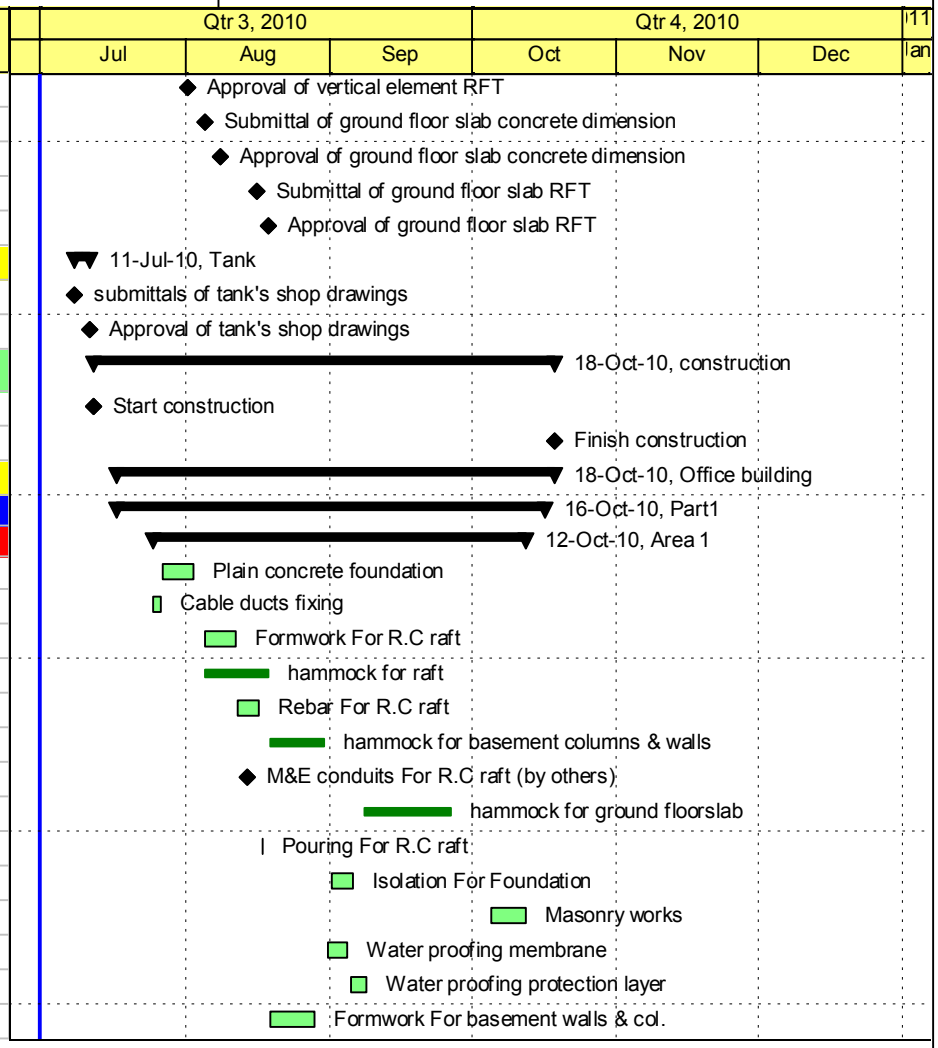

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		

Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
A1370	Rebar For basement walls & col.	4	22-Aug-10	25-Aug-10
A1380	Pouring For basement walls & col.	1	29-Aug-10	29-Aug-10
A1390	Formwork For Ground Floor Slab	6	08-Sep-10	14-Sep-10
A1400	Rebar For Ground Floor Slab	3	13-Sep-10	15-Sep-10
A1410	M&E conduits For Ground Floor Slab (by	0		14-Sep-10
A1420	Pouring For Ground Floor Slab	1	16-Sep-10	16-Sep-10
A2180	Backfilling Around Foundation	8	21-Sep-10	29-Sep-10
Area 2		**78**	**17-Jul-10**	**14-Oct-10**
A1030	Formwork For R.C raft	8	17-Jul-10	25-Jul-10
A1040	Rebar For R.C raft	6	26-Jul-10	01-Aug-10
A1050	M&E conduits For R.C raft (by others)	0		31-Jul-10
A1060	Pouring For R.C raft	2	02-Aug-10	03-Aug-10
A1061	Isolation For Foundation	6	21-Aug-10	26-Aug-10
A1062	Backfilling Around Foundation	8	29-Sep-10	07-Oct-10
A1063	Masonry works	9	05-Oct-10	14-Oct-10
A1064	Water proofing membrane	6	19-Aug-10	25-Aug-10
A1065	Water proofing protection layer	6	26-Aug-10	01-Sep-10
A1070	Formwork For basement walls & col.	8	08-Aug-10	16-Aug-10
A1080	Rebar For basement walls & col.	6	10-Aug-10	16-Aug-10
A1090	Pouring For basement walls & col.	1	17-Aug-10	17-Aug-10
A1100	Formwork For Ground Floor Slab	10	19-Aug-10	30-Aug-10
A1110	Rebar For Ground Floor Slab	6	29-Aug-10	04-Sep-10
A1120	M&E conduits For Ground Floor Slab (by	0		02-Sep-10
A1130	Pouring For Ground Floor Slab	1	05-Sep-10	05-Sep-10
A2220	hammock for raft	17	17-Jul-10	04-Aug-10
A2230	hammock for basement columns & walls	10	08-Aug-10	18-Aug-10
A2240	hammock for ground floorslab	23	19-Aug-10	14-Sep-10
Area 3		**75**	**21-Jul-10**	**16-Oct-10**
A1430	Formwork For R.C raft	6	21-Jul-10	27-Jul-10

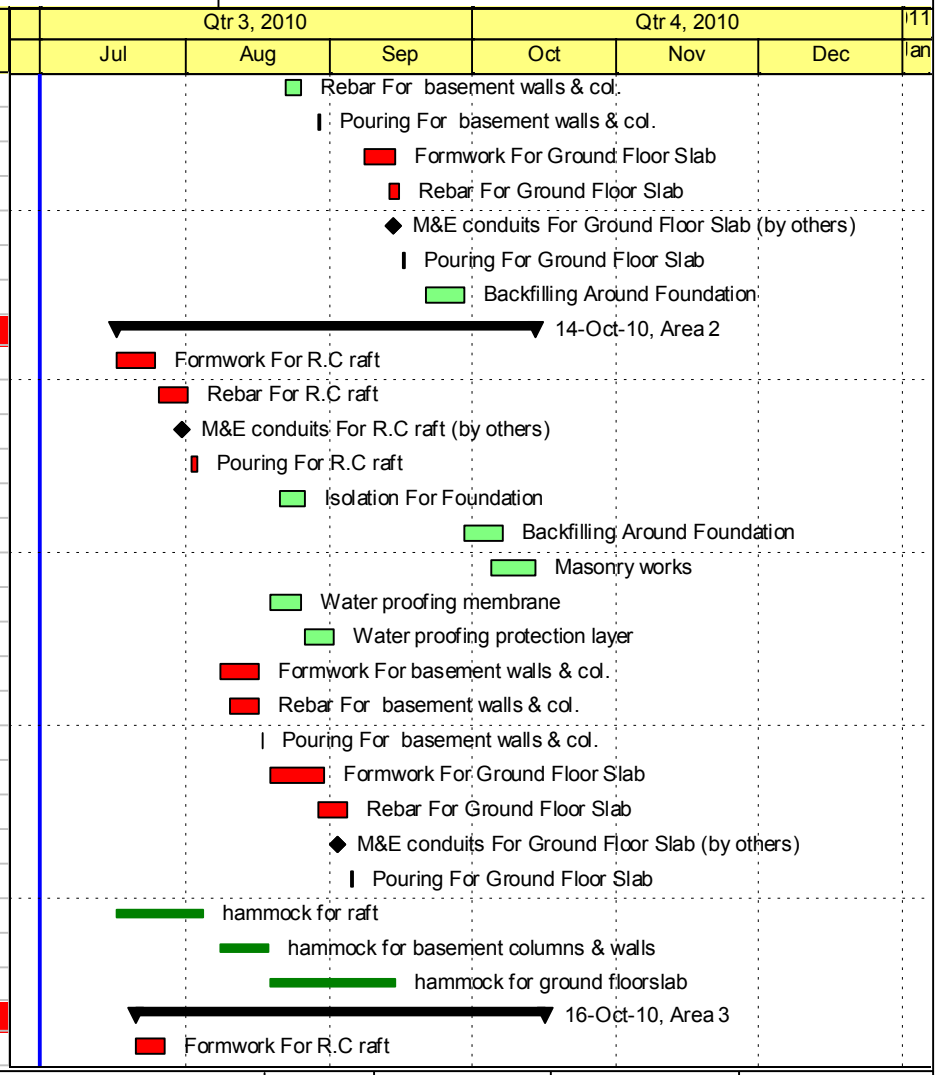

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		

Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
A1440	Rebar For R.C raft	4	26-Jul-10	29-Jul-10
A1450	M&E conduits For R.C raft (by others)	0		28-Jul-10
A1460	Pouring For R.C raft	1	31-Jul-10	31-Jul-10
A1470	Isolation For Foundation	8	21-Aug-10	29-Aug-10
A1480	Masonry works	7	03-Oct-10	10-Oct-10
A1490	Water proofing membrane	6	18-Aug-10	24-Aug-10
A1500	Water proofing protection layer	8	25-Aug-10	02-Sep-10
A1510	Formwork For basement walls & col.	6	08-Aug-10	14-Aug-10
A1520	Rebar For basement walls & col.	4	11-Aug-10	15-Aug-10
A1530	Pouring For basement walls & col.	1	16-Aug-10	16-Aug-10
A1540	Formwork For Ground Floor Slab	8	18-Aug-10	26-Aug-10
A1550	Rebar For Ground Floor Slab	3	25-Aug-10	28-Aug-10
A1560	M&E conduits For Ground Floor Slab (by	0		26-Aug-10
A1570	Pouring For Ground Floor Slab	1	29-Aug-10	29-Aug-10
A2190	Backfilling Around Foundation	12	03-Oct-10	16-Oct-10
A2250	hammock for raft	10	21-Jul-10	01-Aug-10
A2260	hammock for basement columns & walls	9	08-Aug-10	17-Aug-10
A2270	hammock for ground floorslab	18	18-Aug-10	07-Sep-10
Part 2		64	05-Aug-10	18-Oct-10
Area 1		52	19-Aug-10	18-Oct-10
A1760	Formwork For R.C raft	6	19-Aug-10	25-Aug-10
A1770	Rebar For R.C raft	4	26-Aug-10	30-Aug-10
A1780	M&E conduits For R.C raft (by others)	0		29-Aug-10
A1790	Pouring For R.C raft	1	31-Aug-10	31-Aug-10
A1800	Formwork For basement walls & col.	8	02-Sep-10	11-Sep-10
A1810	Rebar For basement walls & col.	4	05-Sep-10	08-Sep-10
A1820	Pouring For basement walls & col.	1	12-Sep-10	12-Sep-10
A1830	Isolation For Foundation	6	16-Sep-10	22-Sep-10

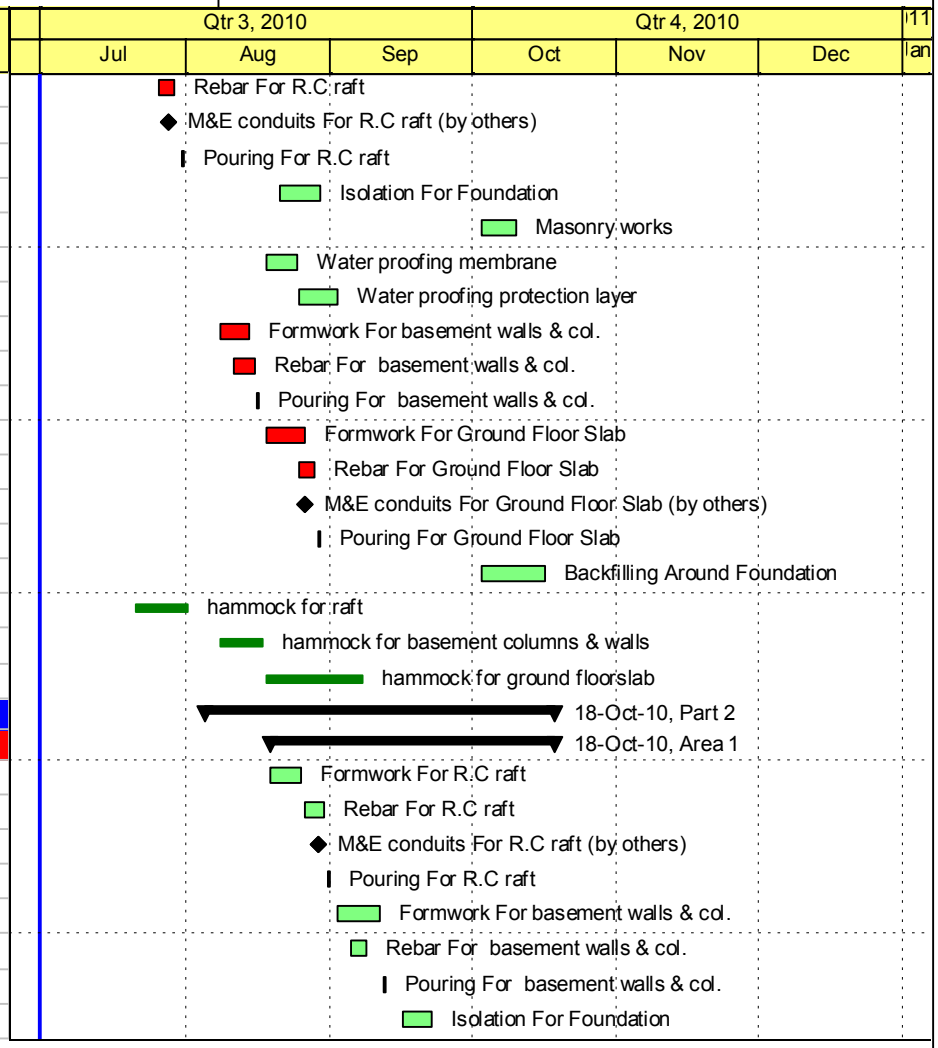

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		

Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
A1840	Formwork For Ground Floor Slab	6	27-Sep-10	03-Oct-10
A1850	Rebar For Ground Floor Slab	3	02-Oct-10	04-Oct-10
A1860	M&E conduits For Ground Floor Slab (by	0		03-Oct-10
A1870	Pouring For Ground Floor Slab	1	05-Oct-10	05-Oct-10
A1880	Masonry works	3	16-Oct-10	18-Oct-10
A1890	Water proofing membrane	4	14-Sep-10	18-Sep-10
A1900	Water proofing protection layer	3	19-Sep-10	21-Sep-10
A2200	Backfilling Around Foundation	12	04-Oct-10	17-Oct-10
A2280	hammock for raft	12	19-Aug-10	01-Sep-10
A2290	hammock for basement columns & walls	10	02-Sep-10	13-Sep-10
A2300	hammock for ground floorslab	16	27-Sep-10	14-Oct-10
Area 2		64	05-Aug-10	18-Oct-10
A1600	Formwork For R.C raft	8	05-Aug-10	14-Aug-10
A1610	Rebar For R.C raft	6	10-Aug-10	16-Aug-10
A1620	M&E conduits For R.C raft (by others)	0		15-Aug-10
A1630	Pouring For R.C raft	2	17-Aug-10	18-Aug-10
A1640	Formwork For basement walls & col.	10	21-Aug-10	31-Aug-10
A1650	Rebar For basement walls & col.	8	23-Aug-10	31-Aug-10
A1660	Pouring For basement walls & col.	1	01-Sep-10	01-Sep-10
A1670	Isolation For Foundation	8	06-Sep-10	14-Sep-10
A1680	Backfilling Around Foundation	10	05-Oct-10	16-Oct-10
A1690	Formwork For Ground Floor Slab	10	15-Sep-10	26-Sep-10
A1700	Rebar For Ground Floor Slab	6	25-Sep-10	30-Sep-10
A1710	M&E conduits For Ground Floor Slab (by	0		29-Sep-10
A1720	Pouring For Ground Floor Slab	1	02-Oct-10	02-Oct-10
A1730	Masonry works	6	12-Oct-10	18-Oct-10
A1740	Water proofing membrane	7	04-Sep-10	11-Sep-10
A1750	Water proofing protection layer	6	12-Sep-10	18-Sep-10

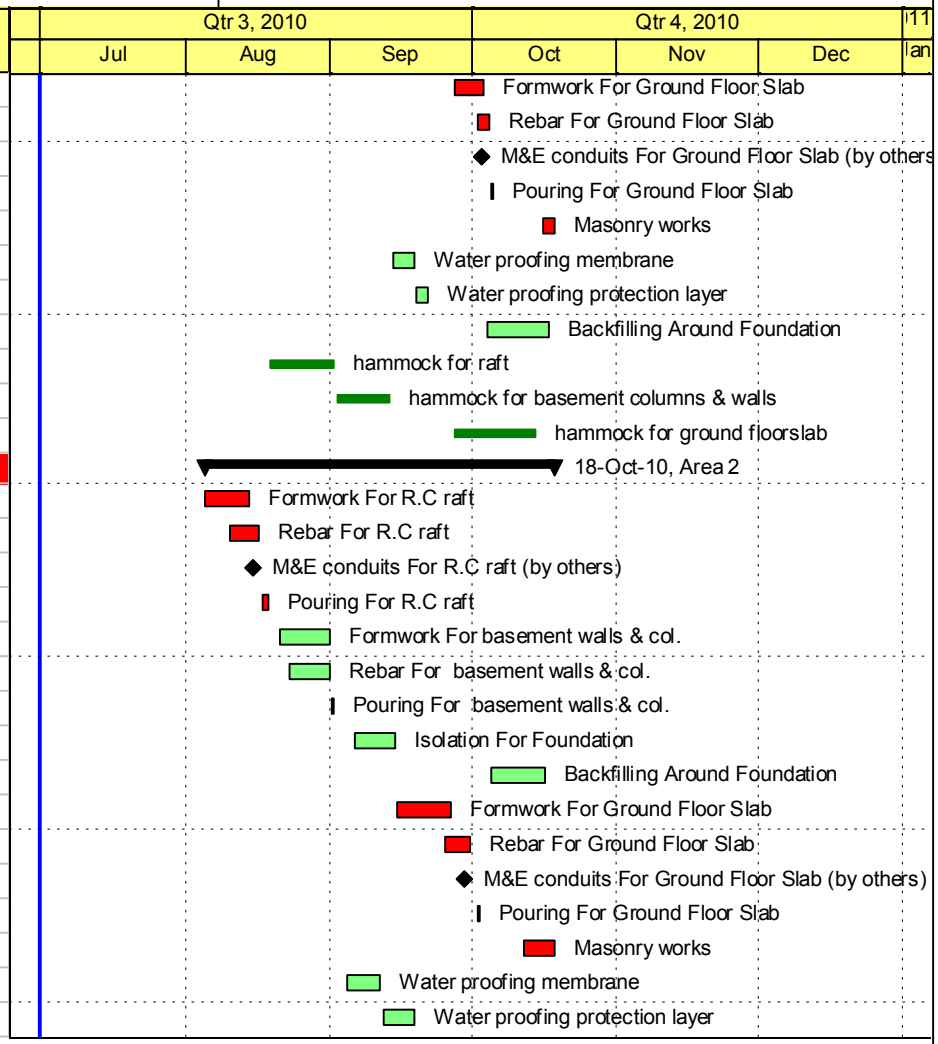

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		

Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
A2310	hammock for raft	13	05-Aug-10	19-Aug-10
A2320	hammock for basement columns & walls	12	21-Aug-10	02-Sep-10
A2330	hammock for ground floorslab	23	15-Sep-10	11-Oct-10
Area 3		51	21-Aug-10	18-Oct-10
A1910	Formwork For R.C raft	9	21-Aug-10	30-Aug-10
A1920	Rebar For R.C raft	6	23-Aug-10	29-Aug-10
A1930	M&E conduits For R.C raft (by others)	0		28-Aug-10
A1940	Pouring For R.C raft	1	30-Aug-10	30-Aug-10
A1950	Formwork For basement walls & col.	10	01-Sep-10	12-Sep-10
A1960	Rebar For basement walls & col.	8	04-Sep-10	12-Sep-10
A1970	Pouring For basement walls & col.	1	13-Sep-10	13-Sep-10
A1980	Isolation For Foundation	6	18-Sep-10	23-Sep-10
A1990	Formwork For Ground Floor Slab	6	21-Sep-10	27-Sep-10
A2000	Rebar For Ground Floor Slab	3	28-Sep-10	30-Sep-10
A2010	M&E conduits For Ground Floor Slab (by	0		29-Sep-10
A2020	Pouring For Ground Floor Slab	1	04-Oct-10	04-Oct-10
A2030	Masonry works	4	14-Oct-10	18-Oct-10
A2040	Water proofing membrane	6	15-Sep-10	21-Sep-10
A2050	Water proofing protection layer	6	22-Sep-10	28-Sep-10
A2210	Backfilling Around Foundation	12	05-Oct-10	18-Oct-10
A2340	hammock for raft	10	21-Aug-10	31-Aug-10
A2350	hammock for basement columns & walls	12	01-Sep-10	14-Sep-10
A2360	hammock for ground floorslab	20	21-Sep-10	13-Oct-10
Tank		63	25-Jul-10	05-Oct-10
A2060	Formworks for R.C raft	2	25-Jul-10	26-Jul-10
A2070	Rebar for R.C raft	3	27-Jul-10	29-Jul-10
A2079	M&E conduits For R.C raft (by others)	0		28-Jul-10
A2080	Pouring For R.C raft	1	31-Jul-10	31-Jul-10

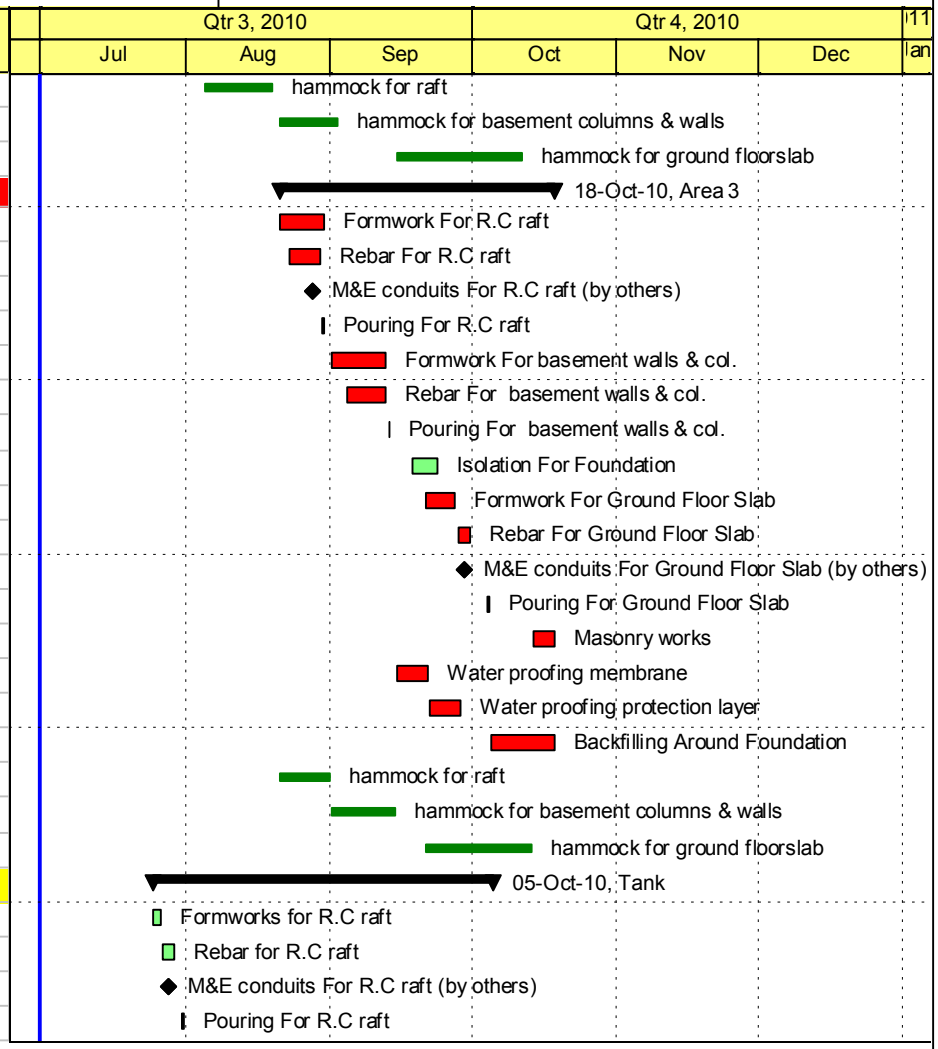

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		

Office Building.14B01 Substructure Package

Contractor : Mivan Ltd's

Activity ID	Activity Name	Original Duration	Start	Finish
A2090	Formwork For Tank walls	8	01-Aug-10	09-Aug-10
A2100	Rebar For Tank walls	6	10-Aug-10	16-Aug-10
A2109	M&E conduits For R.C walls (by others)	0		15-Aug-10
A2110	Pouring For Tank walls	1	17-Aug-10	17-Aug-10
A2119	M&E conduits For tank's slab (by others)	0		04-Sep-10
A2120	Formwork For Tank Slab	10	18-Aug-10	29-Aug-10
A2130	Rebar For Tank Slab	6	30-Aug-10	05-Sep-10
A2140	Pouring For Tank slab	1	06-Sep-10	06-Sep-10
A2150	Internal insulation	15	07-Sep-10	23-Sep-10
A2160	External insulation	10	25-Sep-10	05-Oct-10

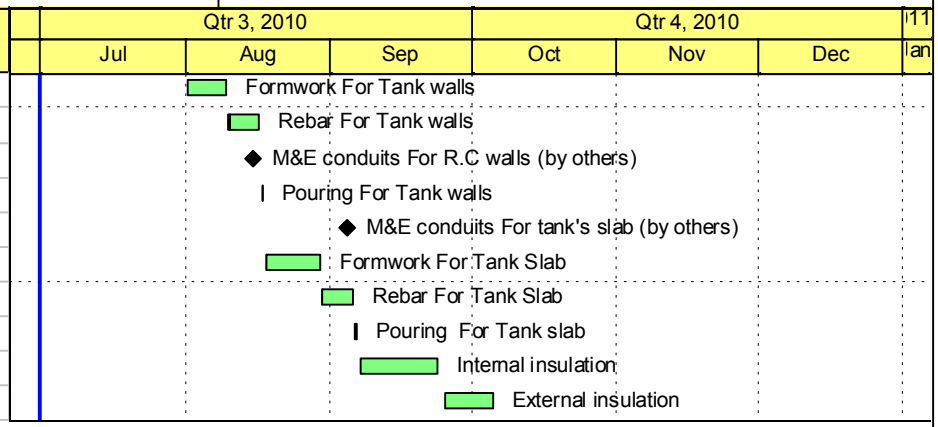

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
17-Jul-10	Revision 0		
