Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Cleopatra Jungle	144	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
Startup Phase	0	21-Jun-10 A	21-Jun-10 A	21-Jun-10	21-Jun-10	
Project Start	0	21-Jun-10 A		21-Jun-10		100%
Site Taking Over	0	21-Jun-10 A		21-Jun-10		100%
Construction Phase	144	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
Zone.No 1	136	21-Jun-10 A	30-Nov-10	21-Jun-10	23-Oct-10	
Villa Number D9	102	31-Jul-10	30-Nov-10	21-Jun-10	20-Oct-10	
general dates	102	31-Jul-10	30-Nov-10	21-Jun-10	20-Oct-10	
Start Villa construction	0	31-Jul-10		21-Jun-10		0%
IFC drawings	0	31-Jul-10		21-Jun-10		0%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Nov-10		20-Oct-10	0%
earth works	14	31-Jul-10	15-Aug-10	21-Jun-10	06-Jul-10	
excavation	2	31-Jul-10	01-Aug-10	21-Jun-10	22-Jun-10	0%
soil replacement	12	02-Aug-10	15-Aug-10	23-Jun-10	06-Jul-10	0%
foundation level	56	16-Aug-10	19-Oct-10	07-Jul-10	13-Sep-10	
Plain Concrete Foundation	2	16-Aug-10	17-Aug-10	07-Jul-10	08-Jul-10	0%
backfilling between P.C Foundation	2	19-Aug-10	21-Aug-10	11-Jul-10	12-Jul-10	0%
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	14-Jul-10	21-Jul-10	0%
under ground brick works	2	06-Sep-10	07-Sep-10	29-Jul-10	31-Jul-10	0%
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	01-Aug-10	02-Aug-10	0%
backfilling for under ground	4	11-Sep-10	14-Sep-10	03-Aug-10	07-Aug-10	0%
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	06-Sep-10	06-Sep-10	0%
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	07-Sep-10	11-Sep-10	0%
R.C slab on grade	2	18-Oct-10	19-Oct-10	12-Sep-10	13-Sep-10	0%
skeleton & brick walls	74	30-Aug-10	28-Nov-10	22-Jul-10	18-Oct-10	
columns for ground floor	6	30-Aug-10	05-Sep-10	22-Jul-10	28-Jul-10	0%

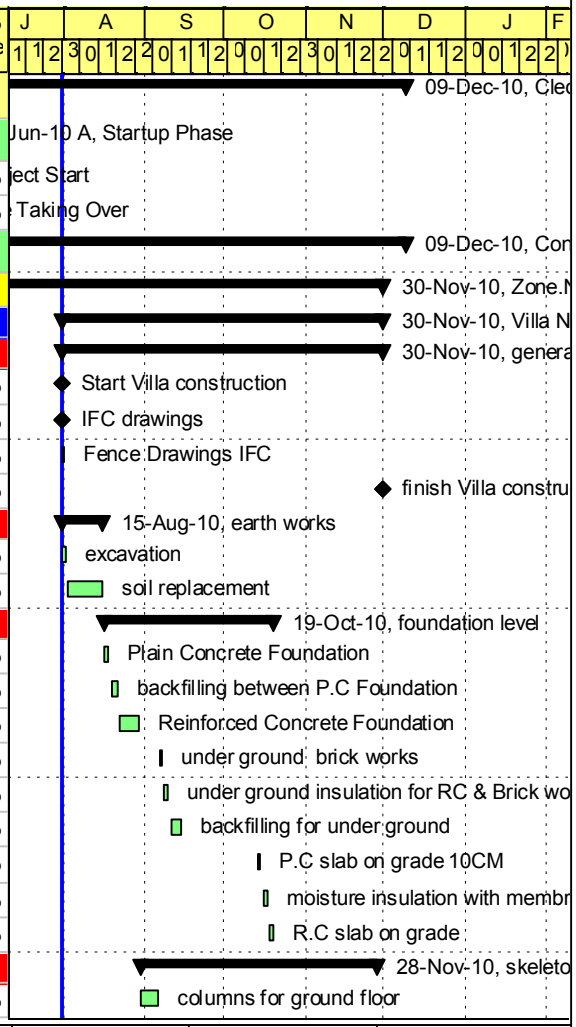

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
slab for ground floor	9	15-Sep-10	25-Sep-10	08-Aug-10	17-Aug-10	0%
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	18-Aug-10	18-Aug-10	0%
columns for 1st floor	6	27-Sep-10	03-Oct-10	19-Aug-10	25-Aug-10	0%
Fence work	50	27-Sep-10	28-Nov-10	19-Aug-10	18-Oct-10	0%
slab for 1st floor	9	04-Oct-10	13-Oct-10	26-Aug-10	05-Sep-10	0%
Brick works for ground floor	5	09-Oct-10	13-Oct-10	31-Aug-10	05-Sep-10	0%
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	06-Sep-10	06-Sep-10	0%
columns for roof floor	4	18-Oct-10	21-Oct-10	12-Sep-10	15-Sep-10	0%
slab for roof floor	6	23-Oct-10	28-Oct-10	16-Sep-10	22-Sep-10	0%
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	21-Sep-10	26-Sep-10	0%
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	23-Sep-10	23-Sep-10	0%
Brick works for roof floor	5	09-Nov-10	14-Nov-10	04-Oct-10	09-Oct-10	0%
electro mechanical	52	15-Sep-10	16-Nov-10	08-Aug-10	11-Oct-10	
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	08-Aug-10	09-Aug-10	0%
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	12-Aug-10	14-Aug-10	0%
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	31-Aug-10	01-Sep-10	0%
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	15-Sep-10	16-Sep-10	0%
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	20-Sep-10	20-Sep-10	0%
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	27-Sep-10	28-Sep-10	0%
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	10-Oct-10	11-Oct-10	0%
finishing	29	24-Oct-10	30-Nov-10	18-Sep-10	20-Oct-10	
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	18-Sep-10	26-Sep-10	0%
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	29-Sep-10	07-Oct-10	0%
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	12-Oct-10	17-Oct-10	0%
External plastering	10	20-Nov-10	30-Nov-10	10-Oct-10	20-Oct-10	0%
Villa Number D10	110	21-Jun-10 A	26-Oct-10	21-Jun-10	05-Oct-10	
general dates	85	21-Jun-10 A	26-Oct-10	21-Jun-10	05-Oct-10	

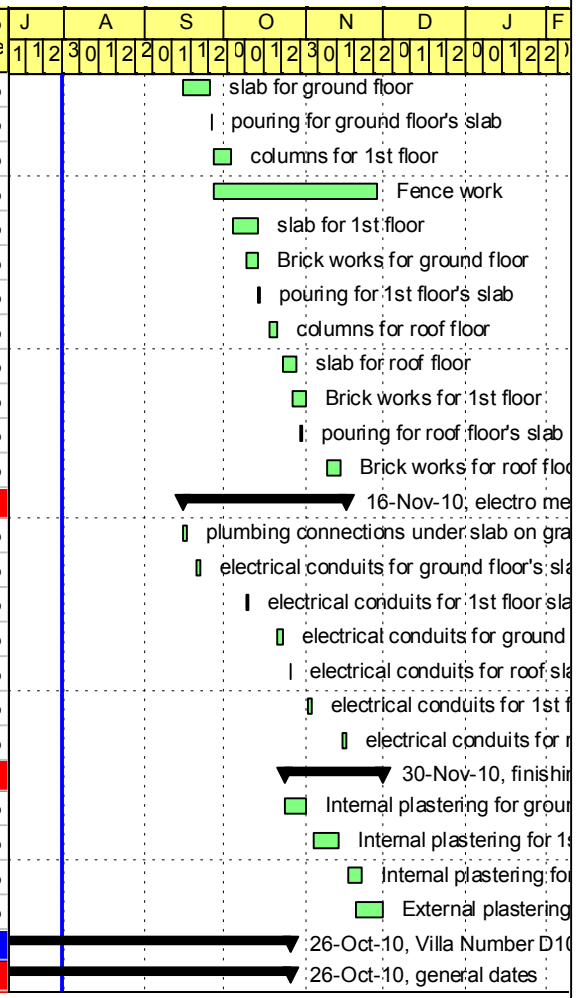

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

Page 2 of 39

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		26-Oct-10		05-Oct-10	0%
earth works	1	21-Jun-10 A	03-Jul-10 A	21-Jun-10	22-Jun-10	
excavation	1	21-Jun-10 A	03-Jul-10 A	21-Jun-10	21-Jun-10	100%
soil replacement	0	03-Jul-10 A	03-Jul-10 A	22-Jun-10	22-Jun-10	100%
foundation level	77	04-Jul-10 A	19-Sep-10	22-Jun-10	26-Aug-10	
Plain Concrete Foundation	2	04-Jul-10 A	06-Jul-10 A	22-Jun-10	23-Jun-10	100%
backfilling between P.C Foundation	2	07-Jul-10 A	09-Jul-10 A	26-Jun-10	27-Jun-10	100%
Reinforced Concrete Foundation	7	10-Jul-10 A	27-Jul-10 A	29-Jun-10	06-Jul-10	100%
under ground brick works	2	07-Aug-10	08-Aug-10	14-Jul-10	15-Jul-10	0%
under ground insulation for RC & Brick work	2	09-Aug-10	10-Aug-10	17-Jul-10	18-Jul-10	0%
backfilling for under ground	4	11-Aug-10	15-Aug-10	19-Jul-10	22-Jul-10	0%
P.C slab on grade 10CM	1	14-Sep-10	14-Sep-10	22-Aug-10	22-Aug-10	0%
moisture insulation with membrane sheets	2	15-Sep-10	16-Sep-10	23-Aug-10	24-Aug-10	0%
R.C slab on grade	2	18-Sep-10	19-Sep-10	25-Aug-10	26-Aug-10	0%
skeleton & brick walls	74	31-Jul-10	24-Oct-10	07-Jul-10	03-Oct-10	
columns for ground floor	6	31-Jul-10	05-Aug-10	07-Jul-10	13-Jul-10	0%
slab for ground floor	9	16-Aug-10	25-Aug-10	24-Jul-10	02-Aug-10	0%
pouring for ground floor's slab	1	26-Aug-10	26-Aug-10	03-Aug-10	03-Aug-10	0%
columns for 1st floor	6	28-Aug-10	02-Sep-10	04-Aug-10	10-Aug-10	0%
Fence work	50	28-Aug-10	24-Oct-10	04-Aug-10	03-Oct-10	0%
slab for 1st floor	9	04-Sep-10	13-Sep-10	11-Aug-10	21-Aug-10	0%
Brick works for ground floor	5	08-Sep-10	13-Sep-10	16-Aug-10	21-Aug-10	0%
pouring for 1st floor's slab	1	14-Sep-10	14-Sep-10	22-Aug-10	22-Aug-10	0%
columns for roof floor	4	18-Sep-10	21-Sep-10	25-Aug-10	29-Aug-10	0%

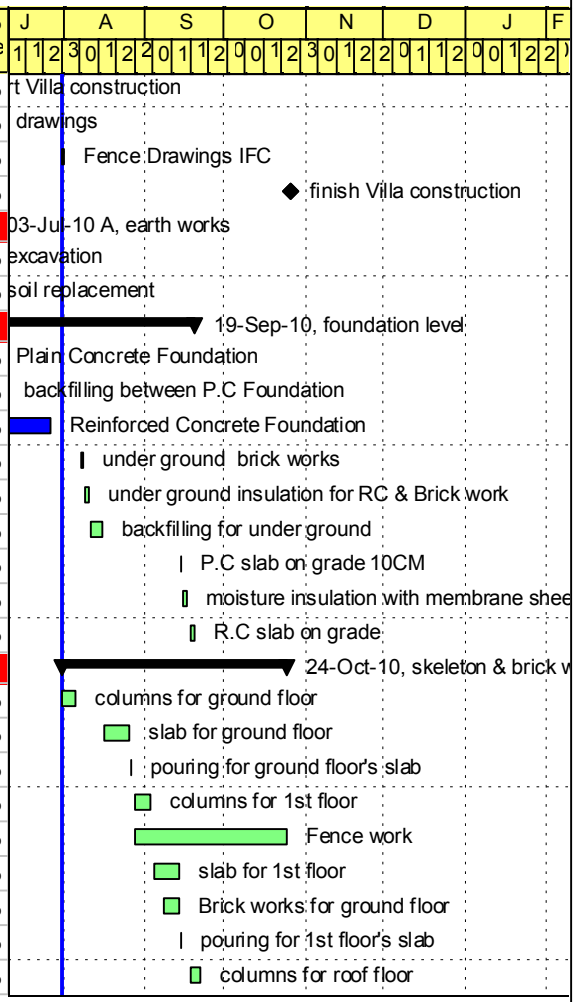

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
slab for roof floor	6	22-Sep-10	28-Sep-10	30-Aug-10	05-Sep-10	0%
Brick works for 1st floor	5	27-Sep-10	02-Oct-10	04-Sep-10	13-Sep-10	0%
pouring for roof floor's slab	1	29-Sep-10	29-Sep-10	06-Sep-10	06-Sep-10	0%
Brick works for roof floor	5	10-Oct-10	14-Oct-10	19-Sep-10	23-Sep-10	0%
electro mechanical	54	16-Aug-10	17-Oct-10	24-Jul-10	26-Sep-10	
plumbing connections under slab on grade	2	16-Aug-10	17-Aug-10	24-Jul-10	25-Jul-10	0%
electrical conduits for ground floor's slab	2	21-Aug-10	22-Aug-10	28-Jul-10	29-Jul-10	0%
electrical conduits for 1st floor slab	2	08-Sep-10	09-Sep-10	16-Aug-10	17-Aug-10	0%
electrical conduits for ground floor walls	2	21-Sep-10	22-Sep-10	29-Aug-10	30-Aug-10	0%
electrical conduits for roof slab	1	26-Sep-10	26-Sep-10	02-Sep-10	02-Sep-10	0%
electrical conduits for 1st floor walls	2	03-Oct-10	04-Oct-10	14-Sep-10	15-Sep-10	0%
electrical conduits for roof floor walls	2	16-Oct-10	17-Oct-10	25-Sep-10	26-Sep-10	0%
finishing	29	23-Sep-10	26-Oct-10	31-Aug-10	05-Oct-10	
Internal plastering for ground floor	8	23-Sep-10	02-Oct-10	31-Aug-10	11-Sep-10	0%
Internal plastering for 1st floor	8	05-Oct-10	13-Oct-10	16-Sep-10	25-Sep-10	0%
External plastering	10	16-Oct-10	26-Oct-10	25-Sep-10	05-Oct-10	0%
Internal plastering for roof floor	5	18-Oct-10	23-Oct-10	27-Sep-10	02-Oct-10	0%
Villa Number B11	106	21-Jun-10 A	23-Oct-10	21-Jun-10	19-Oct-10	
general dates	82	21-Jun-10 A	23-Oct-10	21-Jun-10	19-Oct-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		23-Oct-10		19-Oct-10	0%
earth works	12	21-Jun-10 A	06-Jul-10 A	22-Jun-10	05-Jul-10	
excavation	0	21-Jun-10 A	23-Jun-10 A	22-Jun-10	22-Jun-10	100%
soil replacement	12	24-Jun-10 A	06-Jul-10 A	22-Jun-10	05-Jul-10	100%
foundation level	62	09-Jul-10 A	15-Sep-10	06-Jul-10	12-Sep-10	
Plain Concrete Foundation	2	09-Jul-10 A	11-Jul-10 A	06-Jul-10	07-Jul-10	100%

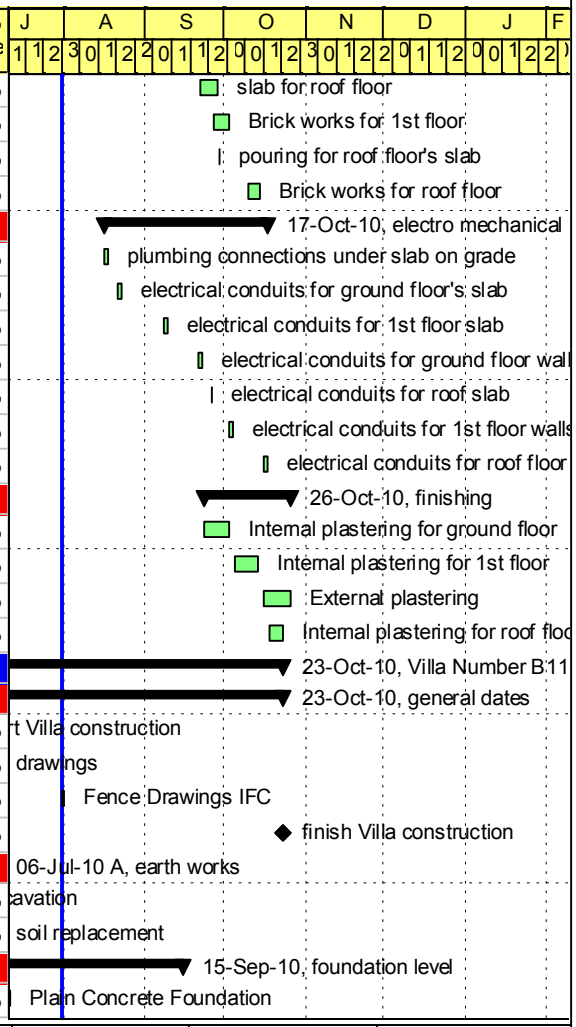

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
backfilling between P.C Foundation	2	12-Jul-10 A	14-Jul-10 A	10-Jul-10	11-Jul-10	100%
Reinforced Concrete Foundation	7	15-Jul-10 A	25-Jul-10 A	13-Jul-10	20-Jul-10	100%
under ground brick works	2	03-Aug-10	04-Aug-10	28-Jul-10	29-Jul-10	0%
under ground insulation for RC & Brick work	2	05-Aug-10	07-Aug-10	31-Jul-10	01-Aug-10	0%
backfilling for under ground	4	08-Aug-10	11-Aug-10	02-Aug-10	05-Aug-10	0%
P.C slab on grade 10CM	1	11-Sep-10	11-Sep-10	05-Sep-10	05-Sep-10	0%
moisture insulation with membrane sheets	2	12-Sep-10	13-Sep-10	06-Sep-10	07-Sep-10	0%
R.C slab on grade	2	14-Sep-10	15-Sep-10	11-Sep-10	12-Sep-10	0%
skeleton & brick walls	73	26-Jul-10 A	20-Oct-10	21-Jul-10	17-Oct-10	
columns for ground floor	6	26-Jul-10 A	02-Aug-10	21-Jul-10	27-Jul-10	50%
slab for ground floor	9	12-Aug-10	22-Aug-10	07-Aug-10	16-Aug-10	0%
pouring for ground floor's slab	1	23-Aug-10	23-Aug-10	17-Aug-10	17-Aug-10	0%
columns for 1st floor	6	24-Aug-10	30-Aug-10	18-Aug-10	24-Aug-10	0%
Fence work	50	24-Aug-10	20-Oct-10	18-Aug-10	17-Oct-10	0%
slab for 1st floor	9	31-Aug-10	09-Sep-10	25-Aug-10	04-Sep-10	0%
Brick works for ground floor	5	05-Sep-10	09-Sep-10	30-Aug-10	04-Sep-10	0%
pouring for 1st floor's slab	1	11-Sep-10	11-Sep-10	05-Sep-10	05-Sep-10	0%
columns for roof floor	4	14-Sep-10	18-Sep-10	11-Sep-10	14-Sep-10	0%
slab for roof floor	6	19-Sep-10	25-Sep-10	15-Sep-10	21-Sep-10	0%
Brick works for 1st floor	5	23-Sep-10	28-Sep-10	20-Sep-10	25-Sep-10	0%
pouring for roof floor's slab	1	26-Sep-10	26-Sep-10	22-Sep-10	22-Sep-10	0%
Brick works for roof floor	5	06-Oct-10	11-Oct-10	03-Oct-10	07-Oct-10	0%
electro mechanical	54	12-Aug-10	13-Oct-10	07-Aug-10	10-Oct-10	
plumbing connections under slab on grade	2	12-Aug-10	14-Aug-10	07-Aug-10	08-Aug-10	0%
electrical conduits for ground floor's slab	2	17-Aug-10	18-Aug-10	11-Aug-10	12-Aug-10	0%
electrical conduits for 1st floor slab	2	05-Sep-10	06-Sep-10	30-Aug-10	31-Aug-10	0%
electrical conduits for ground floor walls	2	18-Sep-10	19-Sep-10	14-Sep-10	15-Sep-10	0%

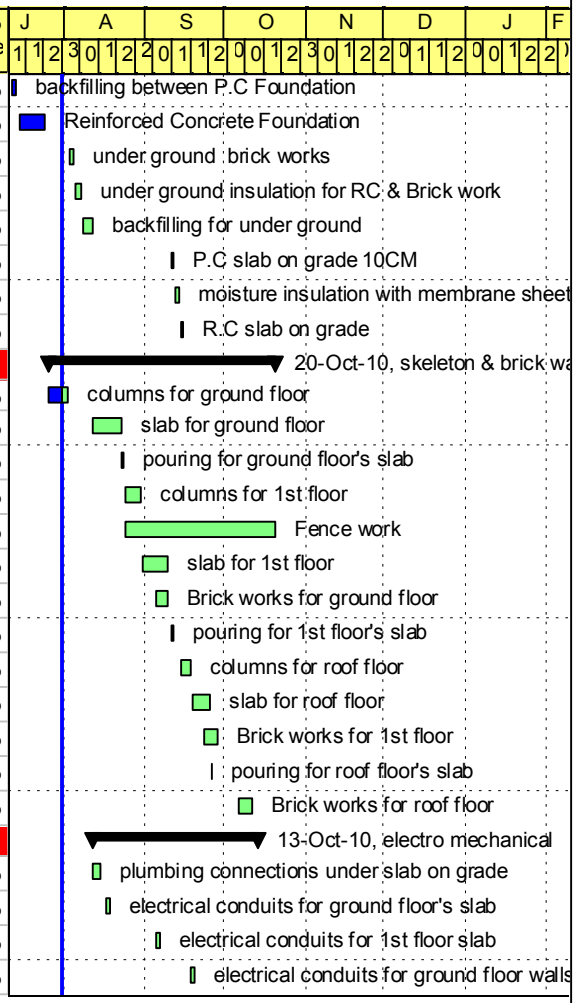

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
electrical conduits for roof slab	1	22-Sep-10	22-Sep-10	19-Sep-10	19-Sep-10	0%
electrical conduits for 1st floor walls	2	29-Sep-10	30-Sep-10	26-Sep-10	27-Sep-10	0%
electrical conduits for roof floor walls	2	12-Oct-10	13-Oct-10	09-Oct-10	10-Oct-10	0%
finishing	29	20-Sep-10	23-Oct-10	16-Sep-10	19-Oct-10	
Internal plastering for ground floor	8	20-Sep-10	28-Sep-10	16-Sep-10	25-Sep-10	0%
Internal plastering for 1st floor	8	02-Oct-10	10-Oct-10	28-Sep-10	06-Oct-10	0%
External plastering	10	12-Oct-10	23-Oct-10	09-Oct-10	19-Oct-10	0%
Internal plastering for roof floor	5	14-Oct-10	19-Oct-10	11-Oct-10	16-Oct-10	0%
Villa Number B12	106	21-Jun-10 A	23-Oct-10	21-Jun-10	19-Oct-10	
general dates	82	21-Jun-10 A	23-Oct-10	21-Jun-10	19-Oct-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		23-Oct-10		19-Oct-10	0%
earth works	12	21-Jun-10 A	05-Jul-10 A	22-Jun-10	05-Jul-10	
excavation	0	21-Jun-10 A	22-Jun-10 A	22-Jun-10	22-Jun-10	100%
soil replacement	12	23-Jun-10 A	05-Jul-10 A	22-Jun-10	05-Jul-10	100%
foundation level	62	06-Jul-10 A	15-Sep-10	06-Jul-10	12-Sep-10	
Plain Concrete Foundation	2	06-Jul-10 A	08-Jul-10 A	06-Jul-10	07-Jul-10	100%
backfilling between P.C Foundation	2	09-Jul-10 A	11-Jul-10 A	10-Jul-10	11-Jul-10	100%
Reinforced Concrete Foundation	7	12-Jul-10 A	25-Jul-10 A	13-Jul-10	20-Jul-10	100%
under ground brick works	2	03-Aug-10	04-Aug-10	28-Jul-10	29-Jul-10	0%
under ground insulation for RC & Brick work	2	05-Aug-10	07-Aug-10	31-Jul-10	01-Aug-10	0%
backfilling for under ground	4	08-Aug-10	11-Aug-10	02-Aug-10	05-Aug-10	0%
P.C slab on grade 10CM	1	11-Sep-10	11-Sep-10	05-Sep-10	05-Sep-10	0%
moisture insulation with membrane sheets	2	12-Sep-10	13-Sep-10	06-Sep-10	07-Sep-10	0%
R.C slab on grade	2	14-Sep-10	15-Sep-10	11-Sep-10	12-Sep-10	0%
skeleton & brick walls	70	26-Jul-10 A	20-Oct-10	21-Jul-10	17-Oct-10	

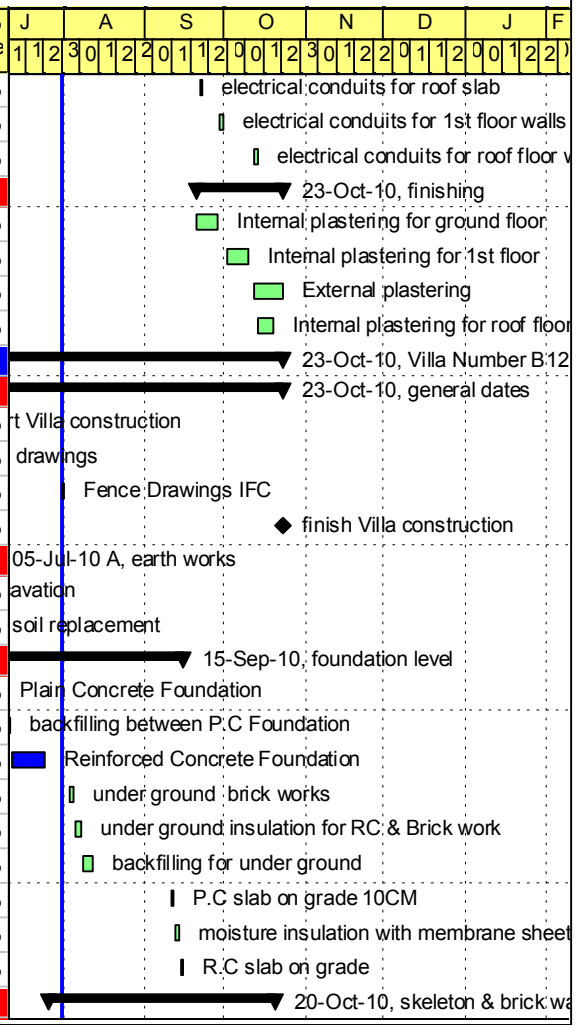

Remaining Level of Effort ◆ Milestone
Actual Work Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
columns for ground floor	6	26-Jul-10 A	02-Aug-10	21-Jul-10	27-Jul-10	50%
slab for ground floor	9	12-Aug-10	22-Aug-10	07-Aug-10	16-Aug-10	0%
pouring for ground floor's slab	1	23-Aug-10	23-Aug-10	17-Aug-10	17-Aug-10	0%
columns for 1st floor	6	24-Aug-10	30-Aug-10	18-Aug-10	24-Aug-10	0%
Fence work	50	24-Aug-10	20-Oct-10	18-Aug-10	17-Oct-10	0%
slab for 1st floor	9	31-Aug-10	09-Sep-10	25-Aug-10	04-Sep-10	0%
Brick works for ground floor	5	05-Sep-10	09-Sep-10	30-Aug-10	04-Sep-10	0%
pouring for 1st floor's slab	1	11-Sep-10	11-Sep-10	05-Sep-10	05-Sep-10	0%
columns for roof floor	4	14-Sep-10	18-Sep-10	11-Sep-10	14-Sep-10	0%
slab for roof floor	6	19-Sep-10	25-Sep-10	15-Sep-10	21-Sep-10	0%
Brick works for 1st floor	5	23-Sep-10	28-Sep-10	20-Sep-10	25-Sep-10	0%
pouring for roof floor's slab	1	26-Sep-10	26-Sep-10	22-Sep-10	22-Sep-10	0%
Brick works for roof floor	5	06-Oct-10	11-Oct-10	03-Oct-10	07-Oct-10	0%
electro mechanical	54	12-Aug-10	13-Oct-10	07-Aug-10	10-Oct-10	
plumbing connections under slab on grade	2	12-Aug-10	14-Aug-10	07-Aug-10	08-Aug-10	0%
electrical conduits for ground floor's slab	2	17-Aug-10	18-Aug-10	11-Aug-10	12-Aug-10	0%
electrical conduits for 1st floor slab	2	05-Sep-10	06-Sep-10	30-Aug-10	31-Aug-10	0%
electrical conduits for ground floor walls	2	18-Sep-10	19-Sep-10	14-Sep-10	15-Sep-10	0%
electrical conduits for roof slab	1	22-Sep-10	22-Sep-10	19-Sep-10	19-Sep-10	0%
electrical conduits for 1st floor walls	2	29-Sep-10	30-Sep-10	26-Sep-10	27-Sep-10	0%
electrical conduits for roof floor walls	2	12-Oct-10	13-Oct-10	09-Oct-10	10-Oct-10	0%
finishing	29	20-Sep-10	23-Oct-10	16-Sep-10	19-Oct-10	
Internal plastering for ground floor	8	20-Sep-10	28-Sep-10	16-Sep-10	25-Sep-10	0%
Internal plastering for 1st floor	8	02-Oct-10	10-Oct-10	28-Sep-10	06-Oct-10	0%
External plastering	10	12-Oct-10	23-Oct-10	09-Oct-10	19-Oct-10	0%
Internal plastering for roof floor	5	14-Oct-10	19-Oct-10	11-Oct-10	16-Oct-10	0%
Villa Number B13	110	21-Jun-10 A	30-Oct-10	21-Jun-10	20-Oct-10	

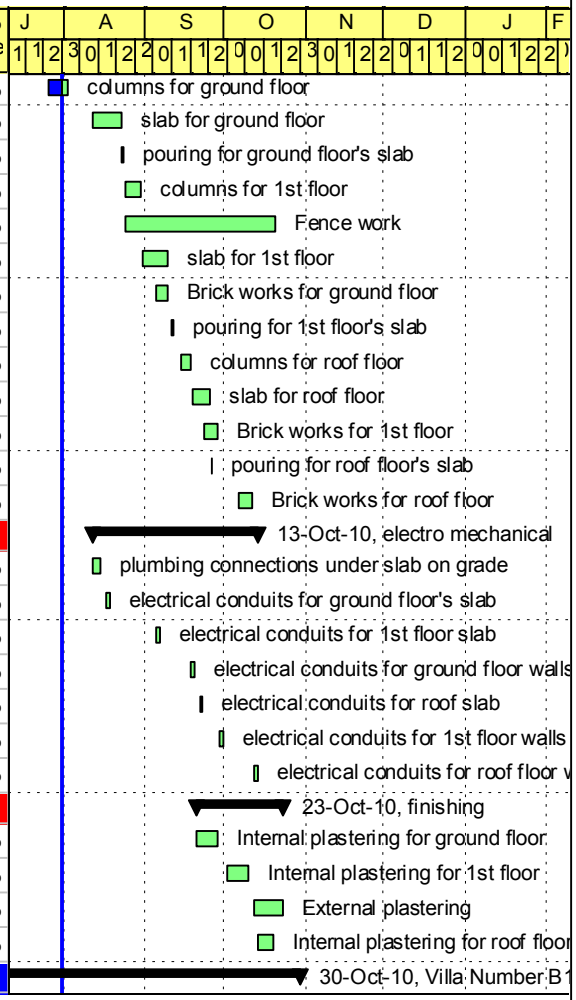

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
general dates	87	21-Jun-10 A	30-Oct-10	21-Jun-10	20-Oct-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Oct-10		20-Oct-10	0%
earth works	12	21-Jun-10 A	05-Jul-10 A	23-Jun-10	06-Jul-10	
excavation	0	21-Jun-10 A	22-Jun-10 A	23-Jun-10	23-Jun-10	100%
soil replacement	12	23-Jun-10 A	05-Jul-10 A	23-Jun-10	06-Jul-10	100%
foundation level	66	06-Jul-10 A	22-Sep-10	07-Jul-10	13-Sep-10	
Plain Concrete Foundation	2	06-Jul-10 A	08-Jul-10 A	07-Jul-10	08-Jul-10	100%
backfilling between P.C Foundation	2	09-Jul-10 A	11-Jul-10 A	11-Jul-10	12-Jul-10	100%
Reinforced Concrete Foundation	7	14-Jul-10 A	02-Aug-10	14-Jul-10	21-Jul-10	70%
under ground brick works	2	09-Aug-10	11-Aug-10	29-Jul-10	31-Jul-10	0%
under ground insulation for RC & Brick work	2	11-Aug-10	14-Aug-10	01-Aug-10	02-Aug-10	0%
backfilling for under ground	4	14-Aug-10	18-Aug-10	03-Aug-10	07-Aug-10	0%
P.C slab on grade 10CM	1	16-Sep-10	18-Sep-10	06-Sep-10	06-Sep-10	0%
moisture insulation with membrane sheets	2	18-Sep-10	20-Sep-10	07-Sep-10	11-Sep-10	0%
R.C slab on grade	2	20-Sep-10	22-Sep-10	12-Sep-10	13-Sep-10	0%
skeleton & brick walls	78	26-Jul-10 A	27-Oct-10	22-Jul-10	18-Oct-10	
columns for ground floor	6	26-Jul-10 A	09-Aug-10	22-Jul-10	28-Jul-10	50%
slab for ground floor	9	18-Aug-10	29-Aug-10	08-Aug-10	17-Aug-10	0%
pouring for ground floor's slab	1	29-Aug-10	30-Aug-10	18-Aug-10	18-Aug-10	0%
columns for 1st floor	6	30-Aug-10	06-Sep-10	19-Aug-10	25-Aug-10	0%
Fence work	50	30-Aug-10	27-Oct-10	19-Aug-10	18-Oct-10	0%
slab for 1st floor	9	06-Sep-10	16-Sep-10	26-Aug-10	05-Sep-10	0%
Brick works for ground floor	5	11-Sep-10	16-Sep-10	31-Aug-10	05-Sep-10	0%
pouring for 1st floor's slab	1	16-Sep-10	18-Sep-10	06-Sep-10	06-Sep-10	0%

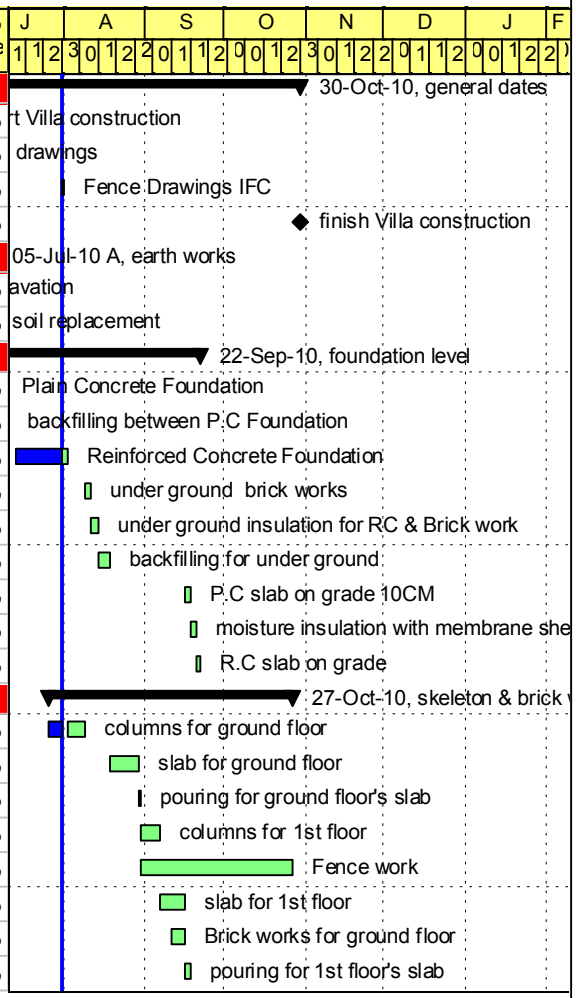

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
columns for roof floor	4	20-Sep-10	25-Sep-10	12-Sep-10	15-Sep-10	0%
slab for roof floor	6	25-Sep-10	02-Oct-10	16-Sep-10	22-Sep-10	0%
Brick works for 1st floor	5	29-Sep-10	05-Oct-10	21-Sep-10	26-Sep-10	0%
pouring for roof floor's slab	1	02-Oct-10	03-Oct-10	23-Sep-10	23-Sep-10	0%
Brick works for roof floor	5	12-Oct-10	18-Oct-10	04-Oct-10	09-Oct-10	0%
electro mechanical	54	18-Aug-10	20-Oct-10	08-Aug-10	11-Oct-10	
plumbing connections under slab on grade	2	18-Aug-10	21-Aug-10	08-Aug-10	09-Aug-10	0%
electrical conduits for ground floor's slab	2	23-Aug-10	25-Aug-10	12-Aug-10	14-Aug-10	0%
electrical conduits for 1st floor slab	2	11-Sep-10	13-Sep-10	31-Aug-10	01-Sep-10	0%
electrical conduits for ground floor walls	2	23-Sep-10	26-Sep-10	15-Sep-10	16-Sep-10	0%
electrical conduits for roof slab	1	28-Sep-10	29-Sep-10	20-Sep-10	20-Sep-10	0%
electrical conduits for 1st floor walls	2	05-Oct-10	07-Oct-10	27-Sep-10	28-Sep-10	0%
electrical conduits for roof floor walls	2	18-Oct-10	20-Oct-10	10-Oct-10	11-Oct-10	0%
finishing	29	26-Sep-10	30-Oct-10	18-Sep-10	20-Oct-10	
Internal plastering for ground floor	8	26-Sep-10	05-Oct-10	18-Sep-10	26-Sep-10	0%
Internal plastering for 1st floor	8	07-Oct-10	17-Oct-10	29-Sep-10	07-Oct-10	0%
External plastering	10	18-Oct-10	30-Oct-10	10-Oct-10	20-Oct-10	0%
Internal plastering for roof floor	5	20-Oct-10	26-Oct-10	12-Oct-10	17-Oct-10	0%
Villa Number B14	109	21-Jun-10 A	28-Oct-10	21-Jun-10	20-Oct-10	
general dates	86	21-Jun-10 A	28-Oct-10	21-Jun-10	20-Oct-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		28-Oct-10		20-Oct-10	0%
earth works	12	21-Jun-10 A	10-Jul-10 A	23-Jun-10	06-Jul-10	
excavation	0	21-Jun-10 A	27-Jun-10 A	23-Jun-10	23-Jun-10	100%
soil replacement	12	28-Jun-10 A	10-Jul-10 A	23-Jun-10	06-Jul-10	100%
foundation level	65	11-Jul-10 A	21-Sep-10	07-Jul-10	13-Sep-10	

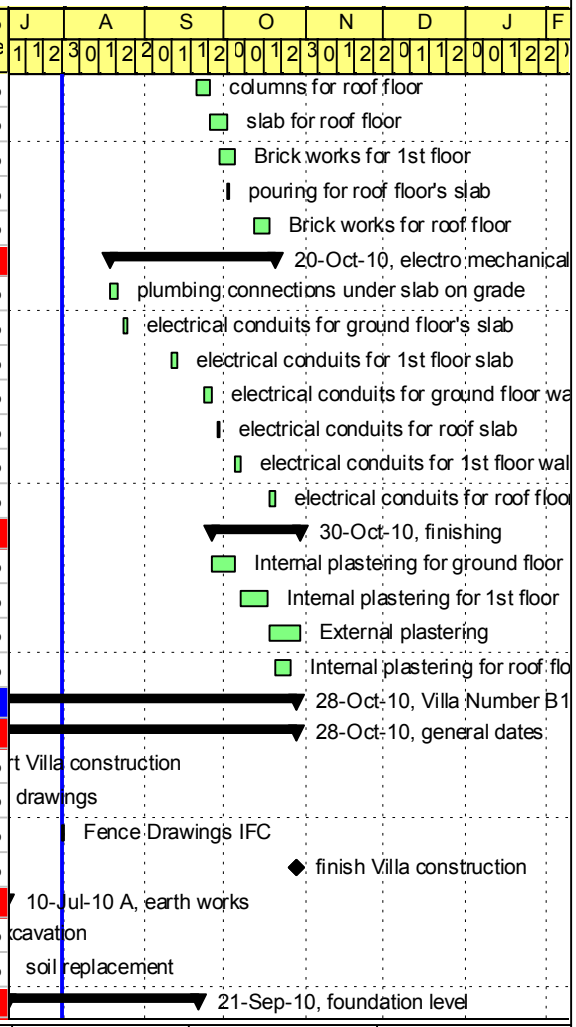

Remaining Level of Effort ◆ ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Plain Concrete Foundation	2	11-Jul-10 A	18-Jul-10 A	07-Jul-10	08-Jul-10	100%
backfilling between P.C Foundation	2	19-Jul-10 A	21-Jul-10 A	11-Jul-10	12-Jul-10	100%
Reinforced Concrete Foundation	7	22-Jul-10 A	01-Aug-10	14-Jul-10	21-Jul-10	80%
under ground brick works	2	08-Aug-10	10-Aug-10	29-Jul-10	31-Jul-10	0%
under ground insulation for RC & Brick work	2	10-Aug-10	12-Aug-10	01-Aug-10	02-Aug-10	0%
backfilling for under ground	4	12-Aug-10	17-Aug-10	03-Aug-10	07-Aug-10	0%
P.C slab on grade 10CM	1	15-Sep-10	16-Sep-10	06-Sep-10	06-Sep-10	0%
moisture insulation with membrane sheets	2	16-Sep-10	19-Sep-10	07-Sep-10	11-Sep-10	0%
R.C slab on grade	2	19-Sep-10	21-Sep-10	12-Sep-10	13-Sep-10	0%
skeleton & brick walls	**74**	**01-Aug-10**	**26-Oct-10**	**22-Jul-10**	**18-Oct-10**	
columns for ground floor	6	01-Aug-10	08-Aug-10	22-Jul-10	28-Jul-10	0%
slab for ground floor	9	17-Aug-10	28-Aug-10	08-Aug-10	17-Aug-10	0%
pouring for ground floor's slab	1	28-Aug-10	29-Aug-10	18-Aug-10	18-Aug-10	0%
columns for 1st floor	6	29-Aug-10	05-Sep-10	19-Aug-10	25-Aug-10	0%
Fence work	50	29-Aug-10	26-Oct-10	19-Aug-10	18-Oct-10	0%
slab for 1st floor	9	05-Sep-10	15-Sep-10	26-Aug-10	05-Sep-10	0%
Brick works for ground floor	5	09-Sep-10	15-Sep-10	31-Aug-10	05-Sep-10	0%
pouring for 1st floor's slab	1	15-Sep-10	16-Sep-10	06-Sep-10	06-Sep-10	0%
columns for roof floor	4	19-Sep-10	23-Sep-10	12-Sep-10	15-Sep-10	0%
slab for roof floor	6	23-Sep-10	30-Sep-10	16-Sep-10	22-Sep-10	0%
Brick works for 1st floor	5	28-Sep-10	04-Oct-10	21-Sep-10	26-Sep-10	0%
pouring for roof floor's slab	1	30-Sep-10	02-Oct-10	23-Sep-10	23-Sep-10	0%
Brick works for roof floor	5	11-Oct-10	17-Oct-10	04-Oct-10	09-Oct-10	0%
electro mechanical	**54**	**17-Aug-10**	**19-Oct-10**	**08-Aug-10**	**11-Oct-10**	
plumbing connections under slab on grade	2	17-Aug-10	19-Aug-10	08-Aug-10	09-Aug-10	0%
electrical conduits for ground floor's slab	2	22-Aug-10	24-Aug-10	12-Aug-10	14-Aug-10	0%
electrical conduits for 1st floor slab	2	09-Sep-10	12-Sep-10	31-Aug-10	01-Sep-10	0%

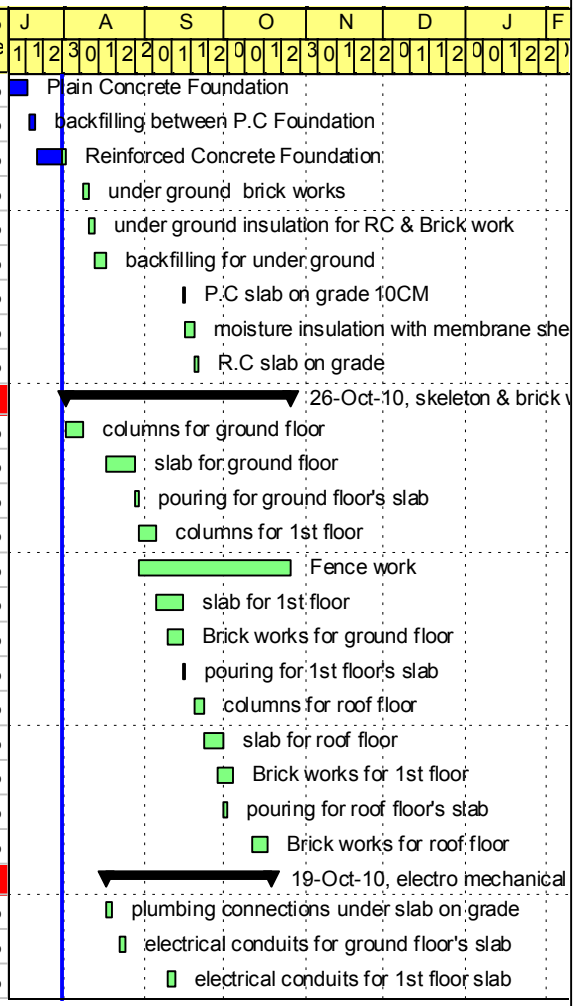

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
electrical conduits for ground floor walls	2	22-Sep-10	25-Sep-10	15-Sep-10	16-Sep-10	0%
electrical conduits for roof slab	1	27-Sep-10	28-Sep-10	20-Sep-10	20-Sep-10	0%
electrical conduits for 1st floor walls	2	04-Oct-10	06-Oct-10	27-Sep-10	28-Sep-10	0%
electrical conduits for roof floor walls	2	17-Oct-10	19-Oct-10	10-Oct-10	11-Oct-10	0%
finishing	29	25-Sep-10	28-Oct-10	18-Sep-10	20-Oct-10	
Internal plastering for ground floor	8	25-Sep-10	04-Oct-10	18-Sep-10	26-Sep-10	0%
Internal plastering for 1st floor	8	06-Oct-10	16-Oct-10	29-Sep-10	07-Oct-10	0%
External plastering	10	17-Oct-10	28-Oct-10	10-Oct-10	20-Oct-10	0%
Internal plastering for roof floor	5	19-Oct-10	25-Oct-10	12-Oct-10	17-Oct-10	0%
Villa Number B102	102	31-Jul-10	30-Nov-10	21-Jun-10	23-Oct-10	
general dates	102	31-Jul-10	30-Nov-10	21-Jun-10	23-Oct-10	
Start Villa construction	0	31-Jul-10		21-Jun-10		0%
IFC drawings	0	31-Jul-10		21-Jun-10		0%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Nov-10		23-Oct-10	0%
earth works	14	02-Aug-10	17-Aug-10	23-Jun-10	08-Jul-10	
excavation	2	02-Aug-10	03-Aug-10	23-Jun-10	24-Jun-10	0%
soil replacement	12	04-Aug-10	17-Aug-10	26-Jun-10	08-Jul-10	0%
foundation level	56	18-Aug-10	21-Oct-10	10-Jul-10	15-Sep-10	
Plain Concrete Foundation	2	18-Aug-10	19-Aug-10	10-Jul-10	11-Jul-10	0%
backfilling between P.C Foundation	2	22-Aug-10	23-Aug-10	13-Jul-10	14-Jul-10	0%
Reinforced Concrete Foundation	7	24-Aug-10	31-Aug-10	17-Jul-10	24-Jul-10	0%
under ground brick works	2	08-Sep-10	09-Sep-10	01-Aug-10	02-Aug-10	0%
under ground insulation for RC & Brick work	2	11-Sep-10	12-Sep-10	03-Aug-10	04-Aug-10	0%
backfilling for under ground	4	13-Sep-10	16-Sep-10	05-Aug-10	09-Aug-10	0%
P.C slab on grade 10CM	1	17-Oct-10	17-Oct-10	11-Sep-10	11-Sep-10	0%
moisture insulation with membrane sheets	2	18-Oct-10	19-Oct-10	12-Sep-10	13-Sep-10	0%
R.C slab on grade	2	20-Oct-10	21-Oct-10	14-Sep-10	15-Sep-10	0%

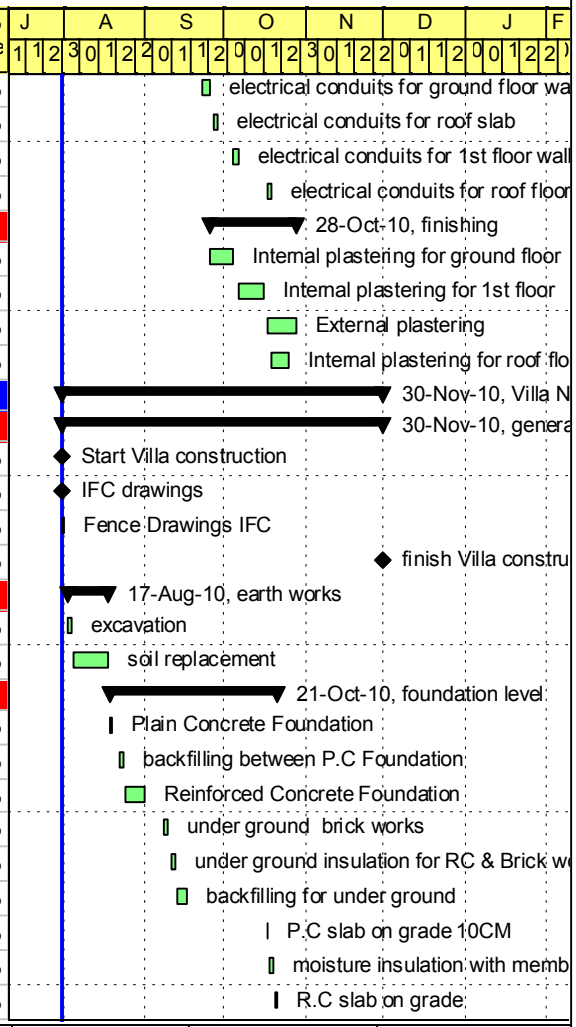

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
skeleton & brick walls	74	01-Sep-10	30-Nov-10	25-Jul-10	20-Oct-10	
columns for ground floor	6	01-Sep-10	07-Sep-10	25-Jul-10	31-Jul-10	0%
slab for ground floor	9	18-Sep-10	27-Sep-10	10-Aug-10	19-Aug-10	0%
pouring for ground floor's slab	1	28-Sep-10	28-Sep-10	21-Aug-10	21-Aug-10	0%
columns for 1st floor	6	29-Sep-10	05-Oct-10	22-Aug-10	28-Aug-10	0%
Fence work	50	29-Sep-10	30-Nov-10	22-Aug-10	20-Oct-10	0%
slab for 1st floor	9	06-Oct-10	16-Oct-10	29-Aug-10	07-Sep-10	0%
Brick works for ground floor	5	11-Oct-10	16-Oct-10	02-Sep-10	07-Sep-10	0%
pouring for 1st floor's slab	1	17-Oct-10	17-Oct-10	11-Sep-10	11-Sep-10	0%
columns for roof floor	4	20-Oct-10	24-Oct-10	14-Sep-10	18-Sep-10	0%
slab for roof floor	6	25-Oct-10	31-Oct-10	19-Sep-10	25-Sep-10	0%
Brick works for 1st floor	5	30-Oct-10	03-Nov-10	23-Sep-10	28-Sep-10	0%
pouring for roof floor's slab	1	01-Nov-10	01-Nov-10	26-Sep-10	26-Sep-10	0%
Brick works for roof floor	5	11-Nov-10	16-Nov-10	06-Oct-10	11-Oct-10	0%
electro mechanical	50	18-Sep-10	18-Nov-10	10-Aug-10	13-Oct-10	
plumbing connections under slab on grade	2	18-Sep-10	19-Sep-10	10-Aug-10	11-Aug-10	0%
electrical conduits for ground floor's slab	2	22-Sep-10	23-Sep-10	15-Aug-10	16-Aug-10	0%
electrical conduits for 1st floor slab	2	11-Oct-10	12-Oct-10	02-Sep-10	04-Sep-10	0%
electrical conduits for ground floor walls	2	24-Oct-10	25-Oct-10	18-Sep-10	19-Sep-10	0%
electrical conduits for roof slab	1	28-Oct-10	28-Oct-10	22-Sep-10	22-Sep-10	0%
electrical conduits for 1st floor walls	2	04-Nov-10	06-Nov-10	29-Sep-10	30-Sep-10	0%
electrical conduits for roof floor walls	2	17-Nov-10	18-Nov-10	12-Oct-10	13-Oct-10	0%
finishing	27	26-Oct-10	30-Nov-10	20-Sep-10	23-Oct-10	
Internal plastering for ground floor	8	26-Oct-10	03-Nov-10	20-Sep-10	28-Sep-10	0%
Internal plastering for 1st floor	8	07-Nov-10	15-Nov-10	02-Oct-10	10-Oct-10	0%
External plastering	10	20-Nov-10	30-Nov-10	12-Oct-10	23-Oct-10	0%
Internal plastering for roof floor	5	20-Nov-10	24-Nov-10	14-Oct-10	19-Oct-10	0%

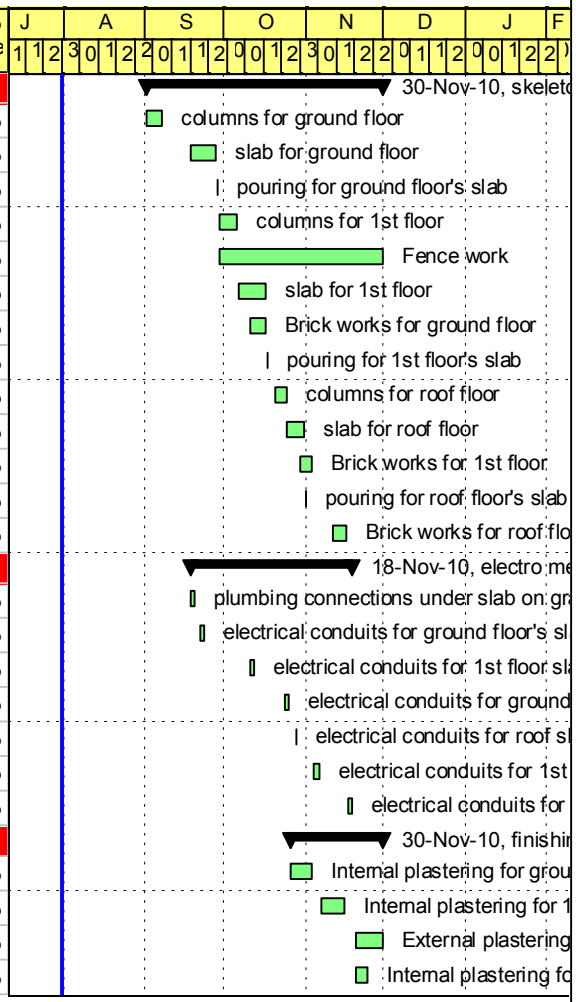

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Villa Number B107	102	31-Jul-10	30-Nov-10	21-Jun-10	23-Oct-10	
general dates	102	31-Jul-10	30-Nov-10	21-Jun-10	23-Oct-10	
Start Villa construction	0	31-Jul-10		21-Jun-10		0%
IFC drawings	0	31-Jul-10		21-Jun-10		0%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Nov-10		23-Oct-10	0%
earth works	14	02-Aug-10	17-Aug-10	23-Jun-10	08-Jul-10	
excavation	2	02-Aug-10	03-Aug-10	23-Jun-10	24-Jun-10	0%
soil replacement	12	04-Aug-10	17-Aug-10	26-Jun-10	08-Jul-10	0%
foundation level	56	18-Aug-10	21-Oct-10	10-Jul-10	15-Sep-10	
Plain Concrete Foundation	2	18-Aug-10	19-Aug-10	10-Jul-10	11-Jul-10	0%
backfilling between P.C Foundation	2	22-Aug-10	23-Aug-10	13-Jul-10	14-Jul-10	0%
Reinforced Concrete Foundation	7	24-Aug-10	31-Aug-10	17-Jul-10	24-Jul-10	0%
under ground brick works	2	08-Sep-10	09-Sep-10	01-Aug-10	02-Aug-10	0%
under ground insulation for RC & Brick work	2	11-Sep-10	12-Sep-10	03-Aug-10	04-Aug-10	0%
backfilling for under ground	4	13-Sep-10	16-Sep-10	05-Aug-10	09-Aug-10	0%
P.C slab on grade 10CM	1	17-Oct-10	17-Oct-10	11-Sep-10	11-Sep-10	0%
moisture insulation with membrane sheets	2	18-Oct-10	19-Oct-10	12-Sep-10	13-Sep-10	0%
R.C slab on grade	2	20-Oct-10	21-Oct-10	14-Sep-10	15-Sep-10	0%
skeleton & brick walls	74	01-Sep-10	30-Nov-10	25-Jul-10	20-Oct-10	
columns for ground floor	6	01-Sep-10	07-Sep-10	25-Jul-10	31-Jul-10	0%
slab for ground floor	9	18-Sep-10	27-Sep-10	10-Aug-10	19-Aug-10	0%
pouring for ground floor's slab	1	28-Sep-10	28-Sep-10	21-Aug-10	21-Aug-10	0%
columns for 1st floor	6	29-Sep-10	05-Oct-10	22-Aug-10	28-Aug-10	0%
Fence work	50	29-Sep-10	30-Nov-10	22-Aug-10	20-Oct-10	0%
slab for 1st floor	9	06-Oct-10	16-Oct-10	29-Aug-10	07-Sep-10	0%
Brick works for ground floor	5	11-Oct-10	16-Oct-10	02-Sep-10	07-Sep-10	0%
pouring for 1st floor's slab	1	17-Oct-10	17-Oct-10	11-Sep-10	11-Sep-10	0%

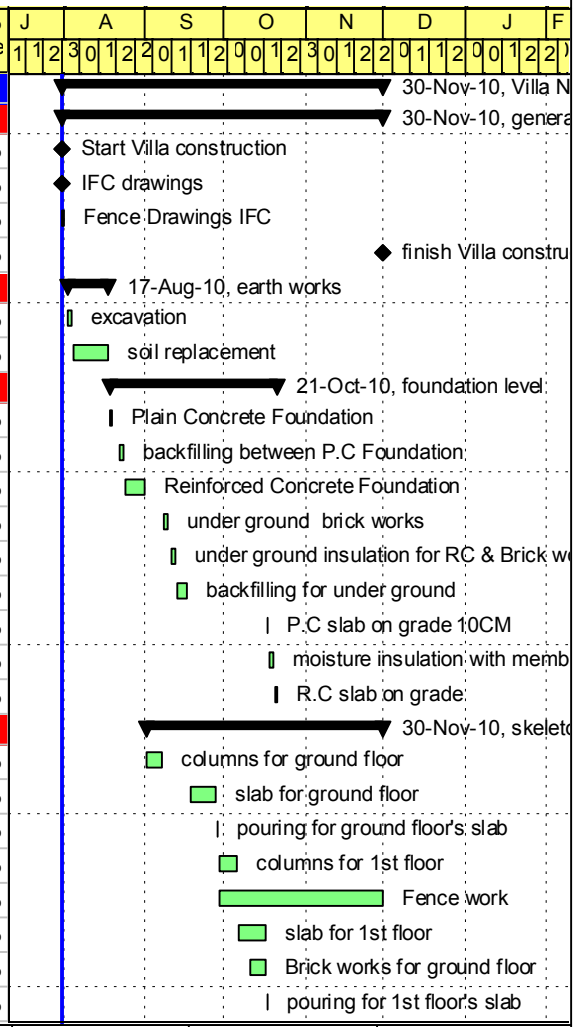

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
columns for roof floor	4	20-Oct-10	24-Oct-10	14-Sep-10	18-Sep-10	0%
slab for roof floor	6	25-Oct-10	31-Oct-10	19-Sep-10	25-Sep-10	0%
Brick works for 1st floor	5	30-Oct-10	03-Nov-10	23-Sep-10	28-Sep-10	0%
pouring for roof floor's slab	1	01-Nov-10	01-Nov-10	26-Sep-10	26-Sep-10	0%
Brick works for roof floor	5	11-Nov-10	16-Nov-10	06-Oct-10	11-Oct-10	0%
electro mechanical	50	18-Sep-10	18-Nov-10	10-Aug-10	13-Oct-10	
plumbing connections under slab on grade	2	18-Sep-10	19-Sep-10	10-Aug-10	11-Aug-10	0%
electrical conduits for ground floor's slab	2	22-Sep-10	23-Sep-10	15-Aug-10	16-Aug-10	0%
electrical conduits for 1st floor slab	2	11-Oct-10	12-Oct-10	02-Sep-10	04-Sep-10	0%
electrical conduits for ground floor walls	2	24-Oct-10	25-Oct-10	18-Sep-10	19-Sep-10	0%
electrical conduits for roof slab	1	28-Oct-10	28-Oct-10	22-Sep-10	22-Sep-10	0%
electrical conduits for 1st floor walls	2	04-Nov-10	06-Nov-10	29-Sep-10	30-Sep-10	0%
electrical conduits for roof floor walls	2	17-Nov-10	18-Nov-10	12-Oct-10	13-Oct-10	0%
finishing	27	26-Oct-10	30-Nov-10	20-Sep-10	23-Oct-10	
Internal plastering for ground floor	8	26-Oct-10	03-Nov-10	20-Sep-10	28-Sep-10	0%
Internal plastering for 1st floor	8	07-Nov-10	15-Nov-10	02-Oct-10	10-Oct-10	0%
External plastering	10	20-Nov-10	30-Nov-10	12-Oct-10	23-Oct-10	0%
Internal plastering for roof floor	5	20-Nov-10	24-Nov-10	14-Oct-10	19-Oct-10	0%
Zone.No 2	108	28-Jun-10 A	09-Nov-10	21-Jun-10	13-Nov-10	
Villa Number D89	105	29-Jun-10 A	06-Nov-10	21-Jun-10	06-Nov-10	
general dates	94	29-Jun-10 A	06-Nov-10	21-Jun-10	06-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		06-Nov-10		06-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	07-Jul-10	22-Jul-10	
excavation	2	30-Jun-10 A	01-Jul-10 A	07-Jul-10	08-Jul-10	100%

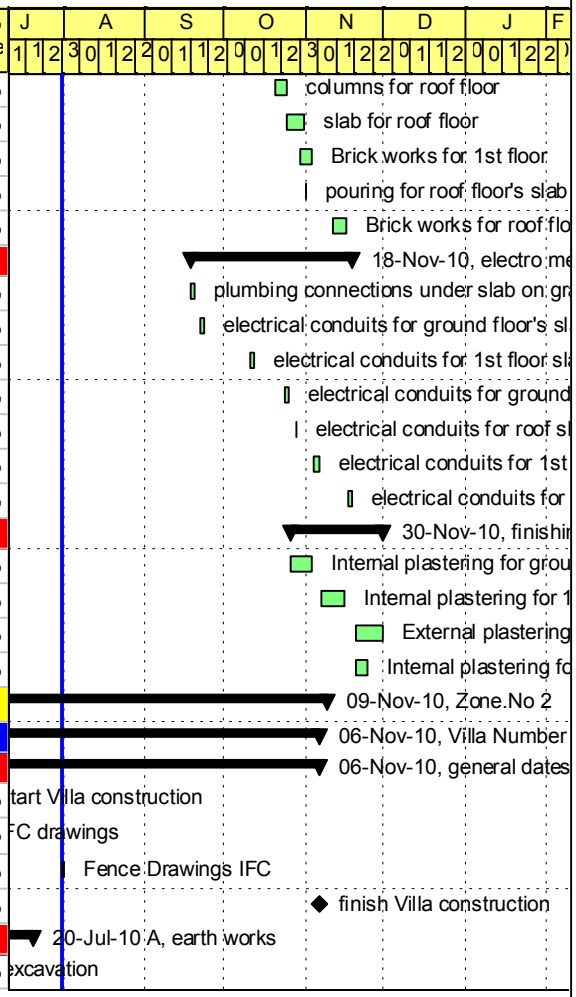

Remaining Level of Effort ◆ Milestone
Actual Work Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
soil replacement	12	02-Jul-10 A	20-Jul-10 A	10-Jul-10	22-Jul-10	100%
foundation level	62	21-Jul-10 A	29-Sep-10	24-Jul-10	29-Sep-10	
Plain Concrete Foundation	2	21-Jul-10 A	25-Jul-10 A	24-Jul-10	25-Jul-10	100%
backfilling between P.C Foundation	2	31-Jul-10 A	01-Aug-10	27-Jul-10	28-Jul-10	20%
Reinforced Concrete Foundation	7	02-Aug-10	09-Aug-10	31-Jul-10	07-Aug-10	0%
under ground brick works	2	17-Aug-10	18-Aug-10	15-Aug-10	16-Aug-10	0%
under ground insulation for RC & Brick work	2	19-Aug-10	21-Aug-10	17-Aug-10	18-Aug-10	0%
backfilling for under ground	4	22-Aug-10	25-Aug-10	19-Aug-10	23-Aug-10	0%
P.C slab on grade 10CM	1	25-Sep-10	25-Sep-10	25-Sep-10	25-Sep-10	0%
moisture insulation with membrane sheets	2	26-Sep-10	27-Sep-10	26-Sep-10	27-Sep-10	0%
R.C slab on grade	2	28-Sep-10	29-Sep-10	28-Sep-10	29-Sep-10	0%
skeleton & brick walls	74	10-Aug-10	03-Nov-10	08-Aug-10	03-Nov-10	
columns for ground floor	6	10-Aug-10	16-Aug-10	08-Aug-10	14-Aug-10	0%
slab for ground floor	9	26-Aug-10	05-Sep-10	24-Aug-10	02-Sep-10	0%
pouring for ground floor's slab	1	06-Sep-10	06-Sep-10	04-Sep-10	04-Sep-10	0%
columns for 1st floor	6	07-Sep-10	13-Sep-10	05-Sep-10	13-Sep-10	0%
Fence work	50	07-Sep-10	03-Nov-10	05-Sep-10	03-Nov-10	0%
slab for 1st floor	9	14-Sep-10	23-Sep-10	14-Sep-10	23-Sep-10	0%
Brick works for ground floor	5	19-Sep-10	23-Sep-10	19-Sep-10	23-Sep-10	0%
pouring for 1st floor's slab	1	25-Sep-10	25-Sep-10	25-Sep-10	25-Sep-10	0%
columns for roof floor	4	28-Sep-10	02-Oct-10	28-Sep-10	02-Oct-10	0%
slab for roof floor	6	03-Oct-10	09-Oct-10	03-Oct-10	09-Oct-10	0%
Brick works for 1st floor	5	07-Oct-10	12-Oct-10	07-Oct-10	12-Oct-10	0%
pouring for roof floor's slab	1	10-Oct-10	10-Oct-10	10-Oct-10	10-Oct-10	0%
Brick works for roof floor	5	20-Oct-10	25-Oct-10	20-Oct-10	25-Oct-10	0%
electro mechanical	54	26-Aug-10	27-Oct-10	24-Aug-10	27-Oct-10	
plumbing connections under slab on grade	2	26-Aug-10	28-Aug-10	24-Aug-10	25-Aug-10	0%

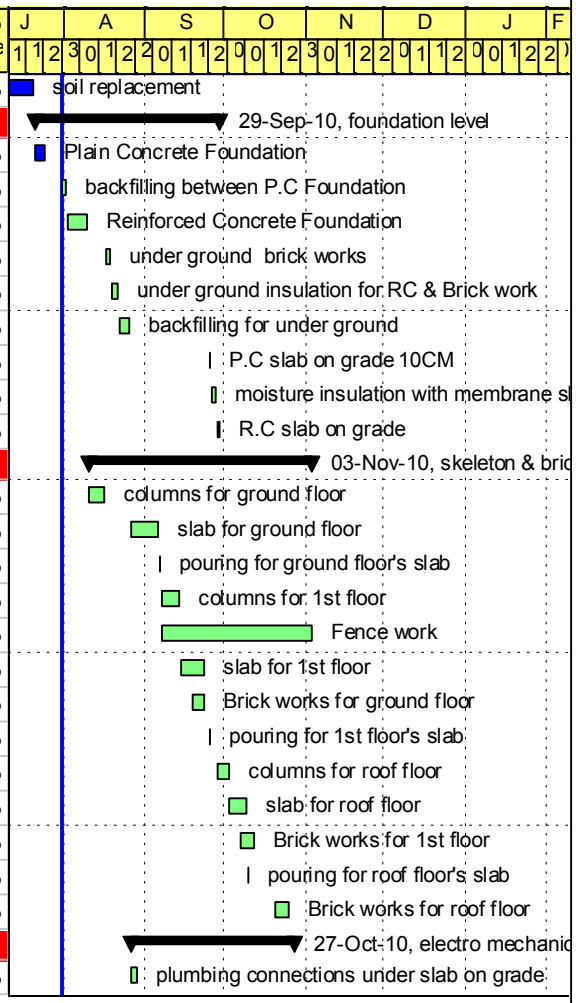

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
electrical conduits for ground floor's slab	2	31-Aug-10	01-Sep-10	29-Aug-10	30-Aug-10	0%
electrical conduits for 1st floor slab	2	19-Sep-10	20-Sep-10	19-Sep-10	20-Sep-10	0%
electrical conduits for ground floor walls	2	02-Oct-10	03-Oct-10	02-Oct-10	03-Oct-10	0%
electrical conduits for roof slab	1	06-Oct-10	06-Oct-10	06-Oct-10	06-Oct-10	0%
electrical conduits for 1st floor walls	2	13-Oct-10	14-Oct-10	13-Oct-10	14-Oct-10	0%
electrical conduits for roof floor walls	2	26-Oct-10	27-Oct-10	26-Oct-10	27-Oct-10	0%
finishing	29	04-Oct-10	06-Nov-10	04-Oct-10	06-Nov-10	
Internal plastering for ground floor	8	04-Oct-10	12-Oct-10	04-Oct-10	12-Oct-10	0%
Internal plastering for 1st floor	8	16-Oct-10	24-Oct-10	16-Oct-10	24-Oct-10	0%
External plastering	10	26-Oct-10	06-Nov-10	26-Oct-10	06-Nov-10	0%
Internal plastering for roof floor	5	28-Oct-10	02-Nov-10	28-Oct-10	02-Nov-10	0%
Villa Number D90	104	29-Jun-10 A	06-Nov-10	21-Jun-10	07-Nov-10	
general dates	94	29-Jun-10 A	06-Nov-10	21-Jun-10	07-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		06-Nov-10		07-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	08-Jul-10	24-Jul-10	
excavation	0	30-Jun-10 A	01-Jul-10 A	08-Jul-10	08-Jul-10	100%
soil replacement	14	02-Jul-10 A	20-Jul-10 A	08-Jul-10	24-Jul-10	100%
foundation level	62	21-Jul-10 A	29-Sep-10	25-Jul-10	30-Sep-10	
Plain Concrete Foundation	2	21-Jul-10 A	25-Jul-10 A	25-Jul-10	26-Jul-10	100%
backfilling between P.C Foundation	2	31-Jul-10 A	01-Aug-10	28-Jul-10	29-Jul-10	20%
Reinforced Concrete Foundation	7	02-Aug-10	09-Aug-10	01-Aug-10	08-Aug-10	0%
under ground brick works	2	17-Aug-10	18-Aug-10	16-Aug-10	17-Aug-10	0%
under ground insulation for RC & Brick work	2	19-Aug-10	21-Aug-10	18-Aug-10	19-Aug-10	0%
backfilling for under ground	4	22-Aug-10	25-Aug-10	21-Aug-10	24-Aug-10	0%
P.C slab on grade 10CM	1	25-Sep-10	25-Sep-10	26-Sep-10	26-Sep-10	0%

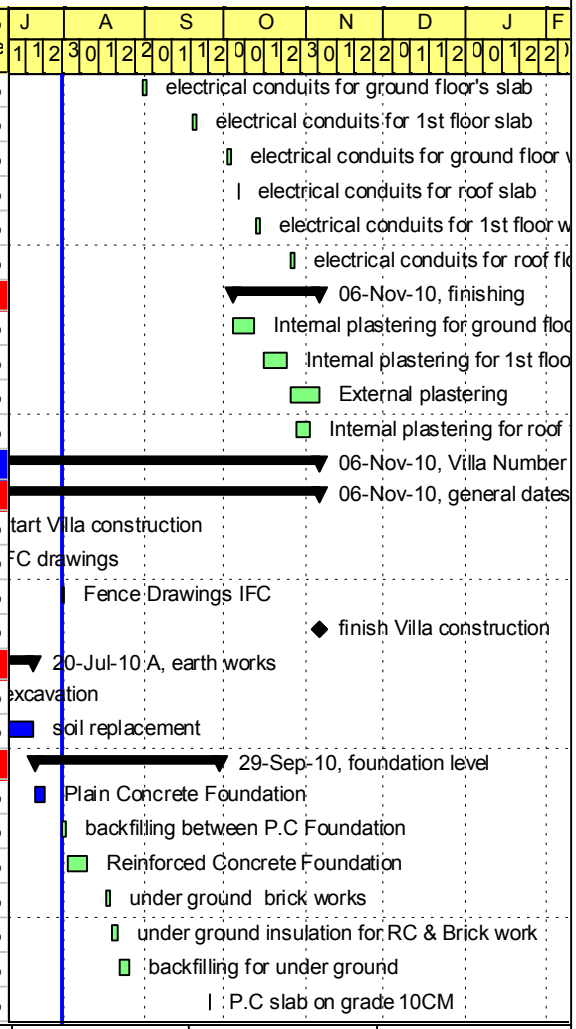

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
moisture insulation with membrane sheets	2	26-Sep-10	27-Sep-10	27-Sep-10	28-Sep-10	0%
R.C slab on grade	2	28-Sep-10	29-Sep-10	29-Sep-10	30-Sep-10	0%
skeleton & brick walls	**74**	**10-Aug-10**	**03-Nov-10**	**09-Aug-10**	**04-Nov-10**	
columns for ground floor	6	10-Aug-10	16-Aug-10	09-Aug-10	15-Aug-10	0%
slab for ground floor	9	26-Aug-10	05-Sep-10	25-Aug-10	04-Sep-10	0%
pouring for ground floor's slab	1	06-Sep-10	06-Sep-10	05-Sep-10	05-Sep-10	0%
columns for 1st floor	6	07-Sep-10	13-Sep-10	06-Sep-10	14-Sep-10	0%
Fence work	50	07-Sep-10	03-Nov-10	06-Sep-10	04-Nov-10	0%
slab for 1st floor	9	14-Sep-10	23-Sep-10	15-Sep-10	25-Sep-10	0%
Brick works for ground floor	5	19-Sep-10	23-Sep-10	20-Sep-10	25-Sep-10	0%
pouring for 1st floor's slab	1	25-Sep-10	25-Sep-10	26-Sep-10	26-Sep-10	0%
columns for roof floor	4	28-Sep-10	02-Oct-10	29-Sep-10	03-Oct-10	0%
slab for roof floor	6	03-Oct-10	09-Oct-10	04-Oct-10	10-Oct-10	0%
Brick works for 1st floor	5	07-Oct-10	12-Oct-10	09-Oct-10	13-Oct-10	0%
pouring for roof floor's slab	1	10-Oct-10	10-Oct-10	11-Oct-10	11-Oct-10	0%
Brick works for roof floor	5	20-Oct-10	25-Oct-10	21-Oct-10	26-Oct-10	0%
electro mechanical	**54**	**26-Aug-10**	**27-Oct-10**	**25-Aug-10**	**28-Oct-10**	
plumbing connections under slab on grade	2	26-Aug-10	28-Aug-10	25-Aug-10	26-Aug-10	0%
electrical conduits for ground floor's slab	2	31-Aug-10	01-Sep-10	30-Aug-10	31-Aug-10	0%
electrical conduits for 1st floor slab	2	19-Sep-10	20-Sep-10	20-Sep-10	21-Sep-10	0%
electrical conduits for ground floor walls	2	02-Oct-10	03-Oct-10	03-Oct-10	04-Oct-10	0%
electrical conduits for roof slab	1	06-Oct-10	06-Oct-10	07-Oct-10	07-Oct-10	0%
electrical conduits for 1st floor walls	2	13-Oct-10	14-Oct-10	14-Oct-10	16-Oct-10	0%
electrical conduits for roof floor walls	2	26-Oct-10	27-Oct-10	27-Oct-10	28-Oct-10	0%
finishing	**29**	**04-Oct-10**	**06-Nov-10**	**05-Oct-10**	**07-Nov-10**	
Internal plastering for ground floor	8	04-Oct-10	12-Oct-10	05-Oct-10	13-Oct-10	0%
Internal plastering for 1st floor	8	16-Oct-10	24-Oct-10	17-Oct-10	25-Oct-10	0%

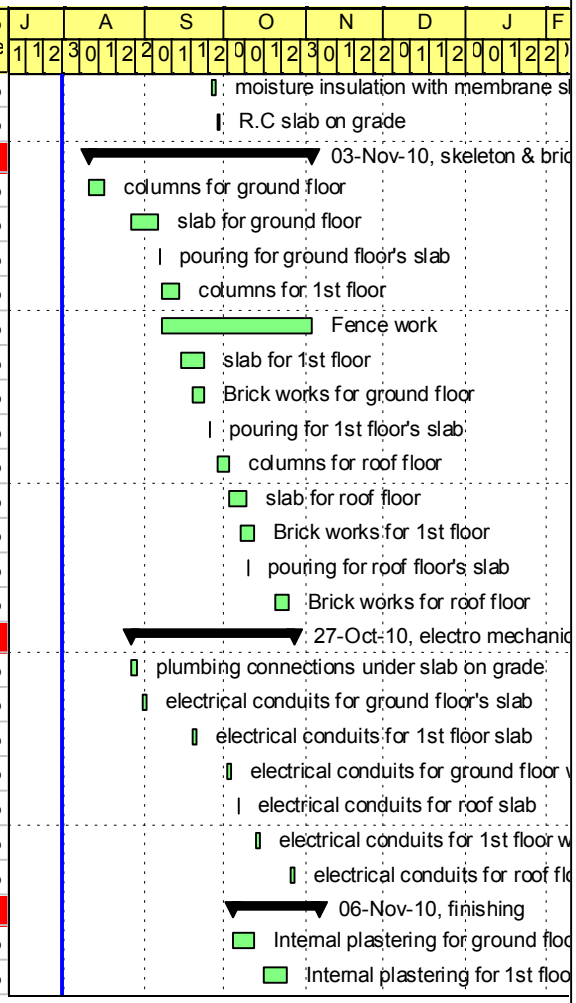

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
External plastering	10	26-Oct-10	06-Nov-10	27-Oct-10	07-Nov-10	0%
Internal plastering for roof floor	5	28-Oct-10	02-Nov-10	30-Oct-10	03-Nov-10	0%
Villa Number D91	103	29-Jun-10 A	06-Nov-10	21-Jun-10	08-Nov-10	
general dates	94	29-Jun-10 A	06-Nov-10	21-Jun-10	08-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jul-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		06-Nov-10		08-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	10-Jul-10	25-Jul-10	
excavation	2	30-Jun-10 A	01-Jul-10 A	10-Jul-10	11-Jul-10	100%
soil replacement	12	02-Jul-10 A	20-Jul-10 A	12-Jul-10	25-Jul-10	100%
foundation level	62	21-Jul-10 A	29-Sep-10	26-Jul-10	02-Oct-10	
Plain Concrete Foundation	2	21-Jul-10 A	29-Jul-10 A	26-Jul-10	27-Jul-10	100%
backfilling between P.C Foundation	2	31-Jul-10	01-Aug-10	29-Jul-10	31-Jul-10	0%
Reinforced Concrete Foundation	7	02-Aug-10	09-Aug-10	02-Aug-10	09-Aug-10	0%
under ground brick works	2	17-Aug-10	18-Aug-10	17-Aug-10	18-Aug-10	0%
under ground insulation for RC & Brick work	2	19-Aug-10	21-Aug-10	19-Aug-10	21-Aug-10	0%
backfilling for under ground	4	22-Aug-10	25-Aug-10	22-Aug-10	25-Aug-10	0%
P.C slab on grade 10CM	1	25-Sep-10	25-Sep-10	27-Sep-10	27-Sep-10	0%
moisture insulation with membrane sheets	2	26-Sep-10	27-Sep-10	28-Sep-10	29-Sep-10	0%
R.C slab on grade	2	28-Sep-10	29-Sep-10	30-Sep-10	02-Oct-10	0%
skeleton & brick walls	74	10-Aug-10	03-Nov-10	10-Aug-10	06-Nov-10	
columns for ground floor	6	10-Aug-10	16-Aug-10	10-Aug-10	16-Aug-10	0%
slab for ground floor	9	26-Aug-10	05-Sep-10	26-Aug-10	05-Sep-10	0%
pouring for ground floor's slab	1	06-Sep-10	06-Sep-10	06-Sep-10	06-Sep-10	0%
columns for 1st floor	6	07-Sep-10	13-Sep-10	07-Sep-10	15-Sep-10	0%
Fence work	50	07-Sep-10	03-Nov-10	07-Sep-10	06-Nov-10	0%
slab for 1st floor	9	14-Sep-10	23-Sep-10	16-Sep-10	26-Sep-10	0%

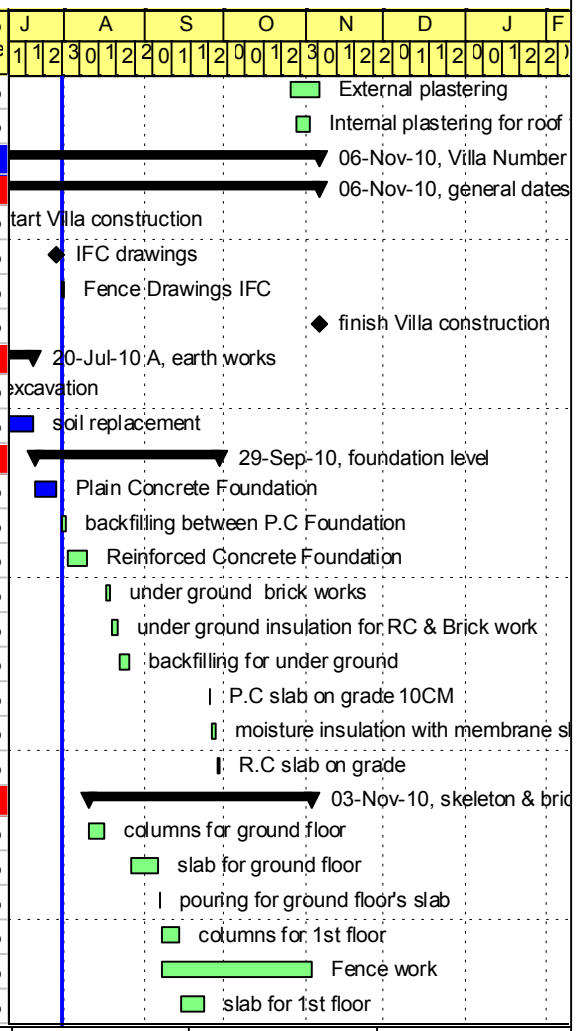

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Brick works for ground floor	5	19-Sep-10	23-Sep-10	21-Sep-10	26-Sep-10	0%
pouring for 1st floor's slab	1	25-Sep-10	25-Sep-10	27-Sep-10	27-Sep-10	0%
columns for roof floor	4	28-Sep-10	02-Oct-10	30-Sep-10	04-Oct-10	0%
slab for roof floor	6	03-Oct-10	09-Oct-10	05-Oct-10	11-Oct-10	0%
Brick works for 1st floor	5	07-Oct-10	12-Oct-10	10-Oct-10	14-Oct-10	0%
pouring for roof floor's slab	1	10-Oct-10	10-Oct-10	12-Oct-10	12-Oct-10	0%
Brick works for roof floor	5	20-Oct-10	25-Oct-10	23-Oct-10	27-Oct-10	0%
electro mechanical	54	26-Aug-10	27-Oct-10	26-Aug-10	30-Oct-10	
plumbing connections under slab on grade	2	26-Aug-10	28-Aug-10	26-Aug-10	28-Aug-10	0%
electrical conduits for ground floor's slab	2	31-Aug-10	01-Sep-10	31-Aug-10	01-Sep-10	0%
electrical conduits for 1st floor slab	2	19-Sep-10	20-Sep-10	21-Sep-10	22-Sep-10	0%
electrical conduits for ground floor walls	2	02-Oct-10	03-Oct-10	04-Oct-10	05-Oct-10	0%
electrical conduits for roof slab	1	06-Oct-10	06-Oct-10	09-Oct-10	09-Oct-10	0%
electrical conduits for 1st floor walls	2	13-Oct-10	14-Oct-10	16-Oct-10	17-Oct-10	0%
electrical conduits for roof floor walls	2	26-Oct-10	27-Oct-10	28-Oct-10	30-Oct-10	0%
finishing	29	04-Oct-10	06-Nov-10	06-Oct-10	08-Nov-10	
Internal plastering for ground floor	8	04-Oct-10	12-Oct-10	06-Oct-10	14-Oct-10	0%
Internal plastering for 1st floor	8	16-Oct-10	24-Oct-10	18-Oct-10	26-Oct-10	0%
External plastering	10	26-Oct-10	06-Nov-10	28-Oct-10	08-Nov-10	0%
Internal plastering for roof floor	5	28-Oct-10	02-Nov-10	31-Oct-10	04-Nov-10	0%
Villa Number A92	105	29-Jun-10 A	09-Nov-10	21-Jun-10	09-Nov-10	
general dates	97	29-Jun-10 A	09-Nov-10	21-Jun-10	09-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Nov-10		09-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	11-Jul-10	26-Jul-10	
excavation	2	30-Jun-10 A	01-Jul-10 A	11-Jul-10	12-Jul-10	100%

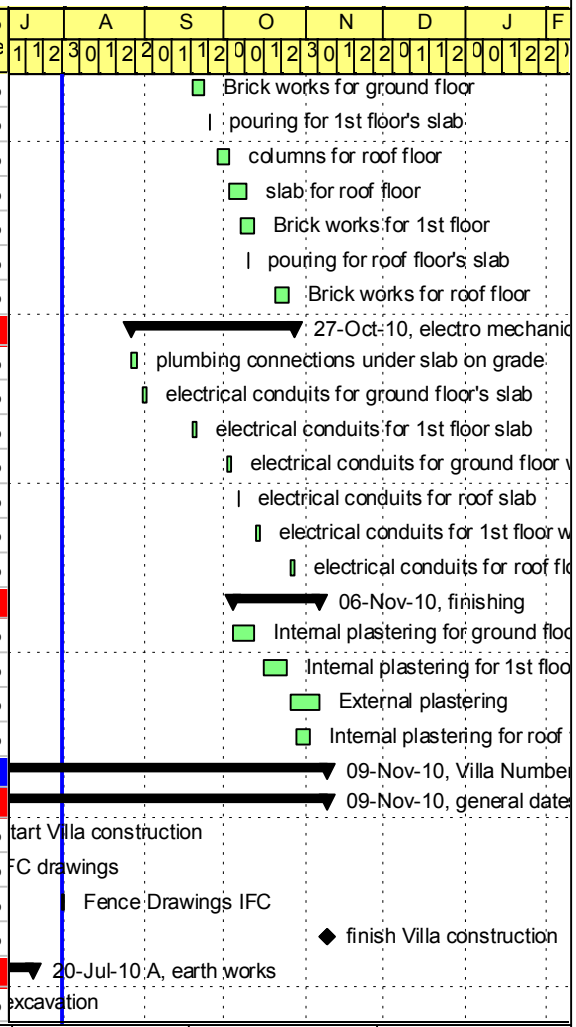

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
soil replacement	12	02-Jul-10 A	20-Jul-10 A	13-Jul-10	26-Jul-10	100%
foundation level	56	31-Jul-10	03-Oct-10	27-Jul-10	03-Oct-10	
Plain Concrete Foundation	2	31-Jul-10	01-Aug-10	27-Jul-10	28-Jul-10	0%
backfilling between P.C Foundation	2	03-Aug-10	04-Aug-10	31-Jul-10	01-Aug-10	0%
Reinforced Concrete Foundation	7	05-Aug-10	12-Aug-10	03-Aug-10	10-Aug-10	0%
under ground brick works	2	21-Aug-10	22-Aug-10	18-Aug-10	19-Aug-10	0%
under ground insulation for RC & Brick work	2	23-Aug-10	24-Aug-10	21-Aug-10	22-Aug-10	0%
backfilling for under ground	4	25-Aug-10	29-Aug-10	23-Aug-10	26-Aug-10	0%
P.C slab on grade 10CM	1	28-Sep-10	28-Sep-10	28-Sep-10	28-Sep-10	0%
moisture insulation with membrane sheets	2	29-Sep-10	30-Sep-10	29-Sep-10	30-Sep-10	0%
R.C slab on grade	2	02-Oct-10	03-Oct-10	02-Oct-10	03-Oct-10	0%
skeleton & brick walls	74	14-Aug-10	07-Nov-10	11-Aug-10	07-Nov-10	
columns for ground floor	6	14-Aug-10	19-Aug-10	11-Aug-10	17-Aug-10	0%
slab for ground floor	9	30-Aug-10	08-Sep-10	28-Aug-10	06-Sep-10	0%
pouring for ground floor's slab	1	09-Sep-10	09-Sep-10	07-Sep-10	07-Sep-10	0%
columns for 1st floor	6	11-Sep-10	16-Sep-10	11-Sep-10	16-Sep-10	0%
Fence work	50	11-Sep-10	07-Nov-10	11-Sep-10	07-Nov-10	0%
slab for 1st floor	9	18-Sep-10	27-Sep-10	18-Sep-10	27-Sep-10	0%
Brick works for ground floor	5	22-Sep-10	27-Sep-10	22-Sep-10	27-Sep-10	0%
pouring for 1st floor's slab	1	28-Sep-10	28-Sep-10	28-Sep-10	28-Sep-10	0%
columns for roof floor	4	02-Oct-10	05-Oct-10	02-Oct-10	05-Oct-10	0%
slab for roof floor	6	06-Oct-10	12-Oct-10	06-Oct-10	12-Oct-10	0%
Brick works for 1st floor	5	11-Oct-10	16-Oct-10	11-Oct-10	16-Oct-10	0%
pouring for roof floor's slab	1	13-Oct-10	13-Oct-10	13-Oct-10	13-Oct-10	0%
Brick works for roof floor	5	24-Oct-10	28-Oct-10	24-Oct-10	28-Oct-10	0%
electro mechanical	54	30-Aug-10	31-Oct-10	28-Aug-10	31-Oct-10	
plumbing connections under slab on grade	2	30-Aug-10	31-Aug-10	28-Aug-10	29-Aug-10	0%

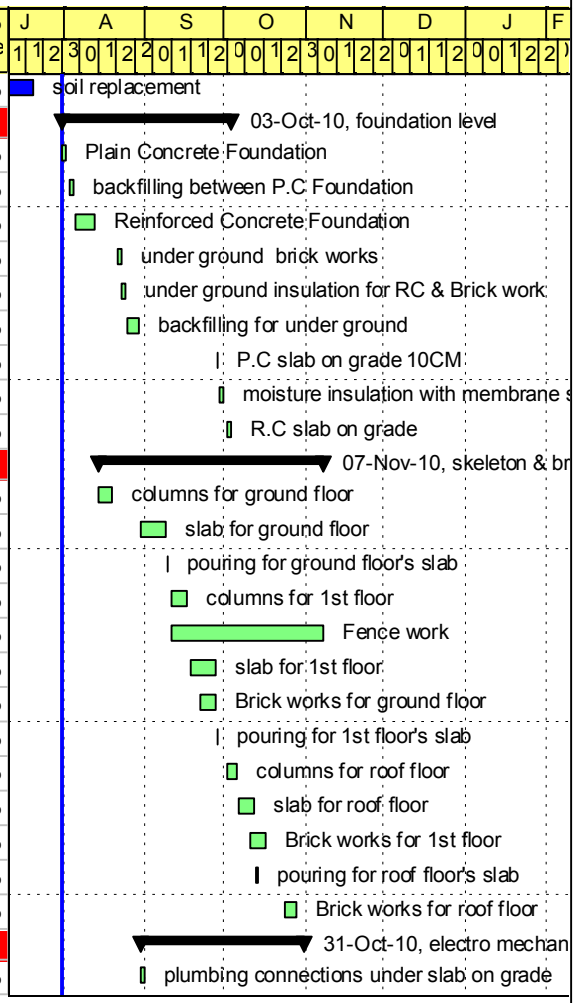

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
electrical conduits for ground floor's slab	2	04-Sep-10	05-Sep-10	01-Sep-10	02-Sep-10	0%
electrical conduits for 1st floor slab	2	22-Sep-10	23-Sep-10	22-Sep-10	23-Sep-10	0%
electrical conduits for ground floor walls	2	05-Oct-10	06-Oct-10	05-Oct-10	06-Oct-10	0%
electrical conduits for roof slab	1	10-Oct-10	10-Oct-10	10-Oct-10	10-Oct-10	0%
electrical conduits for 1st floor walls	2	17-Oct-10	18-Oct-10	17-Oct-10	18-Oct-10	0%
electrical conduits for roof floor walls	2	30-Oct-10	31-Oct-10	30-Oct-10	31-Oct-10	0%
finishing	29	07-Oct-10	09-Nov-10	07-Oct-10	09-Nov-10	
Internal plastering for ground floor	8	07-Oct-10	16-Oct-10	07-Oct-10	16-Oct-10	0%
Internal plastering for 1st floor	8	19-Oct-10	27-Oct-10	19-Oct-10	27-Oct-10	0%
External plastering	10	30-Oct-10	09-Nov-10	30-Oct-10	09-Nov-10	0%
Internal plastering for roof floor	5	01-Nov-10	06-Nov-10	01-Nov-10	06-Nov-10	0%
Villa Number F93	104	28-Jun-10 A	09-Nov-10	21-Jun-10	10-Nov-10	
general dates	97	28-Jun-10 A	09-Nov-10	21-Jun-10	10-Nov-10	
Start Villa construction	0	28-Jun-10 A		21-Jun-10		100%
IFC drawings	0	28-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Nov-10		10-Nov-10	0%
earth works	14	29-Jun-10 A	20-Jul-10 A	12-Jul-10	27-Jul-10	
excavation	0	29-Jun-10 A	01-Jul-10 A	12-Jul-10	12-Jul-10	100%
soil replacement	14	02-Jul-10 A	20-Jul-10 A	12-Jul-10	27-Jul-10	100%
foundation level	56	31-Jul-10	03-Oct-10	28-Jul-10	04-Oct-10	
Plain Concrete Foundation	2	31-Jul-10	01-Aug-10	28-Jul-10	29-Jul-10	0%
backfilling between P.C Foundation	2	03-Aug-10	04-Aug-10	01-Aug-10	02-Aug-10	0%
Reinforced Concrete Foundation	7	05-Aug-10	12-Aug-10	04-Aug-10	11-Aug-10	0%
under ground brick works	2	21-Aug-10	22-Aug-10	19-Aug-10	21-Aug-10	0%
under ground insulation for RC & Brick work	2	23-Aug-10	24-Aug-10	22-Aug-10	23-Aug-10	0%
backfilling for under ground	4	25-Aug-10	29-Aug-10	24-Aug-10	28-Aug-10	0%
P.C slab on grade 10CM	1	28-Sep-10	28-Sep-10	29-Sep-10	29-Sep-10	0%

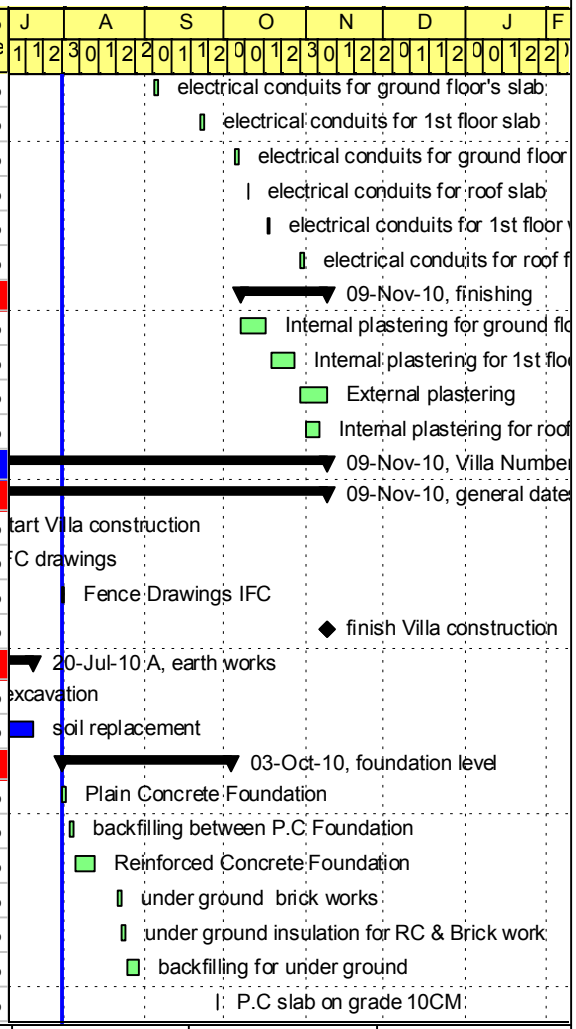

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
moisture insulation with membrane sheets	2	29-Sep-10	30-Sep-10	30-Sep-10	02-Oct-10	0%
R.C slab on grade	2	02-Oct-10	03-Oct-10	03-Oct-10	04-Oct-10	0%
skeleton & brick walls	**74**	**14-Aug-10**	**07-Nov-10**	**12-Aug-10**	**08-Nov-10**	
columns for ground floor	6	14-Aug-10	19-Aug-10	12-Aug-10	18-Aug-10	0%
slab for ground floor	9	30-Aug-10	08-Sep-10	29-Aug-10	07-Sep-10	0%
pouring for ground floor's slab	1	09-Sep-10	09-Sep-10	11-Sep-10	11-Sep-10	0%
columns for 1st floor	6	11-Sep-10	16-Sep-10	12-Sep-10	18-Sep-10	0%
Fence work	50	11-Sep-10	07-Nov-10	12-Sep-10	08-Nov-10	0%
slab for 1st floor	9	18-Sep-10	27-Sep-10	19-Sep-10	28-Sep-10	0%
Brick works for ground floor	5	22-Sep-10	27-Sep-10	23-Sep-10	28-Sep-10	0%
pouring for 1st floor's slab	1	28-Sep-10	28-Sep-10	29-Sep-10	29-Sep-10	0%
columns for roof floor	4	02-Oct-10	05-Oct-10	03-Oct-10	06-Oct-10	0%
slab for roof floor	6	06-Oct-10	12-Oct-10	07-Oct-10	13-Oct-10	0%
Brick works for 1st floor	5	11-Oct-10	16-Oct-10	12-Oct-10	17-Oct-10	0%
pouring for roof floor's slab	1	13-Oct-10	13-Oct-10	14-Oct-10	14-Oct-10	0%
Brick works for roof floor	5	24-Oct-10	28-Oct-10	25-Oct-10	30-Oct-10	0%
electro mechanical	**54**	**30-Aug-10**	**31-Oct-10**	**29-Aug-10**	**01-Nov-10**	
plumbing connections under slab on grade	2	30-Aug-10	31-Aug-10	29-Aug-10	30-Aug-10	0%
electrical conduits for ground floor's slab	2	04-Sep-10	05-Sep-10	02-Sep-10	04-Sep-10	0%
electrical conduits for 1st floor slab	2	22-Sep-10	23-Sep-10	23-Sep-10	25-Sep-10	0%
electrical conduits for ground floor walls	2	05-Oct-10	06-Oct-10	06-Oct-10	07-Oct-10	0%
electrical conduits for roof slab	1	10-Oct-10	10-Oct-10	11-Oct-10	11-Oct-10	0%
electrical conduits for 1st floor walls	2	17-Oct-10	18-Oct-10	18-Oct-10	19-Oct-10	0%
electrical conduits for roof floor walls	2	30-Oct-10	31-Oct-10	31-Oct-10	01-Nov-10	0%
finishing	**29**	**07-Oct-10**	**09-Nov-10**	**09-Oct-10**	**10-Nov-10**	
Internal plastering for ground floor	8	07-Oct-10	16-Oct-10	09-Oct-10	17-Oct-10	0%
Internal plastering for 1st floor	8	19-Oct-10	27-Oct-10	20-Oct-10	28-Oct-10	0%

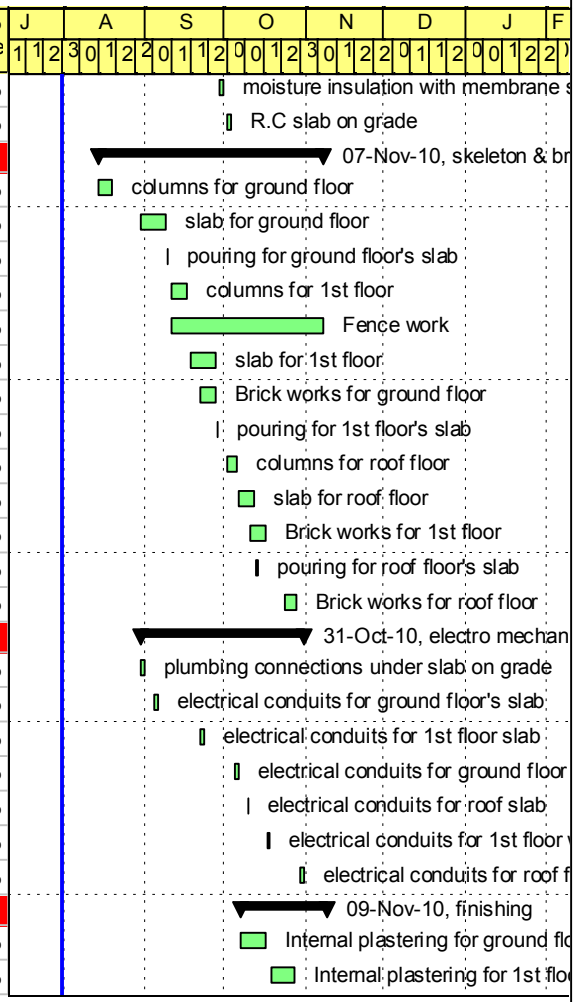

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
External plastering	10	30-Oct-10	09-Nov-10	31-Oct-10	10-Nov-10	0%
Internal plastering for roof floor	5	01-Nov-10	06-Nov-10	02-Nov-10	07-Nov-10	0%
Villa Number F94	103	29-Jun-10 A	09-Nov-10	21-Jun-10	11-Nov-10	
general dates	97	29-Jun-10 A	09-Nov-10	21-Jun-10	11-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Nov-10		11-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	13-Jul-10	28-Jul-10	
excavation	0	30-Jun-10 A	01-Jul-10 A	13-Jul-10	13-Jul-10	100%
soil replacement	14	02-Jul-10 A	20-Jul-10 A	13-Jul-10	28-Jul-10	100%
foundation level	56	31-Jul-10	03-Oct-10	29-Jul-10	05-Oct-10	
Plain Concrete Foundation	2	31-Jul-10	01-Aug-10	29-Jul-10	31-Jul-10	0%
backfilling between P.C Foundation	2	03-Aug-10	04-Aug-10	02-Aug-10	03-Aug-10	0%
Reinforced Concrete Foundation	7	05-Aug-10	12-Aug-10	05-Aug-10	12-Aug-10	0%
under ground brick works	2	21-Aug-10	22-Aug-10	21-Aug-10	22-Aug-10	0%
under ground insulation for RC & Brick work	2	23-Aug-10	24-Aug-10	23-Aug-10	24-Aug-10	0%
backfilling for under ground	4	25-Aug-10	29-Aug-10	25-Aug-10	29-Aug-10	0%
P.C slab on grade 10CM	1	28-Sep-10	28-Sep-10	30-Sep-10	30-Sep-10	0%
moisture insulation with membrane sheets	2	29-Sep-10	30-Sep-10	02-Oct-10	03-Oct-10	0%
R.C slab on grade	2	02-Oct-10	03-Oct-10	04-Oct-10	05-Oct-10	0%
skeleton & brick walls	74	14-Aug-10	07-Nov-10	14-Aug-10	09-Nov-10	
columns for ground floor	6	14-Aug-10	19-Aug-10	14-Aug-10	19-Aug-10	0%
slab for ground floor	9	30-Aug-10	08-Sep-10	30-Aug-10	11-Sep-10	0%
pouring for ground floor's slab	1	09-Sep-10	09-Sep-10	12-Sep-10	12-Sep-10	0%
columns for 1st floor	6	11-Sep-10	16-Sep-10	13-Sep-10	19-Sep-10	0%
Fence work	50	11-Sep-10	07-Nov-10	13-Sep-10	09-Nov-10	0%
slab for 1st floor	9	18-Sep-10	27-Sep-10	20-Sep-10	29-Sep-10	0%

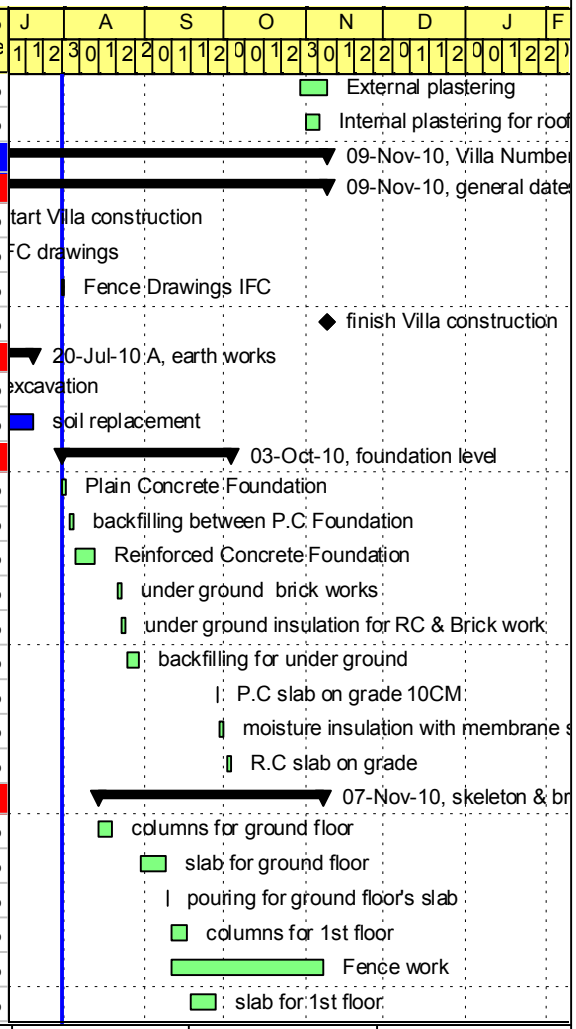

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Brick works for ground floor	5	22-Sep-10	27-Sep-10	25-Sep-10	29-Sep-10	0%
pouring for 1st floor's slab	1	28-Sep-10	28-Sep-10	30-Sep-10	30-Sep-10	0%
columns for roof floor	4	02-Oct-10	05-Oct-10	04-Oct-10	07-Oct-10	0%
slab for roof floor	6	06-Oct-10	12-Oct-10	09-Oct-10	14-Oct-10	0%
Brick works for 1st floor	5	11-Oct-10	16-Oct-10	13-Oct-10	18-Oct-10	0%
pouring for roof floor's slab	1	13-Oct-10	13-Oct-10	16-Oct-10	16-Oct-10	0%
Brick works for roof floor	5	24-Oct-10	28-Oct-10	26-Oct-10	31-Oct-10	0%
electro mechanical	54	30-Aug-10	31-Oct-10	30-Aug-10	02-Nov-10	
plumbing connections under slab on grade	2	30-Aug-10	31-Aug-10	30-Aug-10	31-Aug-10	0%
electrical conduits for ground floor's slab	2	04-Sep-10	05-Sep-10	04-Sep-10	05-Sep-10	0%
electrical conduits for 1st floor slab	2	22-Sep-10	23-Sep-10	25-Sep-10	26-Sep-10	0%
electrical conduits for ground floor walls	2	05-Oct-10	06-Oct-10	07-Oct-10	09-Oct-10	0%
electrical conduits for roof slab	1	10-Oct-10	10-Oct-10	12-Oct-10	12-Oct-10	0%
electrical conduits for 1st floor walls	2	17-Oct-10	18-Oct-10	19-Oct-10	20-Oct-10	0%
electrical conduits for roof floor walls	2	30-Oct-10	31-Oct-10	01-Nov-10	02-Nov-10	0%
finishing	29	07-Oct-10	09-Nov-10	10-Oct-10	11-Nov-10	
Internal plastering for ground floor	8	07-Oct-10	16-Oct-10	10-Oct-10	18-Oct-10	0%
Internal plastering for 1st floor	8	19-Oct-10	27-Oct-10	21-Oct-10	30-Oct-10	0%
External plastering	10	30-Oct-10	09-Nov-10	01-Nov-10	11-Nov-10	0%
Internal plastering for roof floor	5	01-Nov-10	06-Nov-10	03-Nov-10	08-Nov-10	0%
Villa Number A95	104	29-Jun-10 A	09-Nov-10	21-Jun-10	10-Nov-10	
general dates	97	29-Jun-10 A	09-Nov-10	21-Jun-10	10-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Nov-10		10-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	12-Jul-10	27-Jul-10	
excavation	2	30-Jun-10 A	30-Jun-10 A	12-Jul-10	13-Jul-10	100%

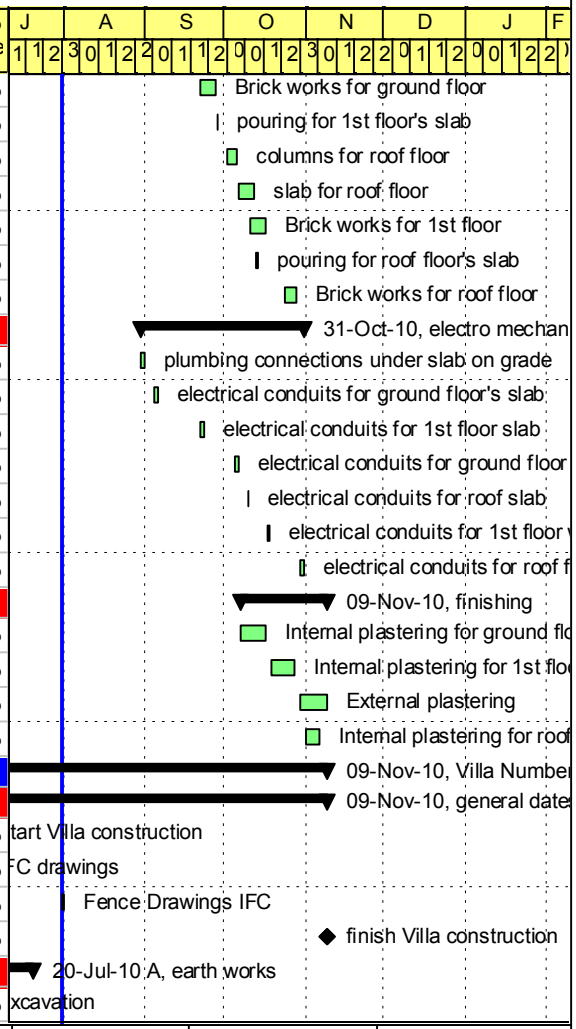

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
soil replacement	12	02-Jul-10 A	20-Jul-10 A	14-Jul-10	27-Jul-10	100%
foundation level	56	31-Jul-10	03-Oct-10	28-Jul-10	04-Oct-10	
Plain Concrete Foundation	2	31-Jul-10	01-Aug-10	28-Jul-10	29-Jul-10	0%
backfilling between P.C Foundation	2	03-Aug-10	04-Aug-10	01-Aug-10	02-Aug-10	0%
Reinforced Concrete Foundation	7	05-Aug-10	12-Aug-10	04-Aug-10	11-Aug-10	0%
under ground brick works	2	21-Aug-10	22-Aug-10	19-Aug-10	21-Aug-10	0%
under ground insulation for RC & Brick work	2	23-Aug-10	24-Aug-10	22-Aug-10	23-Aug-10	0%
backfilling for under ground	4	25-Aug-10	29-Aug-10	24-Aug-10	28-Aug-10	0%
P.C slab on grade 10CM	1	28-Sep-10	28-Sep-10	29-Sep-10	29-Sep-10	0%
moisture insulation with membrane sheets	2	29-Sep-10	30-Sep-10	30-Sep-10	02-Oct-10	0%
R.C slab on grade	2	02-Oct-10	03-Oct-10	03-Oct-10	04-Oct-10	0%
skeleton & brick walls	74	14-Aug-10	07-Nov-10	12-Aug-10	08-Nov-10	
columns for ground floor	6	14-Aug-10	19-Aug-10	12-Aug-10	18-Aug-10	0%
slab for ground floor	9	30-Aug-10	08-Sep-10	29-Aug-10	07-Sep-10	0%
pouring for ground floor's slab	1	09-Sep-10	09-Sep-10	11-Sep-10	11-Sep-10	0%
columns for 1st floor	6	11-Sep-10	16-Sep-10	12-Sep-10	18-Sep-10	0%
Fence work	50	11-Sep-10	07-Nov-10	12-Sep-10	08-Nov-10	0%
slab for 1st floor	9	18-Sep-10	27-Sep-10	19-Sep-10	28-Sep-10	0%
Brick works for ground floor	5	22-Sep-10	27-Sep-10	23-Sep-10	28-Sep-10	0%
pouring for 1st floor's slab	1	28-Sep-10	28-Sep-10	29-Sep-10	29-Sep-10	0%
columns for roof floor	4	02-Oct-10	05-Oct-10	03-Oct-10	06-Oct-10	0%
slab for roof floor	6	06-Oct-10	12-Oct-10	07-Oct-10	13-Oct-10	0%
Brick works for 1st floor	5	11-Oct-10	16-Oct-10	12-Oct-10	17-Oct-10	0%
pouring for roof floor's slab	1	13-Oct-10	13-Oct-10	14-Oct-10	14-Oct-10	0%
Brick works for roof floor	5	24-Oct-10	28-Oct-10	25-Oct-10	30-Oct-10	0%
electro mechanical	54	30-Aug-10	31-Oct-10	29-Aug-10	01-Nov-10	
plumbing connections under slab on grade	2	30-Aug-10	31-Aug-10	29-Aug-10	30-Aug-10	0%

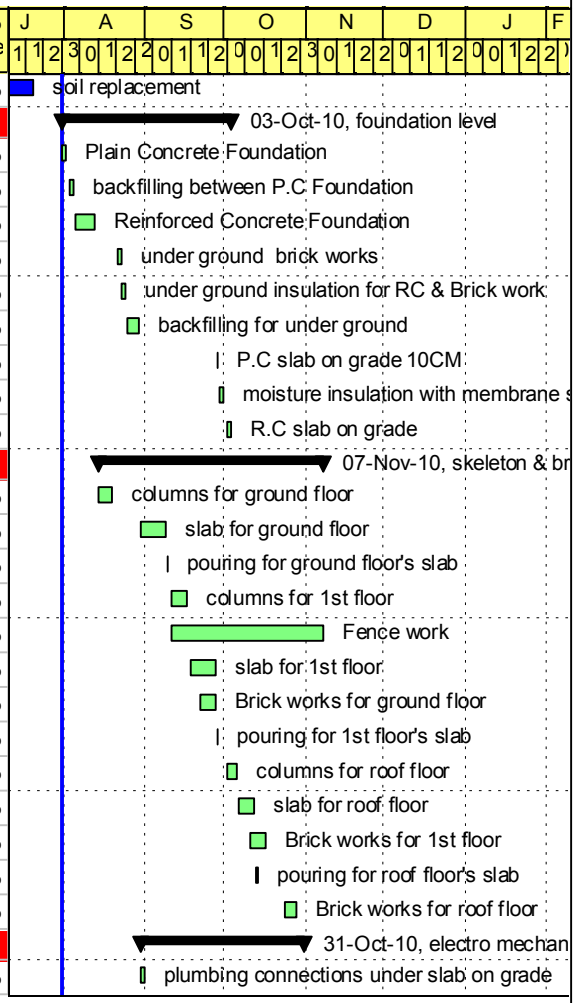

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
electrical conduits for ground floor's slab	2	04-Sep-10	05-Sep-10	02-Sep-10	04-Sep-10	0%
electrical conduits for 1st floor slab	2	22-Sep-10	23-Sep-10	23-Sep-10	25-Sep-10	0%
electrical conduits for ground floor walls	2	05-Oct-10	06-Oct-10	06-Oct-10	07-Oct-10	0%
electrical conduits for roof slab	1	10-Oct-10	10-Oct-10	11-Oct-10	11-Oct-10	0%
electrical conduits for 1st floor walls	2	17-Oct-10	18-Oct-10	18-Oct-10	19-Oct-10	0%
electrical conduits for roof floor walls	2	30-Oct-10	31-Oct-10	31-Oct-10	01-Nov-10	0%
finishing	29	07-Oct-10	09-Nov-10	09-Oct-10	10-Nov-10	
Internal plastering for ground floor	8	07-Oct-10	16-Oct-10	09-Oct-10	17-Oct-10	0%
Internal plastering for 1st floor	8	19-Oct-10	27-Oct-10	20-Oct-10	28-Oct-10	0%
External plastering	10	30-Oct-10	09-Nov-10	31-Oct-10	10-Nov-10	0%
Internal plastering for roof floor	5	01-Nov-10	06-Nov-10	02-Nov-10	07-Nov-10	0%
Villa Number A96	103	29-Jun-10 A	09-Nov-10	21-Jun-10	11-Nov-10	
general dates	97	29-Jun-10 A	09-Nov-10	21-Jun-10	11-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Nov-10		11-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	13-Jul-10	28-Jul-10	
excavation	2	30-Jun-10 A	30-Jun-10 A	13-Jul-10	14-Jul-10	100%
soil replacement	12	02-Jul-10 A	20-Jul-10 A	15-Jul-10	28-Jul-10	100%
foundation level	56	31-Jul-10	03-Oct-10	29-Jul-10	05-Oct-10	
Plain Concrete Foundation	2	31-Jul-10	01-Aug-10	29-Jul-10	31-Jul-10	0%
backfilling between P.C Foundation	2	03-Aug-10	04-Aug-10	02-Aug-10	03-Aug-10	0%
Reinforced Concrete Foundation	7	05-Aug-10	12-Aug-10	05-Aug-10	12-Aug-10	0%
under ground brick works	2	21-Aug-10	22-Aug-10	21-Aug-10	22-Aug-10	0%
under ground insulation for RC & Brick work	2	23-Aug-10	24-Aug-10	23-Aug-10	24-Aug-10	0%
backfilling for under ground	4	25-Aug-10	29-Aug-10	25-Aug-10	29-Aug-10	0%
P.C slab on grade 10CM	1	28-Sep-10	28-Sep-10	30-Sep-10	30-Sep-10	0%

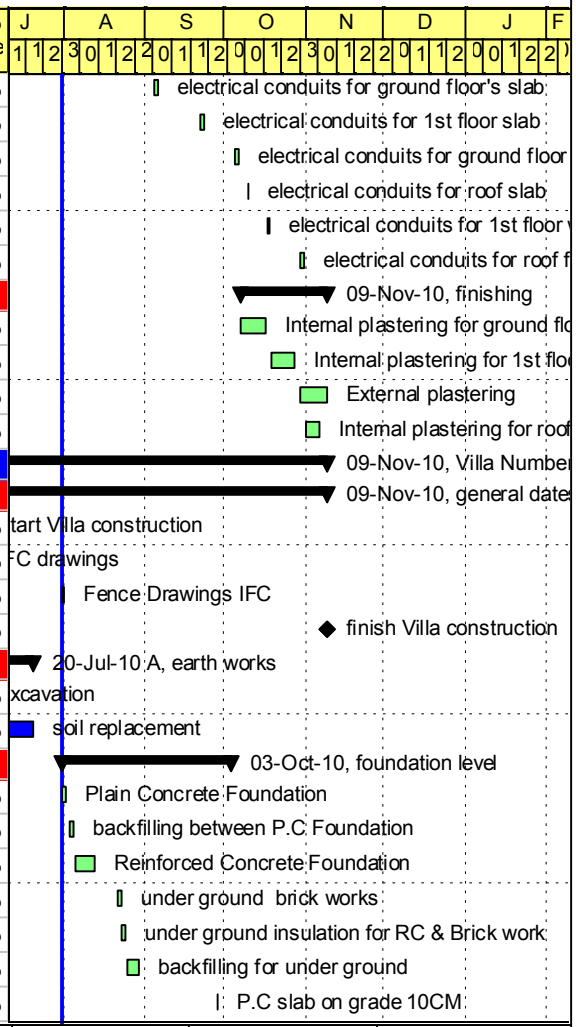

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
moisture insulation with membrane sheets	2	29-Sep-10	30-Sep-10	02-Oct-10	03-Oct-10	0%
R.C slab on grade	2	02-Oct-10	03-Oct-10	04-Oct-10	05-Oct-10	0%
skeleton & brick walls	**74**	**14-Aug-10**	**07-Nov-10**	**14-Aug-10**	**09-Nov-10**	
columns for ground floor	6	14-Aug-10	19-Aug-10	14-Aug-10	19-Aug-10	0%
slab for ground floor	9	30-Aug-10	08-Sep-10	30-Aug-10	11-Sep-10	0%
pouring for ground floor's slab	1	09-Sep-10	09-Sep-10	12-Sep-10	12-Sep-10	0%
columns for 1st floor	6	11-Sep-10	16-Sep-10	13-Sep-10	19-Sep-10	0%
Fence work	50	11-Sep-10	07-Nov-10	13-Sep-10	09-Nov-10	0%
slab for 1st floor	9	18-Sep-10	27-Sep-10	20-Sep-10	29-Sep-10	0%
Brick works for ground floor	5	22-Sep-10	27-Sep-10	25-Sep-10	29-Sep-10	0%
pouring for 1st floor's slab	1	28-Sep-10	28-Sep-10	30-Sep-10	30-Sep-10	0%
columns for roof floor	4	02-Oct-10	05-Oct-10	04-Oct-10	07-Oct-10	0%
slab for roof floor	6	06-Oct-10	12-Oct-10	09-Oct-10	14-Oct-10	0%
Brick works for 1st floor	5	11-Oct-10	16-Oct-10	13-Oct-10	18-Oct-10	0%
pouring for roof floor's slab	1	13-Oct-10	13-Oct-10	16-Oct-10	16-Oct-10	0%
Brick works for roof floor	5	24-Oct-10	28-Oct-10	26-Oct-10	31-Oct-10	0%
electro mechanical	**54**	**30-Aug-10**	**31-Oct-10**	**30-Aug-10**	**02-Nov-10**	
plumbing connections under slab on grade	2	30-Aug-10	31-Aug-10	30-Aug-10	31-Aug-10	0%
electrical conduits for ground floor's slab	2	04-Sep-10	05-Sep-10	04-Sep-10	05-Sep-10	0%
electrical conduits for 1st floor slab	2	22-Sep-10	23-Sep-10	25-Sep-10	26-Sep-10	0%
electrical conduits for ground floor walls	2	05-Oct-10	06-Oct-10	07-Oct-10	09-Oct-10	0%
electrical conduits for roof slab	1	10-Oct-10	10-Oct-10	12-Oct-10	12-Oct-10	0%
electrical conduits for 1st floor walls	2	17-Oct-10	18-Oct-10	19-Oct-10	20-Oct-10	0%
electrical conduits for roof floor walls	2	30-Oct-10	31-Oct-10	01-Nov-10	02-Nov-10	0%
finishing	**29**	**07-Oct-10**	**09-Nov-10**	**10-Oct-10**	**11-Nov-10**	
Internal plastering for ground floor	8	07-Oct-10	16-Oct-10	10-Oct-10	18-Oct-10	0%
Internal plastering for 1st floor	8	19-Oct-10	27-Oct-10	21-Oct-10	30-Oct-10	0%

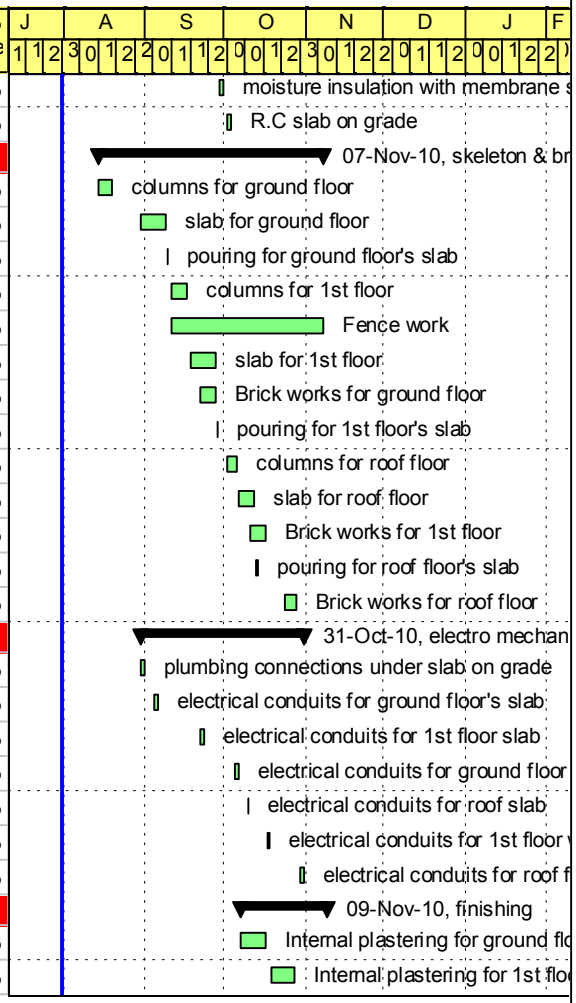

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
External plastering	10	30-Oct-10	09-Nov-10	01-Nov-10	11-Nov-10	0%
Internal plastering for roof floor	5	01-Nov-10	06-Nov-10	03-Nov-10	08-Nov-10	0%
Villa Number A97	102	29-Jun-10 A	09-Nov-10	21-Jun-10	13-Nov-10	
general dates	97	29-Jun-10 A	09-Nov-10	21-Jun-10	13-Nov-10	
Start Villa construction	0	29-Jun-10 A		21-Jun-10		100%
IFC drawings	0	29-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Nov-10		13-Nov-10	0%
earth works	14	30-Jun-10 A	20-Jul-10 A	14-Jul-10	29-Jul-10	
excavation	2	30-Jun-10 A	01-Jul-10 A	14-Jul-10	15-Jul-10	100%
soil replacement	12	02-Jul-10 A	20-Jul-10 A	17-Jul-10	29-Jul-10	100%
foundation level	56	31-Jul-10	03-Oct-10	31-Jul-10	06-Oct-10	
Plain Concrete Foundation	2	31-Jul-10	01-Aug-10	31-Jul-10	01-Aug-10	0%
backfilling between P.C Foundation	2	03-Aug-10	04-Aug-10	03-Aug-10	04-Aug-10	0%
Reinforced Concrete Foundation	7	05-Aug-10	12-Aug-10	07-Aug-10	14-Aug-10	0%
under ground brick works	2	21-Aug-10	22-Aug-10	22-Aug-10	23-Aug-10	0%
under ground insulation for RC & Brick work	2	23-Aug-10	24-Aug-10	24-Aug-10	25-Aug-10	0%
backfilling for under ground	4	25-Aug-10	29-Aug-10	26-Aug-10	30-Aug-10	0%
P.C slab on grade 10CM	1	28-Sep-10	28-Sep-10	02-Oct-10	02-Oct-10	0%
moisture insulation with membrane sheets	2	29-Sep-10	30-Sep-10	03-Oct-10	04-Oct-10	0%
R.C slab on grade	2	02-Oct-10	03-Oct-10	05-Oct-10	06-Oct-10	0%
skeleton & brick walls	74	14-Aug-10	07-Nov-10	15-Aug-10	10-Nov-10	
columns for ground floor	6	14-Aug-10	19-Aug-10	15-Aug-10	21-Aug-10	0%
slab for ground floor	9	30-Aug-10	08-Sep-10	31-Aug-10	12-Sep-10	0%
pouring for ground floor's slab	1	09-Sep-10	09-Sep-10	13-Sep-10	13-Sep-10	0%
columns for 1st floor	6	11-Sep-10	16-Sep-10	14-Sep-10	20-Sep-10	0%
Fence work	50	11-Sep-10	07-Nov-10	14-Sep-10	10-Nov-10	0%
slab for 1st floor	9	18-Sep-10	27-Sep-10	21-Sep-10	30-Sep-10	0%

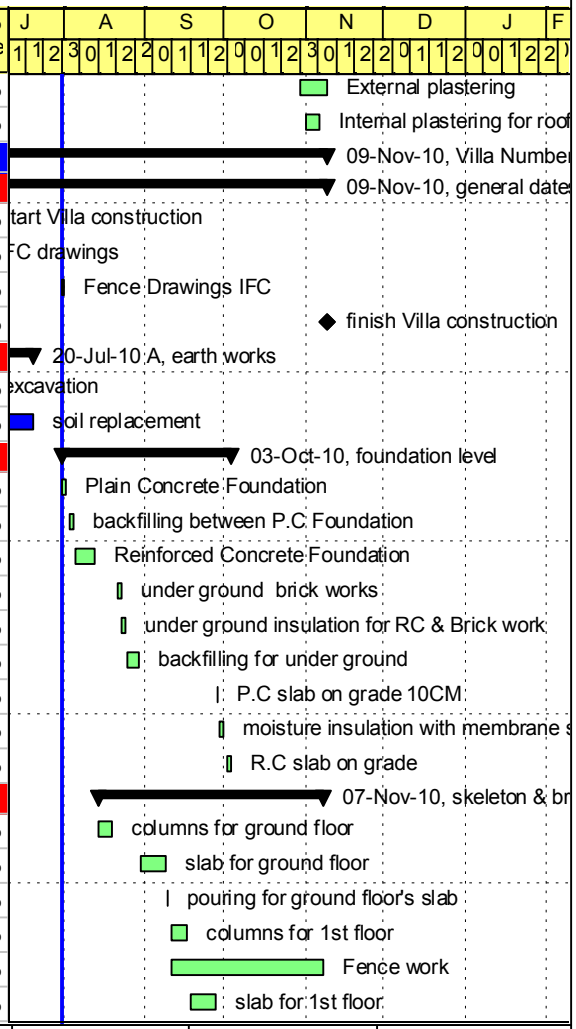

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Brick works for ground floor	5	22-Sep-10	27-Sep-10	26-Sep-10	30-Sep-10	0%
pouring for 1st floor's slab	1	28-Sep-10	28-Sep-10	02-Oct-10	02-Oct-10	0%
columns for roof floor	4	02-Oct-10	05-Oct-10	05-Oct-10	09-Oct-10	0%
slab for roof floor	6	06-Oct-10	12-Oct-10	10-Oct-10	16-Oct-10	0%
Brick works for 1st floor	5	11-Oct-10	16-Oct-10	14-Oct-10	19-Oct-10	0%
pouring for roof floor's slab	1	13-Oct-10	13-Oct-10	17-Oct-10	17-Oct-10	0%
Brick works for roof floor	5	24-Oct-10	28-Oct-10	27-Oct-10	01-Nov-10	0%
electro mechanical	54	30-Aug-10	31-Oct-10	31-Aug-10	03-Nov-10	
plumbing connections under slab on grade	2	30-Aug-10	31-Aug-10	31-Aug-10	01-Sep-10	0%
electrical conduits for ground floor's slab	2	04-Sep-10	05-Sep-10	05-Sep-10	06-Sep-10	0%
electrical conduits for 1st floor slab	2	22-Sep-10	23-Sep-10	26-Sep-10	27-Sep-10	0%
electrical conduits for ground floor walls	2	05-Oct-10	06-Oct-10	09-Oct-10	10-Oct-10	0%
electrical conduits for roof slab	1	10-Oct-10	10-Oct-10	13-Oct-10	13-Oct-10	0%
electrical conduits for 1st floor walls	2	17-Oct-10	18-Oct-10	20-Oct-10	21-Oct-10	0%
electrical conduits for roof floor walls	2	30-Oct-10	31-Oct-10	02-Nov-10	03-Nov-10	0%
finishing	29	07-Oct-10	09-Nov-10	11-Oct-10	13-Nov-10	
Internal plastering for ground floor	8	07-Oct-10	16-Oct-10	11-Oct-10	19-Oct-10	0%
Internal plastering for 1st floor	8	19-Oct-10	27-Oct-10	23-Oct-10	31-Oct-10	0%
External plastering	10	30-Oct-10	09-Nov-10	02-Nov-10	13-Nov-10	0%
Internal plastering for roof floor	5	01-Nov-10	06-Nov-10	04-Nov-10	09-Nov-10	0%
Zone.No 3	144	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
Villa Number E08	111	21-Jun-10 A	30-Nov-10	21-Jun-10	22-Nov-10	
general dates	111	21-Jun-10 A	30-Nov-10	21-Jun-10	22-Nov-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Nov-10		22-Nov-10	0%
earth works	14	31-Jul-10	15-Aug-10	19-Jul-10	03-Aug-10	

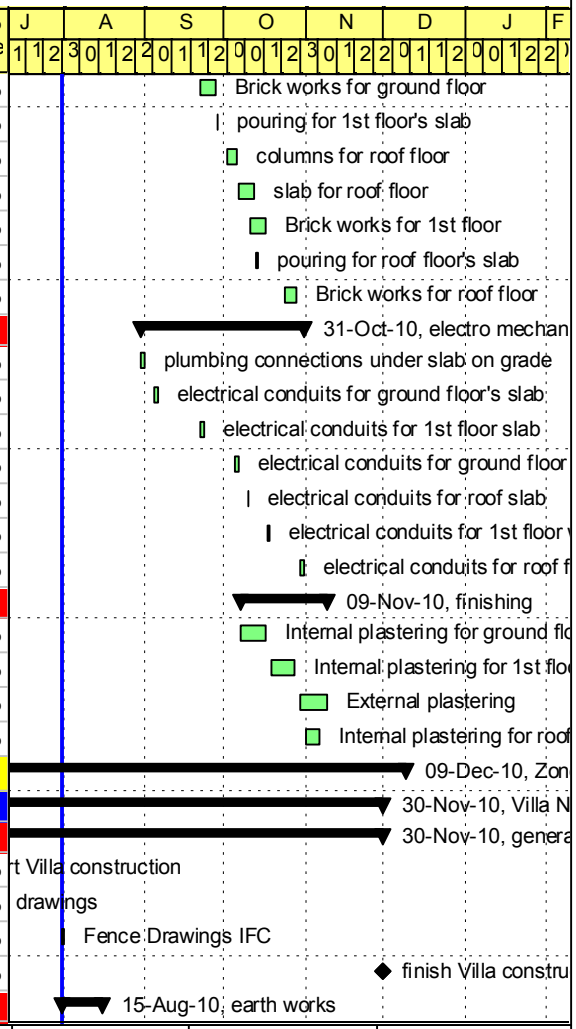

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
excavation	2	31-Jul-10	01-Aug-10	19-Jul-10	20-Jul-10	0%
soil replacement	12	02-Aug-10	15-Aug-10	21-Jul-10	03-Aug-10	0%
foundation level	56	16-Aug-10	19-Oct-10	04-Aug-10	11-Oct-10	
Plain Concrete Foundation	2	16-Aug-10	17-Aug-10	04-Aug-10	05-Aug-10	0%
backfilling between P.C Foundation	2	19-Aug-10	21-Aug-10	08-Aug-10	09-Aug-10	0%
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	11-Aug-10	18-Aug-10	0%
under ground brick works	2	06-Sep-10	07-Sep-10	26-Aug-10	28-Aug-10	0%
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	29-Aug-10	30-Aug-10	0%
backfilling for under ground	4	11-Sep-10	14-Sep-10	31-Aug-10	04-Sep-10	0%
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	06-Oct-10	06-Oct-10	0%
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	07-Oct-10	09-Oct-10	0%
R.C slab on grade	2	18-Oct-10	19-Oct-10	10-Oct-10	11-Oct-10	0%
skeleton & brick walls	74	30-Aug-10	28-Nov-10	19-Aug-10	20-Nov-10	
columns for ground floor	6	30-Aug-10	05-Sep-10	19-Aug-10	25-Aug-10	0%
slab for ground floor	9	15-Sep-10	25-Sep-10	05-Sep-10	16-Sep-10	0%
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	18-Sep-10	18-Sep-10	0%
columns for 1st floor	6	27-Sep-10	03-Oct-10	19-Sep-10	25-Sep-10	0%
Fence work	50	27-Sep-10	28-Nov-10	19-Sep-10	20-Nov-10	0%
slab for 1st floor	9	04-Oct-10	13-Oct-10	26-Sep-10	05-Oct-10	0%
Brick works for ground floor	5	09-Oct-10	13-Oct-10	30-Sep-10	05-Oct-10	0%
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	06-Oct-10	06-Oct-10	0%
columns for roof floor	4	18-Oct-10	21-Oct-10	10-Oct-10	13-Oct-10	0%
slab for roof floor	6	23-Oct-10	28-Oct-10	14-Oct-10	20-Oct-10	0%
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	19-Oct-10	24-Oct-10	0%
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	21-Oct-10	21-Oct-10	0%
Brick works for roof floor	5	09-Nov-10	14-Nov-10	01-Nov-10	06-Nov-10	0%
electro mechanical	52	15-Sep-10	16-Nov-10	05-Sep-10	08-Nov-10	

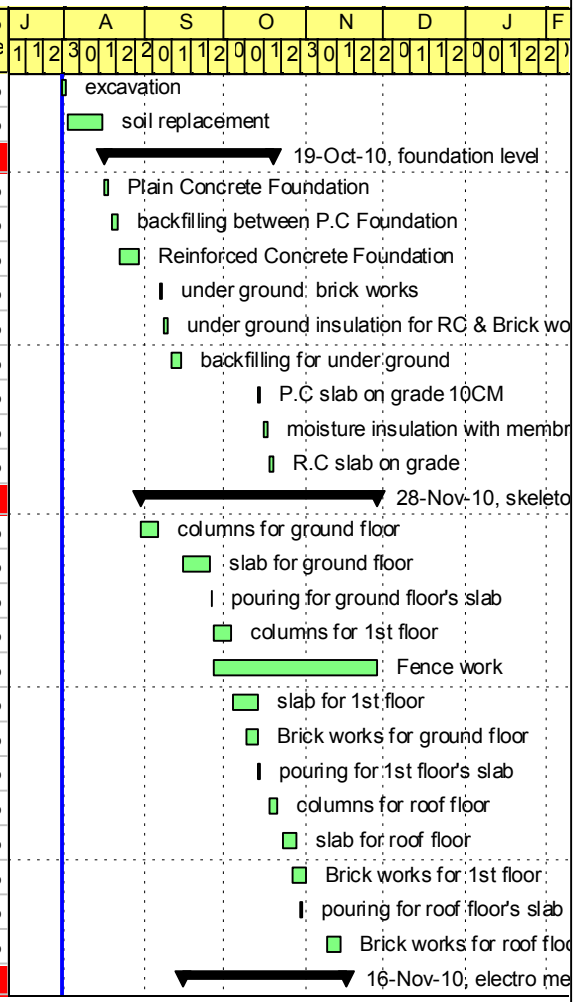

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	05-Sep-10	06-Sep-10	0%
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	12-Sep-10	13-Sep-10	0%
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	30-Sep-10	02-Oct-10	0%
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	13-Oct-10	14-Oct-10	0%
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	18-Oct-10	18-Oct-10	0%
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	25-Oct-10	26-Oct-10	0%
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	07-Nov-10	08-Nov-10	0%
finishing	29	24-Oct-10	30-Nov-10	16-Oct-10	22-Nov-10	
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	16-Oct-10	24-Oct-10	0%
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	27-Oct-10	04-Nov-10	0%
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	09-Nov-10	14-Nov-10	0%
External plastering	10	20-Nov-10	30-Nov-10	07-Nov-10	22-Nov-10	0%
Villa Number A55	119	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
general dates	119	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Dec-10		30-Nov-10	0%
earth works	22	31-Jul-10	24-Aug-10	20-Jul-10	14-Aug-10	
excavation	10	31-Jul-10	10-Aug-10	20-Jul-10	31-Jul-10	0%
soil replacement	12	11-Aug-10	24-Aug-10	01-Aug-10	14-Aug-10	0%
foundation level	56	25-Aug-10	28-Oct-10	15-Aug-10	21-Oct-10	
Plain Concrete Foundation	2	25-Aug-10	26-Aug-10	15-Aug-10	16-Aug-10	0%
backfilling between P.C Foundation	2	29-Aug-10	30-Aug-10	18-Aug-10	19-Aug-10	0%
Reinforced Concrete Foundation	7	31-Aug-10	07-Sep-10	22-Aug-10	29-Aug-10	0%
under ground brick works	2	15-Sep-10	16-Sep-10	06-Sep-10	07-Sep-10	0%
under ground insulation for RC & Brick work	2	18-Sep-10	19-Sep-10	11-Sep-10	12-Sep-10	0%
backfilling for under ground	4	20-Sep-10	23-Sep-10	13-Sep-10	16-Sep-10	0%

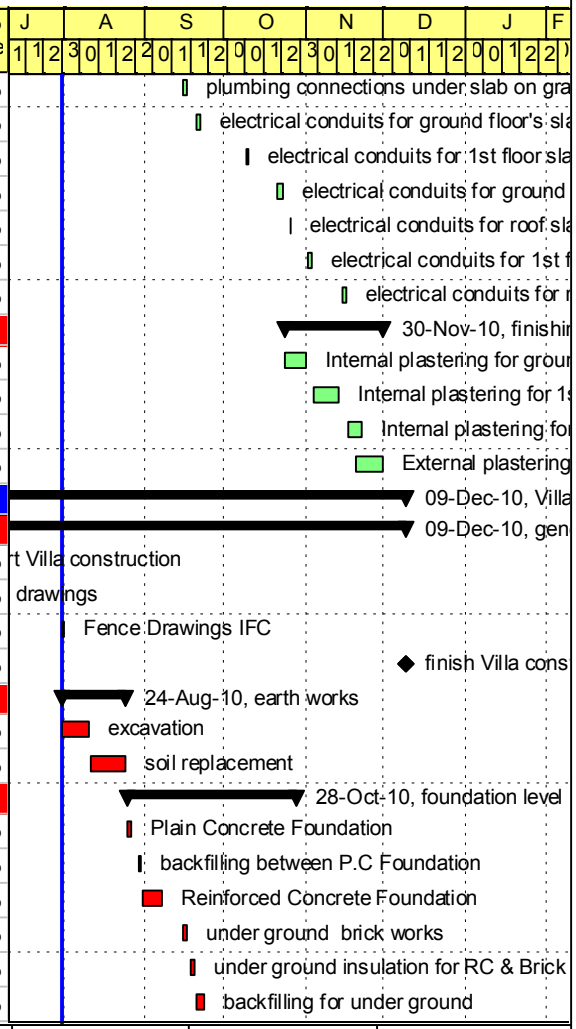

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
P.C slab on grade 10CM	1	24-Oct-10	24-Oct-10	17-Oct-10	17-Oct-10	0%
moisture insulation with membrane sheets	2	25-Oct-10	26-Oct-10	18-Oct-10	19-Oct-10	0%
R.C slab on grade	2	27-Oct-10	28-Oct-10	20-Oct-10	21-Oct-10	0%
skeleton & brick walls	74	08-Sep-10	07-Dec-10	30-Aug-10	30-Nov-10	
columns for ground floor	6	08-Sep-10	14-Sep-10	30-Aug-10	05-Sep-10	0%
slab for ground floor	9	25-Sep-10	04-Oct-10	18-Sep-10	27-Sep-10	0%
pouring for ground floor's slab	1	05-Oct-10	05-Oct-10	28-Sep-10	28-Sep-10	0%
columns for 1st floor	6	06-Oct-10	12-Oct-10	29-Sep-10	05-Oct-10	0%
Fence work	50	06-Oct-10	07-Dec-10	29-Sep-10	30-Nov-10	0%
slab for 1st floor	9	13-Oct-10	23-Oct-10	06-Oct-10	16-Oct-10	0%
Brick works for ground floor	5	18-Oct-10	23-Oct-10	11-Oct-10	16-Oct-10	0%
pouring for 1st floor's slab	1	24-Oct-10	24-Oct-10	17-Oct-10	17-Oct-10	0%
columns for roof floor	4	27-Oct-10	31-Oct-10	20-Oct-10	24-Oct-10	0%
slab for roof floor	6	01-Nov-10	07-Nov-10	25-Oct-10	31-Oct-10	0%
Brick works for 1st floor	5	06-Nov-10	10-Nov-10	30-Oct-10	03-Nov-10	0%
pouring for roof floor's slab	1	08-Nov-10	08-Nov-10	01-Nov-10	01-Nov-10	0%
Brick works for roof floor	5	23-Nov-10	28-Nov-10	11-Nov-10	16-Nov-10	0%
electro mechanical	54	25-Sep-10	30-Nov-10	18-Sep-10	18-Nov-10	
plumbing connections under slab on grade	2	25-Sep-10	26-Sep-10	18-Sep-10	19-Sep-10	0%
electrical conduits for ground floor's slab	2	29-Sep-10	30-Sep-10	22-Sep-10	23-Sep-10	0%
electrical conduits for 1st floor slab	2	18-Oct-10	19-Oct-10	11-Oct-10	12-Oct-10	0%
electrical conduits for ground floor walls	2	31-Oct-10	01-Nov-10	24-Oct-10	25-Oct-10	0%
electrical conduits for roof slab	1	04-Nov-10	04-Nov-10	28-Oct-10	28-Oct-10	0%
electrical conduits for 1st floor walls	2	11-Nov-10	13-Nov-10	04-Nov-10	06-Nov-10	0%
electrical conduits for roof floor walls	2	29-Nov-10	30-Nov-10	17-Nov-10	18-Nov-10	0%
finishing	29	02-Nov-10	09-Dec-10	26-Oct-10	30-Nov-10	
Internal plastering for ground floor	8	02-Nov-10	10-Nov-10	26-Oct-10	03-Nov-10	0%

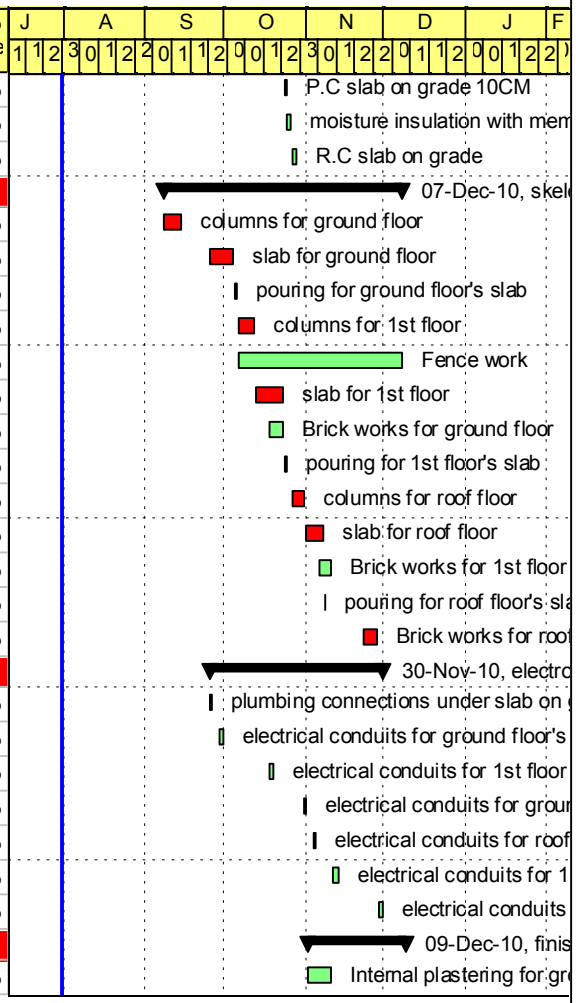

Remaining Level of Effort ◆ Milestone
Actual Work Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Internal plastering for 1st floor	8	14-Nov-10	22-Nov-10	07-Nov-10	15-Nov-10	0%
External plastering	10	29-Nov-10	09-Dec-10	20-Nov-10	30-Nov-10	0%
Internal plastering for roof floor	5	01-Dec-10	06-Dec-10	20-Nov-10	24-Nov-10	0%
Villa Number A86	119	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
general dates	119	21-Jun-10 A	09-Dec-10	21-Jun-10	30-Nov-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Dec-10		30-Nov-10	0%
earth works	22	31-Jul-10	24-Aug-10	18-Jul-10	11-Aug-10	
excavation	10	31-Jul-10	10-Aug-10	18-Jul-10	28-Jul-10	0%
soil replacement	12	11-Aug-10	24-Aug-10	29-Jul-10	11-Aug-10	0%
foundation level	56	25-Aug-10	28-Oct-10	12-Aug-10	19-Oct-10	
Plain Concrete Foundation	2	25-Aug-10	26-Aug-10	12-Aug-10	14-Aug-10	0%
backfilling between P.C Foundation	2	29-Aug-10	30-Aug-10	16-Aug-10	17-Aug-10	0%
Reinforced Concrete Foundation	7	31-Aug-10	07-Sep-10	19-Aug-10	26-Aug-10	0%
under ground brick works	2	15-Sep-10	16-Sep-10	04-Sep-10	05-Sep-10	0%
under ground insulation for RC & Brick work	2	18-Sep-10	19-Sep-10	06-Sep-10	07-Sep-10	0%
backfilling for under ground	4	20-Sep-10	23-Sep-10	11-Sep-10	14-Sep-10	0%
P.C slab on grade 10CM	1	24-Oct-10	24-Oct-10	14-Oct-10	14-Oct-10	0%
moisture insulation with membrane sheets	2	25-Oct-10	26-Oct-10	16-Oct-10	17-Oct-10	0%
R.C slab on grade	2	27-Oct-10	28-Oct-10	18-Oct-10	19-Oct-10	0%
skeleton & brick walls	74	08-Sep-10	07-Dec-10	28-Aug-10	28-Nov-10	
columns for ground floor	6	08-Sep-10	14-Sep-10	28-Aug-10	02-Sep-10	0%
slab for ground floor	9	25-Sep-10	04-Oct-10	15-Sep-10	25-Sep-10	0%
pouring for ground floor's slab	1	05-Oct-10	05-Oct-10	26-Sep-10	26-Sep-10	0%
columns for 1st floor	6	06-Oct-10	12-Oct-10	27-Sep-10	03-Oct-10	0%
Fence work	50	06-Oct-10	07-Dec-10	27-Sep-10	28-Nov-10	0%

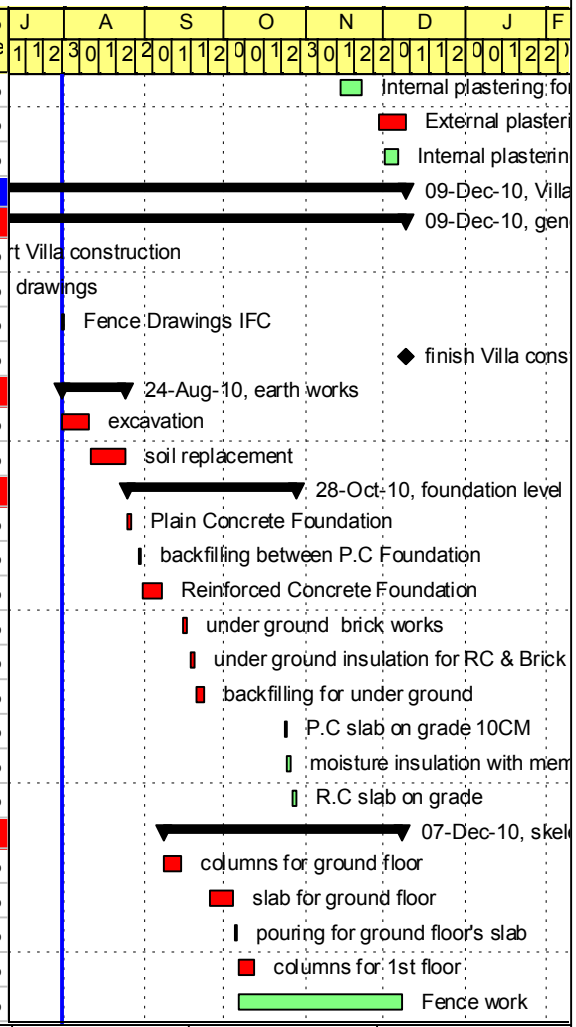

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
slab for 1st floor	9	13-Oct-10	23-Oct-10	04-Oct-10	13-Oct-10	0%
Brick works for ground floor	5	18-Oct-10	23-Oct-10	09-Oct-10	13-Oct-10	0%
pouring for 1st floor's slab	1	24-Oct-10	24-Oct-10	14-Oct-10	14-Oct-10	0%
columns for roof floor	4	27-Oct-10	31-Oct-10	18-Oct-10	21-Oct-10	0%
slab for roof floor	6	01-Nov-10	07-Nov-10	23-Oct-10	28-Oct-10	0%
Brick works for 1st floor	5	06-Nov-10	10-Nov-10	27-Oct-10	01-Nov-10	0%
pouring for roof floor's slab	1	08-Nov-10	08-Nov-10	30-Oct-10	30-Oct-10	0%
Brick works for roof floor	5	23-Nov-10	28-Nov-10	09-Nov-10	14-Nov-10	0%
electro mechanical	54	25-Sep-10	30-Nov-10	15-Sep-10	16-Nov-10	
plumbing connections under slab on grade	2	25-Sep-10	26-Sep-10	15-Sep-10	16-Sep-10	0%
electrical conduits for ground floor's slab	2	29-Sep-10	30-Sep-10	20-Sep-10	21-Sep-10	0%
electrical conduits for 1st floor slab	2	18-Oct-10	19-Oct-10	09-Oct-10	10-Oct-10	0%
electrical conduits for ground floor walls	2	31-Oct-10	01-Nov-10	21-Oct-10	23-Oct-10	0%
electrical conduits for roof slab	1	04-Nov-10	04-Nov-10	26-Oct-10	26-Oct-10	0%
electrical conduits for 1st floor walls	2	11-Nov-10	13-Nov-10	02-Nov-10	03-Nov-10	0%
electrical conduits for roof floor walls	2	29-Nov-10	30-Nov-10	15-Nov-10	16-Nov-10	0%
finishing	29	02-Nov-10	09-Dec-10	24-Oct-10	30-Nov-10	
Internal plastering for ground floor	8	02-Nov-10	10-Nov-10	24-Oct-10	01-Nov-10	0%
Internal plastering for 1st floor	8	14-Nov-10	22-Nov-10	04-Nov-10	13-Nov-10	0%
External plastering	10	29-Nov-10	09-Dec-10	20-Nov-10	30-Nov-10	0%
Internal plastering for roof floor	5	01-Dec-10	06-Dec-10	17-Nov-10	22-Nov-10	0%
Villa Number A87	119	21-Jun-10 A	09-Dec-10	21-Jun-10	27-Nov-10	
general dates	119	21-Jun-10 A	09-Dec-10	21-Jun-10	27-Nov-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		09-Dec-10		27-Nov-10	0%
earth works	22	31-Jul-10	24-Aug-10	14-Jul-10	08-Aug-10	

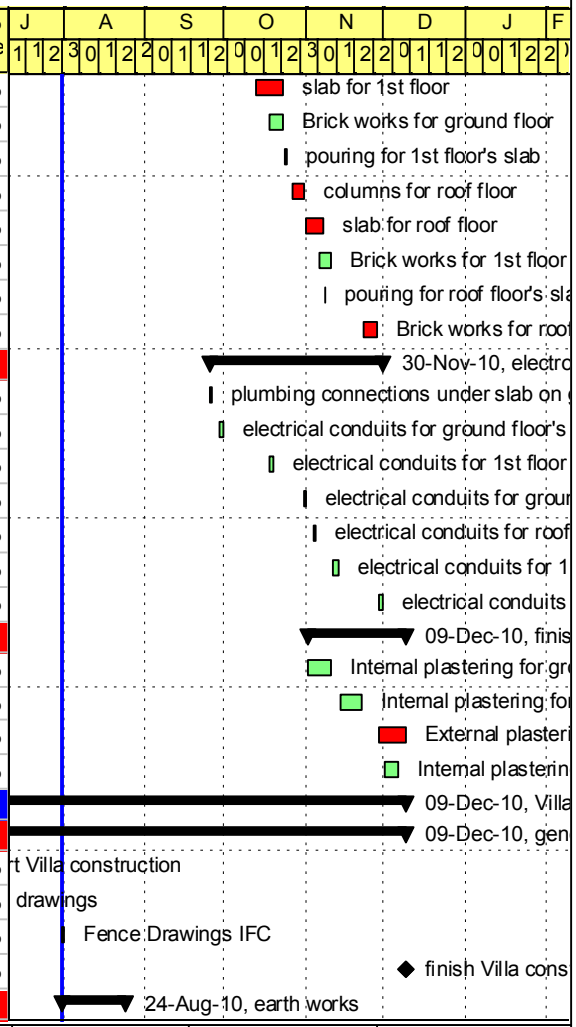

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
excavation	10	31-Jul-10	10-Aug-10	14-Jul-10	25-Jul-10	0%
soil replacement	12	11-Aug-10	24-Aug-10	26-Jul-10	08-Aug-10	0%
foundation level	56	25-Aug-10	28-Oct-10	09-Aug-10	16-Oct-10	
Plain Concrete Foundation	2	25-Aug-10	26-Aug-10	09-Aug-10	10-Aug-10	0%
backfilling between P.C Foundation	2	29-Aug-10	30-Aug-10	12-Aug-10	14-Aug-10	0%
Reinforced Concrete Foundation	7	31-Aug-10	07-Sep-10	16-Aug-10	23-Aug-10	0%
under ground brick works	2	15-Sep-10	16-Sep-10	31-Aug-10	01-Sep-10	0%
under ground insulation for RC & Brick work	2	18-Sep-10	19-Sep-10	02-Sep-10	04-Sep-10	0%
backfilling for under ground	4	20-Sep-10	23-Sep-10	05-Sep-10	11-Sep-10	0%
P.C slab on grade 10CM	1	24-Oct-10	24-Oct-10	11-Oct-10	11-Oct-10	0%
moisture insulation with membrane sheets	2	25-Oct-10	26-Oct-10	12-Oct-10	13-Oct-10	0%
R.C slab on grade	2	27-Oct-10	28-Oct-10	14-Oct-10	16-Oct-10	0%
skeleton & brick walls	74	08-Sep-10	07-Dec-10	24-Aug-10	24-Nov-10	
columns for ground floor	6	08-Sep-10	14-Sep-10	24-Aug-10	30-Aug-10	0%
slab for ground floor	9	25-Sep-10	04-Oct-10	12-Sep-10	21-Sep-10	0%
pouring for ground floor's slab	1	05-Oct-10	05-Oct-10	22-Sep-10	22-Sep-10	0%
columns for 1st floor	6	06-Oct-10	12-Oct-10	23-Sep-10	29-Sep-10	0%
Fence work	50	06-Oct-10	07-Dec-10	23-Sep-10	24-Nov-10	0%
slab for 1st floor	9	13-Oct-10	23-Oct-10	30-Sep-10	10-Oct-10	0%
Brick works for ground floor	5	18-Oct-10	23-Oct-10	05-Oct-10	10-Oct-10	0%
pouring for 1st floor's slab	1	24-Oct-10	24-Oct-10	11-Oct-10	11-Oct-10	0%
columns for roof floor	4	27-Oct-10	31-Oct-10	14-Oct-10	18-Oct-10	0%
slab for roof floor	6	01-Nov-10	07-Nov-10	19-Oct-10	25-Oct-10	0%
Brick works for 1st floor	5	06-Nov-10	10-Nov-10	24-Oct-10	28-Oct-10	0%
pouring for roof floor's slab	1	08-Nov-10	08-Nov-10	26-Oct-10	26-Oct-10	0%
Brick works for roof floor	5	23-Nov-10	28-Nov-10	06-Nov-10	10-Nov-10	0%
electro mechanical	54	25-Sep-10	30-Nov-10	12-Sep-10	13-Nov-10	

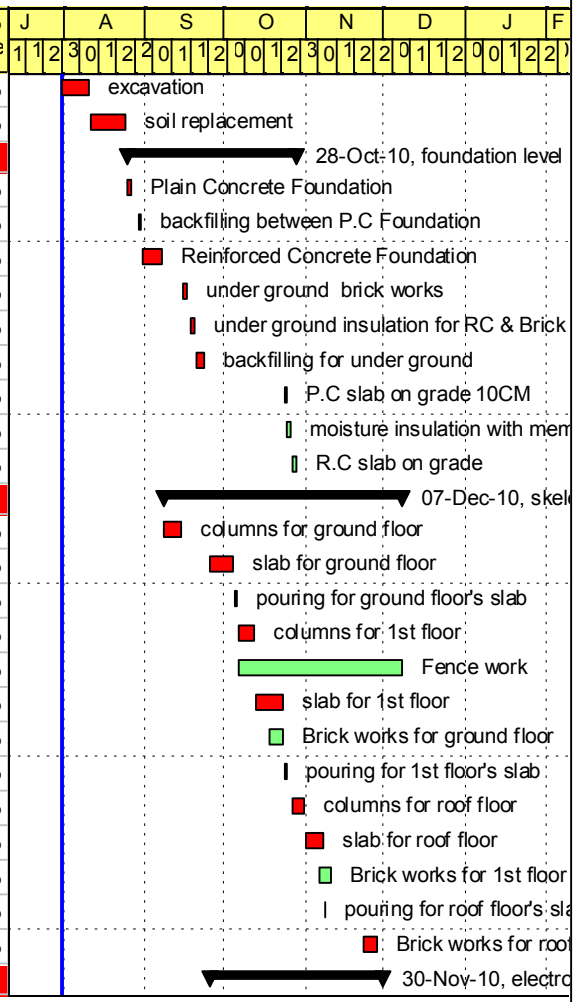

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
plumbing connections under slab on grade	2	25-Sep-10	26-Sep-10	12-Sep-10	13-Sep-10	0%
electrical conduits for ground floor's slab	2	29-Sep-10	30-Sep-10	16-Sep-10	18-Sep-10	0%
electrical conduits for 1st floor slab	2	18-Oct-10	19-Oct-10	05-Oct-10	06-Oct-10	0%
electrical conduits for ground floor walls	2	31-Oct-10	01-Nov-10	18-Oct-10	19-Oct-10	0%
electrical conduits for roof slab	1	04-Nov-10	04-Nov-10	23-Oct-10	23-Oct-10	0%
electrical conduits for 1st floor walls	2	11-Nov-10	13-Nov-10	30-Oct-10	31-Oct-10	0%
electrical conduits for roof floor walls	2	29-Nov-10	30-Nov-10	11-Nov-10	13-Nov-10	0%
finishing	29	02-Nov-10	09-Dec-10	20-Oct-10	27-Nov-10	
Internal plastering for ground floor	8	02-Nov-10	10-Nov-10	20-Oct-10	28-Oct-10	0%
Internal plastering for 1st floor	8	14-Nov-10	22-Nov-10	01-Nov-10	09-Nov-10	0%
External plastering	10	29-Nov-10	09-Dec-10	11-Nov-10	27-Nov-10	0%
Internal plastering for roof floor	5	01-Dec-10	06-Dec-10	14-Nov-10	18-Nov-10	0%
Villa Number B106	111	21-Jun-10 A	30-Nov-10	21-Jun-10	23-Nov-10	
general dates	111	21-Jun-10 A	30-Nov-10	21-Jun-10	23-Nov-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Nov-10		23-Nov-10	0%
earth works	14	31-Jul-10	15-Aug-10	20-Jul-10	04-Aug-10	
excavation	2	31-Jul-10	01-Aug-10	20-Jul-10	21-Jul-10	0%
soil replacement	12	02-Aug-10	15-Aug-10	22-Jul-10	04-Aug-10	0%
foundation level	56	16-Aug-10	19-Oct-10	05-Aug-10	12-Oct-10	
Plain Concrete Foundation	2	16-Aug-10	17-Aug-10	05-Aug-10	07-Aug-10	0%
backfilling between P.C Foundation	2	19-Aug-10	21-Aug-10	09-Aug-10	10-Aug-10	0%
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	12-Aug-10	19-Aug-10	0%
under ground brick works	2	06-Sep-10	07-Sep-10	28-Aug-10	29-Aug-10	0%
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	30-Aug-10	31-Aug-10	0%
backfilling for under ground	4	11-Sep-10	14-Sep-10	01-Sep-10	05-Sep-10	0%

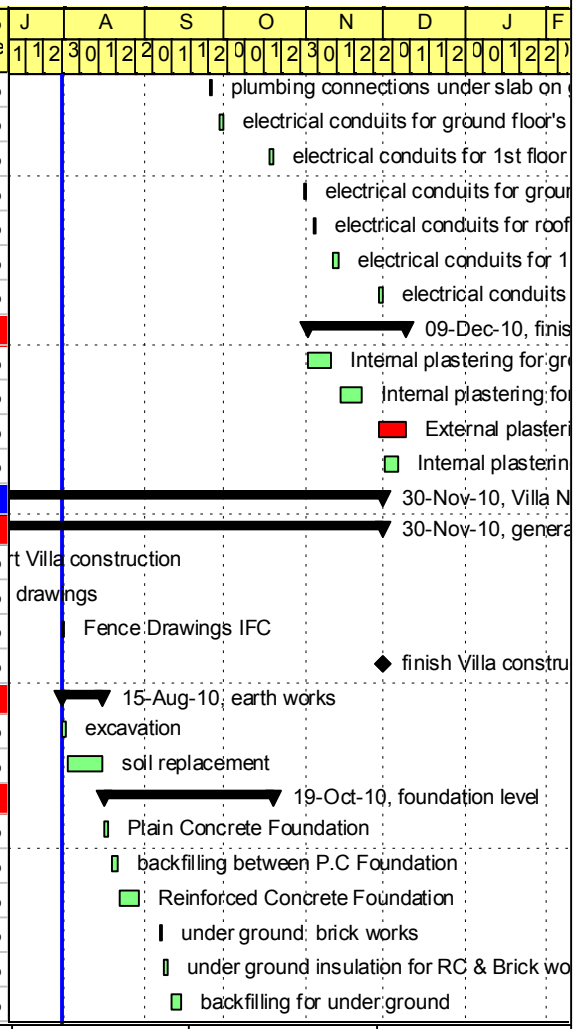

Remaining Level of Effort ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	07-Oct-10	07-Oct-10	0%
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	09-Oct-10	10-Oct-10	0%
R.C slab on grade	2	18-Oct-10	19-Oct-10	11-Oct-10	12-Oct-10	0%
skeleton & brick walls	74	30-Aug-10	28-Nov-10	21-Aug-10	21-Nov-10	
columns for ground floor	6	30-Aug-10	05-Sep-10	21-Aug-10	26-Aug-10	0%
slab for ground floor	9	15-Sep-10	25-Sep-10	06-Sep-10	18-Sep-10	0%
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	19-Sep-10	19-Sep-10	0%
columns for 1st floor	6	27-Sep-10	03-Oct-10	20-Sep-10	26-Sep-10	0%
Fence work	50	27-Sep-10	28-Nov-10	20-Sep-10	21-Nov-10	0%
slab for 1st floor	9	04-Oct-10	13-Oct-10	27-Sep-10	06-Oct-10	0%
Brick works for ground floor	5	09-Oct-10	13-Oct-10	02-Oct-10	06-Oct-10	0%
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	07-Oct-10	07-Oct-10	0%
columns for roof floor	4	18-Oct-10	21-Oct-10	11-Oct-10	14-Oct-10	0%
slab for roof floor	6	23-Oct-10	28-Oct-10	16-Oct-10	21-Oct-10	0%
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	20-Oct-10	25-Oct-10	0%
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	23-Oct-10	23-Oct-10	0%
Brick works for roof floor	5	09-Nov-10	14-Nov-10	02-Nov-10	07-Nov-10	0%
electro mechanical	52	15-Sep-10	16-Nov-10	06-Sep-10	09-Nov-10	
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	06-Sep-10	07-Sep-10	0%
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	13-Sep-10	14-Sep-10	0%
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	02-Oct-10	03-Oct-10	0%
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	14-Oct-10	16-Oct-10	0%
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	19-Oct-10	19-Oct-10	0%
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	26-Oct-10	27-Oct-10	0%
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	08-Nov-10	09-Nov-10	0%
finishing	29	24-Oct-10	30-Nov-10	17-Oct-10	23-Nov-10	
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	17-Oct-10	25-Oct-10	0%

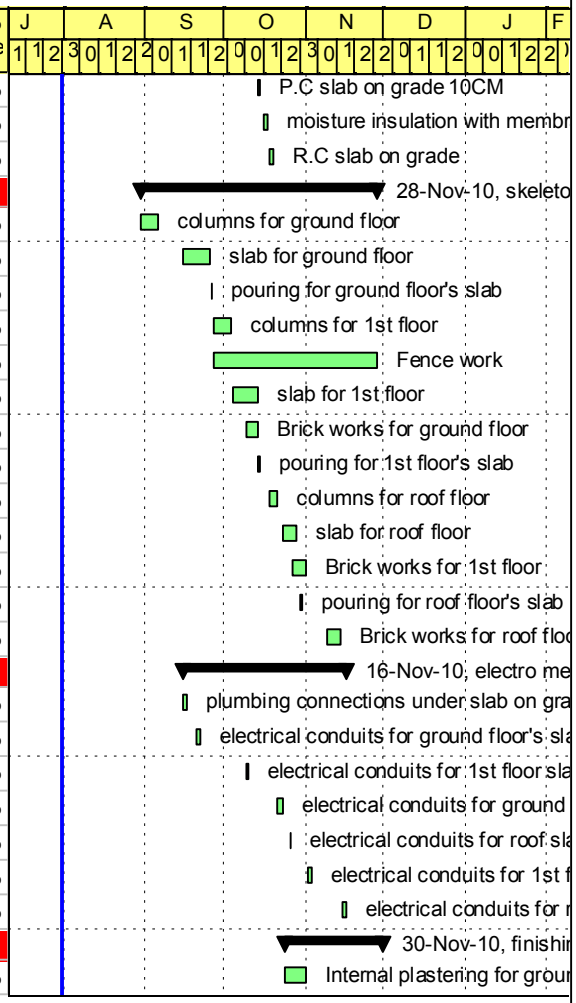

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	28-Oct-10	06-Nov-10	0%
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	10-Nov-10	15-Nov-10	0%
External plastering	10	20-Nov-10	30-Nov-10	08-Nov-10	23-Nov-10	0%
Villa Number B105	136	21-Jun-10 A	30-Nov-10	21-Jun-10	23-Nov-10	
general dates	136	21-Jun-10 A	30-Nov-10	21-Jun-10	23-Nov-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10		100%
Start Villa construction	0	21-Jun-10 A		21-Jun-10		100%
Fence Drawings IFC	1	31-Jul-10	31-Jul-10	21-Jun-10	21-Jun-10	0%
finish Villa construction	0		30-Nov-10		23-Nov-10	0%
earth works	14	31-Jul-10	15-Aug-10	20-Jul-10	04-Aug-10	
excavation	2	31-Jul-10	01-Aug-10	20-Jul-10	21-Jul-10	0%
soil replacement	12	02-Aug-10	15-Aug-10	22-Jul-10	04-Aug-10	0%
foundation level	56	16-Aug-10	19-Oct-10	05-Aug-10	12-Oct-10	
Plain Concrete Foundation	2	16-Aug-10	17-Aug-10	05-Aug-10	07-Aug-10	0%
backfilling between P.C Foundation	2	19-Aug-10	21-Aug-10	09-Aug-10	10-Aug-10	0%
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	12-Aug-10	19-Aug-10	0%
under ground brick works	2	06-Sep-10	07-Sep-10	28-Aug-10	29-Aug-10	0%
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	30-Aug-10	31-Aug-10	0%
backfilling for under ground	4	11-Sep-10	14-Sep-10	01-Sep-10	05-Sep-10	0%
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	07-Oct-10	07-Oct-10	0%
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	09-Oct-10	10-Oct-10	0%
R.C slab on grade	2	18-Oct-10	19-Oct-10	11-Oct-10	12-Oct-10	0%
skeleton & brick walls	74	30-Aug-10	28-Nov-10	21-Aug-10	21-Nov-10	
columns for ground floor	6	30-Aug-10	05-Sep-10	21-Aug-10	26-Aug-10	0%
slab for ground floor	9	15-Sep-10	25-Sep-10	06-Sep-10	18-Sep-10	0%
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	19-Sep-10	19-Sep-10	0%
columns for 1st floor	6	27-Sep-10	03-Oct-10	20-Sep-10	26-Sep-10	0%
Fence work	50	27-Sep-10	28-Nov-10	20-Sep-10	21-Nov-10	0%

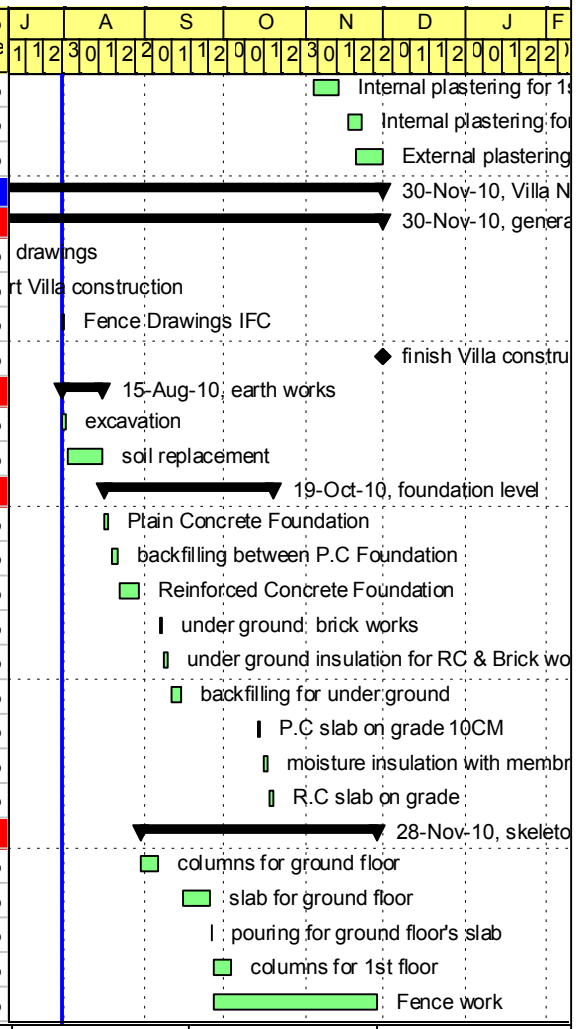

Remaining Level of Effort ◆ ◆ Milestone
Actual Work ▼ Summary
Remaining Work
Critical Remaining Work

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish	Activity % Complete
slab for 1st floor	9	04-Oct-10	13-Oct-10	27-Sep-10	06-Oct-10	0%
Brick works for ground floor	5	09-Oct-10	13-Oct-10	02-Oct-10	06-Oct-10	0%
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	07-Oct-10	07-Oct-10	0%
columns for roof floor	4	18-Oct-10	21-Oct-10	11-Oct-10	14-Oct-10	0%
slab for roof floor	6	23-Oct-10	28-Oct-10	16-Oct-10	21-Oct-10	0%
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	20-Oct-10	25-Oct-10	0%
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	23-Oct-10	23-Oct-10	0%
Brick works for roof floor	5	09-Nov-10	14-Nov-10	02-Nov-10	07-Nov-10	0%
electro mechanical	52	15-Sep-10	16-Nov-10	06-Sep-10	09-Nov-10	
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	06-Sep-10	07-Sep-10	0%
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	13-Sep-10	14-Sep-10	0%
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	02-Oct-10	03-Oct-10	0%
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	14-Oct-10	16-Oct-10	0%
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	19-Oct-10	19-Oct-10	0%
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	26-Oct-10	27-Oct-10	0%
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	08-Nov-10	09-Nov-10	0%
finishing	29	24-Oct-10	30-Nov-10	17-Oct-10	23-Nov-10	
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	17-Oct-10	25-Oct-10	0%
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	28-Oct-10	06-Nov-10	0%
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	10-Nov-10	15-Nov-10	0%
External plastering	10	20-Nov-10	30-Nov-10	08-Nov-10	23-Nov-10	0%
Closing phase	0	09-Dec-10	09-Dec-10	30-Nov-10	30-Nov-10	
end project	0		09-Dec-10		30-Nov-10	0%

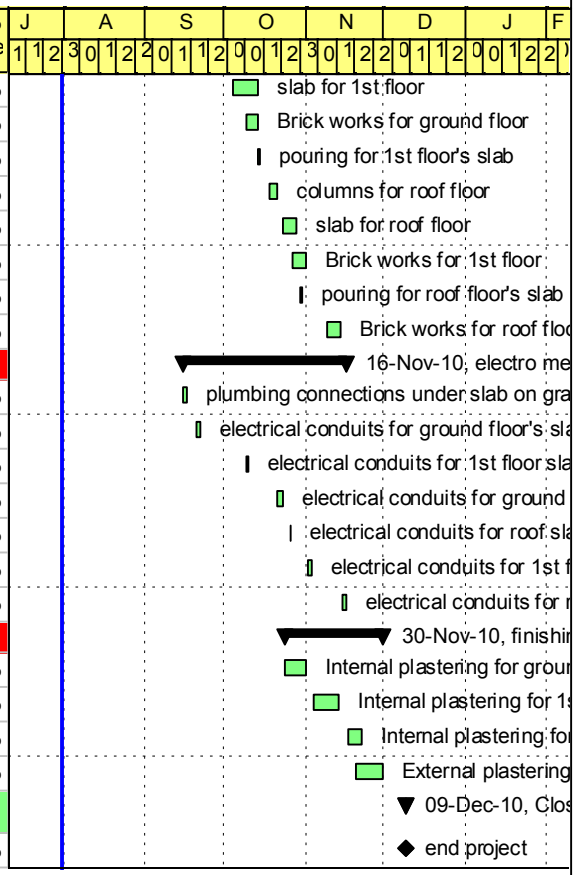

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

update 31-07-2010

Date	Revision	Checked	Approved
