Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Cleopatra Jungle	136	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
Startup Phase	0	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
Project Start	0	20-Jul-10		21-Jun-10	
Site Taking Over	0	20-Jul-10		21-Jun-10	
Construction Phase	136	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
Zone.No 1	130	21-Jun-10 A	23-Nov-10	21-Jun-10	23-Oct-10
Villa Number D9	103	20-Jul-10	21-Nov-10	21-Jun-10	20-Oct-10
general dates	103	20-Jul-10	21-Nov-10	21-Jun-10	20-Oct-10
Start Villa construction	0	20-Jul-10		21-Jun-10	
IFC drawings	0	20-Jul-10		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		21-Nov-10		20-Oct-10
earth works	14	20-Jul-10	04-Aug-10	21-Jun-10	06-Jul-10
excavation	2	20-Jul-10	21-Jul-10	21-Jun-10	22-Jun-10
soil replacement	12	22-Jul-10	04-Aug-10	23-Jun-10	06-Jul-10
foundation level	57	05-Aug-10	10-Oct-10	07-Jul-10	13-Sep-10
Plain Concrete Foundation	2	05-Aug-10	07-Aug-10	07-Jul-10	08-Jul-10
backfilling between P.C Foundation	2	09-Aug-10	10-Aug-10	11-Jul-10	12-Jul-10
P.C Under Smells	1	11-Aug-10	11-Aug-10	13-Jul-10	13-Jul-10
Reinforced Concrete Foundation	7	12-Aug-10	19-Aug-10	14-Jul-10	21-Jul-10
under ground brick works	2	28-Aug-10	29-Aug-10	29-Jul-10	31-Jul-10
under ground insulation for RC & Brick work	2	30-Aug-10	31-Aug-10	01-Aug-10	02-Aug-10
backfilling for under ground	4	01-Sep-10	05-Sep-10	03-Aug-10	07-Aug-10
P.C slab on grade 10CM	1	05-Oct-10	05-Oct-10	06-Sep-10	06-Sep-10
moisture insulation with membrane sheets	2	06-Oct-10	07-Oct-10	07-Sep-10	11-Sep-10
R.C slab on grade	2	09-Oct-10	10-Oct-10	12-Sep-10	13-Sep-10
skeleton & brick walls	74	21-Aug-10	14-Nov-10	22-Jul-10	18-Oct-10
columns for ground floor	6	21-Aug-10	26-Aug-10	22-Jul-10	28-Jul-10

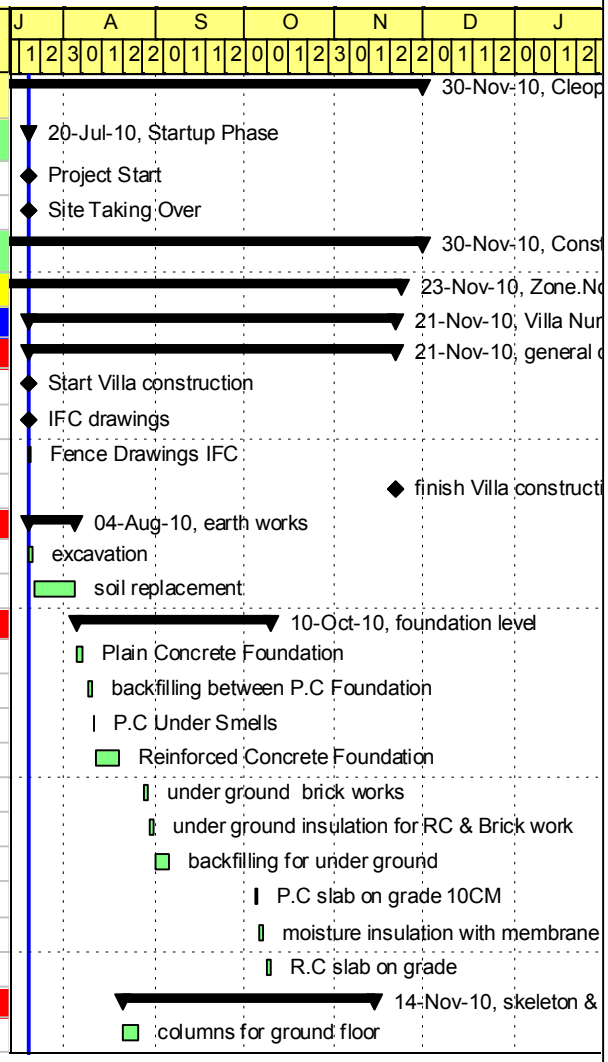

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for ground floor	9	06-Sep-10	15-Sep-10	08-Aug-10	17-Aug-10
pouring for ground floor's slab	1	16-Sep-10	16-Sep-10	18-Aug-10	18-Aug-10
columns for 1st floor	6	18-Sep-10	23-Sep-10	19-Aug-10	25-Aug-10
Fence work	50	18-Sep-10	14-Nov-10	19-Aug-10	18-Oct-10
slab for 1st floor	9	25-Sep-10	04-Oct-10	26-Aug-10	05-Sep-10
Brick works for ground floor	5	29-Sep-10	04-Oct-10	31-Aug-10	05-Sep-10
pouring for 1st floor's slab	1	05-Oct-10	05-Oct-10	06-Sep-10	06-Sep-10
columns for roof floor	4	09-Oct-10	12-Oct-10	12-Sep-10	15-Sep-10
slab for roof floor	6	13-Oct-10	19-Oct-10	16-Sep-10	22-Sep-10
Brick works for 1st floor	5	18-Oct-10	23-Oct-10	21-Sep-10	26-Sep-10
pouring for roof floor's slab	1	20-Oct-10	20-Oct-10	23-Sep-10	23-Sep-10
Brick works for roof floor	5	31-Oct-10	04-Nov-10	04-Oct-10	09-Oct-10
electro mechanical	54	06-Sep-10	07-Nov-10	08-Aug-10	11-Oct-10
plumbing connections under slab on grade	2	06-Sep-10	07-Sep-10	08-Aug-10	09-Aug-10
electrical conduits for ground floor's slab	2	11-Sep-10	12-Sep-10	12-Aug-10	14-Aug-10
electrical conduits for 1st floor slab	2	29-Sep-10	30-Sep-10	31-Aug-10	01-Sep-10
electrical conduits for ground floor walls	2	12-Oct-10	13-Oct-10	15-Sep-10	16-Sep-10
electrical conduits for roof slab	1	17-Oct-10	17-Oct-10	20-Sep-10	20-Sep-10
electrical conduits for 1st floor walls	2	24-Oct-10	25-Oct-10	27-Sep-10	28-Sep-10
electrical conduits for roof floor walls	2	06-Nov-10	07-Nov-10	10-Oct-10	11-Oct-10
finishing	29	14-Oct-10	21-Nov-10	18-Sep-10	20-Oct-10
Internal plastering for ground floor	8	14-Oct-10	23-Oct-10	18-Sep-10	26-Sep-10
Internal plastering for 1st floor	8	26-Oct-10	03-Nov-10	29-Sep-10	07-Oct-10
External plastering	10	06-Nov-10	21-Nov-10	10-Oct-10	20-Oct-10
Internal plastering for roof floor	5	08-Nov-10	13-Nov-10	12-Oct-10	17-Oct-10
Villa Number D10	103	21-Jun-10 A	19-Oct-10	21-Jun-10	05-Oct-10
general dates	78	21-Jun-10 A	19-Oct-10	21-Jun-10	05-Oct-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	

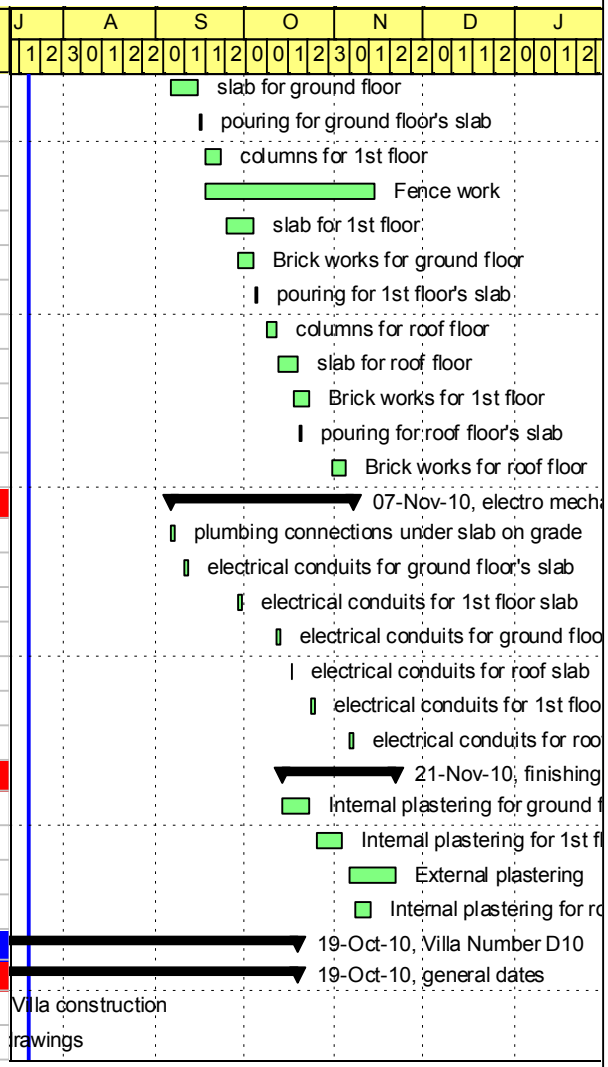

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		19-Oct-10		05-Oct-10
earth works	1	21-Jun-10 A	03-Jul-10 A	21-Jun-10	22-Jun-10
excavation	1	21-Jun-10 A	03-Jul-10 A	21-Jun-10	21-Jun-10
soil replacement	0	03-Jul-10 A	03-Jul-10 A	22-Jun-10	22-Jun-10
foundation level	70	04-Jul-10 A	12-Sep-10	22-Jun-10	26-Aug-10
Plain Concrete Foundation	2	04-Jul-10 A	06-Jul-10 A	22-Jun-10	23-Jun-10
backfilling between P.C Foundation	2	07-Jul-10 A	09-Jul-10 A	26-Jun-10	27-Jun-10
Reinforced Concrete Foundation	7	10-Jul-10 A	22-Jul-10	29-Jun-10	06-Jul-10
P.C Under Smells	1	20-Jul-10	20-Jul-10	28-Jun-10	28-Jun-10
under ground brick works	2	29-Jul-10	01-Aug-10	14-Jul-10	15-Jul-10
under ground insulation for RC & Brick work	2	01-Aug-10	03-Aug-10	17-Jul-10	18-Jul-10
backfilling for under ground	4	03-Aug-10	08-Aug-10	19-Jul-10	22-Jul-10
P.C slab on grade 10CM	1	06-Sep-10	07-Sep-10	22-Aug-10	22-Aug-10
moisture insulation with membrane sheets	2	07-Sep-10	09-Sep-10	23-Aug-10	24-Aug-10
R.C slab on grade	2	09-Sep-10	12-Sep-10	25-Aug-10	26-Aug-10
skeleton & brick walls	74	22-Jul-10	17-Oct-10	07-Jul-10	03-Oct-10
columns for ground floor	6	22-Jul-10	29-Jul-10	07-Jul-10	13-Jul-10
slab for ground floor	9	08-Aug-10	18-Aug-10	24-Jul-10	02-Aug-10
pouring for ground floor's slab	1	18-Aug-10	19-Aug-10	03-Aug-10	03-Aug-10
columns for 1st floor	6	19-Aug-10	26-Aug-10	04-Aug-10	10-Aug-10
Fence work	50	19-Aug-10	17-Oct-10	04-Aug-10	03-Oct-10
slab for 1st floor	9	26-Aug-10	06-Sep-10	11-Aug-10	21-Aug-10
Brick works for ground floor	5	31-Aug-10	06-Sep-10	16-Aug-10	21-Aug-10
pouring for 1st floor's slab	1	06-Sep-10	07-Sep-10	22-Aug-10	22-Aug-10
columns for roof floor	4	09-Sep-10	14-Sep-10	25-Aug-10	29-Aug-10
slab for roof floor	6	14-Sep-10	21-Sep-10	30-Aug-10	05-Sep-10
Brick works for 1st floor	5	19-Sep-10	25-Sep-10	04-Sep-10	13-Sep-10
pouring for roof floor's slab	1	21-Sep-10	22-Sep-10	06-Sep-10	06-Sep-10

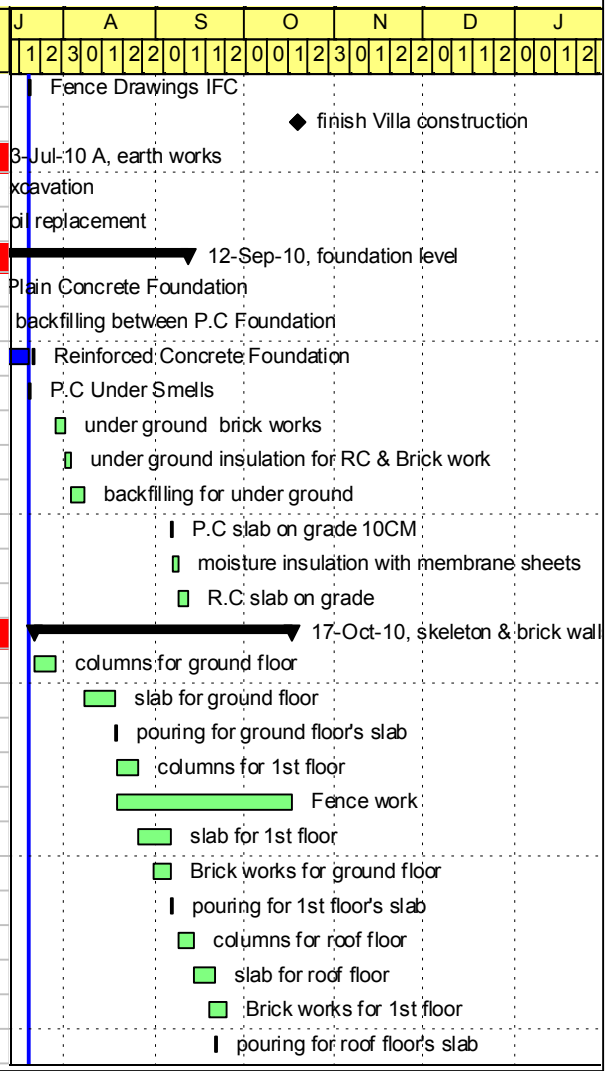

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Brick works for roof floor	5	02-Oct-10	07-Oct-10	19-Sep-10	23-Sep-10
electro mechanical	54	08-Aug-10	10-Oct-10	24-Jul-10	26-Sep-10
plumbing connections under slab on grade	2	08-Aug-10	10-Aug-10	24-Jul-10	25-Jul-10
electrical conduits for ground floor's slab	2	12-Aug-10	15-Aug-10	28-Jul-10	29-Jul-10
electrical conduits for 1st floor slab	2	31-Aug-10	02-Sep-10	16-Aug-10	17-Aug-10
electrical conduits for ground floor walls	2	13-Sep-10	15-Sep-10	29-Aug-10	30-Aug-10
electrical conduits for roof slab	1	18-Sep-10	19-Sep-10	02-Sep-10	02-Sep-10
electrical conduits for 1st floor walls	2	25-Sep-10	27-Sep-10	14-Sep-10	15-Sep-10
electrical conduits for roof floor walls	2	07-Oct-10	10-Oct-10	25-Sep-10	26-Sep-10
finishing	29	15-Sep-10	19-Oct-10	31-Aug-10	05-Oct-10
Internal plastering for ground floor	8	15-Sep-10	25-Sep-10	31-Aug-10	11-Sep-10
Internal plastering for 1st floor	8	27-Sep-10	06-Oct-10	16-Sep-10	25-Sep-10
External plastering	10	07-Oct-10	19-Oct-10	25-Sep-10	05-Oct-10
Internal plastering for roof floor	5	10-Oct-10	16-Oct-10	27-Sep-10	02-Oct-10
Villa Number B11	108	21-Jun-10 A	25-Oct-10	21-Jun-10	19-Oct-10
general dates	84	21-Jun-10 A	25-Oct-10	21-Jun-10	19-Oct-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		25-Oct-10		19-Oct-10
earth works	12	21-Jun-10 A	06-Jul-10 A	22-Jun-10	05-Jul-10
excavation	0	21-Jun-10 A	23-Jun-10 A	22-Jun-10	22-Jun-10
soil replacement	12	24-Jun-10 A	06-Jul-10 A	22-Jun-10	05-Jul-10
foundation level	64	09-Jul-10 A	18-Sep-10	06-Jul-10	12-Sep-10
Plain Concrete Foundation	2	09-Jul-10 A	11-Jul-10 A	06-Jul-10	07-Jul-10
backfilling between P.C Foundation	2	12-Jul-10 A	14-Jul-10 A	10-Jul-10	11-Jul-10
P.C Under Smells	1	20-Jul-10	20-Jul-10	12-Jul-10	12-Jul-10
Reinforced Concrete Foundation	7	21-Jul-10	28-Jul-10	13-Jul-10	20-Jul-10
under ground brick works	2	05-Aug-10	07-Aug-10	28-Jul-10	29-Jul-10

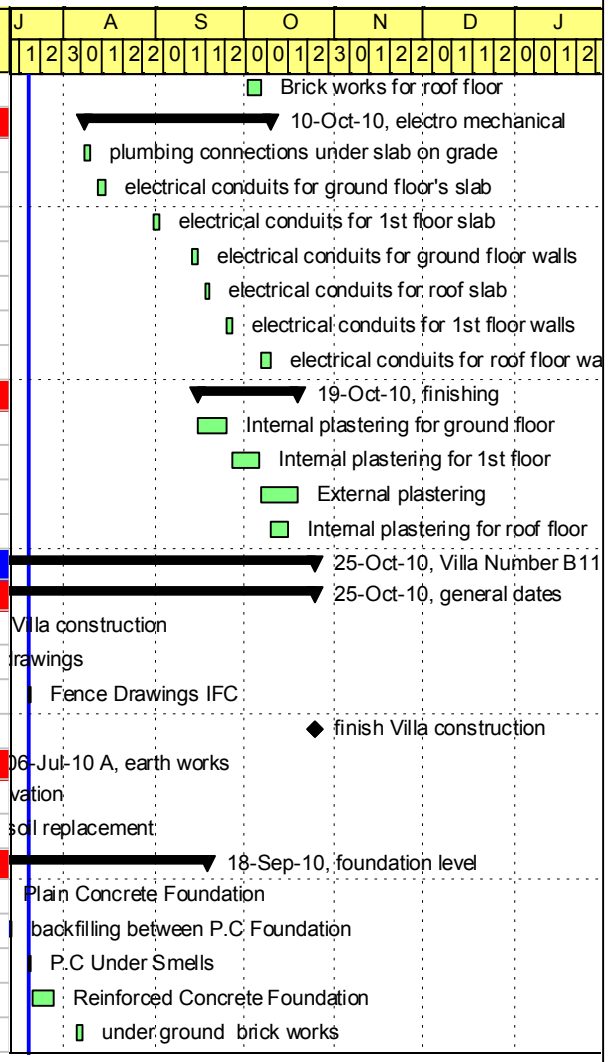

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
under ground insulation for RC & Brick work	2	08-Aug-10	09-Aug-10	31-Jul-10	01-Aug-10
backfilling for under ground	4	10-Aug-10	14-Aug-10	02-Aug-10	05-Aug-10
P.C slab on grade 10CM	1	13-Sep-10	13-Sep-10	05-Sep-10	05-Sep-10
moisture insulation with membrane sheets	2	14-Sep-10	15-Sep-10	06-Sep-10	07-Sep-10
R.C slab on grade	2	16-Sep-10	18-Sep-10	11-Sep-10	12-Sep-10
skeleton & brick walls	74	29-Jul-10	23-Oct-10	21-Jul-10	17-Oct-10
columns for ground floor	6	29-Jul-10	04-Aug-10	21-Jul-10	27-Jul-10
slab for ground floor	9	15-Aug-10	24-Aug-10	07-Aug-10	16-Aug-10
pouring for ground floor's slab	1	25-Aug-10	25-Aug-10	17-Aug-10	17-Aug-10
columns for 1st floor	6	26-Aug-10	01-Sep-10	18-Aug-10	24-Aug-10
Fence work	50	26-Aug-10	23-Oct-10	18-Aug-10	17-Oct-10
slab for 1st floor	9	02-Sep-10	12-Sep-10	25-Aug-10	04-Sep-10
Brick works for ground floor	5	07-Sep-10	12-Sep-10	30-Aug-10	04-Sep-10
pouring for 1st floor's slab	1	13-Sep-10	13-Sep-10	05-Sep-10	05-Sep-10
columns for roof floor	4	16-Sep-10	20-Sep-10	11-Sep-10	14-Sep-10
slab for roof floor	6	21-Sep-10	27-Sep-10	15-Sep-10	21-Sep-10
Brick works for 1st floor	5	26-Sep-10	30-Sep-10	20-Sep-10	25-Sep-10
pouring for roof floor's slab	1	28-Sep-10	28-Sep-10	22-Sep-10	22-Sep-10
Brick works for roof floor	5	09-Oct-10	13-Oct-10	03-Oct-10	07-Oct-10
electro mechanical	54	15-Aug-10	16-Oct-10	07-Aug-10	10-Oct-10
plumbing connections under slab on grade	2	15-Aug-10	16-Aug-10	07-Aug-10	08-Aug-10
electrical conduits for ground floor's slab	2	19-Aug-10	21-Aug-10	11-Aug-10	12-Aug-10
electrical conduits for 1st floor slab	2	07-Sep-10	08-Sep-10	30-Aug-10	31-Aug-10
electrical conduits for ground floor walls	2	20-Sep-10	21-Sep-10	14-Sep-10	15-Sep-10
electrical conduits for roof slab	1	25-Sep-10	25-Sep-10	19-Sep-10	19-Sep-10
electrical conduits for 1st floor walls	2	02-Oct-10	03-Oct-10	26-Sep-10	27-Sep-10
electrical conduits for roof floor walls	2	14-Oct-10	16-Oct-10	09-Oct-10	10-Oct-10
finishing	29	22-Sep-10	25-Oct-10	16-Sep-10	19-Oct-10
Internal plastering for ground floor	8	22-Sep-10	30-Sep-10	16-Sep-10	25-Sep-10

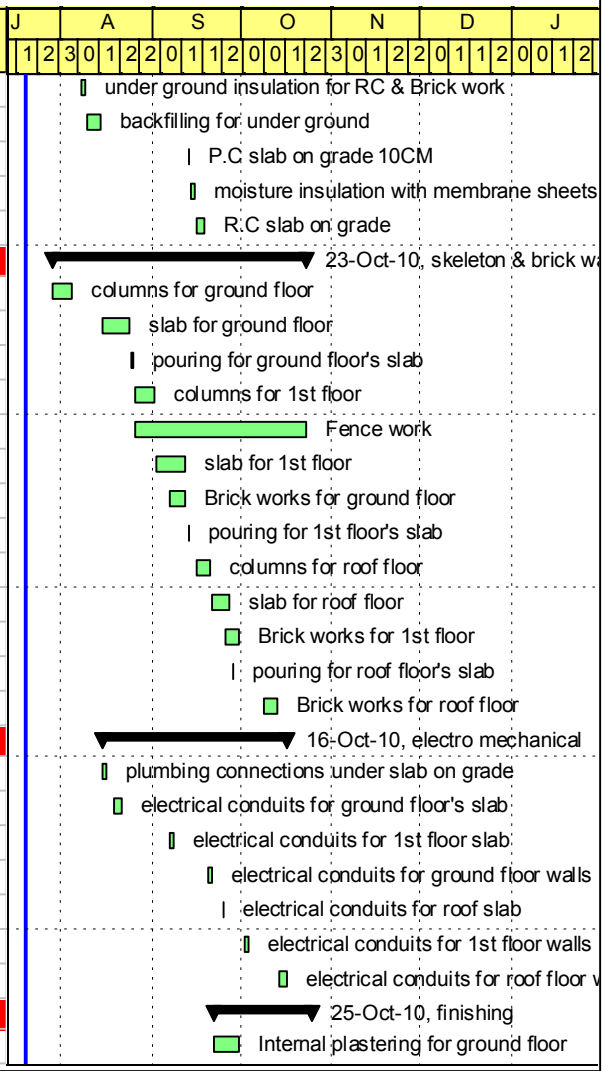

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Internal plastering for 1st floor	8	04-Oct-10	12-Oct-10	28-Sep-10	06-Oct-10
External plastering	10	14-Oct-10	25-Oct-10	09-Oct-10	19-Oct-10
Internal plastering for roof floor	5	17-Oct-10	21-Oct-10	11-Oct-10	16-Oct-10
Villa Number B12	102	21-Jun-10 A	19-Oct-10	21-Jun-10	19-Oct-10
general dates	78	21-Jun-10 A	19-Oct-10	21-Jun-10	19-Oct-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		19-Oct-10		19-Oct-10
earth works	12	21-Jun-10 A	05-Jul-10 A	22-Jun-10	05-Jul-10
excavation	0	21-Jun-10 A	22-Jun-10 A	22-Jun-10	22-Jun-10
soil replacement	12	23-Jun-10 A	05-Jul-10 A	22-Jun-10	05-Jul-10
foundation level	58	06-Jul-10 A	12-Sep-10	06-Jul-10	12-Sep-10
Plain Concrete Foundation	2	06-Jul-10 A	08-Jul-10 A	06-Jul-10	07-Jul-10
backfilling between P.C Foundation	2	09-Jul-10 A	11-Jul-10 A	10-Jul-10	11-Jul-10
Reinforced Concrete Foundation	7	12-Jul-10 A	22-Jul-10	13-Jul-10	20-Jul-10
P.C Under Smells	1	20-Jul-10	20-Jul-10	12-Jul-10	12-Jul-10
under ground brick works	2	29-Jul-10	01-Aug-10	28-Jul-10	29-Jul-10
under ground insulation for RC & Brick work	2	01-Aug-10	03-Aug-10	31-Jul-10	01-Aug-10
backfilling for under ground	4	03-Aug-10	08-Aug-10	02-Aug-10	05-Aug-10
P.C slab on grade 10CM	1	06-Sep-10	07-Sep-10	05-Sep-10	05-Sep-10
moisture insulation with membrane sheets	2	07-Sep-10	09-Sep-10	06-Sep-10	07-Sep-10
R.C slab on grade	2	09-Sep-10	12-Sep-10	11-Sep-10	12-Sep-10
skeleton & brick walls	74	22-Jul-10	17-Oct-10	21-Jul-10	17-Oct-10
columns for ground floor	6	22-Jul-10	29-Jul-10	21-Jul-10	27-Jul-10
slab for ground floor	9	08-Aug-10	18-Aug-10	07-Aug-10	16-Aug-10
pouring for ground floor's slab	1	18-Aug-10	19-Aug-10	17-Aug-10	17-Aug-10
columns for 1st floor	6	19-Aug-10	26-Aug-10	18-Aug-10	24-Aug-10
Fence work	50	19-Aug-10	17-Oct-10	18-Aug-10	17-Oct-10

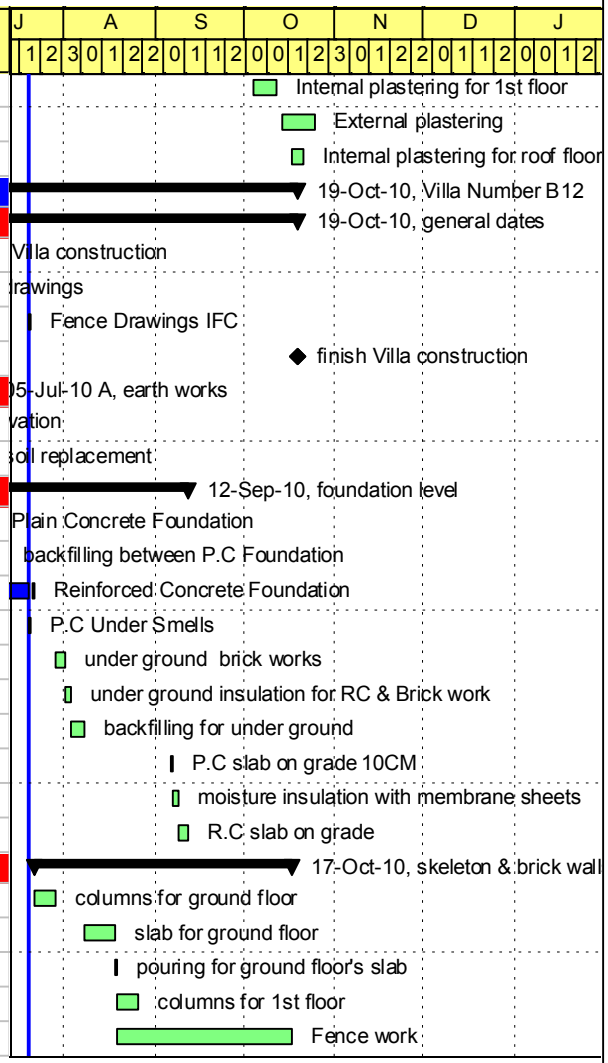

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for 1st floor	9	26-Aug-10	06-Sep-10	25-Aug-10	04-Sep-10
Brick works for ground floor	5	31-Aug-10	06-Sep-10	30-Aug-10	04-Sep-10
pouring for 1st floor's slab	1	06-Sep-10	07-Sep-10	05-Sep-10	05-Sep-10
columns for roof floor	4	09-Sep-10	14-Sep-10	11-Sep-10	14-Sep-10
slab for roof floor	6	14-Sep-10	21-Sep-10	15-Sep-10	21-Sep-10
Brick works for 1st floor	5	19-Sep-10	25-Sep-10	20-Sep-10	25-Sep-10
pouring for roof floor's slab	1	21-Sep-10	22-Sep-10	22-Sep-10	22-Sep-10
Brick works for roof floor	5	02-Oct-10	07-Oct-10	03-Oct-10	07-Oct-10
electro mechanical	54	08-Aug-10	10-Oct-10	07-Aug-10	10-Oct-10
plumbing connections under slab on grade	2	08-Aug-10	10-Aug-10	07-Aug-10	08-Aug-10
electrical conduits for ground floor's slab	2	12-Aug-10	15-Aug-10	11-Aug-10	12-Aug-10
electrical conduits for 1st floor slab	2	31-Aug-10	02-Sep-10	30-Aug-10	31-Aug-10
electrical conduits for ground floor walls	2	13-Sep-10	15-Sep-10	14-Sep-10	15-Sep-10
electrical conduits for roof slab	1	18-Sep-10	19-Sep-10	19-Sep-10	19-Sep-10
electrical conduits for 1st floor walls	2	25-Sep-10	27-Sep-10	26-Sep-10	27-Sep-10
electrical conduits for roof floor walls	2	07-Oct-10	10-Oct-10	09-Oct-10	10-Oct-10
finishing	29	15-Sep-10	19-Oct-10	16-Sep-10	19-Oct-10
Internal plastering for ground floor	8	15-Sep-10	25-Sep-10	16-Sep-10	25-Sep-10
Internal plastering for 1st floor	8	27-Sep-10	06-Oct-10	28-Sep-10	06-Oct-10
External plastering	10	07-Oct-10	19-Oct-10	09-Oct-10	19-Oct-10
Internal plastering for roof floor	5	10-Oct-10	16-Oct-10	11-Oct-10	16-Oct-10
Villa Number B13	107	21-Jun-10 A	25-Oct-10	21-Jun-10	20-Oct-10
general dates	84	21-Jun-10 A	25-Oct-10	21-Jun-10	20-Oct-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		25-Oct-10		20-Oct-10
earth works	12	21-Jun-10 A	05-Jul-10 A	23-Jun-10	06-Jul-10
excavation	0	21-Jun-10 A	22-Jun-10 A	23-Jun-10	23-Jun-10

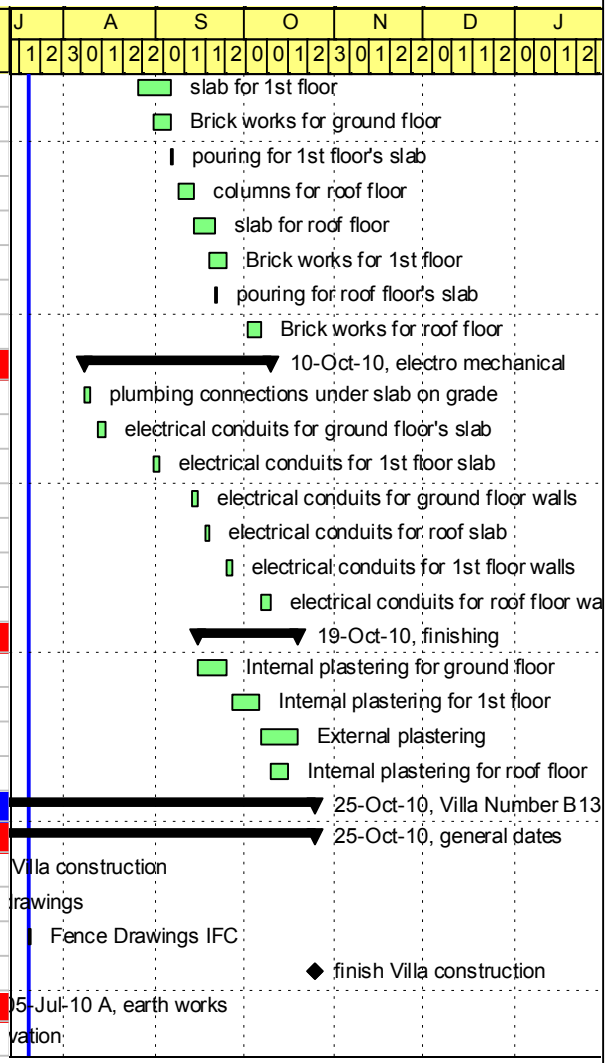

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
soil replacement	12	23-Jun-10 A	05-Jul-10 A	23-Jun-10	06-Jul-10
foundation level	63	06-Jul-10 A	18-Sep-10	07-Jul-10	13-Sep-10
Plain Concrete Foundation	2	06-Jul-10 A	08-Jul-10 A	07-Jul-10	08-Jul-10
backfilling between P.C Foundation	2	09-Jul-10 A	11-Jul-10 A	11-Jul-10	12-Jul-10
P.C Under Smells	1	20-Jul-10	20-Jul-10	13-Jul-10	13-Jul-10
Reinforced Concrete Foundation	7	21-Jul-10	28-Jul-10	14-Jul-10	21-Jul-10
under ground brick works	2	05-Aug-10	07-Aug-10	29-Jul-10	31-Jul-10
under ground insulation for RC & Brick work	2	08-Aug-10	09-Aug-10	01-Aug-10	02-Aug-10
backfilling for under ground	4	10-Aug-10	14-Aug-10	03-Aug-10	07-Aug-10
P.C slab on grade 10CM	1	13-Sep-10	13-Sep-10	06-Sep-10	06-Sep-10
moisture insulation with membrane sheets	2	14-Sep-10	15-Sep-10	07-Sep-10	11-Sep-10
R.C slab on grade	2	16-Sep-10	18-Sep-10	12-Sep-10	13-Sep-10
skeleton & brick walls	74	29-Jul-10	23-Oct-10	22-Jul-10	18-Oct-10
columns for ground floor	6	29-Jul-10	04-Aug-10	22-Jul-10	28-Jul-10
slab for ground floor	9	15-Aug-10	24-Aug-10	08-Aug-10	17-Aug-10
pouring for ground floor's slab	1	25-Aug-10	25-Aug-10	18-Aug-10	18-Aug-10
columns for 1st floor	6	26-Aug-10	01-Sep-10	19-Aug-10	25-Aug-10
Fence work	50	26-Aug-10	23-Oct-10	19-Aug-10	18-Oct-10
slab for 1st floor	9	02-Sep-10	12-Sep-10	26-Aug-10	05-Sep-10
Brick works for ground floor	5	07-Sep-10	12-Sep-10	31-Aug-10	05-Sep-10
pouring for 1st floor's slab	1	13-Sep-10	13-Sep-10	06-Sep-10	06-Sep-10
columns for roof floor	4	16-Sep-10	20-Sep-10	12-Sep-10	15-Sep-10
slab for roof floor	6	21-Sep-10	27-Sep-10	16-Sep-10	22-Sep-10
Brick works for 1st floor	5	26-Sep-10	30-Sep-10	21-Sep-10	26-Sep-10
pouring for roof floor's slab	1	28-Sep-10	28-Sep-10	23-Sep-10	23-Sep-10
Brick works for roof floor	5	09-Oct-10	13-Oct-10	04-Oct-10	09-Oct-10
electro mechanical	54	15-Aug-10	16-Oct-10	08-Aug-10	11-Oct-10
plumbing connections under slab on grade	2	15-Aug-10	16-Aug-10	08-Aug-10	09-Aug-10
electrical conduits for ground floor's slab	2	19-Aug-10	21-Aug-10	12-Aug-10	14-Aug-10

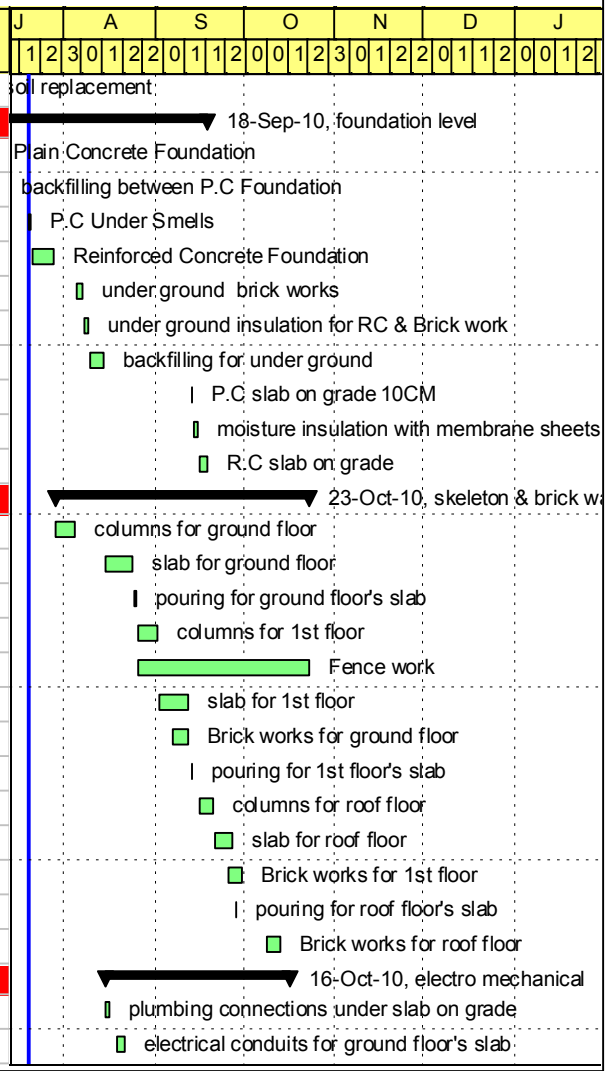

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
electrical conduits for 1st floor slab	2	07-Sep-10	08-Sep-10	31-Aug-10	01-Sep-10
electrical conduits for ground floor walls	2	20-Sep-10	21-Sep-10	15-Sep-10	16-Sep-10
electrical conduits for roof slab	1	25-Sep-10	25-Sep-10	20-Sep-10	20-Sep-10
electrical conduits for 1st floor walls	2	02-Oct-10	03-Oct-10	27-Sep-10	28-Sep-10
electrical conduits for roof floor walls	2	14-Oct-10	16-Oct-10	10-Oct-10	11-Oct-10
finishing	29	22-Sep-10	25-Oct-10	18-Sep-10	20-Oct-10
Internal plastering for ground floor	8	22-Sep-10	30-Sep-10	18-Sep-10	26-Sep-10
Internal plastering for 1st floor	8	04-Oct-10	12-Oct-10	29-Sep-10	07-Oct-10
External plastering	10	14-Oct-10	25-Oct-10	10-Oct-10	20-Oct-10
Internal plastering for roof floor	5	17-Oct-10	21-Oct-10	12-Oct-10	17-Oct-10
Villa Number B14	107	21-Jun-10 A	25-Oct-10	21-Jun-10	20-Oct-10
general dates	84	21-Jun-10 A	25-Oct-10	21-Jun-10	20-Oct-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		25-Oct-10		20-Oct-10
earth works	12	21-Jun-10 A	10-Jul-10 A	23-Jun-10	06-Jul-10
excavation	0	21-Jun-10 A	27-Jun-10 A	23-Jun-10	23-Jun-10
soil replacement	12	28-Jun-10 A	10-Jul-10 A	23-Jun-10	06-Jul-10
foundation level	63	11-Jul-10 A	18-Sep-10	07-Jul-10	13-Sep-10
Plain Concrete Foundation	2	11-Jul-10 A	18-Jul-10 A	07-Jul-10	08-Jul-10
backfilling between P.C Foundation	2	19-Jul-10 A	21-Jul-10 A	11-Jul-10	12-Jul-10
P.C Under Smells	1	20-Jul-10	20-Jul-10	13-Jul-10	13-Jul-10
Reinforced Concrete Foundation	7	21-Jul-10	28-Jul-10	14-Jul-10	21-Jul-10
under ground brick works	2	05-Aug-10	07-Aug-10	29-Jul-10	31-Jul-10
under ground insulation for RC & Brick work	2	08-Aug-10	09-Aug-10	01-Aug-10	02-Aug-10
backfilling for under ground	4	10-Aug-10	14-Aug-10	03-Aug-10	07-Aug-10
P.C slab on grade 10CM	1	13-Sep-10	13-Sep-10	06-Sep-10	06-Sep-10
moisture insulation with membrane sheets	2	14-Sep-10	15-Sep-10	07-Sep-10	11-Sep-10

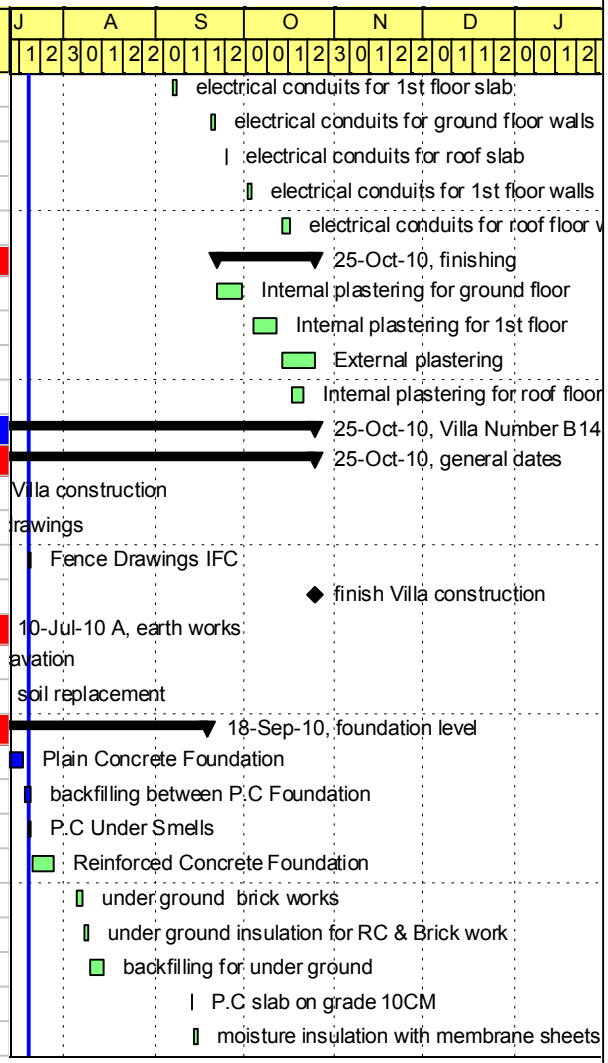

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
R.C slab on grade	2	16-Sep-10	18-Sep-10	12-Sep-10	13-Sep-10
skeleton & brick walls	74	29-Jul-10	23-Oct-10	22-Jul-10	18-Oct-10
columns for ground floor	6	29-Jul-10	04-Aug-10	22-Jul-10	28-Jul-10
slab for ground floor	9	15-Aug-10	24-Aug-10	08-Aug-10	17-Aug-10
pouring for ground floor's slab	1	25-Aug-10	25-Aug-10	18-Aug-10	18-Aug-10
columns for 1st floor	6	26-Aug-10	01-Sep-10	19-Aug-10	25-Aug-10
Fence work	50	26-Aug-10	23-Oct-10	19-Aug-10	18-Oct-10
slab for 1st floor	9	02-Sep-10	12-Sep-10	26-Aug-10	05-Sep-10
Brick works for ground floor	5	07-Sep-10	12-Sep-10	31-Aug-10	05-Sep-10
pouring for 1st floor's slab	1	13-Sep-10	13-Sep-10	06-Sep-10	06-Sep-10
columns for roof floor	4	16-Sep-10	20-Sep-10	12-Sep-10	15-Sep-10
slab for roof floor	6	21-Sep-10	27-Sep-10	16-Sep-10	22-Sep-10
Brick works for 1st floor	5	26-Sep-10	30-Sep-10	21-Sep-10	26-Sep-10
pouring for roof floor's slab	1	28-Sep-10	28-Sep-10	23-Sep-10	23-Sep-10
Brick works for roof floor	5	09-Oct-10	13-Oct-10	04-Oct-10	09-Oct-10
electro mechanical	54	15-Aug-10	16-Oct-10	08-Aug-10	11-Oct-10
plumbing connections under slab on grade	2	15-Aug-10	16-Aug-10	08-Aug-10	09-Aug-10
electrical conduits for ground floor's slab	2	19-Aug-10	21-Aug-10	12-Aug-10	14-Aug-10
electrical conduits for 1st floor slab	2	07-Sep-10	08-Sep-10	31-Aug-10	01-Sep-10
electrical conduits for ground floor walls	2	20-Sep-10	21-Sep-10	15-Sep-10	16-Sep-10
electrical conduits for roof slab	1	25-Sep-10	25-Sep-10	20-Sep-10	20-Sep-10
electrical conduits for 1st floor walls	2	02-Oct-10	03-Oct-10	27-Sep-10	28-Sep-10
electrical conduits for roof floor walls	2	14-Oct-10	16-Oct-10	10-Oct-10	11-Oct-10
finishing	29	22-Sep-10	25-Oct-10	18-Sep-10	20-Oct-10
Internal plastering for ground floor	8	22-Sep-10	30-Sep-10	18-Sep-10	26-Sep-10
Internal plastering for 1st floor	8	04-Oct-10	12-Oct-10	29-Sep-10	07-Oct-10
External plastering	10	14-Oct-10	25-Oct-10	10-Oct-10	20-Oct-10
Internal plastering for roof floor	5	17-Oct-10	21-Oct-10	12-Oct-10	17-Oct-10
Villa Number B102	105	20-Jul-10	23-Nov-10	21-Jun-10	23-Oct-10

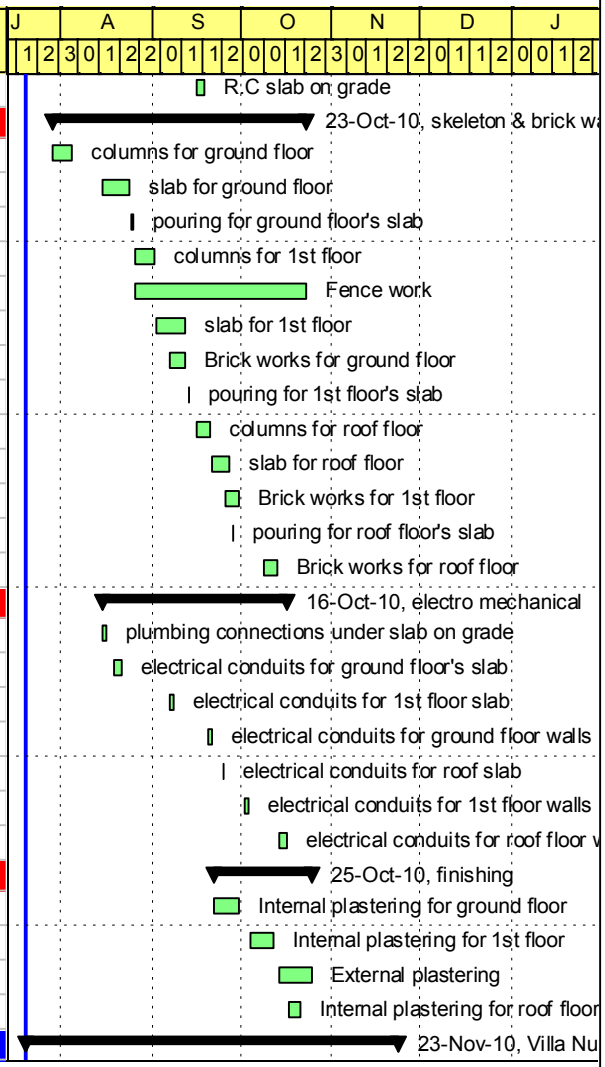

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
general dates	105	20-Jul-10	23-Nov-10	21-Jun-10	23-Oct-10
Start Villa construction	0	20-Jul-10		21-Jun-10	
IFC drawings	0	20-Jul-10		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		23-Nov-10		23-Oct-10
earth works	14	22-Jul-10	07-Aug-10	23-Jun-10	08-Jul-10
excavation	2	22-Jul-10	24-Jul-10	23-Jun-10	24-Jun-10
soil replacement	12	25-Jul-10	07-Aug-10	26-Jun-10	08-Jul-10
foundation level	57	08-Aug-10	12-Oct-10	10-Jul-10	15-Sep-10
Plain Concrete Foundation	2	08-Aug-10	09-Aug-10	10-Jul-10	11-Jul-10
backfilling between P.C Foundation	2	11-Aug-10	12-Aug-10	13-Jul-10	14-Jul-10
P.C Under Smells	1	14-Aug-10	14-Aug-10	15-Jul-10	15-Jul-10
Reinforced Concrete Foundation	7	15-Aug-10	22-Aug-10	17-Jul-10	24-Jul-10
under ground brick works	2	30-Aug-10	31-Aug-10	01-Aug-10	02-Aug-10
under ground insulation for RC & Brick work	2	01-Sep-10	02-Sep-10	03-Aug-10	04-Aug-10
backfilling for under ground	4	04-Sep-10	07-Sep-10	05-Aug-10	09-Aug-10
P.C slab on grade 10CM	1	07-Oct-10	07-Oct-10	11-Sep-10	11-Sep-10
moisture insulation with membrane sheets	2	09-Oct-10	10-Oct-10	12-Sep-10	13-Sep-10
R.C slab on grade	2	11-Oct-10	12-Oct-10	14-Sep-10	15-Sep-10
skeleton & brick walls	74	23-Aug-10	21-Nov-10	25-Jul-10	20-Oct-10
columns for ground floor	6	23-Aug-10	29-Aug-10	25-Jul-10	31-Jul-10
slab for ground floor	9	08-Sep-10	18-Sep-10	10-Aug-10	19-Aug-10
pouring for ground floor's slab	1	19-Sep-10	19-Sep-10	21-Aug-10	21-Aug-10
columns for 1st floor	6	20-Sep-10	26-Sep-10	22-Aug-10	28-Aug-10
Fence work	50	20-Sep-10	21-Nov-10	22-Aug-10	20-Oct-10
slab for 1st floor	9	27-Sep-10	06-Oct-10	29-Aug-10	07-Sep-10
Brick works for ground floor	5	02-Oct-10	06-Oct-10	02-Sep-10	07-Sep-10
pouring for 1st floor's slab	1	07-Oct-10	07-Oct-10	11-Sep-10	11-Sep-10
columns for roof floor	4	11-Oct-10	14-Oct-10	14-Sep-10	18-Sep-10

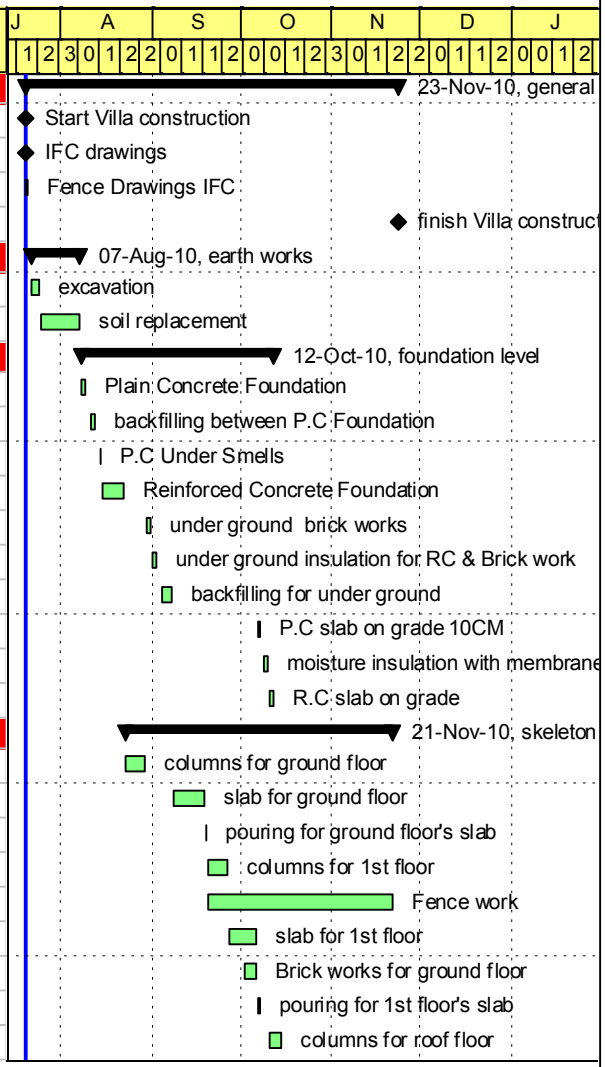

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for roof floor	6	16-Oct-10	21-Oct-10	19-Sep-10	25-Sep-10
Brick works for 1st floor	5	20-Oct-10	25-Oct-10	23-Sep-10	28-Sep-10
pouring for roof floor's slab	1	23-Oct-10	23-Oct-10	26-Sep-10	26-Sep-10
Brick works for roof floor	5	02-Nov-10	07-Nov-10	06-Oct-10	11-Oct-10
electro mechanical	54	08-Sep-10	09-Nov-10	10-Aug-10	13-Oct-10
plumbing connections under slab on grade	2	08-Sep-10	09-Sep-10	10-Aug-10	11-Aug-10
electrical conduits for ground floor's slab	2	13-Sep-10	14-Sep-10	15-Aug-10	16-Aug-10
electrical conduits for 1st floor slab	2	02-Oct-10	03-Oct-10	02-Sep-10	04-Sep-10
electrical conduits for ground floor walls	2	14-Oct-10	16-Oct-10	18-Sep-10	19-Sep-10
electrical conduits for roof slab	1	19-Oct-10	19-Oct-10	22-Sep-10	22-Sep-10
electrical conduits for 1st floor walls	2	26-Oct-10	27-Oct-10	29-Sep-10	30-Sep-10
electrical conduits for roof floor walls	2	08-Nov-10	09-Nov-10	12-Oct-10	13-Oct-10
finishing	29	17-Oct-10	23-Nov-10	20-Sep-10	23-Oct-10
Internal plastering for ground floor	8	17-Oct-10	25-Oct-10	20-Sep-10	28-Sep-10
Internal plastering for 1st floor	8	28-Oct-10	06-Nov-10	02-Oct-10	10-Oct-10
External plastering	10	08-Nov-10	23-Nov-10	12-Oct-10	23-Oct-10
Internal plastering for roof floor	5	10-Nov-10	15-Nov-10	14-Oct-10	19-Oct-10
Villa Number B107	105	20-Jul-10	23-Nov-10	21-Jun-10	23-Oct-10
general dates	105	20-Jul-10	23-Nov-10	21-Jun-10	23-Oct-10
Start Villa construction	0	20-Jul-10		21-Jun-10	
IFC drawings	0	20-Jul-10		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		23-Nov-10		23-Oct-10
earth works	14	22-Jul-10	07-Aug-10	23-Jun-10	08-Jul-10
excavation	2	22-Jul-10	24-Jul-10	23-Jun-10	24-Jun-10
soil replacement	12	25-Jul-10	07-Aug-10	26-Jun-10	08-Jul-10
foundation level	57	08-Aug-10	12-Oct-10	10-Jul-10	15-Sep-10
Plain Concrete Foundation	2	08-Aug-10	09-Aug-10	10-Jul-10	11-Jul-10
backfilling between P.C Foundation	2	11-Aug-10	12-Aug-10	13-Jul-10	14-Jul-10

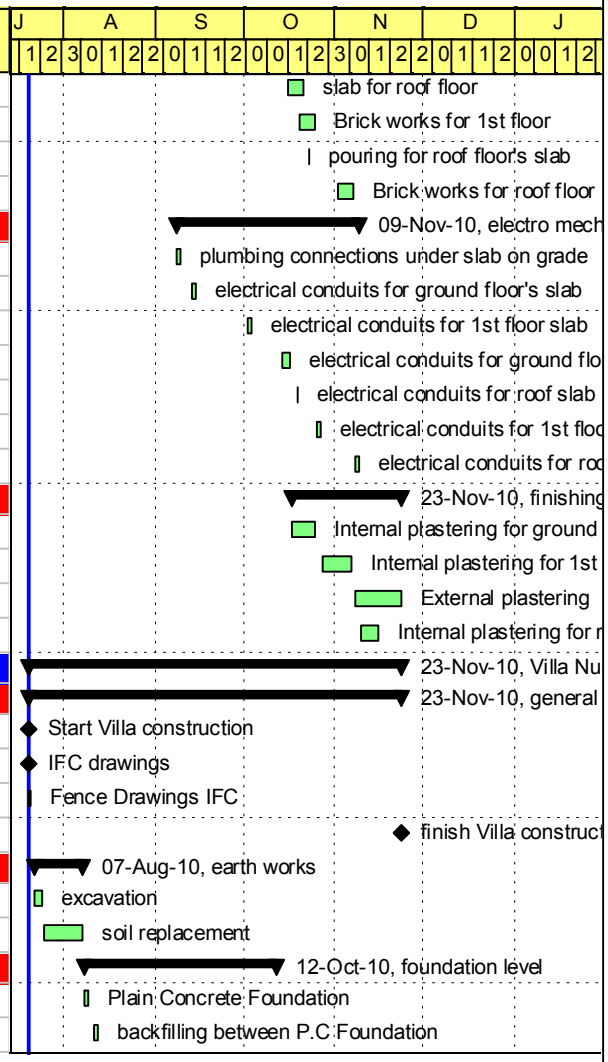

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
P.C Under Smells	1	14-Aug-10	14-Aug-10	15-Jul-10	15-Jul-10
Reinforced Concrete Foundation	7	15-Aug-10	22-Aug-10	17-Jul-10	24-Jul-10
under ground brick works	2	30-Aug-10	31-Aug-10	01-Aug-10	02-Aug-10
under ground insulation for RC & Brick work	2	01-Sep-10	02-Sep-10	03-Aug-10	04-Aug-10
backfilling for under ground	4	04-Sep-10	07-Sep-10	05-Aug-10	09-Aug-10
P.C slab on grade 10CM	1	07-Oct-10	07-Oct-10	11-Sep-10	11-Sep-10
moisture insulation with membrane sheets	2	09-Oct-10	10-Oct-10	12-Sep-10	13-Sep-10
R.C slab on grade	2	11-Oct-10	12-Oct-10	14-Sep-10	15-Sep-10
skeleton & brick walls	74	23-Aug-10	21-Nov-10	25-Jul-10	20-Oct-10
columns for ground floor	6	23-Aug-10	29-Aug-10	25-Jul-10	31-Jul-10
slab for ground floor	9	08-Sep-10	18-Sep-10	10-Aug-10	19-Aug-10
pouring for ground floor's slab	1	19-Sep-10	19-Sep-10	21-Aug-10	21-Aug-10
columns for 1st floor	6	20-Sep-10	26-Sep-10	22-Aug-10	28-Aug-10
Fence work	50	20-Sep-10	21-Nov-10	22-Aug-10	20-Oct-10
slab for 1st floor	9	27-Sep-10	06-Oct-10	29-Aug-10	07-Sep-10
Brick works for ground floor	5	02-Oct-10	06-Oct-10	02-Sep-10	07-Sep-10
pouring for 1st floor's slab	1	07-Oct-10	07-Oct-10	11-Sep-10	11-Sep-10
columns for roof floor	4	11-Oct-10	14-Oct-10	14-Sep-10	18-Sep-10
slab for roof floor	6	16-Oct-10	21-Oct-10	19-Sep-10	25-Sep-10
Brick works for 1st floor	5	20-Oct-10	25-Oct-10	23-Sep-10	28-Sep-10
pouring for roof floor's slab	1	23-Oct-10	23-Oct-10	26-Sep-10	26-Sep-10
Brick works for roof floor	5	02-Nov-10	07-Nov-10	06-Oct-10	11-Oct-10
electro mechanical	54	08-Sep-10	09-Nov-10	10-Aug-10	13-Oct-10
plumbing connections under slab on grade	2	08-Sep-10	09-Sep-10	10-Aug-10	11-Aug-10
electrical conduits for ground floor's slab	2	13-Sep-10	14-Sep-10	15-Aug-10	16-Aug-10
electrical conduits for 1st floor slab	2	02-Oct-10	03-Oct-10	02-Sep-10	04-Sep-10
electrical conduits for ground floor walls	2	14-Oct-10	16-Oct-10	18-Sep-10	19-Sep-10
electrical conduits for roof slab	1	19-Oct-10	19-Oct-10	22-Sep-10	22-Sep-10
electrical conduits for 1st floor walls	2	26-Oct-10	27-Oct-10	29-Sep-10	30-Sep-10

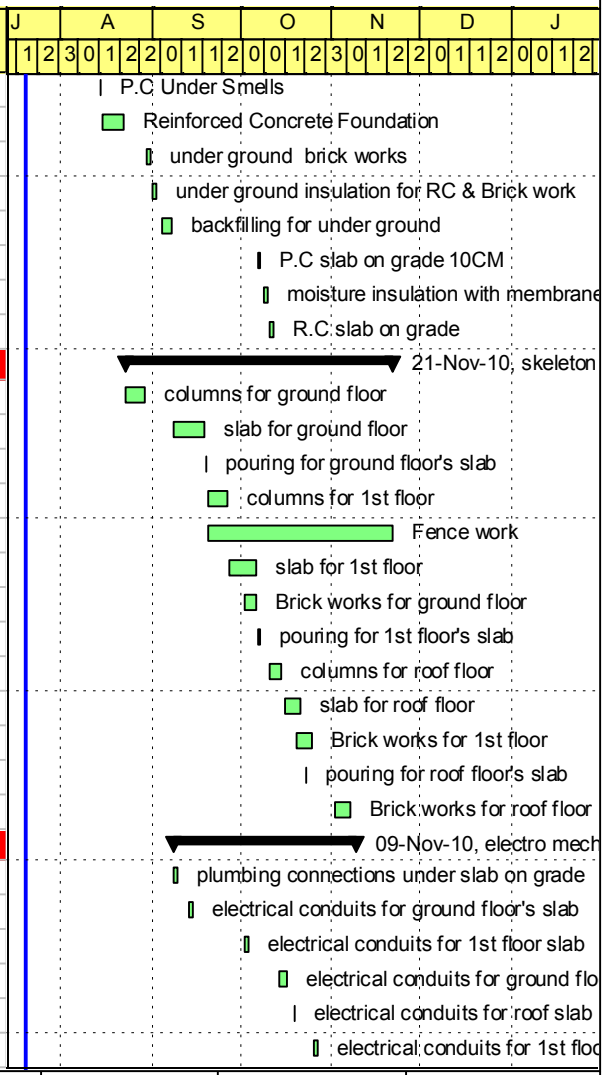

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
electrical conduits for roof floor walls	2	08-Nov-10	09-Nov-10	12-Oct-10	13-Oct-10
finishing	29	17-Oct-10	23-Nov-10	20-Sep-10	23-Oct-10
Internal plastering for ground floor	8	17-Oct-10	25-Oct-10	20-Sep-10	28-Sep-10
Internal plastering for 1st floor	8	28-Oct-10	06-Nov-10	02-Oct-10	10-Oct-10
External plastering	10	08-Nov-10	23-Nov-10	12-Oct-10	23-Oct-10
Internal plastering for roof floor	5	10-Nov-10	15-Nov-10	14-Oct-10	19-Oct-10
Zone.No 2	101	28-Jun-10 A	02-Nov-10	21-Jun-10	13-Nov-10
Villa Number D89	100	29-Jun-10 A	31-Oct-10	21-Jun-10	06-Nov-10
general dates	89	29-Jun-10 A	31-Oct-10	21-Jun-10	06-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		31-Oct-10		06-Nov-10
earth works	14	30-Jun-10 A	20-Jul-10 A	07-Jul-10	22-Jul-10
excavation	2	30-Jun-10 A	01-Jul-10 A	07-Jul-10	08-Jul-10
soil replacement	12	02-Jul-10 A	20-Jul-10 A	10-Jul-10	22-Jul-10
foundation level	57	20-Jul-10	23-Sep-10	24-Jul-10	29-Sep-10
Plain Concrete Foundation	2	20-Jul-10	21-Jul-10	24-Jul-10	25-Jul-10
backfilling between P.C Foundation	2	24-Jul-10	25-Jul-10	27-Jul-10	28-Jul-10
P.C Under Smells	1	26-Jul-10	26-Jul-10	29-Jul-10	29-Jul-10
Reinforced Concrete Foundation	7	27-Jul-10	03-Aug-10	31-Jul-10	07-Aug-10
under ground brick works	2	11-Aug-10	12-Aug-10	15-Aug-10	16-Aug-10
under ground insulation for RC & Brick work	2	14-Aug-10	15-Aug-10	17-Aug-10	18-Aug-10
backfilling for under ground	4	16-Aug-10	19-Aug-10	19-Aug-10	23-Aug-10
P.C slab on grade 10CM	1	19-Sep-10	19-Sep-10	25-Sep-10	25-Sep-10
moisture insulation with membrane sheets	2	20-Sep-10	21-Sep-10	26-Sep-10	27-Sep-10
R.C slab on grade	2	22-Sep-10	23-Sep-10	28-Sep-10	29-Sep-10
skeleton & brick walls	74	04-Aug-10	28-Oct-10	08-Aug-10	03-Nov-10
columns for ground floor	6	04-Aug-10	10-Aug-10	08-Aug-10	14-Aug-10

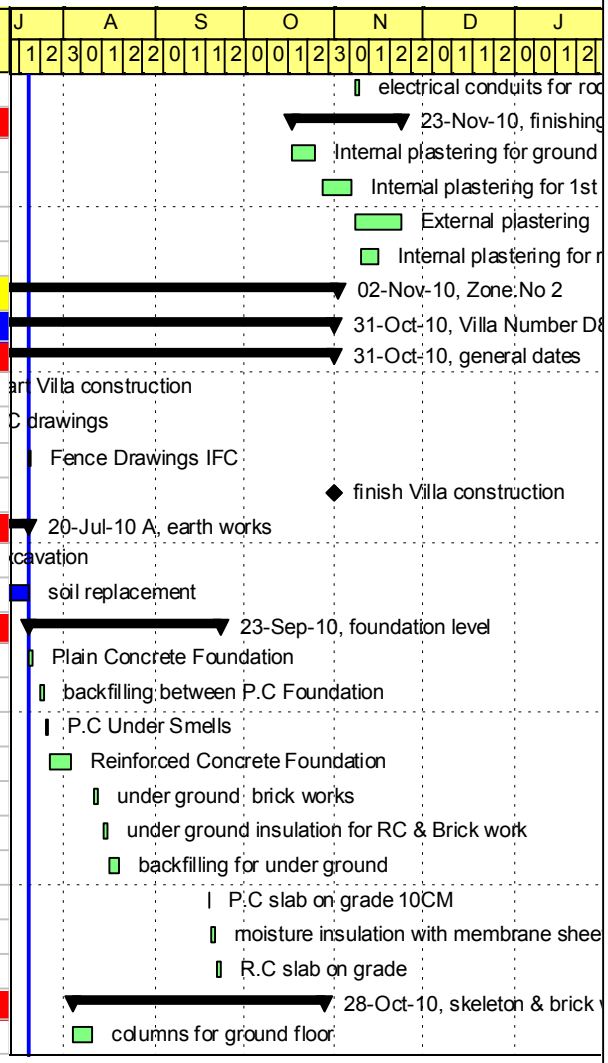

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for ground floor	9	21-Aug-10	30-Aug-10	24-Aug-10	02-Sep-10
pouring for ground floor's slab	1	31-Aug-10	31-Aug-10	04-Sep-10	04-Sep-10
columns for 1st floor	6	01-Sep-10	07-Sep-10	05-Sep-10	13-Sep-10
Fence work	50	01-Sep-10	28-Oct-10	05-Sep-10	03-Nov-10
slab for 1st floor	9	08-Sep-10	18-Sep-10	14-Sep-10	23-Sep-10
Brick works for ground floor	5	13-Sep-10	18-Sep-10	19-Sep-10	23-Sep-10
pouring for 1st floor's slab	1	19-Sep-10	19-Sep-10	25-Sep-10	25-Sep-10
columns for roof floor	4	22-Sep-10	26-Sep-10	28-Sep-10	02-Oct-10
slab for roof floor	6	27-Sep-10	03-Oct-10	03-Oct-10	09-Oct-10
Brick works for 1st floor	5	02-Oct-10	06-Oct-10	07-Oct-10	12-Oct-10
pouring for roof floor's slab	1	04-Oct-10	04-Oct-10	10-Oct-10	10-Oct-10
Brick works for roof floor	5	14-Oct-10	19-Oct-10	20-Oct-10	25-Oct-10
electro mechanical	54	21-Aug-10	21-Oct-10	24-Aug-10	27-Oct-10
plumbing connections under slab on grade	2	21-Aug-10	22-Aug-10	24-Aug-10	25-Aug-10
electrical conduits for ground floor's slab	2	25-Aug-10	26-Aug-10	29-Aug-10	30-Aug-10
electrical conduits for 1st floor slab	2	13-Sep-10	14-Sep-10	19-Sep-10	20-Sep-10
electrical conduits for ground floor walls	2	26-Sep-10	27-Sep-10	02-Oct-10	03-Oct-10
electrical conduits for roof slab	1	30-Sep-10	30-Sep-10	06-Oct-10	06-Oct-10
electrical conduits for 1st floor walls	2	07-Oct-10	09-Oct-10	13-Oct-10	14-Oct-10
electrical conduits for roof floor walls	2	20-Oct-10	21-Oct-10	26-Oct-10	27-Oct-10
finishing	29	28-Sep-10	31-Oct-10	04-Oct-10	06-Nov-10
Internal plastering for ground floor	8	28-Sep-10	06-Oct-10	04-Oct-10	12-Oct-10
Internal plastering for 1st floor	8	10-Oct-10	18-Oct-10	16-Oct-10	24-Oct-10
External plastering	10	20-Oct-10	31-Oct-10	26-Oct-10	06-Nov-10
Internal plastering for roof floor	5	23-Oct-10	27-Oct-10	28-Oct-10	02-Nov-10
Villa Number D90	99	29-Jun-10 A	31-Oct-10	21-Jun-10	07-Nov-10
general dates	89	29-Jun-10 A	31-Oct-10	21-Jun-10	07-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	

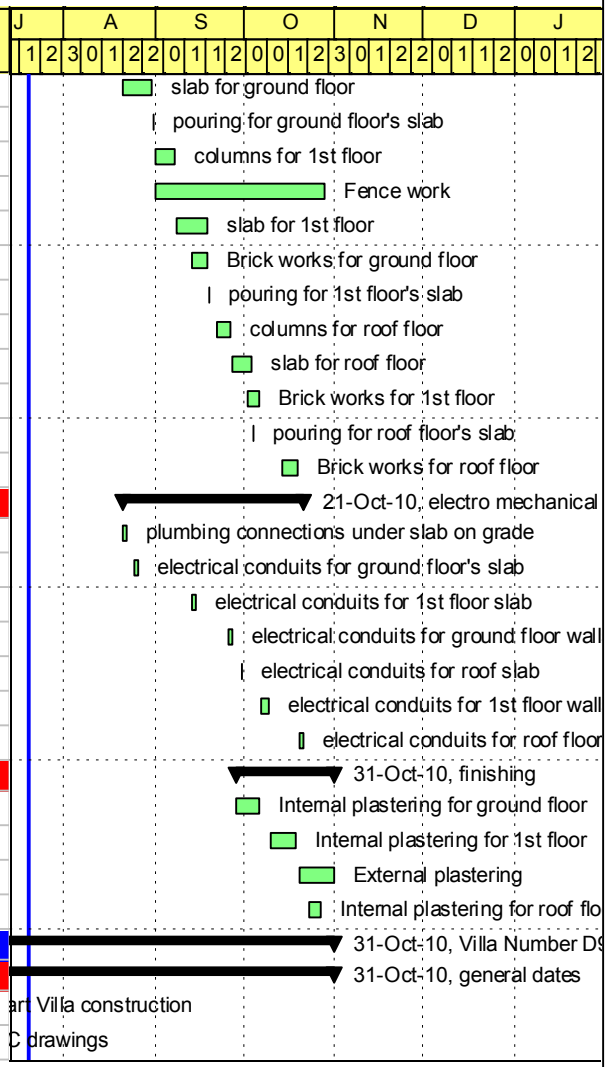

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		31-Oct-10		07-Nov-10
earth works	14	30-Jun-10 A	20-Jul-10 A	08-Jul-10	24-Jul-10
excavation	0	30-Jun-10 A	01-Jul-10 A	08-Jul-10	08-Jul-10
soil replacement	14	02-Jul-10 A	20-Jul-10 A	08-Jul-10	24-Jul-10
foundation level	57	20-Jul-10	23-Sep-10	25-Jul-10	30-Sep-10
Plain Concrete Foundation	2	20-Jul-10	21-Jul-10	25-Jul-10	26-Jul-10
backfilling between P.C Foundation	2	24-Jul-10	25-Jul-10	28-Jul-10	29-Jul-10
P.C Under Smells	1	26-Jul-10	26-Jul-10	31-Jul-10	31-Jul-10
Reinforced Concrete Foundation	7	27-Jul-10	03-Aug-10	01-Aug-10	08-Aug-10
under ground brick works	2	11-Aug-10	12-Aug-10	16-Aug-10	17-Aug-10
under ground insulation for RC & Brick work	2	14-Aug-10	15-Aug-10	18-Aug-10	19-Aug-10
backfilling for under ground	4	16-Aug-10	19-Aug-10	21-Aug-10	24-Aug-10
P.C slab on grade 10CM	1	19-Sep-10	19-Sep-10	26-Sep-10	26-Sep-10
moisture insulation with membrane sheets	2	20-Sep-10	21-Sep-10	27-Sep-10	28-Sep-10
R.C slab on grade	2	22-Sep-10	23-Sep-10	29-Sep-10	30-Sep-10
skeleton & brick walls	74	04-Aug-10	28-Oct-10	09-Aug-10	04-Nov-10
columns for ground floor	6	04-Aug-10	10-Aug-10	09-Aug-10	15-Aug-10
slab for ground floor	9	21-Aug-10	30-Aug-10	25-Aug-10	04-Sep-10
pouring for ground floor's slab	1	31-Aug-10	31-Aug-10	05-Sep-10	05-Sep-10
columns for 1st floor	6	01-Sep-10	07-Sep-10	06-Sep-10	14-Sep-10
Fence work	50	01-Sep-10	28-Oct-10	06-Sep-10	04-Nov-10
slab for 1st floor	9	08-Sep-10	18-Sep-10	15-Sep-10	25-Sep-10
Brick works for ground floor	5	13-Sep-10	18-Sep-10	20-Sep-10	25-Sep-10
pouring for 1st floor's slab	1	19-Sep-10	19-Sep-10	26-Sep-10	26-Sep-10
columns for roof floor	4	22-Sep-10	26-Sep-10	29-Sep-10	03-Oct-10
slab for roof floor	6	27-Sep-10	03-Oct-10	04-Oct-10	10-Oct-10
Brick works for 1st floor	5	02-Oct-10	06-Oct-10	09-Oct-10	13-Oct-10
pouring for roof floor's slab	1	04-Oct-10	04-Oct-10	11-Oct-10	11-Oct-10

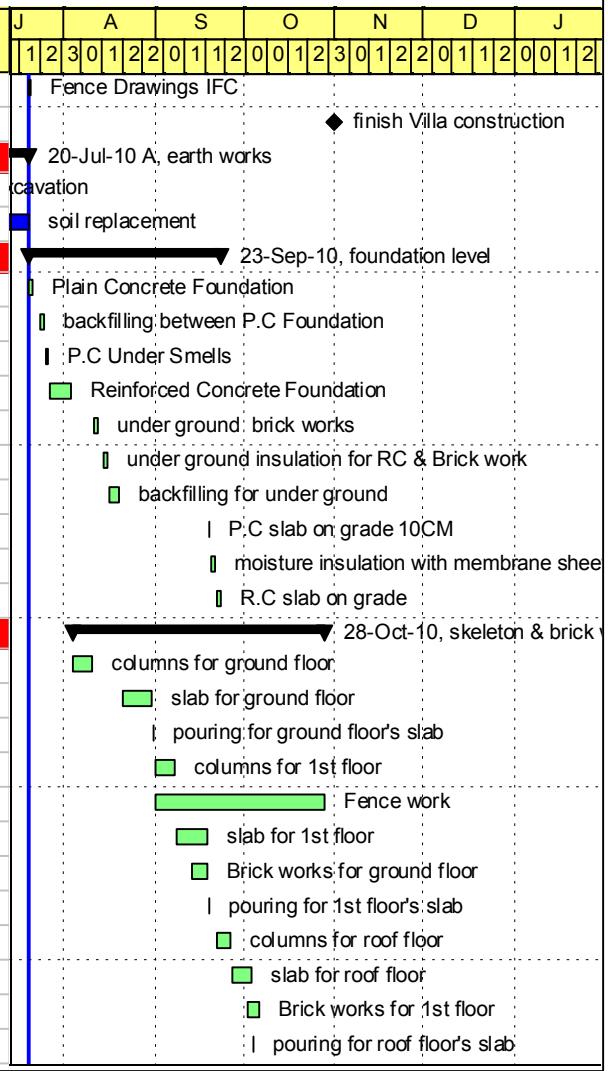

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Brick works for roof floor	5	14-Oct-10	19-Oct-10	21-Oct-10	26-Oct-10
electro mechanical	54	21-Aug-10	21-Oct-10	25-Aug-10	28-Oct-10
plumbing connections under slab on grade	2	21-Aug-10	22-Aug-10	25-Aug-10	26-Aug-10
electrical conduits for ground floor's slab	2	25-Aug-10	26-Aug-10	30-Aug-10	31-Aug-10
electrical conduits for 1st floor slab	2	13-Sep-10	14-Sep-10	20-Sep-10	21-Sep-10
electrical conduits for ground floor walls	2	26-Sep-10	27-Sep-10	03-Oct-10	04-Oct-10
electrical conduits for roof slab	1	30-Sep-10	30-Sep-10	07-Oct-10	07-Oct-10
electrical conduits for 1st floor walls	2	07-Oct-10	09-Oct-10	14-Oct-10	16-Oct-10
electrical conduits for roof floor walls	2	20-Oct-10	21-Oct-10	27-Oct-10	28-Oct-10
finishing	29	28-Sep-10	31-Oct-10	05-Oct-10	07-Nov-10
Internal plastering for ground floor	8	28-Sep-10	06-Oct-10	05-Oct-10	13-Oct-10
Internal plastering for 1st floor	8	10-Oct-10	18-Oct-10	17-Oct-10	25-Oct-10
External plastering	10	20-Oct-10	31-Oct-10	27-Oct-10	07-Nov-10
Internal plastering for roof floor	5	23-Oct-10	27-Oct-10	30-Oct-10	03-Nov-10
Villa Number D91	98	29-Jun-10 A	31-Oct-10	21-Jun-10	08-Nov-10
general dates	89	29-Jun-10 A	31-Oct-10	21-Jun-10	08-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
IFC drawings	0	29-Jul-10 A		21-Jun-10	
finish Villa construction	0		31-Oct-10		08-Nov-10
earth works	14	30-Jun-10 A	20-Jul-10 A	10-Jul-10	25-Jul-10
excavation	2	30-Jun-10 A	01-Jul-10 A	10-Jul-10	11-Jul-10
soil replacement	12	02-Jul-10 A	20-Jul-10 A	12-Jul-10	25-Jul-10
foundation level	57	20-Jul-10	23-Sep-10	26-Jul-10	02-Oct-10
Plain Concrete Foundation	2	20-Jul-10	21-Jul-10	26-Jul-10	27-Jul-10
backfilling between P.C Foundation	2	24-Jul-10	25-Jul-10	29-Jul-10	31-Jul-10
P.C Under Smells	1	26-Jul-10	26-Jul-10	01-Aug-10	01-Aug-10
Reinforced Concrete Foundation	7	27-Jul-10	03-Aug-10	02-Aug-10	09-Aug-10
under ground brick works	2	11-Aug-10	12-Aug-10	17-Aug-10	18-Aug-10

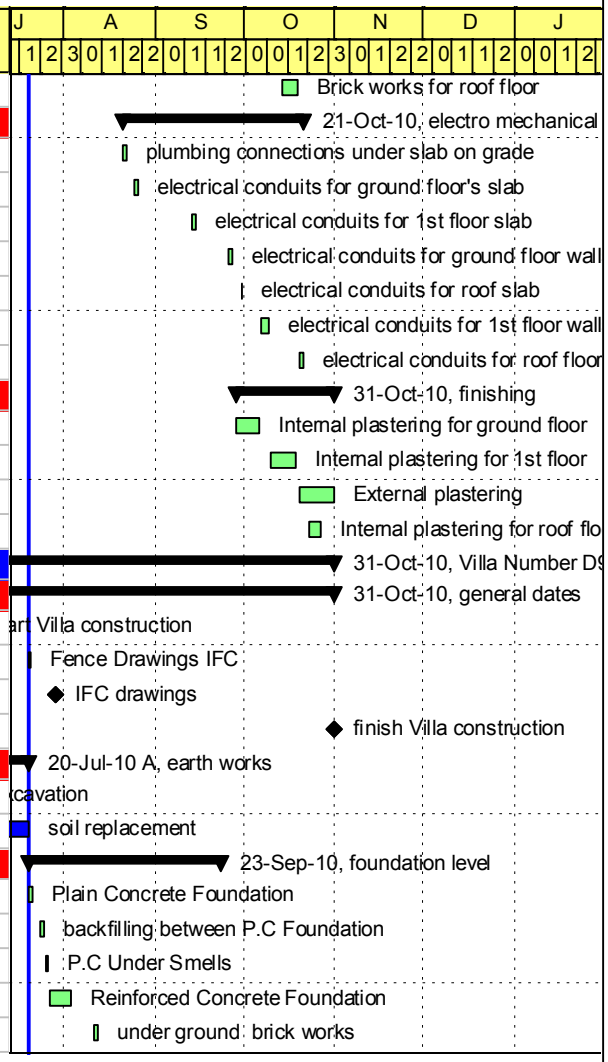

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
under ground insulation for RC & Brick work	2	14-Aug-10	15-Aug-10	19-Aug-10	21-Aug-10
backfilling for under ground	4	16-Aug-10	19-Aug-10	22-Aug-10	25-Aug-10
P.C slab on grade 10CM	1	19-Sep-10	19-Sep-10	27-Sep-10	27-Sep-10
moisture insulation with membrane sheets	2	20-Sep-10	21-Sep-10	28-Sep-10	29-Sep-10
R.C slab on grade	2	22-Sep-10	23-Sep-10	30-Sep-10	02-Oct-10
skeleton & brick walls	74	04-Aug-10	28-Oct-10	10-Aug-10	06-Nov-10
columns for ground floor	6	04-Aug-10	10-Aug-10	10-Aug-10	16-Aug-10
slab for ground floor	9	21-Aug-10	30-Aug-10	26-Aug-10	05-Sep-10
pouring for ground floor's slab	1	31-Aug-10	31-Aug-10	06-Sep-10	06-Sep-10
columns for 1st floor	6	01-Sep-10	07-Sep-10	07-Sep-10	15-Sep-10
Fence work	50	01-Sep-10	28-Oct-10	07-Sep-10	06-Nov-10
slab for 1st floor	9	08-Sep-10	18-Sep-10	16-Sep-10	26-Sep-10
Brick works for ground floor	5	13-Sep-10	18-Sep-10	21-Sep-10	26-Sep-10
pouring for 1st floor's slab	1	19-Sep-10	19-Sep-10	27-Sep-10	27-Sep-10
columns for roof floor	4	22-Sep-10	26-Sep-10	30-Sep-10	04-Oct-10
slab for roof floor	6	27-Sep-10	03-Oct-10	05-Oct-10	11-Oct-10
Brick works for 1st floor	5	02-Oct-10	06-Oct-10	10-Oct-10	14-Oct-10
pouring for roof floor's slab	1	04-Oct-10	04-Oct-10	12-Oct-10	12-Oct-10
Brick works for roof floor	5	14-Oct-10	19-Oct-10	23-Oct-10	27-Oct-10
electro mechanical	54	21-Aug-10	21-Oct-10	26-Aug-10	30-Oct-10
plumbing connections under slab on grade	2	21-Aug-10	22-Aug-10	26-Aug-10	28-Aug-10
electrical conduits for ground floor's slab	2	25-Aug-10	26-Aug-10	31-Aug-10	01-Sep-10
electrical conduits for 1st floor slab	2	13-Sep-10	14-Sep-10	21-Sep-10	22-Sep-10
electrical conduits for ground floor walls	2	26-Sep-10	27-Sep-10	04-Oct-10	05-Oct-10
electrical conduits for roof slab	1	30-Sep-10	30-Sep-10	09-Oct-10	09-Oct-10
electrical conduits for 1st floor walls	2	07-Oct-10	09-Oct-10	16-Oct-10	17-Oct-10
electrical conduits for roof floor walls	2	20-Oct-10	21-Oct-10	28-Oct-10	30-Oct-10
finishing	29	28-Sep-10	31-Oct-10	06-Oct-10	08-Nov-10
Internal plastering for ground floor	8	28-Sep-10	06-Oct-10	06-Oct-10	14-Oct-10

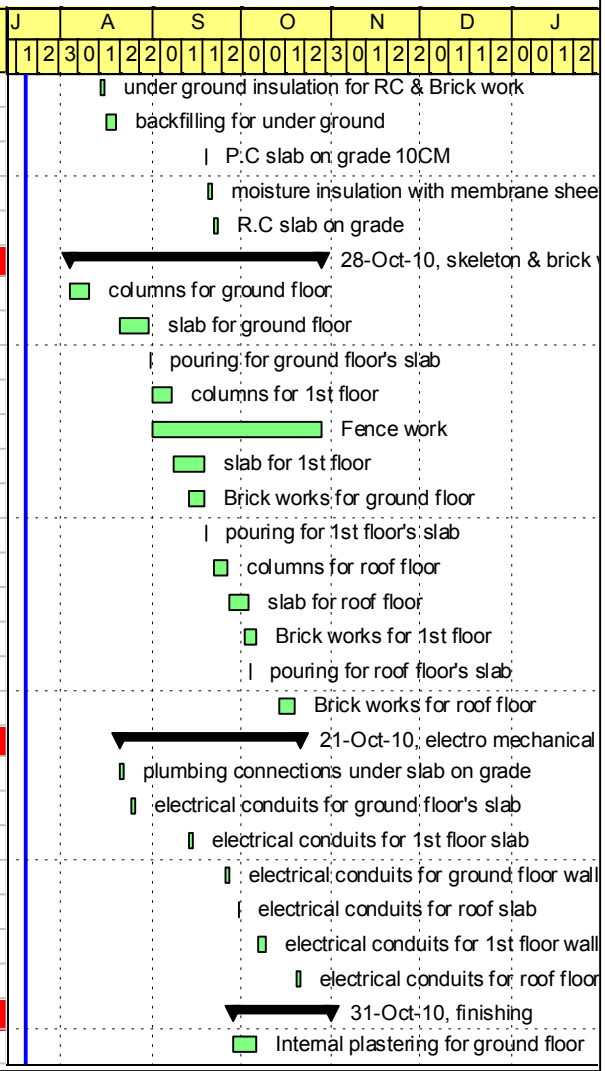

Remaining Level of Effort — Critical Remainin...
Actual Work — Milestone
Remaining Work — Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Internal plastering for 1st floor	8	10-Oct-10	18-Oct-10	18-Oct-10	26-Oct-10
External plastering	10	20-Oct-10	31-Oct-10	28-Oct-10	08-Nov-10
Internal plastering for roof floor	5	23-Oct-10	27-Oct-10	31-Oct-10	04-Nov-10
Villa Number A92	97	29-Jun-10 A	31-Oct-10	21-Jun-10	09-Nov-10
general dates	89	29-Jun-10 A	31-Oct-10	21-Jun-10	09-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		31-Oct-10		09-Nov-10
earth works	14	30-Jun-10 A	20-Jul-10 A	11-Jul-10	26-Jul-10
excavation	2	30-Jun-10 A	01-Jul-10 A	11-Jul-10	12-Jul-10
soil replacement	12	02-Jul-10 A	20-Jul-10 A	13-Jul-10	26-Jul-10
foundation level	57	20-Jul-10	23-Sep-10	27-Jul-10	03-Oct-10
Plain Concrete Foundation	2	20-Jul-10	21-Jul-10	27-Jul-10	28-Jul-10
backfilling between P.C Foundation	2	24-Jul-10	25-Jul-10	31-Jul-10	01-Aug-10
P.C Under Smells	1	26-Jul-10	26-Jul-10	02-Aug-10	02-Aug-10
Reinforced Concrete Foundation	7	27-Jul-10	03-Aug-10	03-Aug-10	10-Aug-10
under ground brick works	2	11-Aug-10	12-Aug-10	18-Aug-10	19-Aug-10
under ground insulation for RC & Brick work	2	14-Aug-10	15-Aug-10	21-Aug-10	22-Aug-10
backfilling for under ground	4	16-Aug-10	19-Aug-10	23-Aug-10	26-Aug-10
P.C slab on grade 10CM	1	19-Sep-10	19-Sep-10	28-Sep-10	28-Sep-10
moisture insulation with membrane sheets	2	20-Sep-10	21-Sep-10	29-Sep-10	30-Sep-10
R.C slab on grade	2	22-Sep-10	23-Sep-10	02-Oct-10	03-Oct-10
skeleton & brick walls	74	04-Aug-10	28-Oct-10	11-Aug-10	07-Nov-10
columns for ground floor	6	04-Aug-10	10-Aug-10	11-Aug-10	17-Aug-10
slab for ground floor	9	21-Aug-10	30-Aug-10	28-Aug-10	06-Sep-10
pouring for ground floor's slab	1	31-Aug-10	31-Aug-10	07-Sep-10	07-Sep-10
columns for 1st floor	6	01-Sep-10	07-Sep-10	11-Sep-10	16-Sep-10
Fence work	50	01-Sep-10	28-Oct-10	11-Sep-10	07-Nov-10

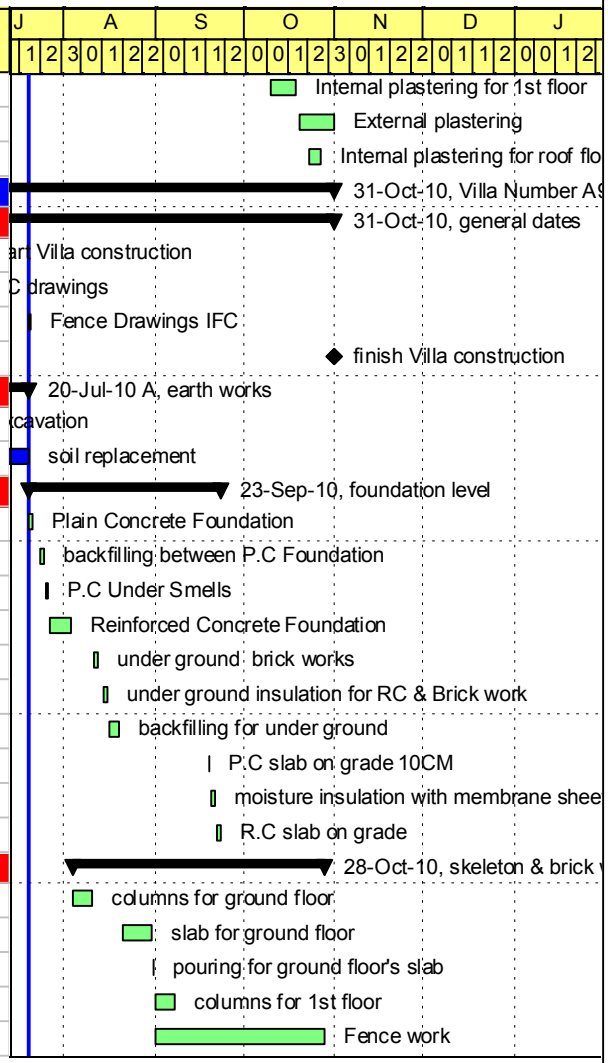

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for 1st floor	9	08-Sep-10	18-Sep-10	18-Sep-10	27-Sep-10
Brick works for ground floor	5	13-Sep-10	18-Sep-10	22-Sep-10	27-Sep-10
pouring for 1st floor's slab	1	19-Sep-10	19-Sep-10	28-Sep-10	28-Sep-10
columns for roof floor	4	22-Sep-10	26-Sep-10	02-Oct-10	05-Oct-10
slab for roof floor	6	27-Sep-10	03-Oct-10	06-Oct-10	12-Oct-10
Brick works for 1st floor	5	02-Oct-10	06-Oct-10	11-Oct-10	16-Oct-10
pouring for roof floor's slab	1	04-Oct-10	04-Oct-10	13-Oct-10	13-Oct-10
Brick works for roof floor	5	14-Oct-10	19-Oct-10	24-Oct-10	28-Oct-10
electro mechanical	54	21-Aug-10	21-Oct-10	28-Aug-10	31-Oct-10
plumbing connections under slab on grade	2	21-Aug-10	22-Aug-10	28-Aug-10	29-Aug-10
electrical conduits for ground floor's slab	2	25-Aug-10	26-Aug-10	01-Sep-10	02-Sep-10
electrical conduits for 1st floor slab	2	13-Sep-10	14-Sep-10	22-Sep-10	23-Sep-10
electrical conduits for ground floor walls	2	26-Sep-10	27-Sep-10	05-Oct-10	06-Oct-10
electrical conduits for roof slab	1	30-Sep-10	30-Sep-10	10-Oct-10	10-Oct-10
electrical conduits for 1st floor walls	2	07-Oct-10	09-Oct-10	17-Oct-10	18-Oct-10
electrical conduits for roof floor walls	2	20-Oct-10	21-Oct-10	30-Oct-10	31-Oct-10
finishing	29	28-Sep-10	31-Oct-10	07-Oct-10	09-Nov-10
Internal plastering for ground floor	8	28-Sep-10	06-Oct-10	07-Oct-10	16-Oct-10
Internal plastering for 1st floor	8	10-Oct-10	18-Oct-10	19-Oct-10	27-Oct-10
External plastering	10	20-Oct-10	31-Oct-10	30-Oct-10	09-Nov-10
Internal plastering for roof floor	5	23-Oct-10	27-Oct-10	01-Nov-10	06-Nov-10
Villa Number F93	97	28-Jun-10 A	02-Nov-10	21-Jun-10	10-Nov-10
general dates	90	28-Jun-10 A	02-Nov-10	21-Jun-10	10-Nov-10
Start Villa construction	0	28-Jun-10 A		21-Jun-10	
IFC drawings	0	28-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		02-Nov-10		10-Nov-10
earth works	14	29-Jun-10 A	21-Jul-10	12-Jul-10	27-Jul-10
excavation	0	29-Jun-10 A	01-Jul-10 A	12-Jul-10	12-Jul-10

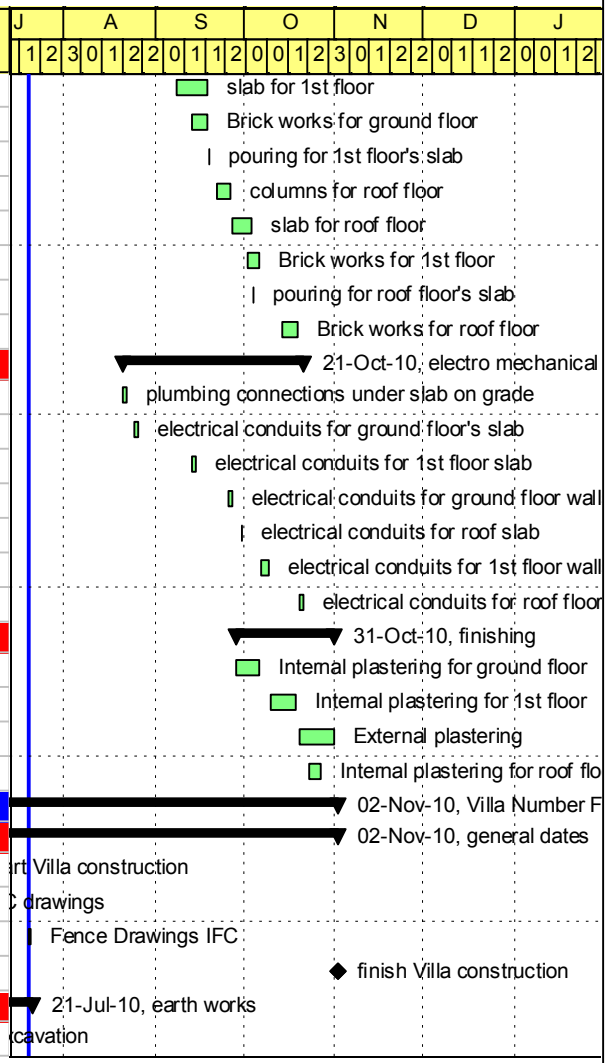

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
soil replacement	14	02-Jul-10 A	21-Jul-10	12-Jul-10	27-Jul-10
foundation level	57	21-Jul-10	26-Sep-10	28-Jul-10	04-Oct-10
Plain Concrete Foundation	2	21-Jul-10	24-Jul-10	28-Jul-10	29-Jul-10
backfilling between P.C Foundation	2	25-Jul-10	27-Jul-10	01-Aug-10	02-Aug-10
P.C Under Smells	1	27-Jul-10	28-Jul-10	03-Aug-10	03-Aug-10
Reinforced Concrete Foundation	7	28-Jul-10	05-Aug-10	04-Aug-10	11-Aug-10
under ground brick works	2	12-Aug-10	15-Aug-10	19-Aug-10	21-Aug-10
under ground insulation for RC & Brick work	2	15-Aug-10	17-Aug-10	22-Aug-10	23-Aug-10
backfilling for under ground	4	17-Aug-10	22-Aug-10	24-Aug-10	28-Aug-10
P.C slab on grade 10CM	1	20-Sep-10	21-Sep-10	29-Sep-10	29-Sep-10
moisture insulation with membrane sheets	2	21-Sep-10	23-Sep-10	30-Sep-10	02-Oct-10
R.C slab on grade	2	23-Sep-10	26-Sep-10	03-Oct-10	04-Oct-10
skeleton & brick walls	74	05-Aug-10	31-Oct-10	12-Aug-10	08-Nov-10
columns for ground floor	6	05-Aug-10	12-Aug-10	12-Aug-10	18-Aug-10
slab for ground floor	9	22-Aug-10	01-Sep-10	29-Aug-10	07-Sep-10
pouring for ground floor's slab	1	01-Sep-10	02-Sep-10	11-Sep-10	11-Sep-10
columns for 1st floor	6	02-Sep-10	09-Sep-10	12-Sep-10	18-Sep-10
Fence work	50	02-Sep-10	31-Oct-10	12-Sep-10	08-Nov-10
slab for 1st floor	9	09-Sep-10	20-Sep-10	19-Sep-10	28-Sep-10
Brick works for ground floor	5	14-Sep-10	20-Sep-10	23-Sep-10	28-Sep-10
pouring for 1st floor's slab	1	20-Sep-10	21-Sep-10	29-Sep-10	29-Sep-10
columns for roof floor	4	23-Sep-10	28-Sep-10	03-Oct-10	06-Oct-10
slab for roof floor	6	28-Sep-10	05-Oct-10	07-Oct-10	13-Oct-10
Brick works for 1st floor	5	03-Oct-10	09-Oct-10	12-Oct-10	17-Oct-10
pouring for roof floor's slab	1	05-Oct-10	06-Oct-10	14-Oct-10	14-Oct-10
Brick works for roof floor	5	16-Oct-10	21-Oct-10	25-Oct-10	30-Oct-10
electro mechanical	54	22-Aug-10	24-Oct-10	29-Aug-10	01-Nov-10
plumbing connections under slab on grade	2	22-Aug-10	24-Aug-10	29-Aug-10	30-Aug-10
electrical conduits for ground floor's slab	2	26-Aug-10	29-Aug-10	02-Sep-10	04-Sep-10

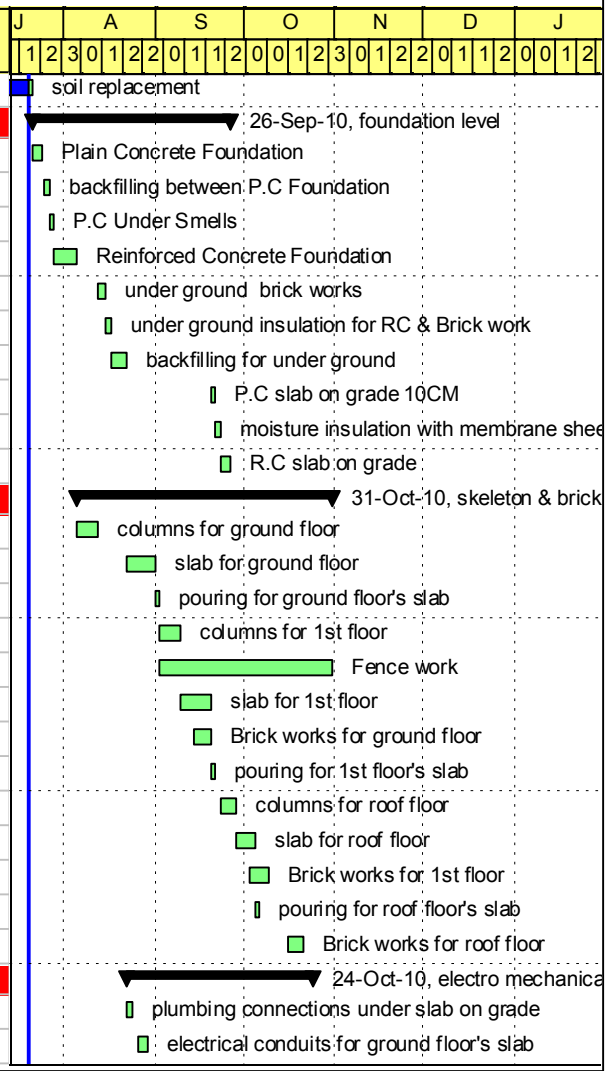

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
electrical conduits for 1st floor slab	2	14-Sep-10	16-Sep-10	23-Sep-10	25-Sep-10
electrical conduits for ground floor walls	2	27-Sep-10	29-Sep-10	06-Oct-10	07-Oct-10
electrical conduits for roof slab	1	02-Oct-10	03-Oct-10	11-Oct-10	11-Oct-10
electrical conduits for 1st floor walls	2	09-Oct-10	11-Oct-10	18-Oct-10	19-Oct-10
electrical conduits for roof floor walls	2	21-Oct-10	24-Oct-10	31-Oct-10	01-Nov-10
finishing	29	29-Sep-10	02-Nov-10	09-Oct-10	10-Nov-10
Internal plastering for ground floor	8	29-Sep-10	09-Oct-10	09-Oct-10	17-Oct-10
Internal plastering for 1st floor	8	11-Oct-10	20-Oct-10	20-Oct-10	28-Oct-10
External plastering	10	21-Oct-10	02-Nov-10	31-Oct-10	10-Nov-10
Internal plastering for roof floor	5	24-Oct-10	30-Oct-10	02-Nov-10	07-Nov-10
Villa Number F94	96	29-Jun-10 A	02-Nov-10	21-Jun-10	11-Nov-10
general dates	90	29-Jun-10 A	02-Nov-10	21-Jun-10	11-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		02-Nov-10		11-Nov-10
earth works	14	30-Jun-10 A	21-Jul-10	13-Jul-10	28-Jul-10
excavation	0	30-Jun-10 A	01-Jul-10 A	13-Jul-10	13-Jul-10
soil replacement	14	02-Jul-10 A	21-Jul-10	13-Jul-10	28-Jul-10
foundation level	57	21-Jul-10	26-Sep-10	29-Jul-10	05-Oct-10
Plain Concrete Foundation	2	21-Jul-10	24-Jul-10	29-Jul-10	31-Jul-10
backfilling between P.C Foundation	2	25-Jul-10	27-Jul-10	02-Aug-10	03-Aug-10
P.C Under Smells	1	27-Jul-10	28-Jul-10	04-Aug-10	04-Aug-10
Reinforced Concrete Foundation	7	28-Jul-10	05-Aug-10	05-Aug-10	12-Aug-10
under ground brick works	2	12-Aug-10	15-Aug-10	21-Aug-10	22-Aug-10
under ground insulation for RC & Brick work	2	15-Aug-10	17-Aug-10	23-Aug-10	24-Aug-10
backfilling for under ground	4	17-Aug-10	22-Aug-10	25-Aug-10	29-Aug-10
P.C slab on grade 10CM	1	20-Sep-10	21-Sep-10	30-Sep-10	30-Sep-10
moisture insulation with membrane sheets	2	21-Sep-10	23-Sep-10	02-Oct-10	03-Oct-10

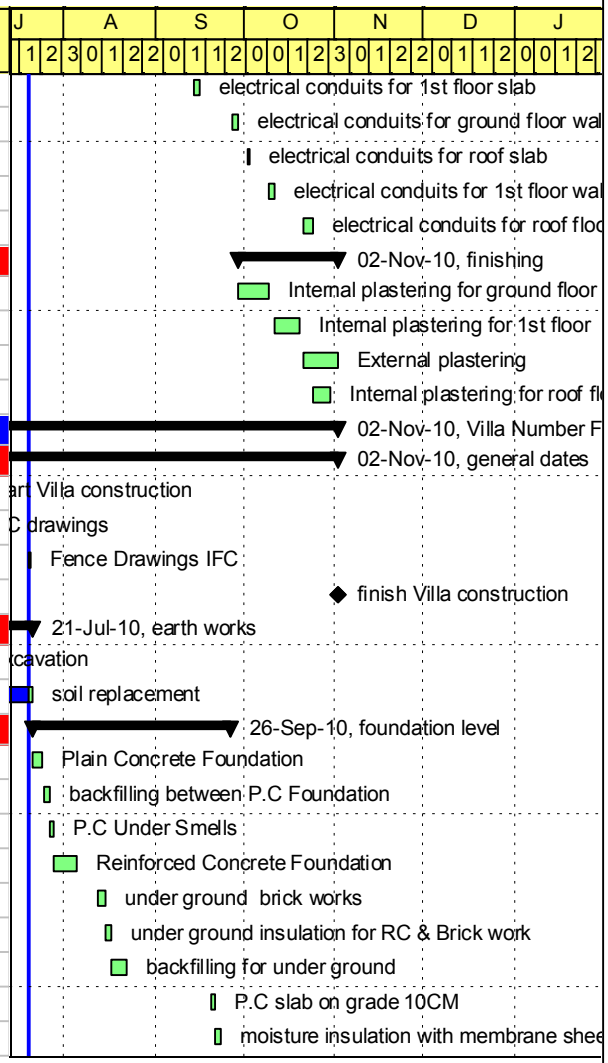

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
R.C slab on grade	2	23-Sep-10	26-Sep-10	04-Oct-10	05-Oct-10
skeleton & brick walls	74	05-Aug-10	31-Oct-10	14-Aug-10	09-Nov-10
columns for ground floor	6	05-Aug-10	12-Aug-10	14-Aug-10	19-Aug-10
slab for ground floor	9	22-Aug-10	01-Sep-10	30-Aug-10	11-Sep-10
pouring for ground floor's slab	1	01-Sep-10	02-Sep-10	12-Sep-10	12-Sep-10
columns for 1st floor	6	02-Sep-10	09-Sep-10	13-Sep-10	19-Sep-10
Fence work	50	02-Sep-10	31-Oct-10	13-Sep-10	09-Nov-10
slab for 1st floor	9	09-Sep-10	20-Sep-10	20-Sep-10	29-Sep-10
Brick works for ground floor	5	14-Sep-10	20-Sep-10	25-Sep-10	29-Sep-10
pouring for 1st floor's slab	1	20-Sep-10	21-Sep-10	30-Sep-10	30-Sep-10
columns for roof floor	4	23-Sep-10	28-Sep-10	04-Oct-10	07-Oct-10
slab for roof floor	6	28-Sep-10	05-Oct-10	09-Oct-10	14-Oct-10
Brick works for 1st floor	5	03-Oct-10	09-Oct-10	13-Oct-10	18-Oct-10
pouring for roof floor's slab	1	05-Oct-10	06-Oct-10	16-Oct-10	16-Oct-10
Brick works for roof floor	5	16-Oct-10	21-Oct-10	26-Oct-10	31-Oct-10
electro mechanical	54	22-Aug-10	24-Oct-10	30-Aug-10	02-Nov-10
plumbing connections under slab on grade	2	22-Aug-10	24-Aug-10	30-Aug-10	31-Aug-10
electrical conduits for ground floor's slab	2	26-Aug-10	29-Aug-10	04-Sep-10	05-Sep-10
electrical conduits for 1st floor slab	2	14-Sep-10	16-Sep-10	25-Sep-10	26-Sep-10
electrical conduits for ground floor walls	2	27-Sep-10	29-Sep-10	07-Oct-10	09-Oct-10
electrical conduits for roof slab	1	02-Oct-10	03-Oct-10	12-Oct-10	12-Oct-10
electrical conduits for 1st floor walls	2	09-Oct-10	11-Oct-10	19-Oct-10	20-Oct-10
electrical conduits for roof floor walls	2	21-Oct-10	24-Oct-10	01-Nov-10	02-Nov-10
finishing	29	29-Sep-10	02-Nov-10	10-Oct-10	11-Nov-10
Internal plastering for ground floor	8	29-Sep-10	09-Oct-10	10-Oct-10	18-Oct-10
Internal plastering for 1st floor	8	11-Oct-10	20-Oct-10	21-Oct-10	30-Oct-10
External plastering	10	21-Oct-10	02-Nov-10	01-Nov-10	11-Nov-10
Internal plastering for roof floor	5	24-Oct-10	30-Oct-10	03-Nov-10	08-Nov-10
Villa Number A95	97	29-Jun-10 A	02-Nov-10	21-Jun-10	10-Nov-10

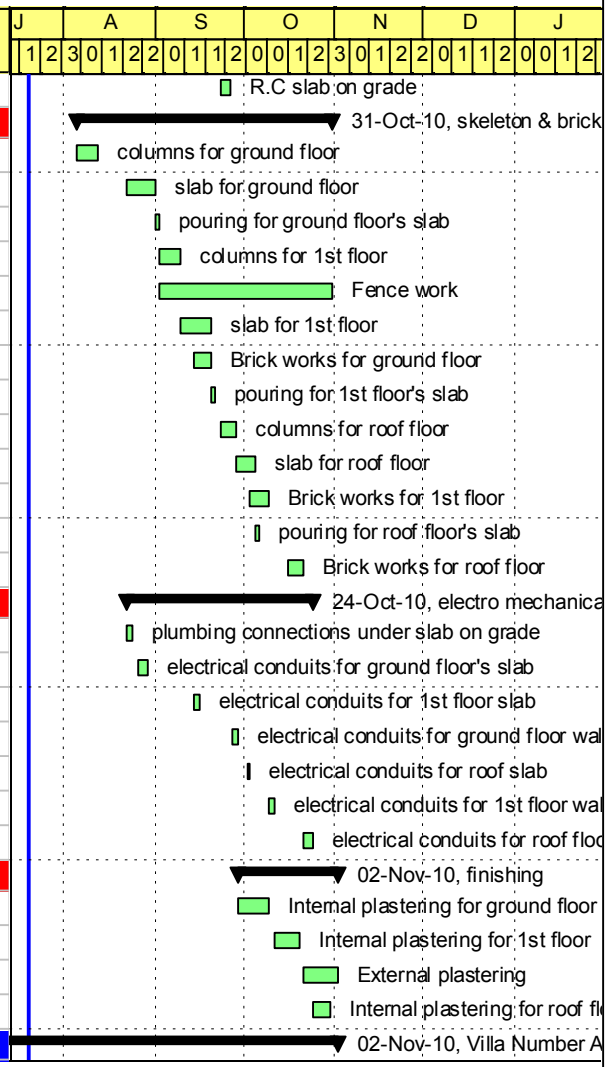

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
general dates	90	29-Jun-10 A	02-Nov-10	21-Jun-10	10-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		02-Nov-10		10-Nov-10
earth works	14	30-Jun-10 A	21-Jul-10	12-Jul-10	27-Jul-10
excavation	2	30-Jun-10 A	30-Jun-10 A	12-Jul-10	13-Jul-10
soil replacement	12	02-Jul-10 A	21-Jul-10	14-Jul-10	27-Jul-10
foundation level	57	21-Jul-10	26-Sep-10	28-Jul-10	04-Oct-10
Plain Concrete Foundation	2	21-Jul-10	24-Jul-10	28-Jul-10	29-Jul-10
backfilling between P.C Foundation	2	25-Jul-10	27-Jul-10	01-Aug-10	02-Aug-10
P.C Under Smells	1	27-Jul-10	28-Jul-10	03-Aug-10	03-Aug-10
Reinforced Concrete Foundation	7	28-Jul-10	05-Aug-10	04-Aug-10	11-Aug-10
under ground brick works	2	12-Aug-10	15-Aug-10	19-Aug-10	21-Aug-10
under ground insulation for RC & Brick work	2	15-Aug-10	17-Aug-10	22-Aug-10	23-Aug-10
backfilling for under ground	4	17-Aug-10	22-Aug-10	24-Aug-10	28-Aug-10
P.C slab on grade 10CM	1	20-Sep-10	21-Sep-10	29-Sep-10	29-Sep-10
moisture insulation with membrane sheets	2	21-Sep-10	23-Sep-10	30-Sep-10	02-Oct-10
R.C slab on grade	2	23-Sep-10	26-Sep-10	03-Oct-10	04-Oct-10
skeleton & brick walls	74	05-Aug-10	31-Oct-10	12-Aug-10	08-Nov-10
columns for ground floor	6	05-Aug-10	12-Aug-10	12-Aug-10	18-Aug-10
slab for ground floor	9	22-Aug-10	01-Sep-10	29-Aug-10	07-Sep-10
pouring for ground floor's slab	1	01-Sep-10	02-Sep-10	11-Sep-10	11-Sep-10
columns for 1st floor	6	02-Sep-10	09-Sep-10	12-Sep-10	18-Sep-10
Fence work	50	02-Sep-10	31-Oct-10	12-Sep-10	08-Nov-10
slab for 1st floor	9	09-Sep-10	20-Sep-10	19-Sep-10	28-Sep-10
Brick works for ground floor	5	14-Sep-10	20-Sep-10	23-Sep-10	28-Sep-10
pouring for 1st floor's slab	1	20-Sep-10	21-Sep-10	29-Sep-10	29-Sep-10
columns for roof floor	4	23-Sep-10	28-Sep-10	03-Oct-10	06-Oct-10

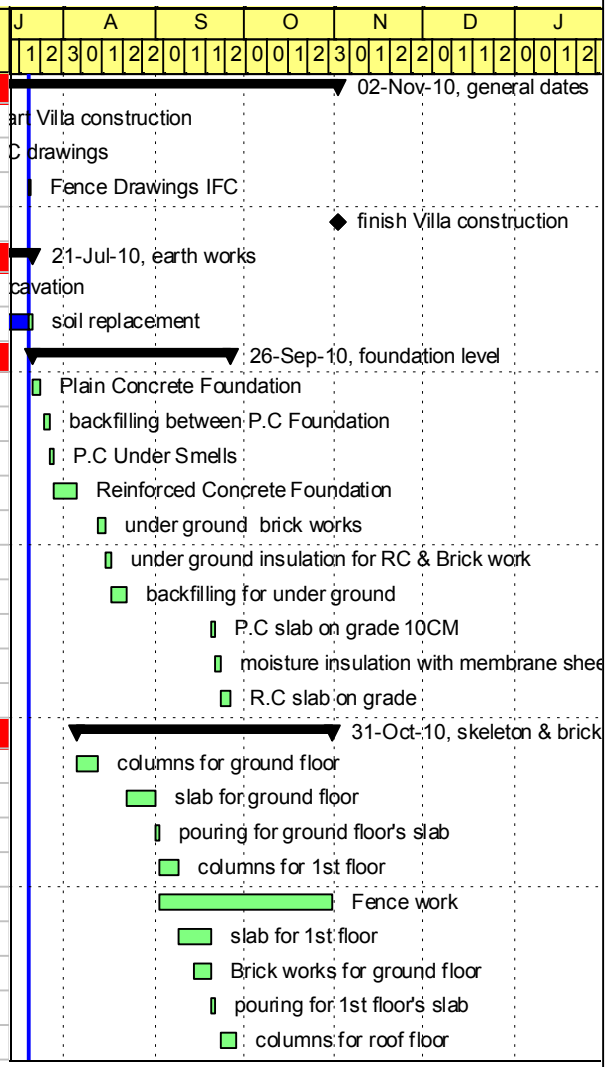

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for roof floor	6	28-Sep-10	05-Oct-10	07-Oct-10	13-Oct-10
Brick works for 1st floor	5	03-Oct-10	09-Oct-10	12-Oct-10	17-Oct-10
pouring for roof floor's slab	1	05-Oct-10	06-Oct-10	14-Oct-10	14-Oct-10
Brick works for roof floor	5	16-Oct-10	21-Oct-10	25-Oct-10	30-Oct-10
electro mechanical	54	22-Aug-10	24-Oct-10	29-Aug-10	01-Nov-10
plumbing connections under slab on grade	2	22-Aug-10	24-Aug-10	29-Aug-10	30-Aug-10
electrical conduits for ground floor's slab	2	26-Aug-10	29-Aug-10	02-Sep-10	04-Sep-10
electrical conduits for 1st floor slab	2	14-Sep-10	16-Sep-10	23-Sep-10	25-Sep-10
electrical conduits for ground floor walls	2	27-Sep-10	29-Sep-10	06-Oct-10	07-Oct-10
electrical conduits for roof slab	1	02-Oct-10	03-Oct-10	11-Oct-10	11-Oct-10
electrical conduits for 1st floor walls	2	09-Oct-10	11-Oct-10	18-Oct-10	19-Oct-10
electrical conduits for roof floor walls	2	21-Oct-10	24-Oct-10	31-Oct-10	01-Nov-10
finishing	29	29-Sep-10	02-Nov-10	09-Oct-10	10-Nov-10
Internal plastering for ground floor	8	29-Sep-10	09-Oct-10	09-Oct-10	17-Oct-10
Internal plastering for 1st floor	8	11-Oct-10	20-Oct-10	20-Oct-10	28-Oct-10
External plastering	10	21-Oct-10	02-Nov-10	31-Oct-10	10-Nov-10
Internal plastering for roof floor	5	24-Oct-10	30-Oct-10	02-Nov-10	07-Nov-10
Villa Number A96	96	29-Jun-10 A	02-Nov-10	21-Jun-10	11-Nov-10
general dates	90	29-Jun-10 A	02-Nov-10	21-Jun-10	11-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		02-Nov-10		11-Nov-10
earth works	14	30-Jun-10 A	21-Jul-10	13-Jul-10	28-Jul-10
excavation	2	30-Jun-10 A	30-Jun-10 A	13-Jul-10	14-Jul-10
soil replacement	12	02-Jul-10 A	21-Jul-10	15-Jul-10	28-Jul-10
foundation level	57	21-Jul-10	26-Sep-10	29-Jul-10	05-Oct-10
Plain Concrete Foundation	2	21-Jul-10	24-Jul-10	29-Jul-10	31-Jul-10
backfilling between P.C Foundation	2	25-Jul-10	27-Jul-10	02-Aug-10	03-Aug-10

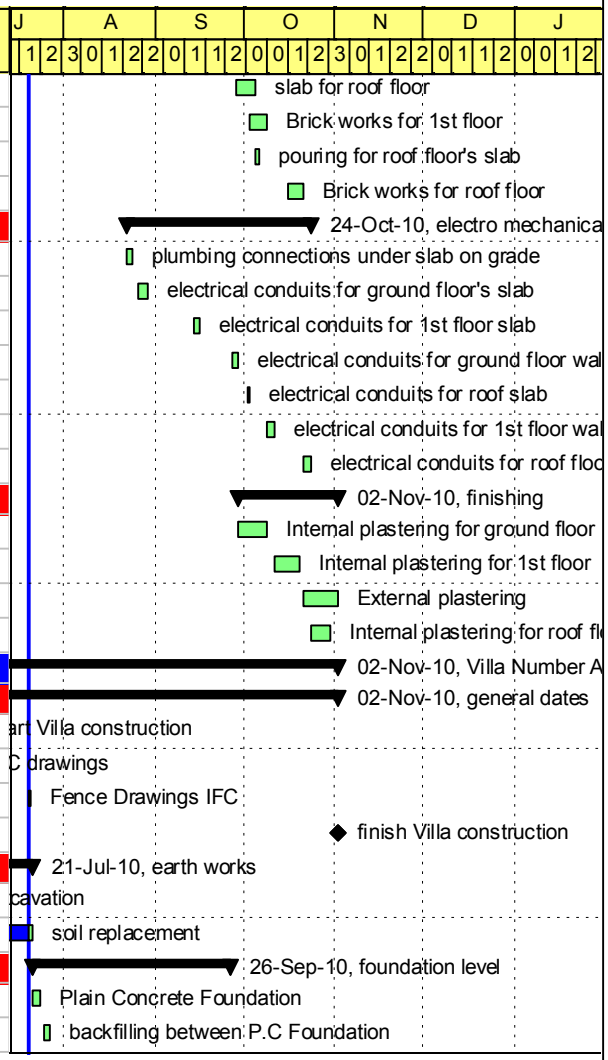

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
P.C Under Smells	1	27-Jul-10	28-Jul-10	04-Aug-10	04-Aug-10
Reinforced Concrete Foundation	7	28-Jul-10	05-Aug-10	05-Aug-10	12-Aug-10
under ground brick works	2	12-Aug-10	15-Aug-10	21-Aug-10	22-Aug-10
under ground insulation for RC & Brick work	2	15-Aug-10	17-Aug-10	23-Aug-10	24-Aug-10
backfilling for under ground	4	17-Aug-10	22-Aug-10	25-Aug-10	29-Aug-10
P.C slab on grade 10CM	1	20-Sep-10	21-Sep-10	30-Sep-10	30-Sep-10
moisture insulation with membrane sheets	2	21-Sep-10	23-Sep-10	02-Oct-10	03-Oct-10
R.C slab on grade	2	23-Sep-10	26-Sep-10	04-Oct-10	05-Oct-10
skeleton & brick walls	74	05-Aug-10	31-Oct-10	14-Aug-10	09-Nov-10
columns for ground floor	6	05-Aug-10	12-Aug-10	14-Aug-10	19-Aug-10
slab for ground floor	9	22-Aug-10	01-Sep-10	30-Aug-10	11-Sep-10
pouring for ground floor's slab	1	01-Sep-10	02-Sep-10	12-Sep-10	12-Sep-10
columns for 1st floor	6	02-Sep-10	09-Sep-10	13-Sep-10	19-Sep-10
Fence work	50	02-Sep-10	31-Oct-10	13-Sep-10	09-Nov-10
slab for 1st floor	9	09-Sep-10	20-Sep-10	20-Sep-10	29-Sep-10
Brick works for ground floor	5	14-Sep-10	20-Sep-10	25-Sep-10	29-Sep-10
pouring for 1st floor's slab	1	20-Sep-10	21-Sep-10	30-Sep-10	30-Sep-10
columns for roof floor	4	23-Sep-10	28-Sep-10	04-Oct-10	07-Oct-10
slab for roof floor	6	28-Sep-10	05-Oct-10	09-Oct-10	14-Oct-10
Brick works for 1st floor	5	03-Oct-10	09-Oct-10	13-Oct-10	18-Oct-10
pouring for roof floor's slab	1	05-Oct-10	06-Oct-10	16-Oct-10	16-Oct-10
Brick works for roof floor	5	16-Oct-10	21-Oct-10	26-Oct-10	31-Oct-10
electro mechanical	54	22-Aug-10	24-Oct-10	30-Aug-10	02-Nov-10
plumbing connections under slab on grade	2	22-Aug-10	24-Aug-10	30-Aug-10	31-Aug-10
electrical conduits for ground floor's slab	2	26-Aug-10	29-Aug-10	04-Sep-10	05-Sep-10
electrical conduits for 1st floor slab	2	14-Sep-10	16-Sep-10	25-Sep-10	26-Sep-10
electrical conduits for ground floor walls	2	27-Sep-10	29-Sep-10	07-Oct-10	09-Oct-10
electrical conduits for roof slab	1	02-Oct-10	03-Oct-10	12-Oct-10	12-Oct-10
electrical conduits for 1st floor walls	2	09-Oct-10	11-Oct-10	19-Oct-10	20-Oct-10

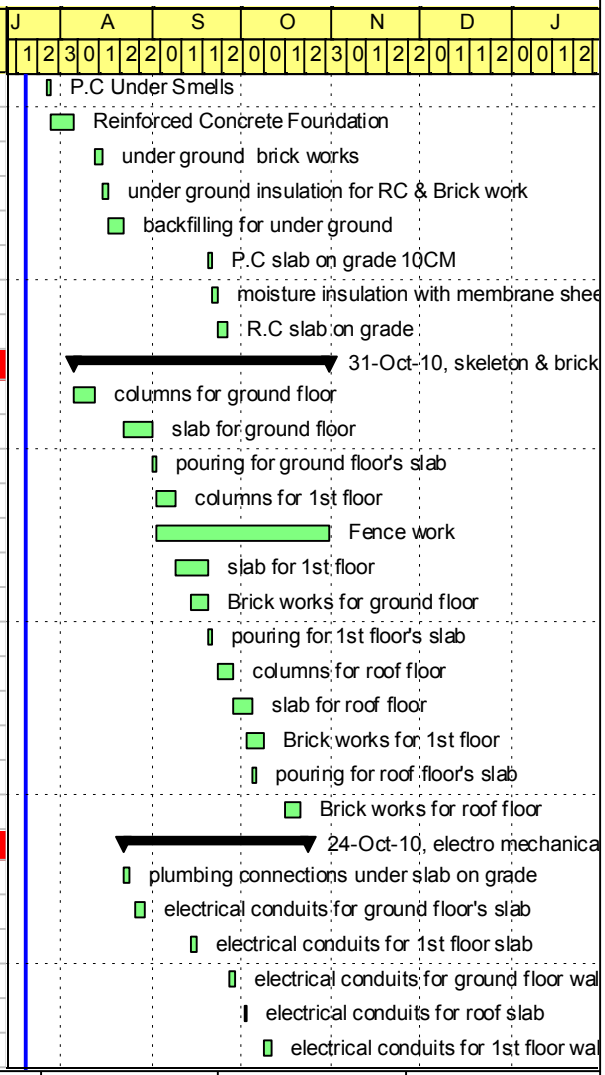

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
electrical conduits for roof floor walls	2	21-Oct-10	24-Oct-10	01-Nov-10	02-Nov-10
finishing	29	29-Sep-10	02-Nov-10	10-Oct-10	11-Nov-10
Internal plastering for ground floor	8	29-Sep-10	09-Oct-10	10-Oct-10	18-Oct-10
Internal plastering for 1st floor	8	11-Oct-10	20-Oct-10	21-Oct-10	30-Oct-10
External plastering	10	21-Oct-10	02-Nov-10	01-Nov-10	11-Nov-10
Internal plastering for roof floor	5	24-Oct-10	30-Oct-10	03-Nov-10	08-Nov-10
Villa Number A97	95	29-Jun-10 A	02-Nov-10	21-Jun-10	13-Nov-10
general dates	90	29-Jun-10 A	02-Nov-10	21-Jun-10	13-Nov-10
Start Villa construction	0	29-Jun-10 A		21-Jun-10	
IFC drawings	0	29-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		02-Nov-10		13-Nov-10
earth works	14	30-Jun-10 A	21-Jul-10	14-Jul-10	29-Jul-10
excavation	2	30-Jun-10 A	01-Jul-10 A	14-Jul-10	15-Jul-10
soil replacement	12	02-Jul-10 A	21-Jul-10	17-Jul-10	29-Jul-10
foundation level	57	21-Jul-10	26-Sep-10	31-Jul-10	06-Oct-10
Plain Concrete Foundation	2	21-Jul-10	24-Jul-10	31-Jul-10	01-Aug-10
backfilling between P.C Foundation	2	25-Jul-10	27-Jul-10	03-Aug-10	04-Aug-10
P.C Under Smells	1	27-Jul-10	28-Jul-10	05-Aug-10	05-Aug-10
Reinforced Concrete Foundation	7	28-Jul-10	05-Aug-10	07-Aug-10	14-Aug-10
under ground brick works	2	12-Aug-10	15-Aug-10	22-Aug-10	23-Aug-10
under ground insulation for RC & Brick work	2	15-Aug-10	17-Aug-10	24-Aug-10	25-Aug-10
backfilling for under ground	4	17-Aug-10	22-Aug-10	26-Aug-10	30-Aug-10
P.C slab on grade 10CM	1	20-Sep-10	21-Sep-10	02-Oct-10	02-Oct-10
moisture insulation with membrane sheets	2	21-Sep-10	23-Sep-10	03-Oct-10	04-Oct-10
R.C slab on grade	2	23-Sep-10	26-Sep-10	05-Oct-10	06-Oct-10
skeleton & brick walls	74	05-Aug-10	31-Oct-10	15-Aug-10	10-Nov-10
columns for ground floor	6	05-Aug-10	12-Aug-10	15-Aug-10	21-Aug-10
slab for ground floor	9	22-Aug-10	01-Sep-10	31-Aug-10	12-Sep-10

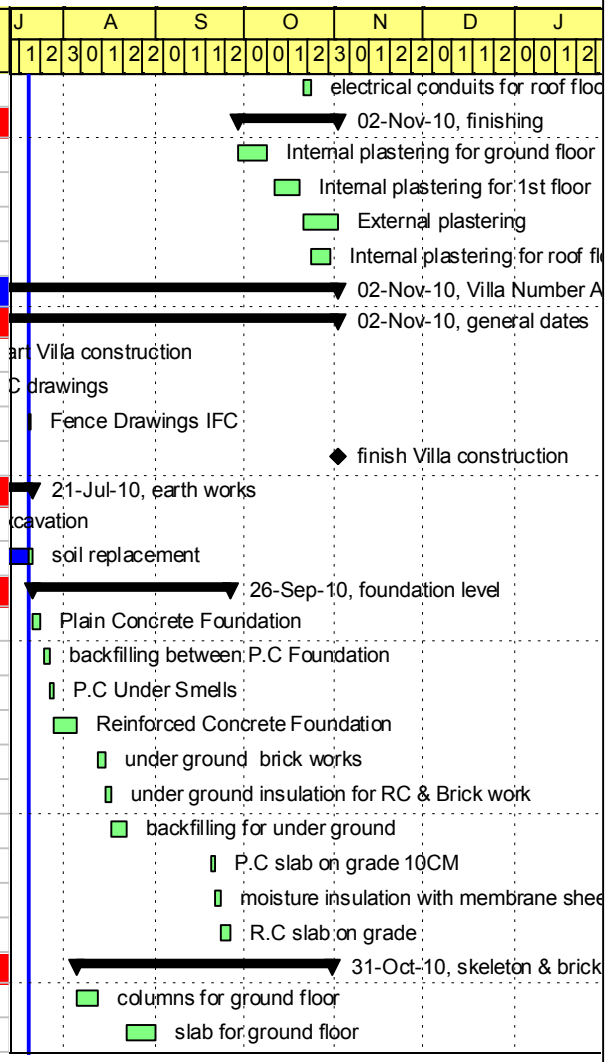

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
pouring for ground floor's slab	1	01-Sep-10	02-Sep-10	13-Sep-10	13-Sep-10
columns for 1st floor	6	02-Sep-10	09-Sep-10	14-Sep-10	20-Sep-10
Fence work	50	02-Sep-10	31-Oct-10	14-Sep-10	10-Nov-10
slab for 1st floor	9	09-Sep-10	20-Sep-10	21-Sep-10	30-Sep-10
Brick works for ground floor	5	14-Sep-10	20-Sep-10	26-Sep-10	30-Sep-10
pouring for 1st floor's slab	1	20-Sep-10	21-Sep-10	02-Oct-10	02-Oct-10
columns for roof floor	4	23-Sep-10	28-Sep-10	05-Oct-10	09-Oct-10
slab for roof floor	6	28-Sep-10	05-Oct-10	10-Oct-10	16-Oct-10
Brick works for 1st floor	5	03-Oct-10	09-Oct-10	14-Oct-10	19-Oct-10
pouring for roof floor's slab	1	05-Oct-10	06-Oct-10	17-Oct-10	17-Oct-10
Brick works for roof floor	5	16-Oct-10	21-Oct-10	27-Oct-10	01-Nov-10
electro mechanical	54	22-Aug-10	24-Oct-10	31-Aug-10	03-Nov-10
plumbing connections under slab on grade	2	22-Aug-10	24-Aug-10	31-Aug-10	01-Sep-10
electrical conduits for ground floor's slab	2	26-Aug-10	29-Aug-10	05-Sep-10	06-Sep-10
electrical conduits for 1st floor slab	2	14-Sep-10	16-Sep-10	26-Sep-10	27-Sep-10
electrical conduits for ground floor walls	2	27-Sep-10	29-Sep-10	09-Oct-10	10-Oct-10
electrical conduits for roof slab	1	02-Oct-10	03-Oct-10	13-Oct-10	13-Oct-10
electrical conduits for 1st floor walls	2	09-Oct-10	11-Oct-10	20-Oct-10	21-Oct-10
electrical conduits for roof floor walls	2	21-Oct-10	24-Oct-10	02-Nov-10	03-Nov-10
finishing	29	29-Sep-10	02-Nov-10	11-Oct-10	13-Nov-10
Internal plastering for ground floor	8	29-Sep-10	09-Oct-10	11-Oct-10	19-Oct-10
Internal plastering for 1st floor	8	11-Oct-10	20-Oct-10	23-Oct-10	31-Oct-10
External plastering	10	21-Oct-10	02-Nov-10	02-Nov-10	13-Nov-10
Internal plastering for roof floor	5	24-Oct-10	30-Oct-10	04-Nov-10	09-Nov-10
Zone.No 3	136	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
Villa Number E08	103	21-Jun-10 A	21-Nov-10	21-Jun-10	22-Nov-10
general dates	103	21-Jun-10 A	21-Nov-10	21-Jun-10	22-Nov-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	

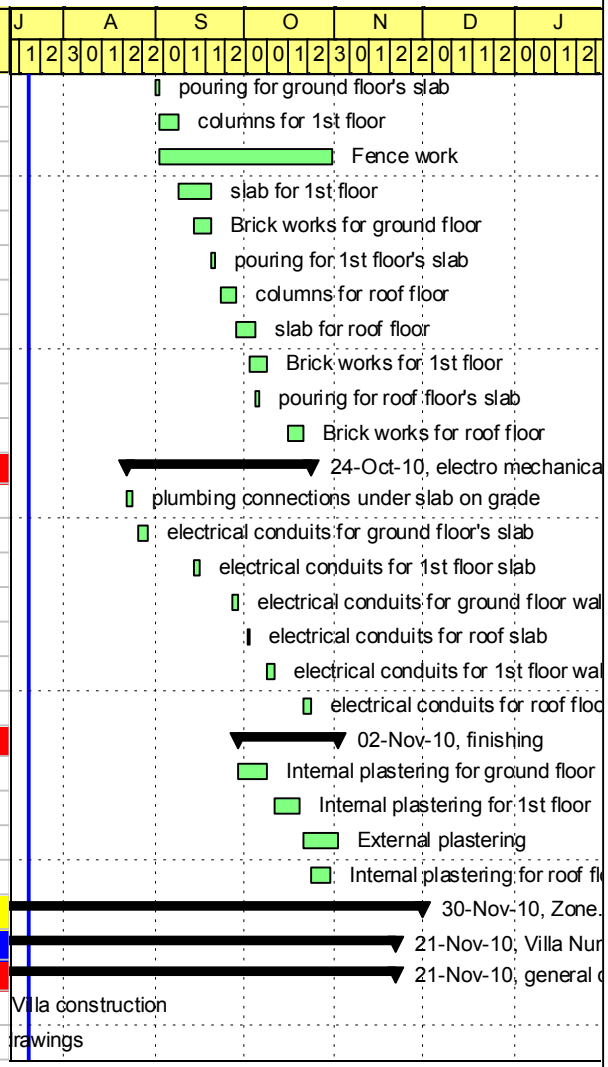

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		21-Nov-10		22-Nov-10
earth works	14	20-Jul-10	04-Aug-10	19-Jul-10	03-Aug-10
excavation	2	20-Jul-10	21-Jul-10	19-Jul-10	20-Jul-10
soil replacement	12	22-Jul-10	04-Aug-10	21-Jul-10	03-Aug-10
foundation level	57	05-Aug-10	10-Oct-10	04-Aug-10	11-Oct-10
Plain Concrete Foundation	2	05-Aug-10	07-Aug-10	04-Aug-10	05-Aug-10
backfilling between P.C Foundation	2	09-Aug-10	10-Aug-10	08-Aug-10	09-Aug-10
P.C Under Smells	1	11-Aug-10	11-Aug-10	10-Aug-10	10-Aug-10
Reinforced Concrete Foundation	7	12-Aug-10	19-Aug-10	11-Aug-10	18-Aug-10
under ground brick works	2	28-Aug-10	29-Aug-10	26-Aug-10	28-Aug-10
under ground insulation for RC & Brick work	2	30-Aug-10	31-Aug-10	29-Aug-10	30-Aug-10
backfilling for under ground	4	01-Sep-10	05-Sep-10	31-Aug-10	04-Sep-10
P.C slab on grade 10CM	1	05-Oct-10	05-Oct-10	06-Oct-10	06-Oct-10
moisture insulation with membrane sheets	2	06-Oct-10	07-Oct-10	07-Oct-10	09-Oct-10
R.C slab on grade	2	09-Oct-10	10-Oct-10	10-Oct-10	11-Oct-10
skeleton & brick walls	74	21-Aug-10	14-Nov-10	19-Aug-10	20-Nov-10
columns for ground floor	6	21-Aug-10	26-Aug-10	19-Aug-10	25-Aug-10
slab for ground floor	9	06-Sep-10	15-Sep-10	05-Sep-10	16-Sep-10
pouring for ground floor's slab	1	16-Sep-10	16-Sep-10	18-Sep-10	18-Sep-10
columns for 1st floor	6	18-Sep-10	23-Sep-10	19-Sep-10	25-Sep-10
Fence work	50	18-Sep-10	14-Nov-10	19-Sep-10	20-Nov-10
slab for 1st floor	9	25-Sep-10	04-Oct-10	26-Sep-10	05-Oct-10
Brick works for ground floor	5	29-Sep-10	04-Oct-10	30-Sep-10	05-Oct-10
pouring for 1st floor's slab	1	05-Oct-10	05-Oct-10	06-Oct-10	06-Oct-10
columns for roof floor	4	09-Oct-10	12-Oct-10	10-Oct-10	13-Oct-10
slab for roof floor	6	13-Oct-10	19-Oct-10	14-Oct-10	20-Oct-10
Brick works for 1st floor	5	18-Oct-10	23-Oct-10	19-Oct-10	24-Oct-10
pouring for roof floor's slab	1	20-Oct-10	20-Oct-10	21-Oct-10	21-Oct-10

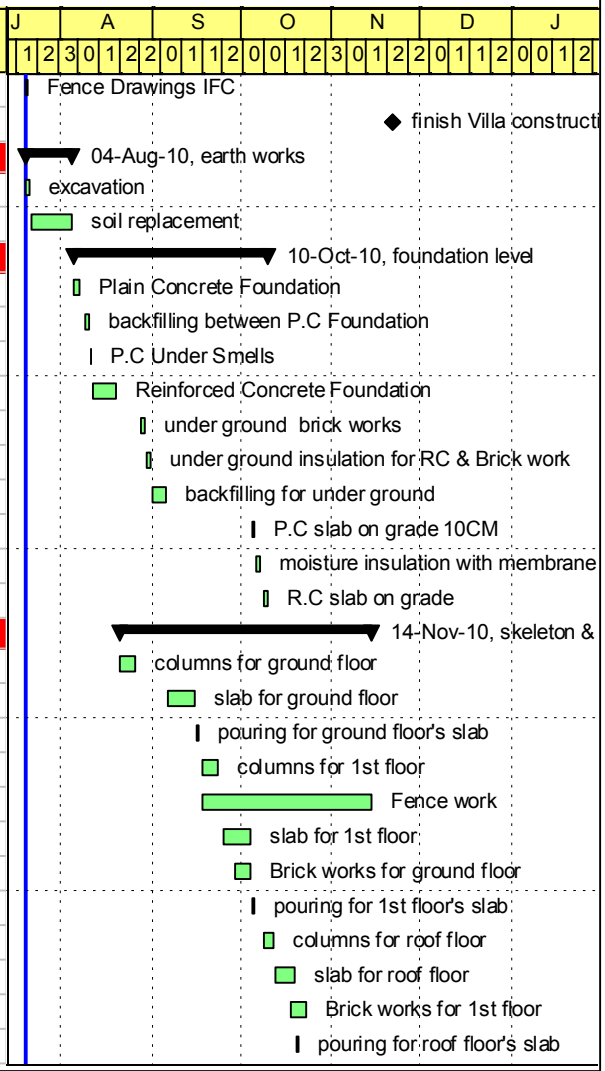

Remaining Level of Effort
Critical Remainin...
Actual Work
Milestone
Remaining Work
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Brick works for roof floor	5	31-Oct-10	04-Nov-10	01-Nov-10	06-Nov-10
electro mechanical	54	06-Sep-10	07-Nov-10	05-Sep-10	08-Nov-10
plumbing connections under slab on grade	2	06-Sep-10	07-Sep-10	05-Sep-10	06-Sep-10
electrical conduits for ground floor's slab	2	11-Sep-10	12-Sep-10	12-Sep-10	13-Sep-10
electrical conduits for 1st floor slab	2	29-Sep-10	30-Sep-10	30-Sep-10	02-Oct-10
electrical conduits for ground floor walls	2	12-Oct-10	13-Oct-10	13-Oct-10	14-Oct-10
electrical conduits for roof slab	1	17-Oct-10	17-Oct-10	18-Oct-10	18-Oct-10
electrical conduits for 1st floor walls	2	24-Oct-10	25-Oct-10	25-Oct-10	26-Oct-10
electrical conduits for roof floor walls	2	06-Nov-10	07-Nov-10	07-Nov-10	08-Nov-10
finishing	29	14-Oct-10	21-Nov-10	16-Oct-10	22-Nov-10
Internal plastering for ground floor	8	14-Oct-10	23-Oct-10	16-Oct-10	24-Oct-10
Internal plastering for 1st floor	8	26-Oct-10	03-Nov-10	27-Oct-10	04-Nov-10
External plastering	10	06-Nov-10	21-Nov-10	07-Nov-10	22-Nov-10
Internal plastering for roof floor	5	08-Nov-10	13-Nov-10	09-Nov-10	14-Nov-10
Villa Number A55	111	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
general dates	111	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		30-Nov-10		30-Nov-10
earth works	22	20-Jul-10	14-Aug-10	20-Jul-10	14-Aug-10
excavation	10	20-Jul-10	31-Jul-10	20-Jul-10	31-Jul-10
soil replacement	12	01-Aug-10	14-Aug-10	01-Aug-10	14-Aug-10
foundation level	57	15-Aug-10	19-Oct-10	15-Aug-10	21-Oct-10
Plain Concrete Foundation	2	15-Aug-10	16-Aug-10	15-Aug-10	16-Aug-10
backfilling between P.C Foundation	2	18-Aug-10	19-Aug-10	18-Aug-10	19-Aug-10
P.C Under Smells	1	21-Aug-10	21-Aug-10	21-Aug-10	21-Aug-10
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	22-Aug-10	29-Aug-10
under ground brick works	2	06-Sep-10	07-Sep-10	06-Sep-10	07-Sep-10

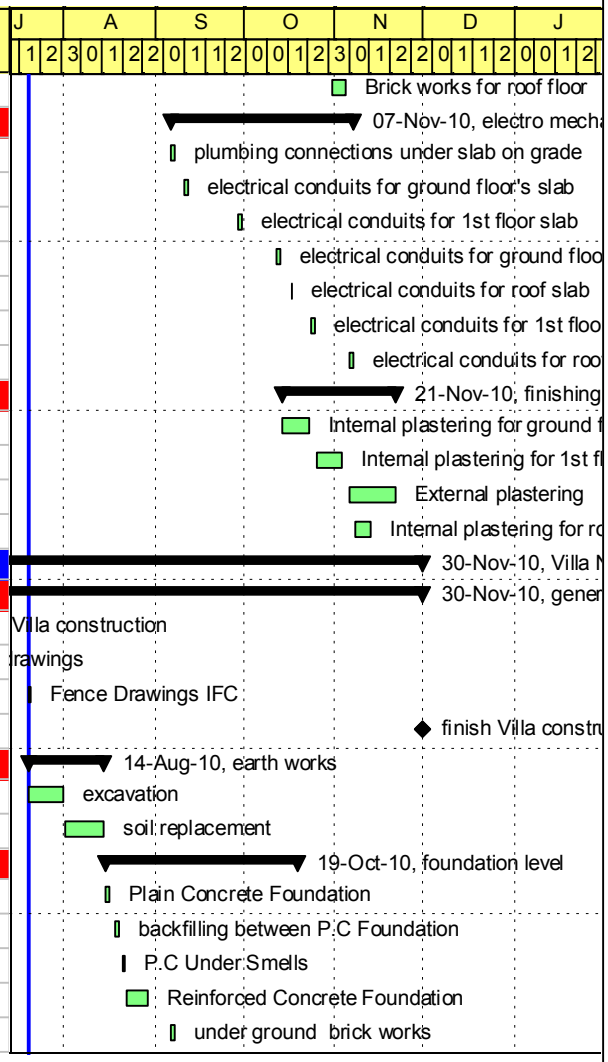

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	11-Sep-10	12-Sep-10
backfilling for under ground	4	11-Sep-10	14-Sep-10	13-Sep-10	16-Sep-10
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	17-Oct-10	17-Oct-10
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	18-Oct-10	19-Oct-10
R.C slab on grade	2	18-Oct-10	19-Oct-10	20-Oct-10	21-Oct-10
skeleton & brick walls	74	30-Aug-10	28-Nov-10	30-Aug-10	30-Nov-10
columns for ground floor	6	30-Aug-10	05-Sep-10	30-Aug-10	05-Sep-10
slab for ground floor	9	15-Sep-10	25-Sep-10	18-Sep-10	27-Sep-10
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	28-Sep-10	28-Sep-10
columns for 1st floor	6	27-Sep-10	03-Oct-10	29-Sep-10	05-Oct-10
Fence work	50	27-Sep-10	28-Nov-10	29-Sep-10	30-Nov-10
slab for 1st floor	9	04-Oct-10	13-Oct-10	06-Oct-10	16-Oct-10
Brick works for ground floor	5	09-Oct-10	13-Oct-10	11-Oct-10	16-Oct-10
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	17-Oct-10	17-Oct-10
columns for roof floor	4	18-Oct-10	21-Oct-10	20-Oct-10	24-Oct-10
slab for roof floor	6	23-Oct-10	28-Oct-10	25-Oct-10	31-Oct-10
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	30-Oct-10	03-Nov-10
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	01-Nov-10	01-Nov-10
Brick works for roof floor	5	09-Nov-10	14-Nov-10	11-Nov-10	16-Nov-10
electro mechanical	52	15-Sep-10	16-Nov-10	18-Sep-10	18-Nov-10
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	18-Sep-10	19-Sep-10
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	22-Sep-10	23-Sep-10
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	11-Oct-10	12-Oct-10
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	24-Oct-10	25-Oct-10
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	28-Oct-10	28-Oct-10
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	04-Nov-10	06-Nov-10
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	17-Nov-10	18-Nov-10
finishing	29	24-Oct-10	30-Nov-10	26-Oct-10	30-Nov-10
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	26-Oct-10	03-Nov-10

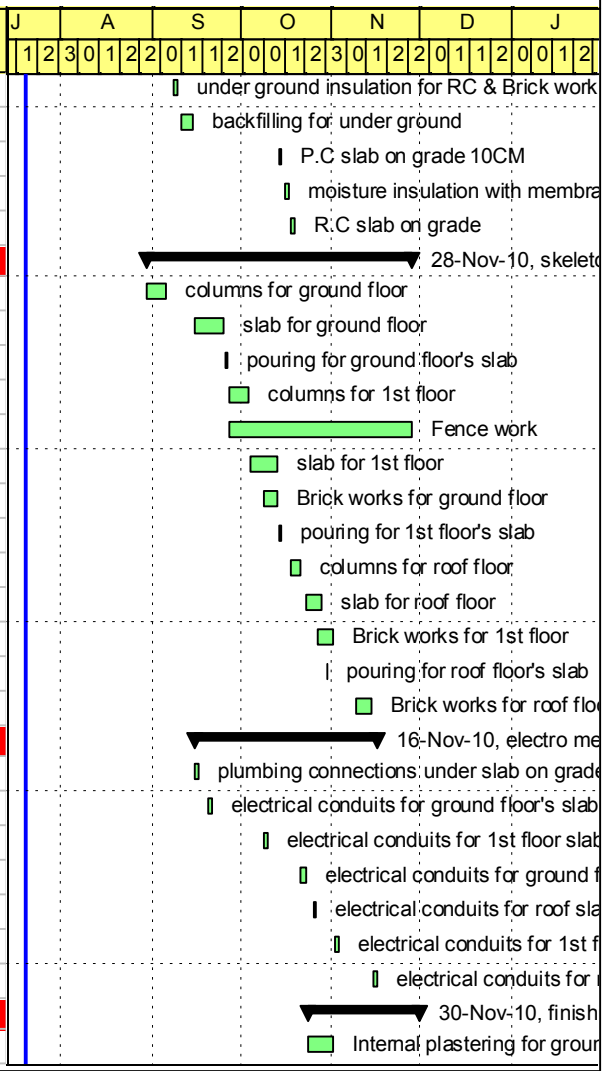

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	07-Nov-10	15-Nov-10
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	20-Nov-10	24-Nov-10
External plastering	10	20-Nov-10	30-Nov-10	20-Nov-10	30-Nov-10
Villa Number A86	111	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
general dates	111	21-Jun-10 A	30-Nov-10	21-Jun-10	30-Nov-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		30-Nov-10		30-Nov-10
earth works	22	20-Jul-10	14-Aug-10	18-Jul-10	11-Aug-10
excavation	10	20-Jul-10	31-Jul-10	18-Jul-10	28-Jul-10
soil replacement	12	01-Aug-10	14-Aug-10	29-Jul-10	11-Aug-10
foundation level	57	15-Aug-10	19-Oct-10	12-Aug-10	19-Oct-10
Plain Concrete Foundation	2	15-Aug-10	16-Aug-10	12-Aug-10	14-Aug-10
backfilling between P.C Foundation	2	18-Aug-10	19-Aug-10	16-Aug-10	17-Aug-10
P.C Under Smells	1	21-Aug-10	21-Aug-10	18-Aug-10	18-Aug-10
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	19-Aug-10	26-Aug-10
under ground brick works	2	06-Sep-10	07-Sep-10	04-Sep-10	05-Sep-10
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	06-Sep-10	07-Sep-10
backfilling for under ground	4	11-Sep-10	14-Sep-10	11-Sep-10	14-Sep-10
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	14-Oct-10	14-Oct-10
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	16-Oct-10	17-Oct-10
R.C slab on grade	2	18-Oct-10	19-Oct-10	18-Oct-10	19-Oct-10
skeleton & brick walls	74	30-Aug-10	28-Nov-10	28-Aug-10	28-Nov-10
columns for ground floor	6	30-Aug-10	05-Sep-10	28-Aug-10	02-Sep-10
slab for ground floor	9	15-Sep-10	25-Sep-10	15-Sep-10	25-Sep-10
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	26-Sep-10	26-Sep-10
columns for 1st floor	6	27-Sep-10	03-Oct-10	27-Sep-10	03-Oct-10
Fence work	50	27-Sep-10	28-Nov-10	27-Sep-10	28-Nov-10

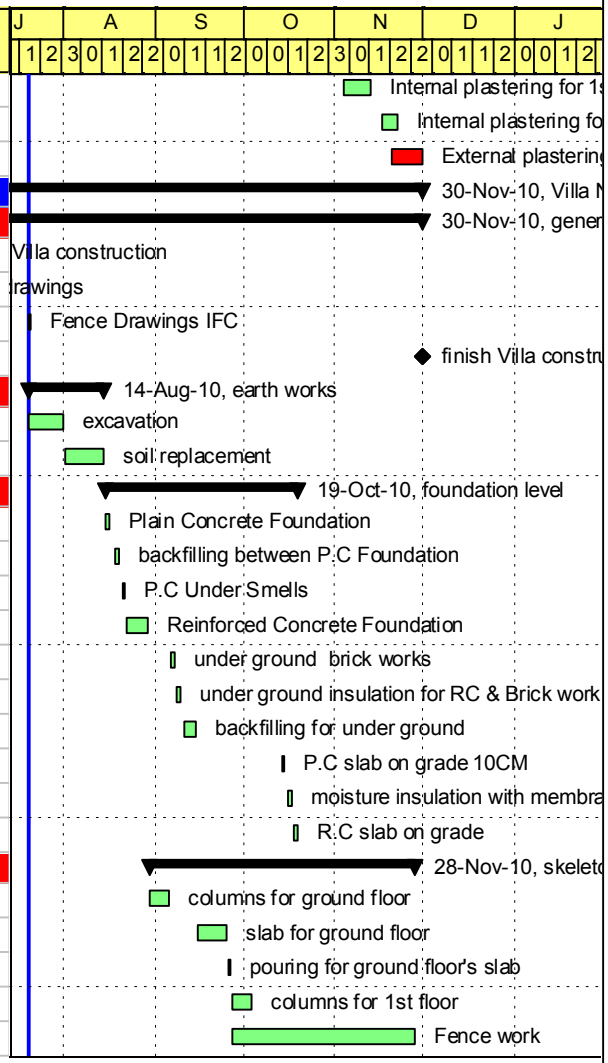

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for 1st floor	9	04-Oct-10	13-Oct-10	04-Oct-10	13-Oct-10
Brick works for ground floor	5	09-Oct-10	13-Oct-10	09-Oct-10	13-Oct-10
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	14-Oct-10	14-Oct-10
columns for roof floor	4	18-Oct-10	21-Oct-10	18-Oct-10	21-Oct-10
slab for roof floor	6	23-Oct-10	28-Oct-10	23-Oct-10	28-Oct-10
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	27-Oct-10	01-Nov-10
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	30-Oct-10	30-Oct-10
Brick works for roof floor	5	09-Nov-10	14-Nov-10	09-Nov-10	14-Nov-10
electro mechanical	52	15-Sep-10	16-Nov-10	15-Sep-10	16-Nov-10
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	15-Sep-10	16-Sep-10
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	20-Sep-10	21-Sep-10
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	09-Oct-10	10-Oct-10
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	21-Oct-10	23-Oct-10
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	26-Oct-10	26-Oct-10
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	02-Nov-10	03-Nov-10
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	15-Nov-10	16-Nov-10
finishing	29	24-Oct-10	30-Nov-10	24-Oct-10	30-Nov-10
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	24-Oct-10	01-Nov-10
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	04-Nov-10	13-Nov-10
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	17-Nov-10	22-Nov-10
External plastering	10	20-Nov-10	30-Nov-10	20-Nov-10	30-Nov-10
Villa Number A87	111	21-Jun-10 A	30-Nov-10	21-Jun-10	27-Nov-10
general dates	111	21-Jun-10 A	30-Nov-10	21-Jun-10	27-Nov-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		30-Nov-10		27-Nov-10
earth works	22	20-Jul-10	14-Aug-10	14-Jul-10	08-Aug-10
excavation	10	20-Jul-10	31-Jul-10	14-Jul-10	25-Jul-10

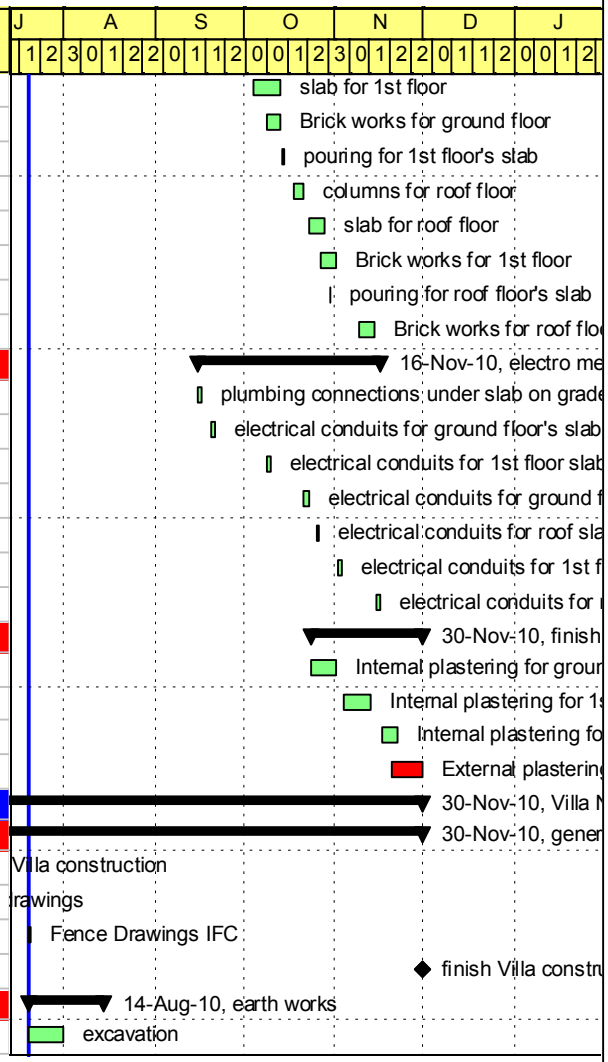

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
soil replacement	12	01-Aug-10	14-Aug-10	26-Jul-10	08-Aug-10
foundation level	57	15-Aug-10	19-Oct-10	09-Aug-10	16-Oct-10
Plain Concrete Foundation	2	15-Aug-10	16-Aug-10	09-Aug-10	10-Aug-10
backfilling between P.C Foundation	2	18-Aug-10	19-Aug-10	12-Aug-10	14-Aug-10
P.C Under Smells	1	21-Aug-10	21-Aug-10	15-Aug-10	15-Aug-10
Reinforced Concrete Foundation	7	22-Aug-10	29-Aug-10	16-Aug-10	23-Aug-10
under ground brick works	2	06-Sep-10	07-Sep-10	31-Aug-10	01-Sep-10
under ground insulation for RC & Brick work	2	08-Sep-10	09-Sep-10	02-Sep-10	04-Sep-10
backfilling for under ground	4	11-Sep-10	14-Sep-10	05-Sep-10	11-Sep-10
P.C slab on grade 10CM	1	14-Oct-10	14-Oct-10	11-Oct-10	11-Oct-10
moisture insulation with membrane sheets	2	16-Oct-10	17-Oct-10	12-Oct-10	13-Oct-10
R.C slab on grade	2	18-Oct-10	19-Oct-10	14-Oct-10	16-Oct-10
skeleton & brick walls	74	30-Aug-10	28-Nov-10	24-Aug-10	24-Nov-10
columns for ground floor	6	30-Aug-10	05-Sep-10	24-Aug-10	30-Aug-10
slab for ground floor	9	15-Sep-10	25-Sep-10	12-Sep-10	21-Sep-10
pouring for ground floor's slab	1	26-Sep-10	26-Sep-10	22-Sep-10	22-Sep-10
columns for 1st floor	6	27-Sep-10	03-Oct-10	23-Sep-10	29-Sep-10
Fence work	50	27-Sep-10	28-Nov-10	23-Sep-10	24-Nov-10
slab for 1st floor	9	04-Oct-10	13-Oct-10	30-Sep-10	10-Oct-10
Brick works for ground floor	5	09-Oct-10	13-Oct-10	05-Oct-10	10-Oct-10
pouring for 1st floor's slab	1	14-Oct-10	14-Oct-10	11-Oct-10	11-Oct-10
columns for roof floor	4	18-Oct-10	21-Oct-10	14-Oct-10	18-Oct-10
slab for roof floor	6	23-Oct-10	28-Oct-10	19-Oct-10	25-Oct-10
Brick works for 1st floor	5	27-Oct-10	01-Nov-10	24-Oct-10	28-Oct-10
pouring for roof floor's slab	1	30-Oct-10	30-Oct-10	26-Oct-10	26-Oct-10
Brick works for roof floor	5	09-Nov-10	14-Nov-10	06-Nov-10	10-Nov-10
electro mechanical	52	15-Sep-10	16-Nov-10	12-Sep-10	13-Nov-10
plumbing connections under slab on grade	2	15-Sep-10	16-Sep-10	12-Sep-10	13-Sep-10
electrical conduits for ground floor's slab	2	20-Sep-10	21-Sep-10	16-Sep-10	18-Sep-10

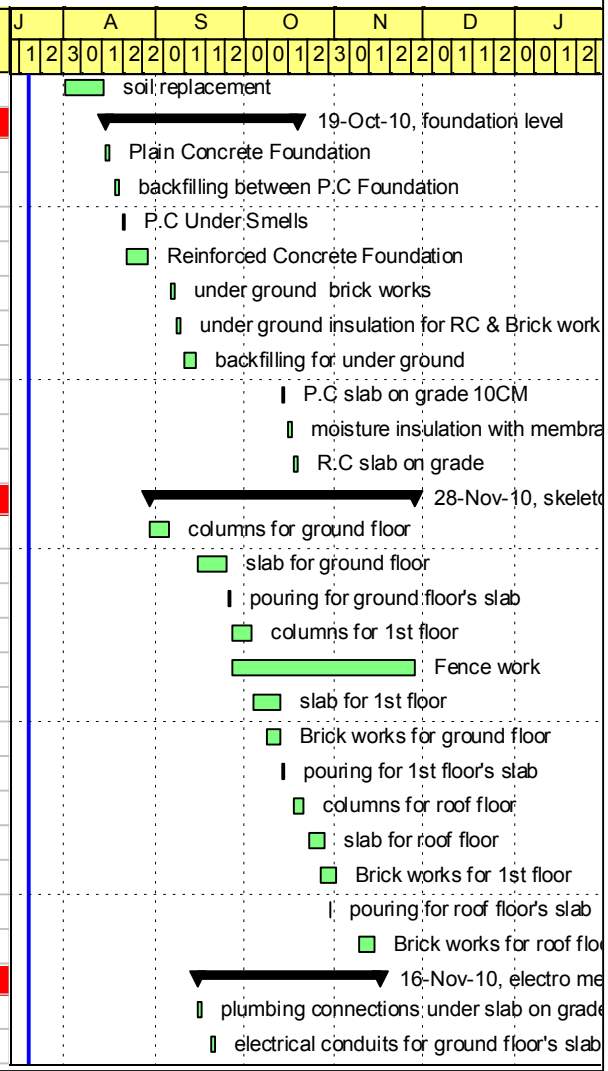

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
electrical conduits for 1st floor slab	2	09-Oct-10	10-Oct-10	05-Oct-10	06-Oct-10
electrical conduits for ground floor walls	2	21-Oct-10	23-Oct-10	18-Oct-10	19-Oct-10
electrical conduits for roof slab	1	26-Oct-10	26-Oct-10	23-Oct-10	23-Oct-10
electrical conduits for 1st floor walls	2	02-Nov-10	03-Nov-10	30-Oct-10	31-Oct-10
electrical conduits for roof floor walls	2	15-Nov-10	16-Nov-10	11-Nov-10	13-Nov-10
finishing	29	24-Oct-10	30-Nov-10	20-Oct-10	27-Nov-10
Internal plastering for ground floor	8	24-Oct-10	01-Nov-10	20-Oct-10	28-Oct-10
Internal plastering for 1st floor	8	04-Nov-10	13-Nov-10	01-Nov-10	09-Nov-10
Internal plastering for roof floor	5	17-Nov-10	22-Nov-10	14-Nov-10	18-Nov-10
External plastering	10	20-Nov-10	30-Nov-10	11-Nov-10	27-Nov-10
Villa Number B106	103	21-Jun-10 A	21-Nov-10	21-Jun-10	23-Nov-10
general dates	103	21-Jun-10 A	21-Nov-10	21-Jun-10	23-Nov-10
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		21-Nov-10		23-Nov-10
earth works	14	20-Jul-10	04-Aug-10	20-Jul-10	04-Aug-10
excavation	2	20-Jul-10	21-Jul-10	20-Jul-10	21-Jul-10
soil replacement	12	22-Jul-10	04-Aug-10	22-Jul-10	04-Aug-10
foundation level	57	05-Aug-10	10-Oct-10	05-Aug-10	12-Oct-10
Plain Concrete Foundation	2	05-Aug-10	07-Aug-10	05-Aug-10	07-Aug-10
backfilling between P.C Foundation	2	09-Aug-10	10-Aug-10	09-Aug-10	10-Aug-10
P.C Under Smells	1	11-Aug-10	11-Aug-10	11-Aug-10	11-Aug-10
Reinforced Concrete Foundation	7	12-Aug-10	19-Aug-10	12-Aug-10	19-Aug-10
under ground brick works	2	28-Aug-10	29-Aug-10	28-Aug-10	29-Aug-10
under ground insulation for RC & Brick work	2	30-Aug-10	31-Aug-10	30-Aug-10	31-Aug-10
backfilling for under ground	4	01-Sep-10	05-Sep-10	01-Sep-10	05-Sep-10
P.C slab on grade 10CM	1	05-Oct-10	05-Oct-10	07-Oct-10	07-Oct-10
moisture insulation with membrane sheets	2	06-Oct-10	07-Oct-10	09-Oct-10	10-Oct-10

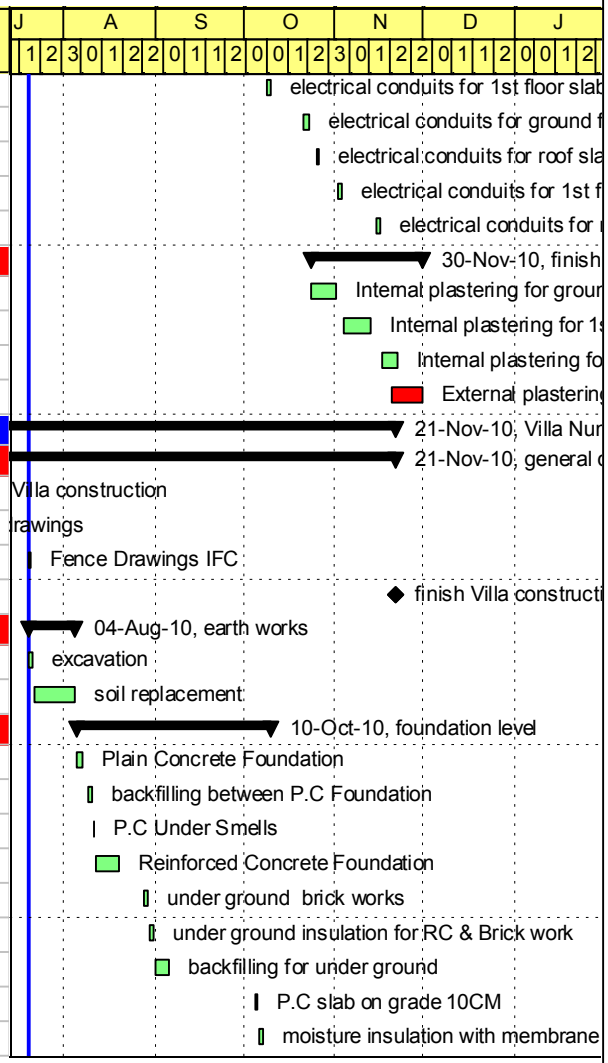

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
R.C slab on grade	2	09-Oct-10	10-Oct-10	11-Oct-10	12-Oct-10
skeleton & brick walls	74	21-Aug-10	14-Nov-10	21-Aug-10	21-Nov-10
columns for ground floor	6	21-Aug-10	26-Aug-10	21-Aug-10	26-Aug-10
slab for ground floor	9	06-Sep-10	15-Sep-10	06-Sep-10	18-Sep-10
pouring for ground floor's slab	1	16-Sep-10	16-Sep-10	19-Sep-10	19-Sep-10
columns for 1st floor	6	18-Sep-10	23-Sep-10	20-Sep-10	26-Sep-10
Fence work	50	18-Sep-10	14-Nov-10	20-Sep-10	21-Nov-10
slab for 1st floor	9	25-Sep-10	04-Oct-10	27-Sep-10	06-Oct-10
Brick works for ground floor	5	29-Sep-10	04-Oct-10	02-Oct-10	06-Oct-10
pouring for 1st floor's slab	1	05-Oct-10	05-Oct-10	07-Oct-10	07-Oct-10
columns for roof floor	4	09-Oct-10	12-Oct-10	11-Oct-10	14-Oct-10
slab for roof floor	6	13-Oct-10	19-Oct-10	16-Oct-10	21-Oct-10
Brick works for 1st floor	5	18-Oct-10	23-Oct-10	20-Oct-10	25-Oct-10
pouring for roof floor's slab	1	20-Oct-10	20-Oct-10	23-Oct-10	23-Oct-10
Brick works for roof floor	5	31-Oct-10	04-Nov-10	02-Nov-10	07-Nov-10
electro mechanical	54	06-Sep-10	07-Nov-10	06-Sep-10	09-Nov-10
plumbing connections under slab on grade	2	06-Sep-10	07-Sep-10	06-Sep-10	07-Sep-10
electrical conduits for ground floor's slab	2	11-Sep-10	12-Sep-10	13-Sep-10	14-Sep-10
electrical conduits for 1st floor slab	2	29-Sep-10	30-Sep-10	02-Oct-10	03-Oct-10
electrical conduits for ground floor walls	2	12-Oct-10	13-Oct-10	14-Oct-10	16-Oct-10
electrical conduits for roof slab	1	17-Oct-10	17-Oct-10	19-Oct-10	19-Oct-10
electrical conduits for 1st floor walls	2	24-Oct-10	25-Oct-10	26-Oct-10	27-Oct-10
electrical conduits for roof floor walls	2	06-Nov-10	07-Nov-10	08-Nov-10	09-Nov-10
finishing	29	14-Oct-10	21-Nov-10	17-Oct-10	23-Nov-10
Internal plastering for ground floor	8	14-Oct-10	23-Oct-10	17-Oct-10	25-Oct-10
Internal plastering for 1st floor	8	26-Oct-10	03-Nov-10	28-Oct-10	06-Nov-10
External plastering	10	06-Nov-10	21-Nov-10	08-Nov-10	23-Nov-10
Internal plastering for roof floor	5	08-Nov-10	13-Nov-10	10-Nov-10	15-Nov-10
Villa Number B105	128	21-Jun-10 A	21-Nov-10	21-Jun-10	23-Nov-10

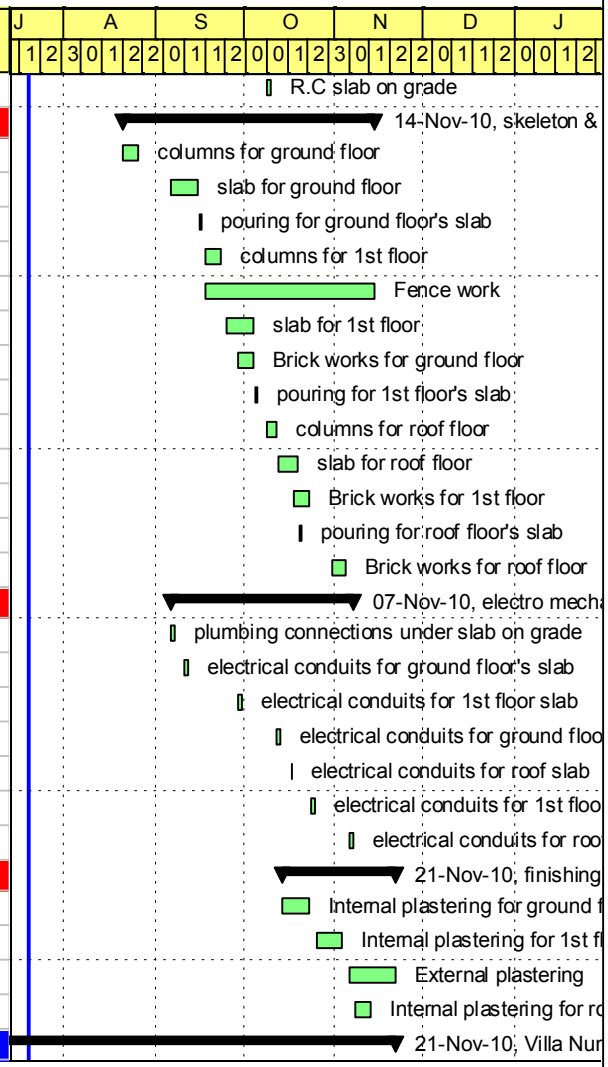

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
general dates	128	21-Jun-10 A	21-Nov-10	21-Jun-10	23-Nov-10
IFC drawings	0	21-Jun-10 A		21-Jun-10	
Start Villa construction	0	21-Jun-10 A		21-Jun-10	
Fence Drawings IFC	1	20-Jul-10	20-Jul-10	21-Jun-10	21-Jun-10
finish Villa construction	0		21-Nov-10		23-Nov-10
earth works	14	20-Jul-10	04-Aug-10	20-Jul-10	04-Aug-10
excavation	2	20-Jul-10	21-Jul-10	20-Jul-10	21-Jul-10
soil replacement	12	22-Jul-10	04-Aug-10	22-Jul-10	04-Aug-10
foundation level	57	05-Aug-10	10-Oct-10	05-Aug-10	12-Oct-10
Plain Concrete Foundation	2	05-Aug-10	07-Aug-10	05-Aug-10	07-Aug-10
backfilling between P.C Foundation	2	09-Aug-10	10-Aug-10	09-Aug-10	10-Aug-10
P.C Under Smells	1	11-Aug-10	11-Aug-10	11-Aug-10	11-Aug-10
Reinforced Concrete Foundation	7	12-Aug-10	19-Aug-10	12-Aug-10	19-Aug-10
under ground brick works	2	28-Aug-10	29-Aug-10	28-Aug-10	29-Aug-10
under ground insulation for RC & Brick work	2	30-Aug-10	31-Aug-10	30-Aug-10	31-Aug-10
backfilling for under ground	4	01-Sep-10	05-Sep-10	01-Sep-10	05-Sep-10
P.C slab on grade 10CM	1	05-Oct-10	05-Oct-10	07-Oct-10	07-Oct-10
moisture insulation with membrane sheets	2	06-Oct-10	07-Oct-10	09-Oct-10	10-Oct-10
R.C slab on grade	2	09-Oct-10	10-Oct-10	11-Oct-10	12-Oct-10
skeleton & brick walls	74	21-Aug-10	14-Nov-10	21-Aug-10	21-Nov-10
columns for ground floor	6	21-Aug-10	26-Aug-10	21-Aug-10	26-Aug-10
slab for ground floor	9	06-Sep-10	15-Sep-10	06-Sep-10	18-Sep-10
pouring for ground floor's slab	1	16-Sep-10	16-Sep-10	19-Sep-10	19-Sep-10
columns for 1st floor	6	18-Sep-10	23-Sep-10	20-Sep-10	26-Sep-10
Fence work	50	18-Sep-10	14-Nov-10	20-Sep-10	21-Nov-10
slab for 1st floor	9	25-Sep-10	04-Oct-10	27-Sep-10	06-Oct-10
Brick works for ground floor	5	29-Sep-10	04-Oct-10	02-Oct-10	06-Oct-10
pouring for 1st floor's slab	1	05-Oct-10	05-Oct-10	07-Oct-10	07-Oct-10
columns for roof floor	4	09-Oct-10	12-Oct-10	11-Oct-10	14-Oct-10

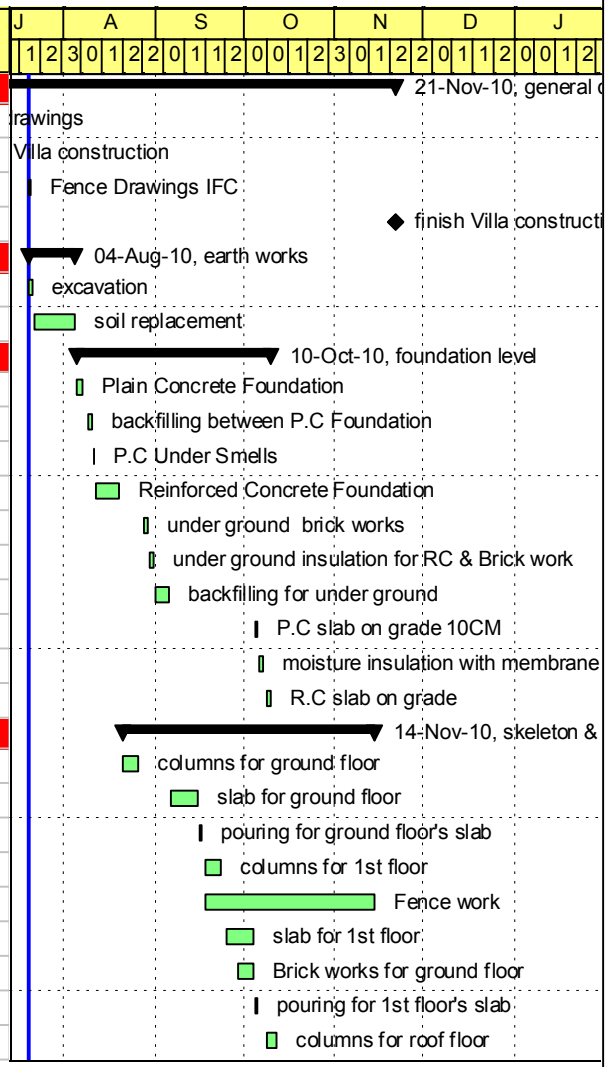

Remaining Level of Effort | Critical Remainin...
Actual Work | Milestone
Remaining Work | Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		

Gama For Trading & Contracting

Cleopatra Jungle

Dr . Ibrahim Mahfouz

Activity Name	Original Duration	Start	Finish	BL Project Start	BL Project Finish
slab for roof floor	6	13-Oct-10	19-Oct-10	16-Oct-10	21-Oct-10
Brick works for 1st floor	5	18-Oct-10	23-Oct-10	20-Oct-10	25-Oct-10
pouring for roof floor's slab	1	20-Oct-10	20-Oct-10	23-Oct-10	23-Oct-10
Brick works for roof floor	5	31-Oct-10	04-Nov-10	02-Nov-10	07-Nov-10
electro mechanical	54	06-Sep-10	07-Nov-10	06-Sep-10	09-Nov-10
plumbing connections under slab on grade	2	06-Sep-10	07-Sep-10	06-Sep-10	07-Sep-10
electrical conduits for ground floor's slab	2	11-Sep-10	12-Sep-10	13-Sep-10	14-Sep-10
electrical conduits for 1st floor slab	2	29-Sep-10	30-Sep-10	02-Oct-10	03-Oct-10
electrical conduits for ground floor walls	2	12-Oct-10	13-Oct-10	14-Oct-10	16-Oct-10
electrical conduits for roof slab	1	17-Oct-10	17-Oct-10	19-Oct-10	19-Oct-10
electrical conduits for 1st floor walls	2	24-Oct-10	25-Oct-10	26-Oct-10	27-Oct-10
electrical conduits for roof floor walls	2	06-Nov-10	07-Nov-10	08-Nov-10	09-Nov-10
finishing	29	14-Oct-10	21-Nov-10	17-Oct-10	23-Nov-10
Internal plastering for ground floor	8	14-Oct-10	23-Oct-10	17-Oct-10	25-Oct-10
Internal plastering for 1st floor	8	26-Oct-10	03-Nov-10	28-Oct-10	06-Nov-10
External plastering	10	06-Nov-10	21-Nov-10	08-Nov-10	23-Nov-10
Internal plastering for roof floor	5	08-Nov-10	13-Nov-10	10-Nov-10	15-Nov-10
Closing phase	0	30-Nov-10	30-Nov-10	30-Nov-10	30-Nov-10
end project	0		30-Nov-10		30-Nov-10

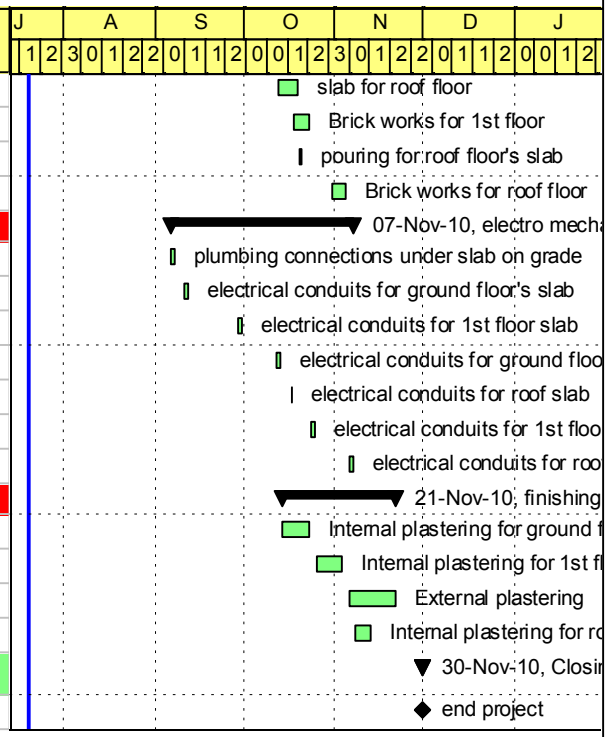

Remaining Level of Effort
Actual Work
Remaining Work
Critical Remainin...
Milestone
Summary

TASK filter: All Activities

Date	Revision	Checked	Approved
22-Jul-10	Revision 0		
